

Green Hill Solar Farm EN010170

Environmental Statement Appendix 13.2: Transport Assessment Revision A (Tracked) (Part 2 of 3)

Prepared by: KMC

Date: ~~May~~ December 2025





Document Reference: ~~APPEX3~~ GH6.3.13.2 A

APFP Regulation 5(2)(a)



Schedule of Changes

<u>Revision</u>	<u>Section Reference</u>	<u>Description of Changes</u>	<u>Reason for Revision</u>
<u>A</u>	<u>[cover]</u>	<u>Updated document reference to Revision A</u>	<u>As required for submission at Deadline 3.</u>
	<u>Appendix C (Parts 1 and 2, of 3)</u>	<u>Updated access drawings showing locations of speed surveys, speed limits, highway boundaries, and any other specific requests made by the relevant highway authorities</u>	<u>In response to Local Impact Reports</u>
	<u>Updated access drawings:</u> <ul style="list-style-type: none"><u>23061-KMC-XX-CR3-DR-CH-0001 – Cable route 3</u><u>23061-KMC-XX-CR4-DR-CH-0001 – Cable route 4</u><u>23061-KMC-XX-CR5-DR-CH-0001 – Cable route 5</u><u>23061-KMC-XX-CR6-DR-CH-0001 – Cable route 6</u><u>23061-KMC-XX-CR7-DR-CH-0001 – Cable route 7</u><u>23061-KMC-XX-CR8-9-DR-CH-0001 – Cable route 8 & 9</u><u>23061-KMC-XX-CR10-DR-CH-0001 – Cable route 10</u><u>23061-KMC-XX-CR11-DR-CH-0001 – Cable route 11</u><u>23061-KMC-XX-CR12-DR-CH-0001 – Cable route 12</u><u>23061-KMC-XX-CR13-DR-CH-0001 – Cable route 13</u><u>23061-KMC-XX-CR14-DR-CH-0001 – Cable route 14</u><u>23061-KMC-XX-CR15-DR-CH-0001 – Cable route 15</u><u>23061-KMC-XX-CR16-DR-CH-0001 – Cable route 16</u><u>23061-KMC-XX-CR17-DR-CH-0001 – Cable route 17</u><u>23061-KMC-XX-CR18-DR-CH-0001 – Cable route 18</u><u>23061-KMC-XX-CR19-20-DR-CH-0001 – Cable route 19 & 20</u><u>23061-KMC-XX-CR21-22-DR-CH-0001 – Cable route 21 & 22</u><u>23061-KMC-XX-CR23-DR-CH-0001 – Cable route 23</u><u>23061-KMC-XX-CR24-DR-CH-0001 – Cable route 24</u>		

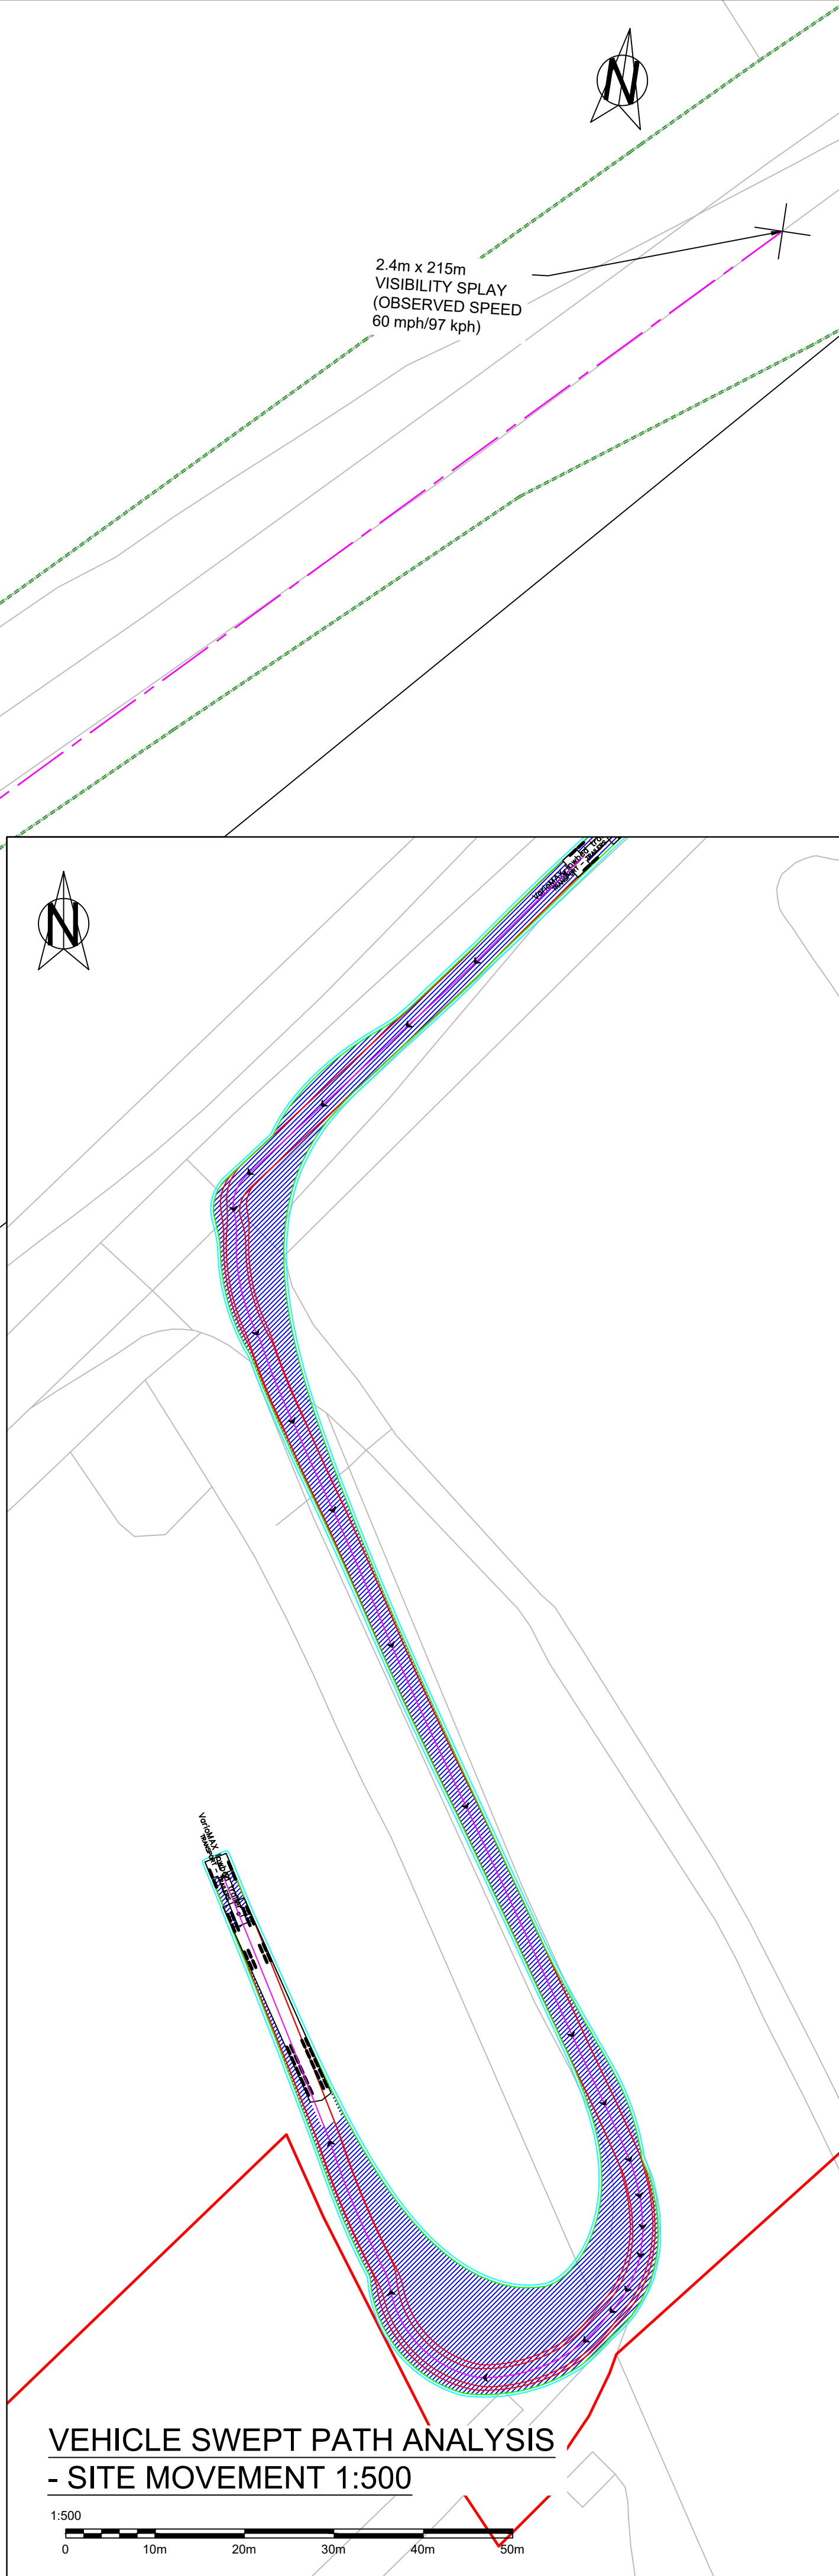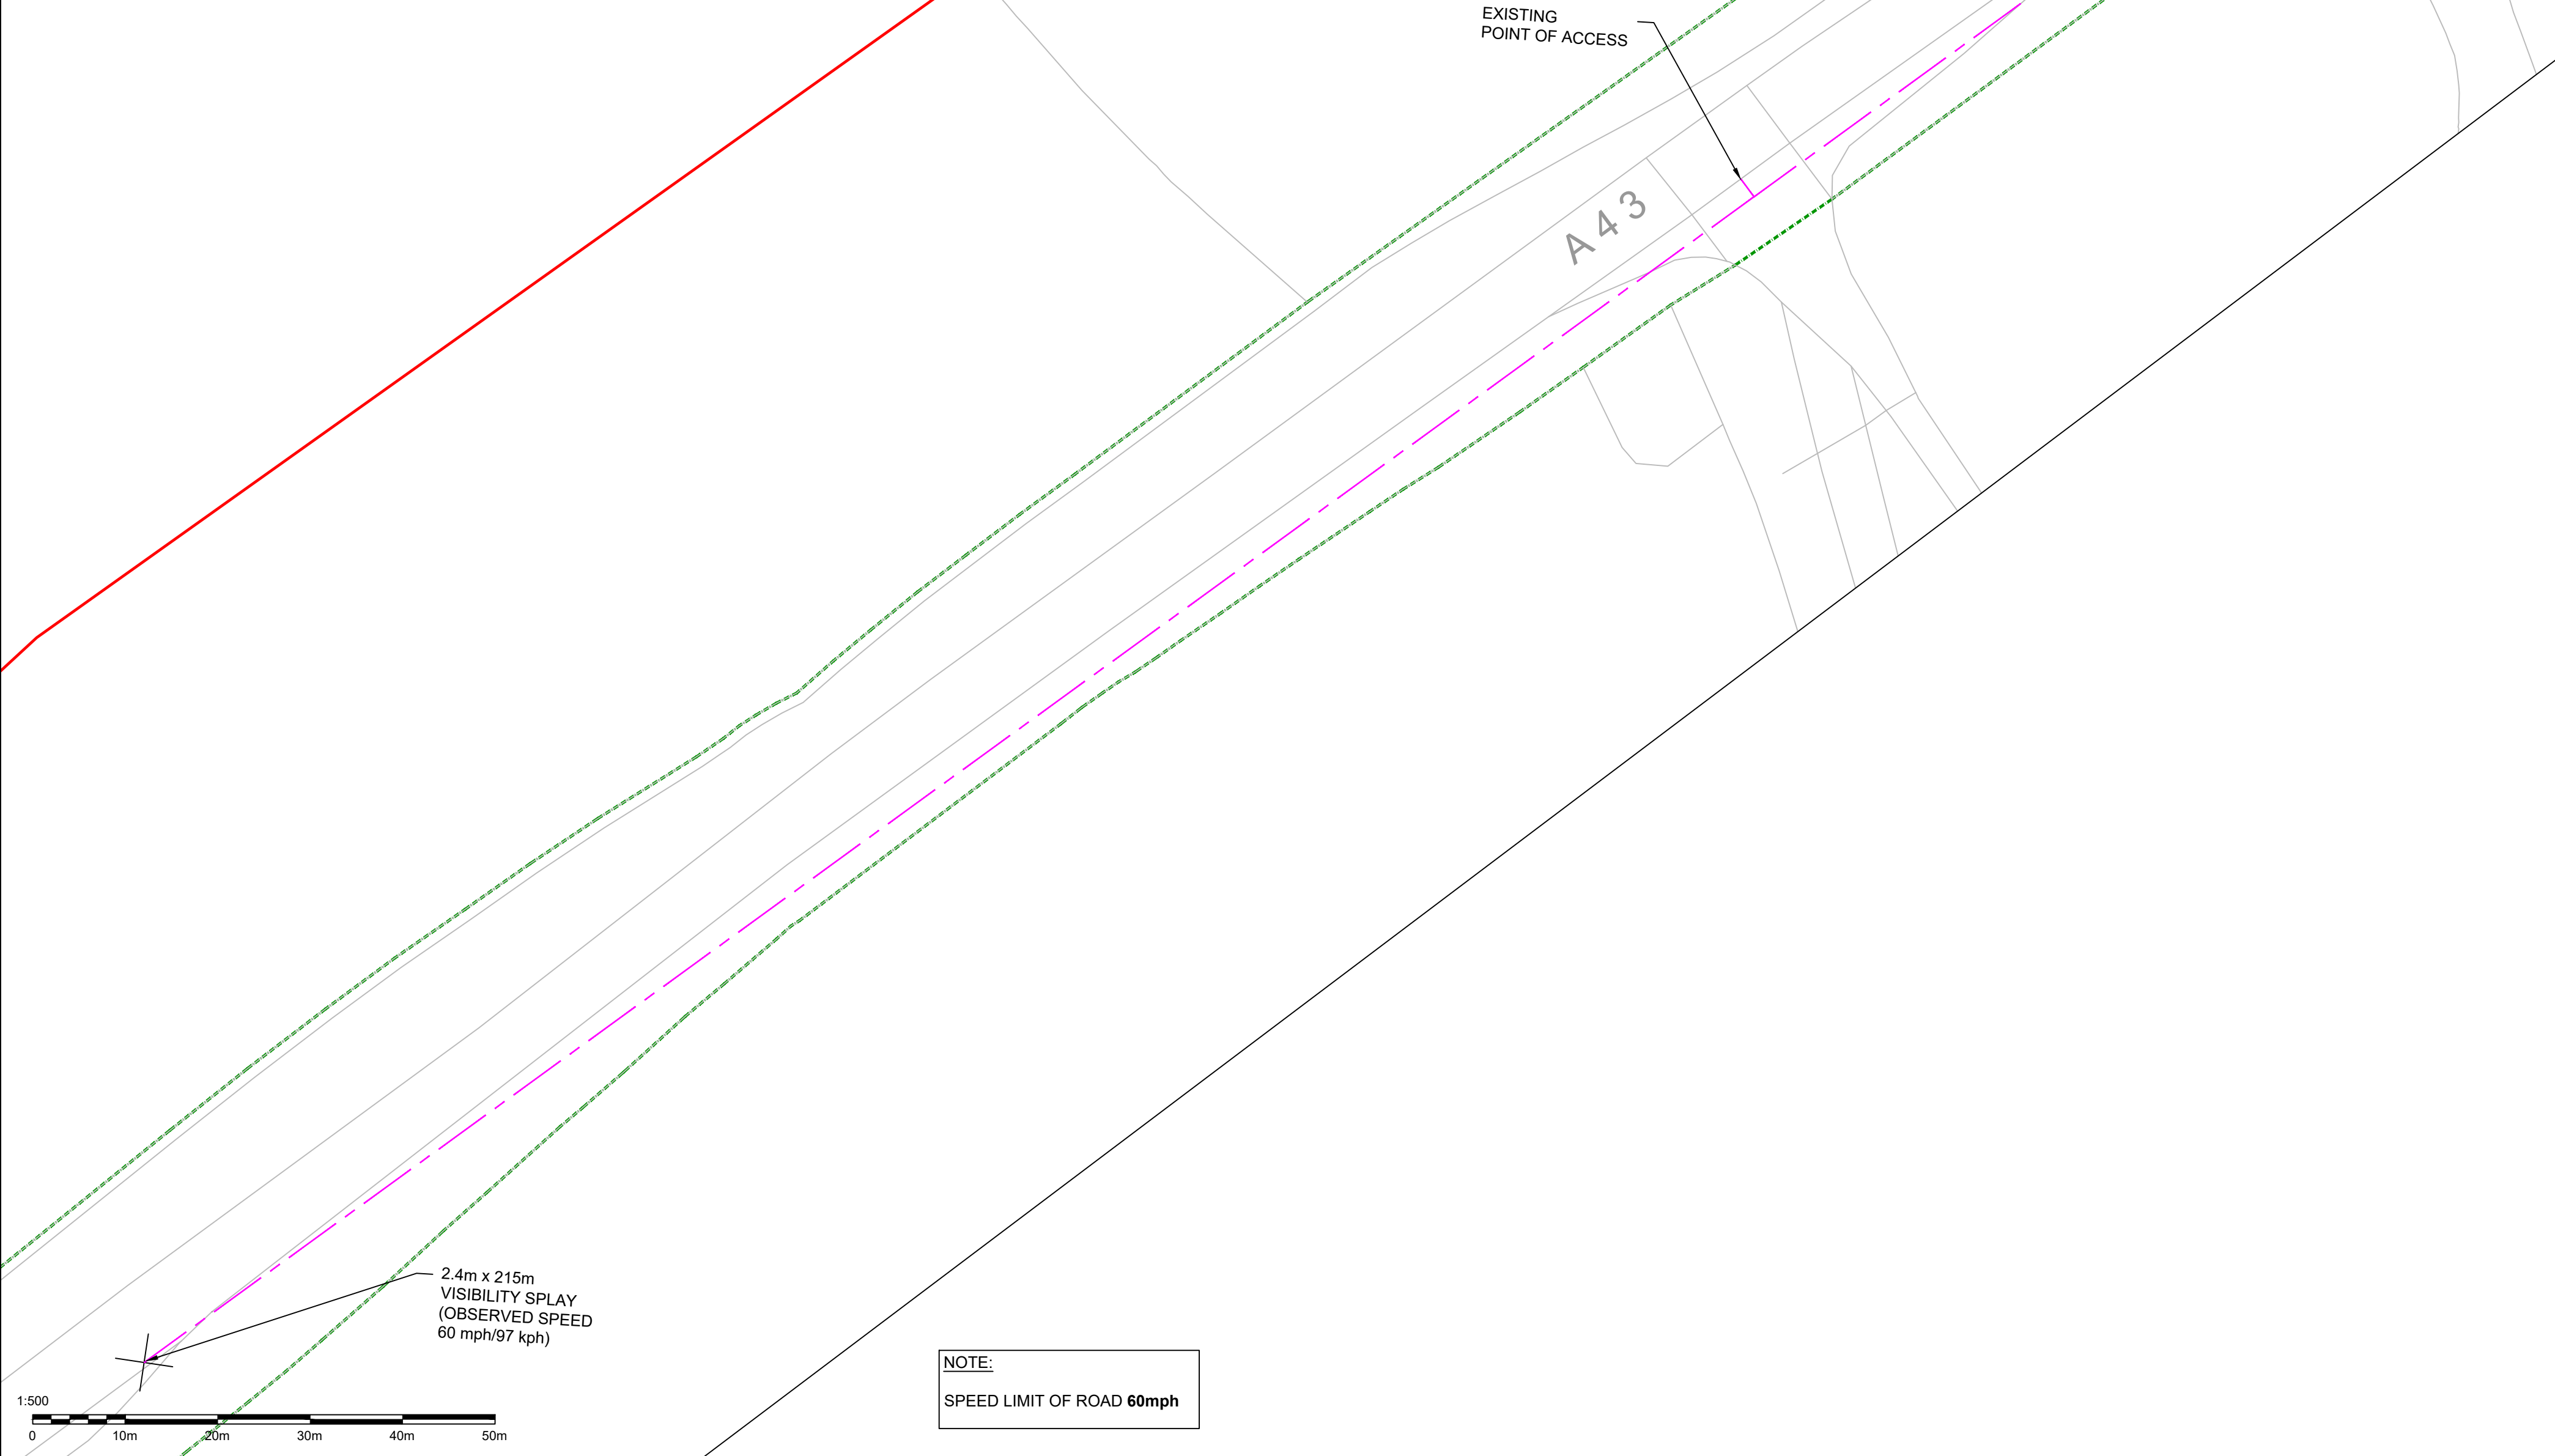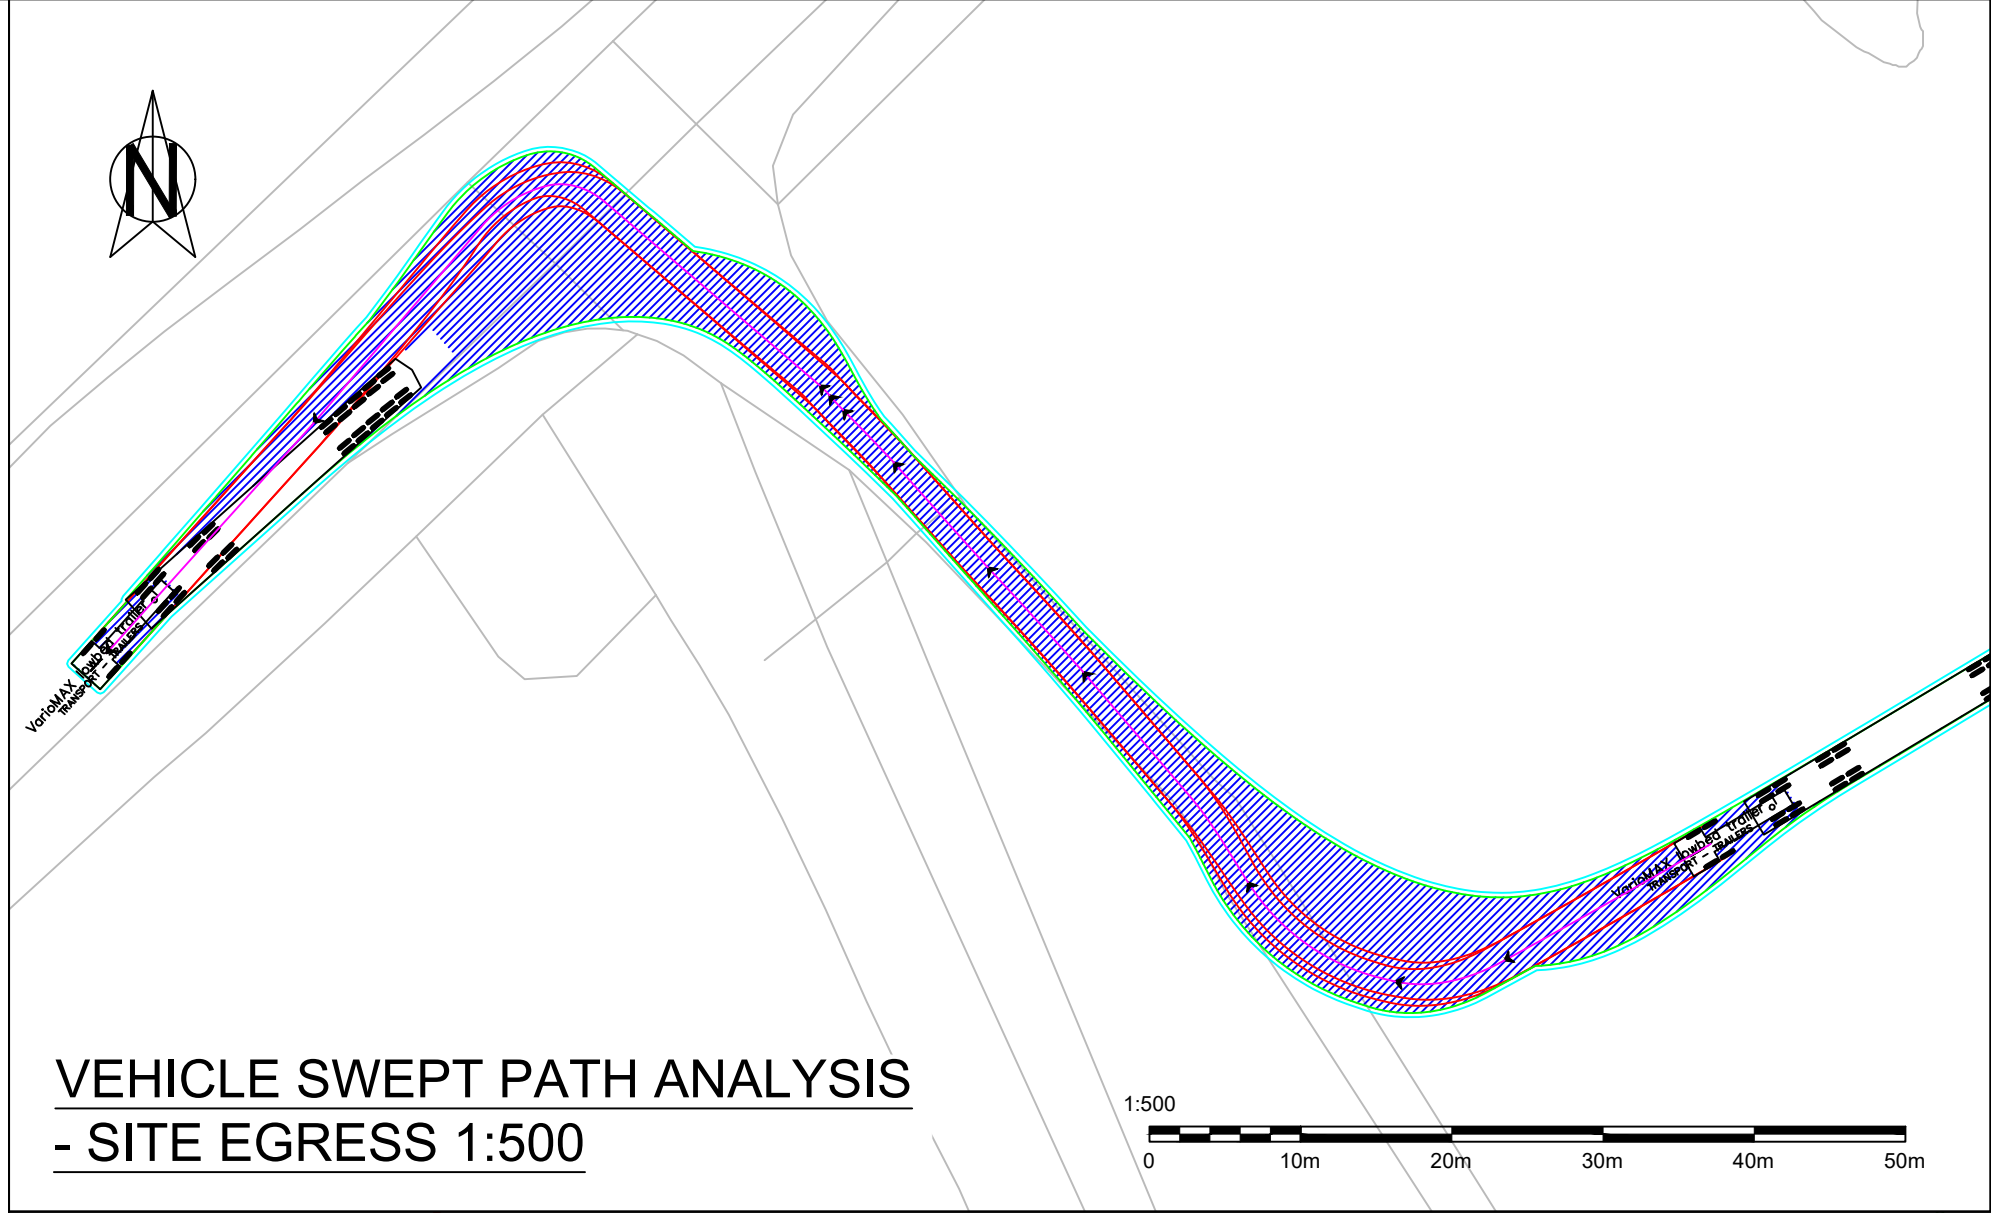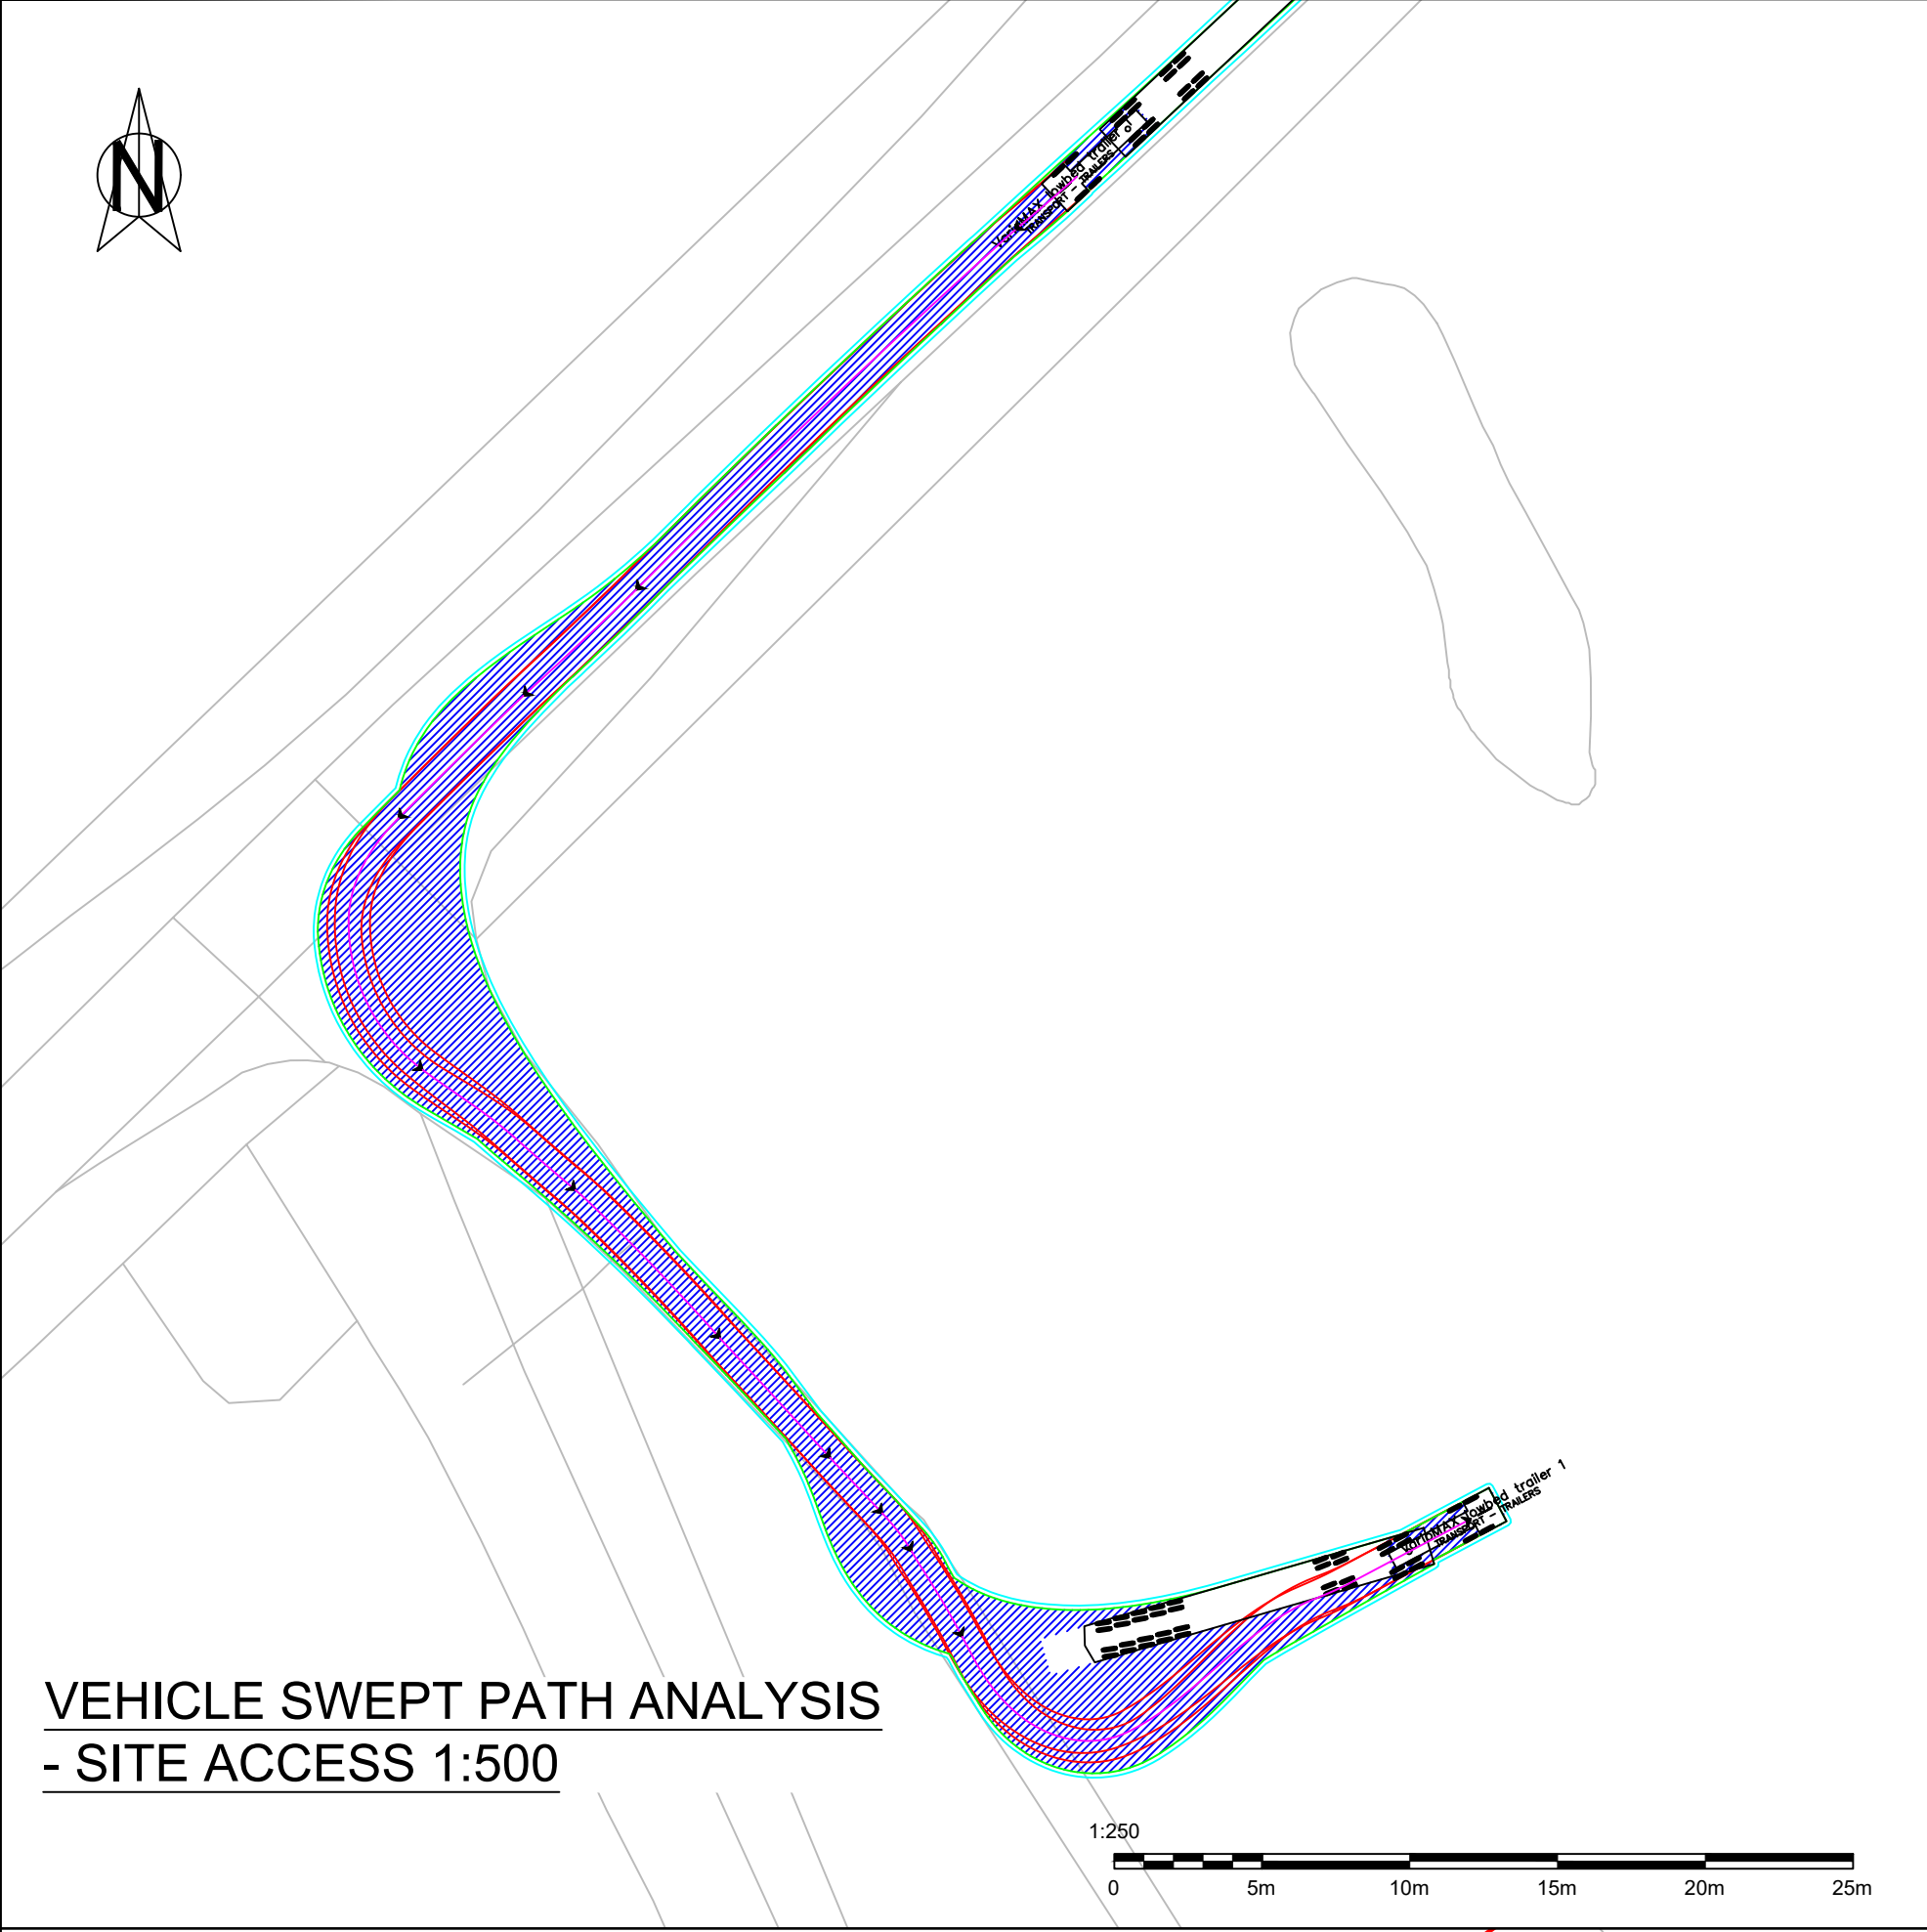

NOTES :

1. (C) This drawing is copyright.
2. All dimensions to be checked on site.
3. Do not scale from this drawing; only figured dimensions are to be worked from.
4. Any discrepancies must be reported immediately before proceeding.
5. This drawing to be read & printed in colour.
6. Ordnance Survey, (c) Crown Copyright 2024. All rights reserved. Licence number 100022432.

KEY PLAN
1:200000@A1

KEY:

- SITE BOUNDARY
- - - TRAFFIC SURVEY LOCATION
- - - HIGHWAY BOUNDARY
- - - VISIBILITY SPLAY EXTENT
- - - EXISTING LAYOUT
- - - PROPOSED EDGE OF ACCESS
- - - EXISTING VEGETATION
- - - EXTENT OF VEGETATION REMOVAL
- - - EXISTING CONTOURS

VEHICLE PROFILE:

VARIO-MAX LOWBED - 29.63m meters

TRACTOR WIDTH	: 2.55
TRAILER WIDTH	: 2.55
TRACTOR TRACK	: 2.55
TRAILER TRACK	: 2.55
LOCK TO LOCK TIME	: 6.0
STEERING ANGLE	: 40.0
ARTICULATING ANGLE	: 70.0

VEHICLE ANALYSIS KEY:

- VEHICLE PATH & DIRECTION
- ▨ VEHICLE BODY ENVELOPE
- VEHICLE FRONT WHEEL PATH
- ▭ 0.3m VEHICLE BUFFER ZONE AROUND TRACKING

D	03.12.2025	Drawing updated as per client comments	CS	OW	SM
C	19.05.2025	Boundary removed	CS	OW	SM
B	10.04.2025	Boundary updated, Drawing combined	CS	OW	SM
A	11.03.2025	Preliminary issue	CS	LF	SM

REV	DATE	DESCRIPTION	DRN	CHKD	APRD

Issue Status

<input type="checkbox"/> CONCEPT	<input type="checkbox"/> CONSTRUCTION
<input checked="" type="checkbox"/> PRELIMINARY	<input type="checkbox"/> AS BUILT
<input type="checkbox"/> TENDER	<input type="checkbox"/> HAS FILE ISSUE



Client:
GREEN HILL SOLAR FARM LTD

Project:
GREEN HILL SOLAR FARM

Drawing Title:
CABLE ROUTE ACCESS 4
GENERAL ARRANGEMENT & VEHICLE TRACKING

Scale @ A1	Drawn	CS	Chkd	OW
As shown	Aprd	SM	Date	MAR 2025

Drawing Ref	Rev
23061-KMC-XX-CR4-DR-CH-0001	D

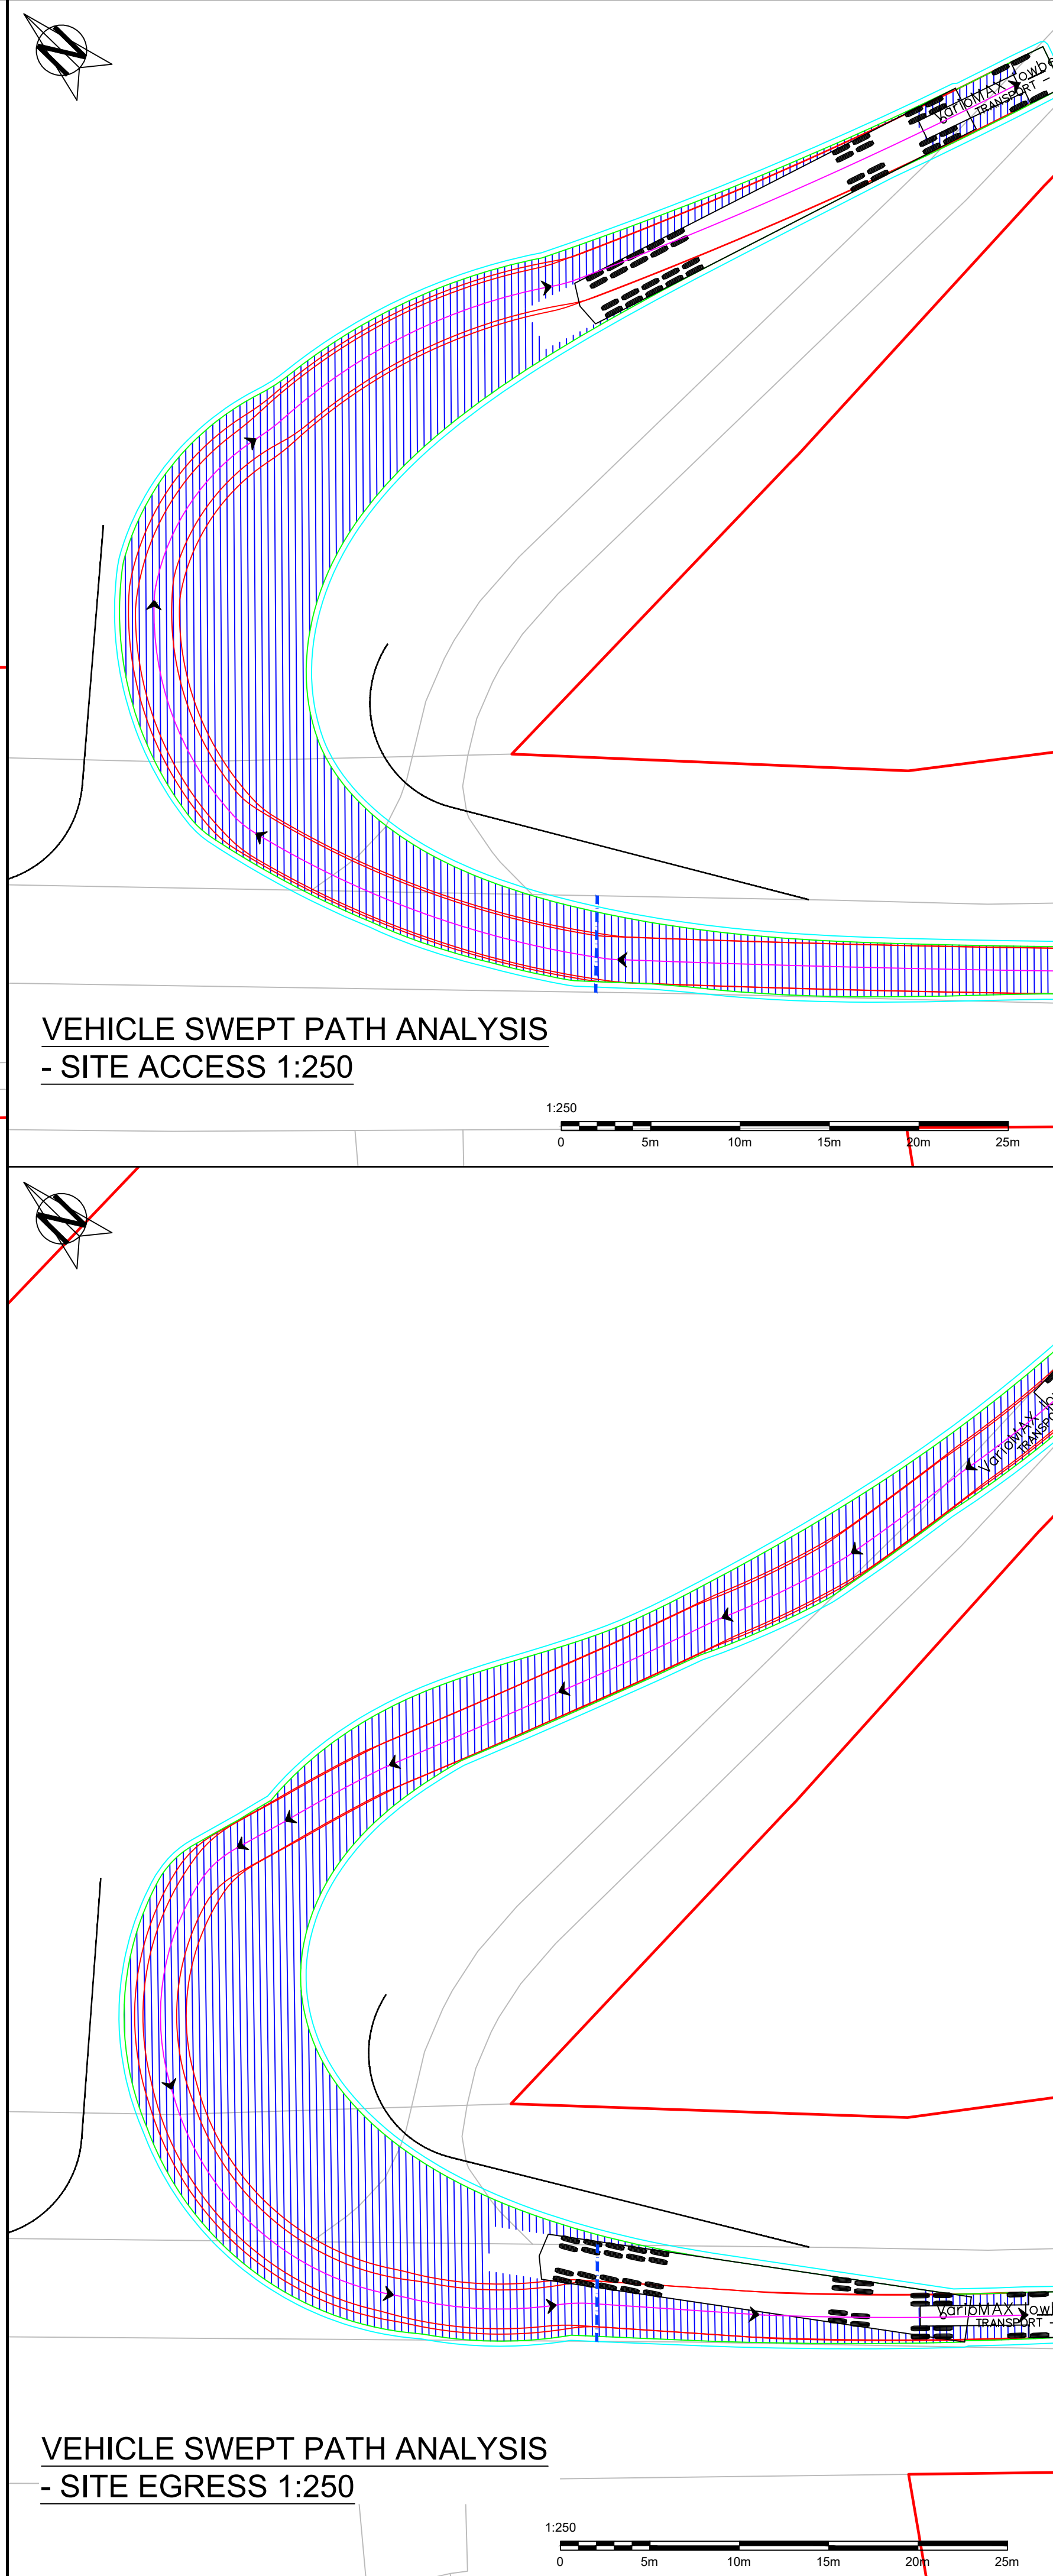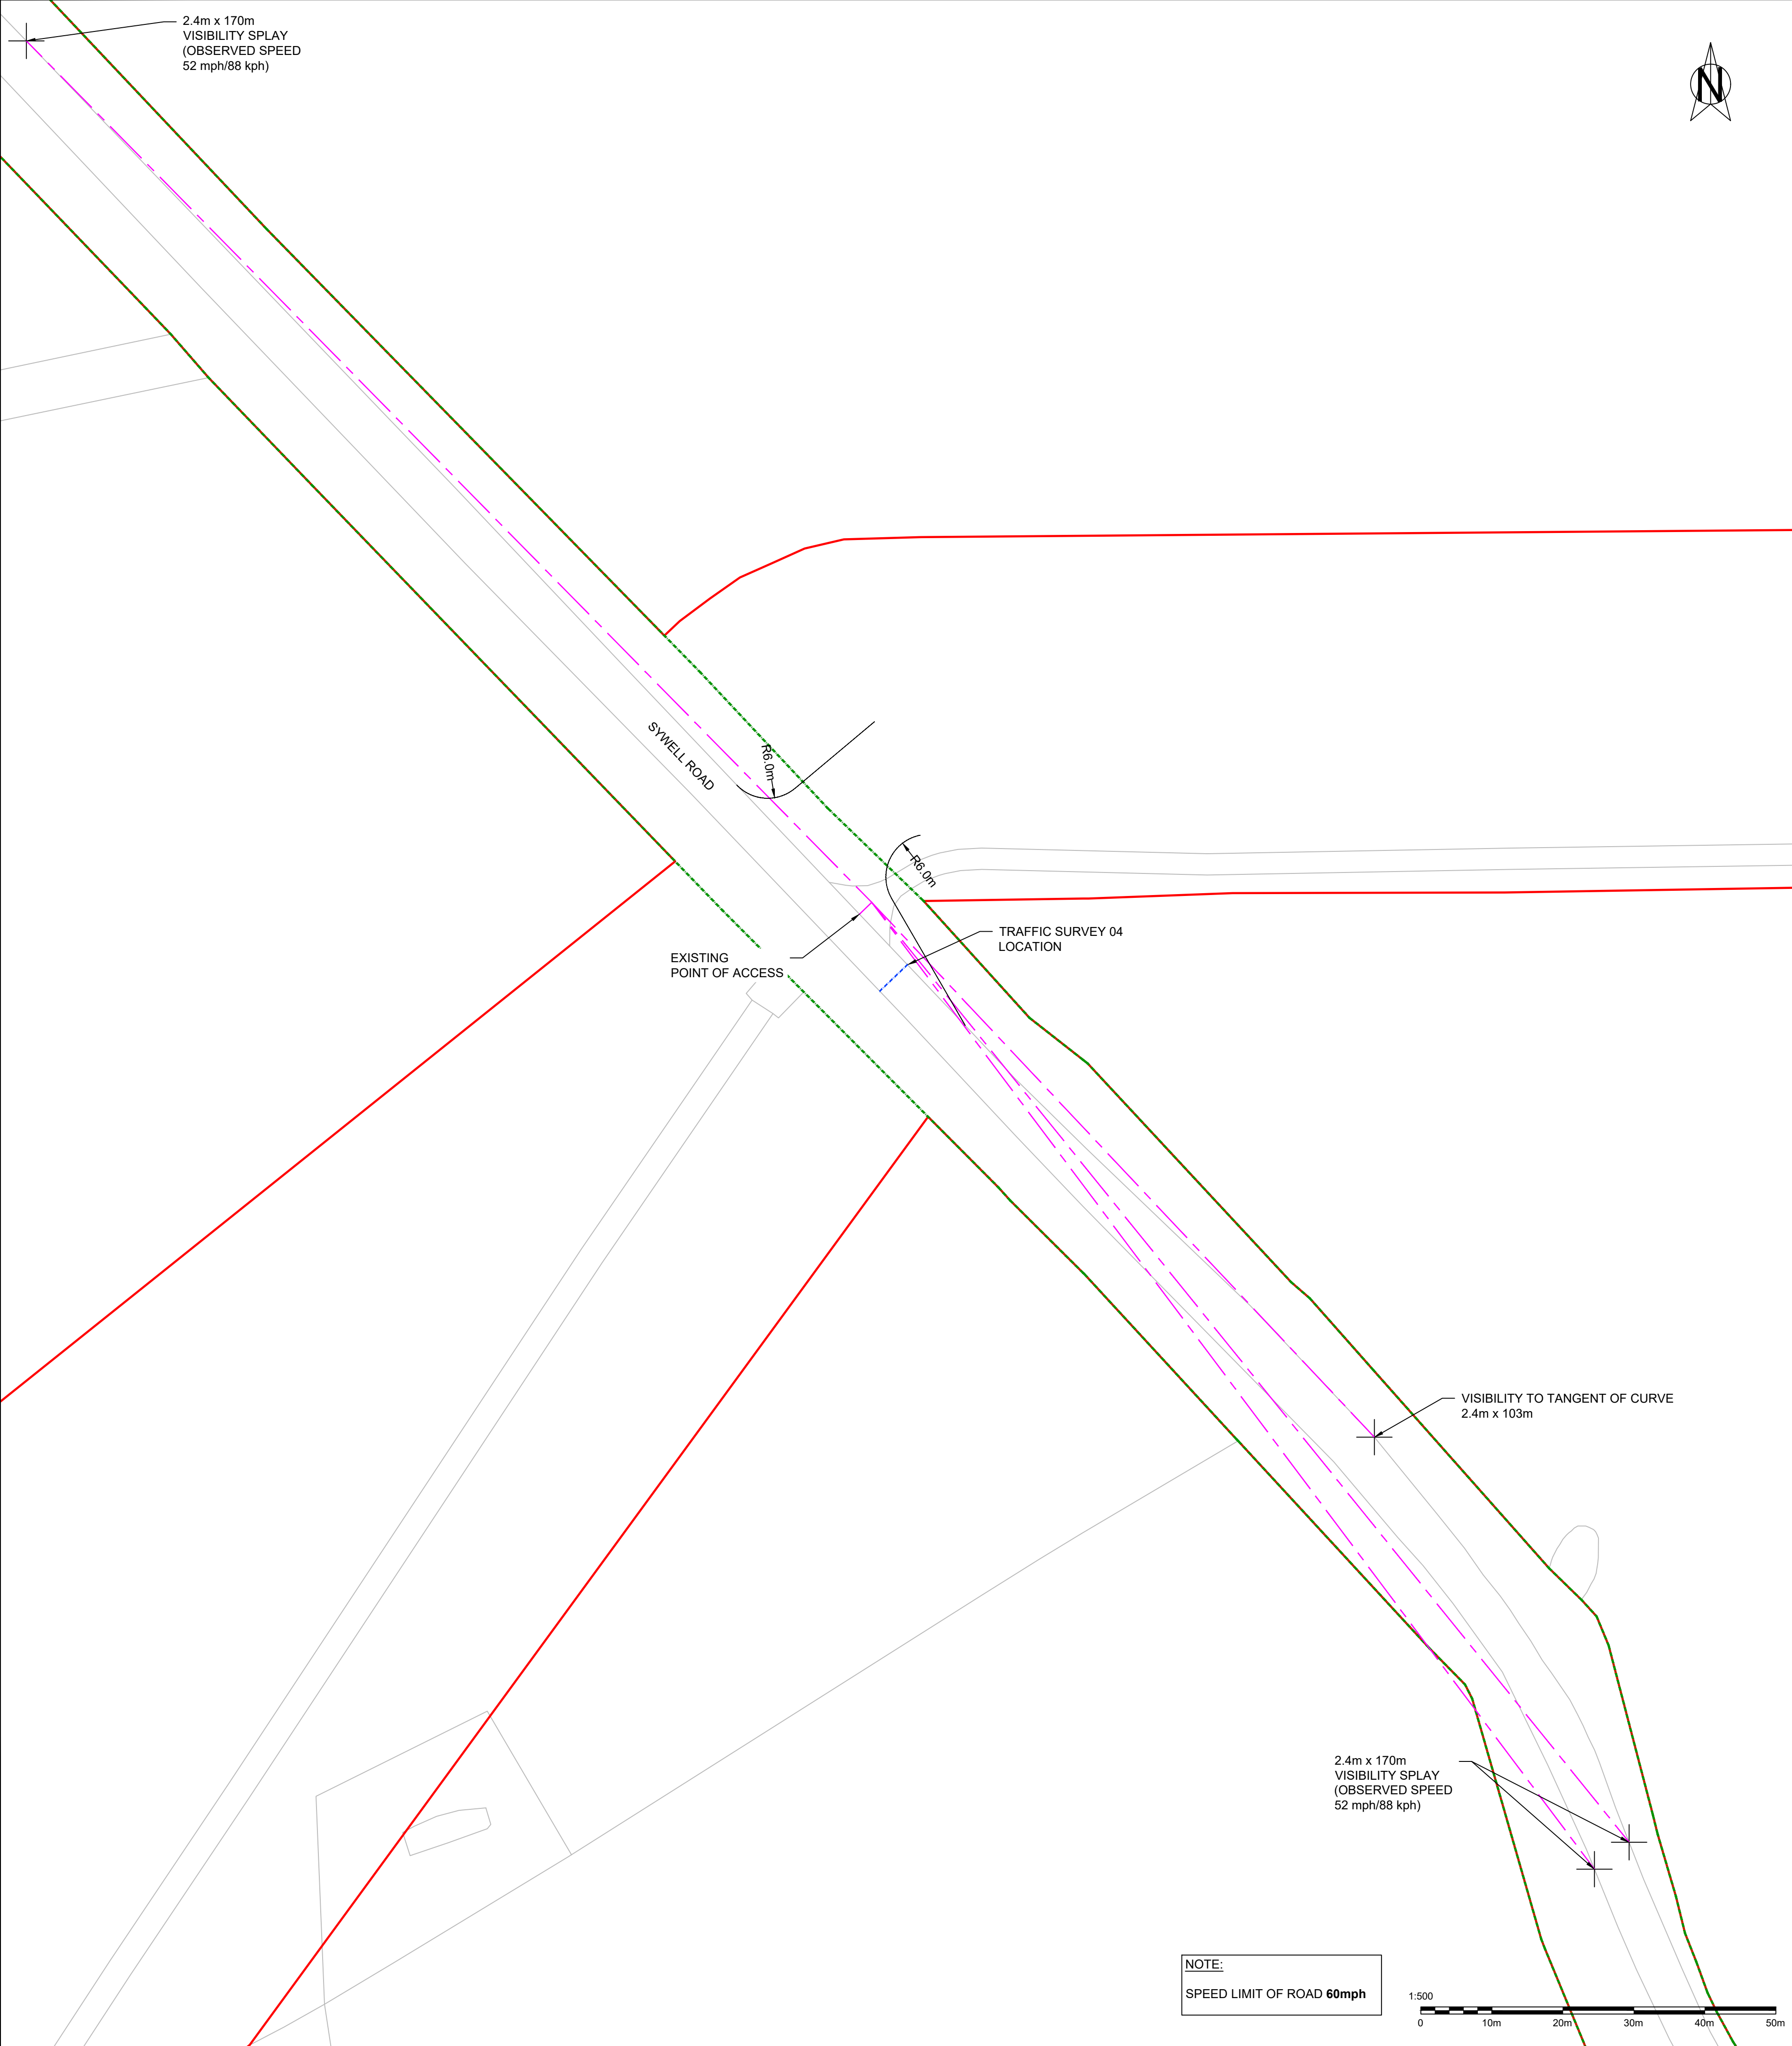

NOTES :

1. (C) This drawing is copyright.
2. All dimensions to be checked on site.
3. Do not scale from this drawing; only figured dimensions are to be worked from.
4. Any discrepancies must be reported immediately before proceeding.
5. This drawing to be read & printed in colour.
6. Ordnance Survey, (c) Crown Copyright 2024. All rights reserved. Licence number 100022432.

KEY PLAN
1:200000@A1

KEY:

- SITE BOUNDARY
- TRAFFIC SURVEY LOCATION
- HIGHWAY BOUNDARY
- VISIBILITY SPLAY EXTENT
- EXISTING LAYOUT
- PROPOSED EDGE OF ACCESS
- EXISTING VEGETATION
- EXTENT OF VEGETATION REMOVAL
- EXISTING CONTOURS

VEHICLE PROFILE:

VARIO-MAX LOWBED - 29.63m meters

TRACTOR WIDTH : 2.55

TRAILER WIDTH : 2.55

TRACTOR TRACK : 2.55

TRAILER TRACK : 2.55

LOCK TO LOCK TIME : 6.0

STEERING ANGLE : 40.0

ARTICULATING ANGLE: 70.0

VEHICLE ANALYSIS KEY:

- VEHICLE PATH & DIRECTION
- ▨ VEHICLE BODY ENVELOPE
- VEHICLE FRONT WHEEL PATH
- ▭ 0.3m VEHICLE BUFFER ZONE AROUND TRACKING

D	03.12.2025	Drawing updated as per client comments	CS	OW	SM
C	19.05.2025	Boundary removed	CS	OW	SM
B	10.04.2025	Boundary updated, Drawing combined	CS	OW	SM
A	11.03.2025	Preliminary issue	CS	LF	SM

REV	DATE	DESCRIPTION	DRN	CHKD	APRD

Issue Status

<input type="checkbox"/> CONCEPT	<input type="checkbox"/> CONSTRUCTION
<input type="checkbox"/> PRELIMINARY	<input type="checkbox"/> AS BUILT
<input type="checkbox"/> TENDER	<input type="checkbox"/> HAS FILE ISSUE

Client
GREEN HILL SOLAR FARM LTD

Project
GREEN HILL SOLAR FARM



Drawing Title
CABLE ROUTE ACCESS 5
GENERAL ARRANGEMENT & VEHICLE TRACKING

Scale @ A1
As shown

CS	OW
Aprd	Date
SM	MAR 2025

Drawing Ref
23061-KMC-XX-CR5-DR-CH-0001

Rev	D
-----	---

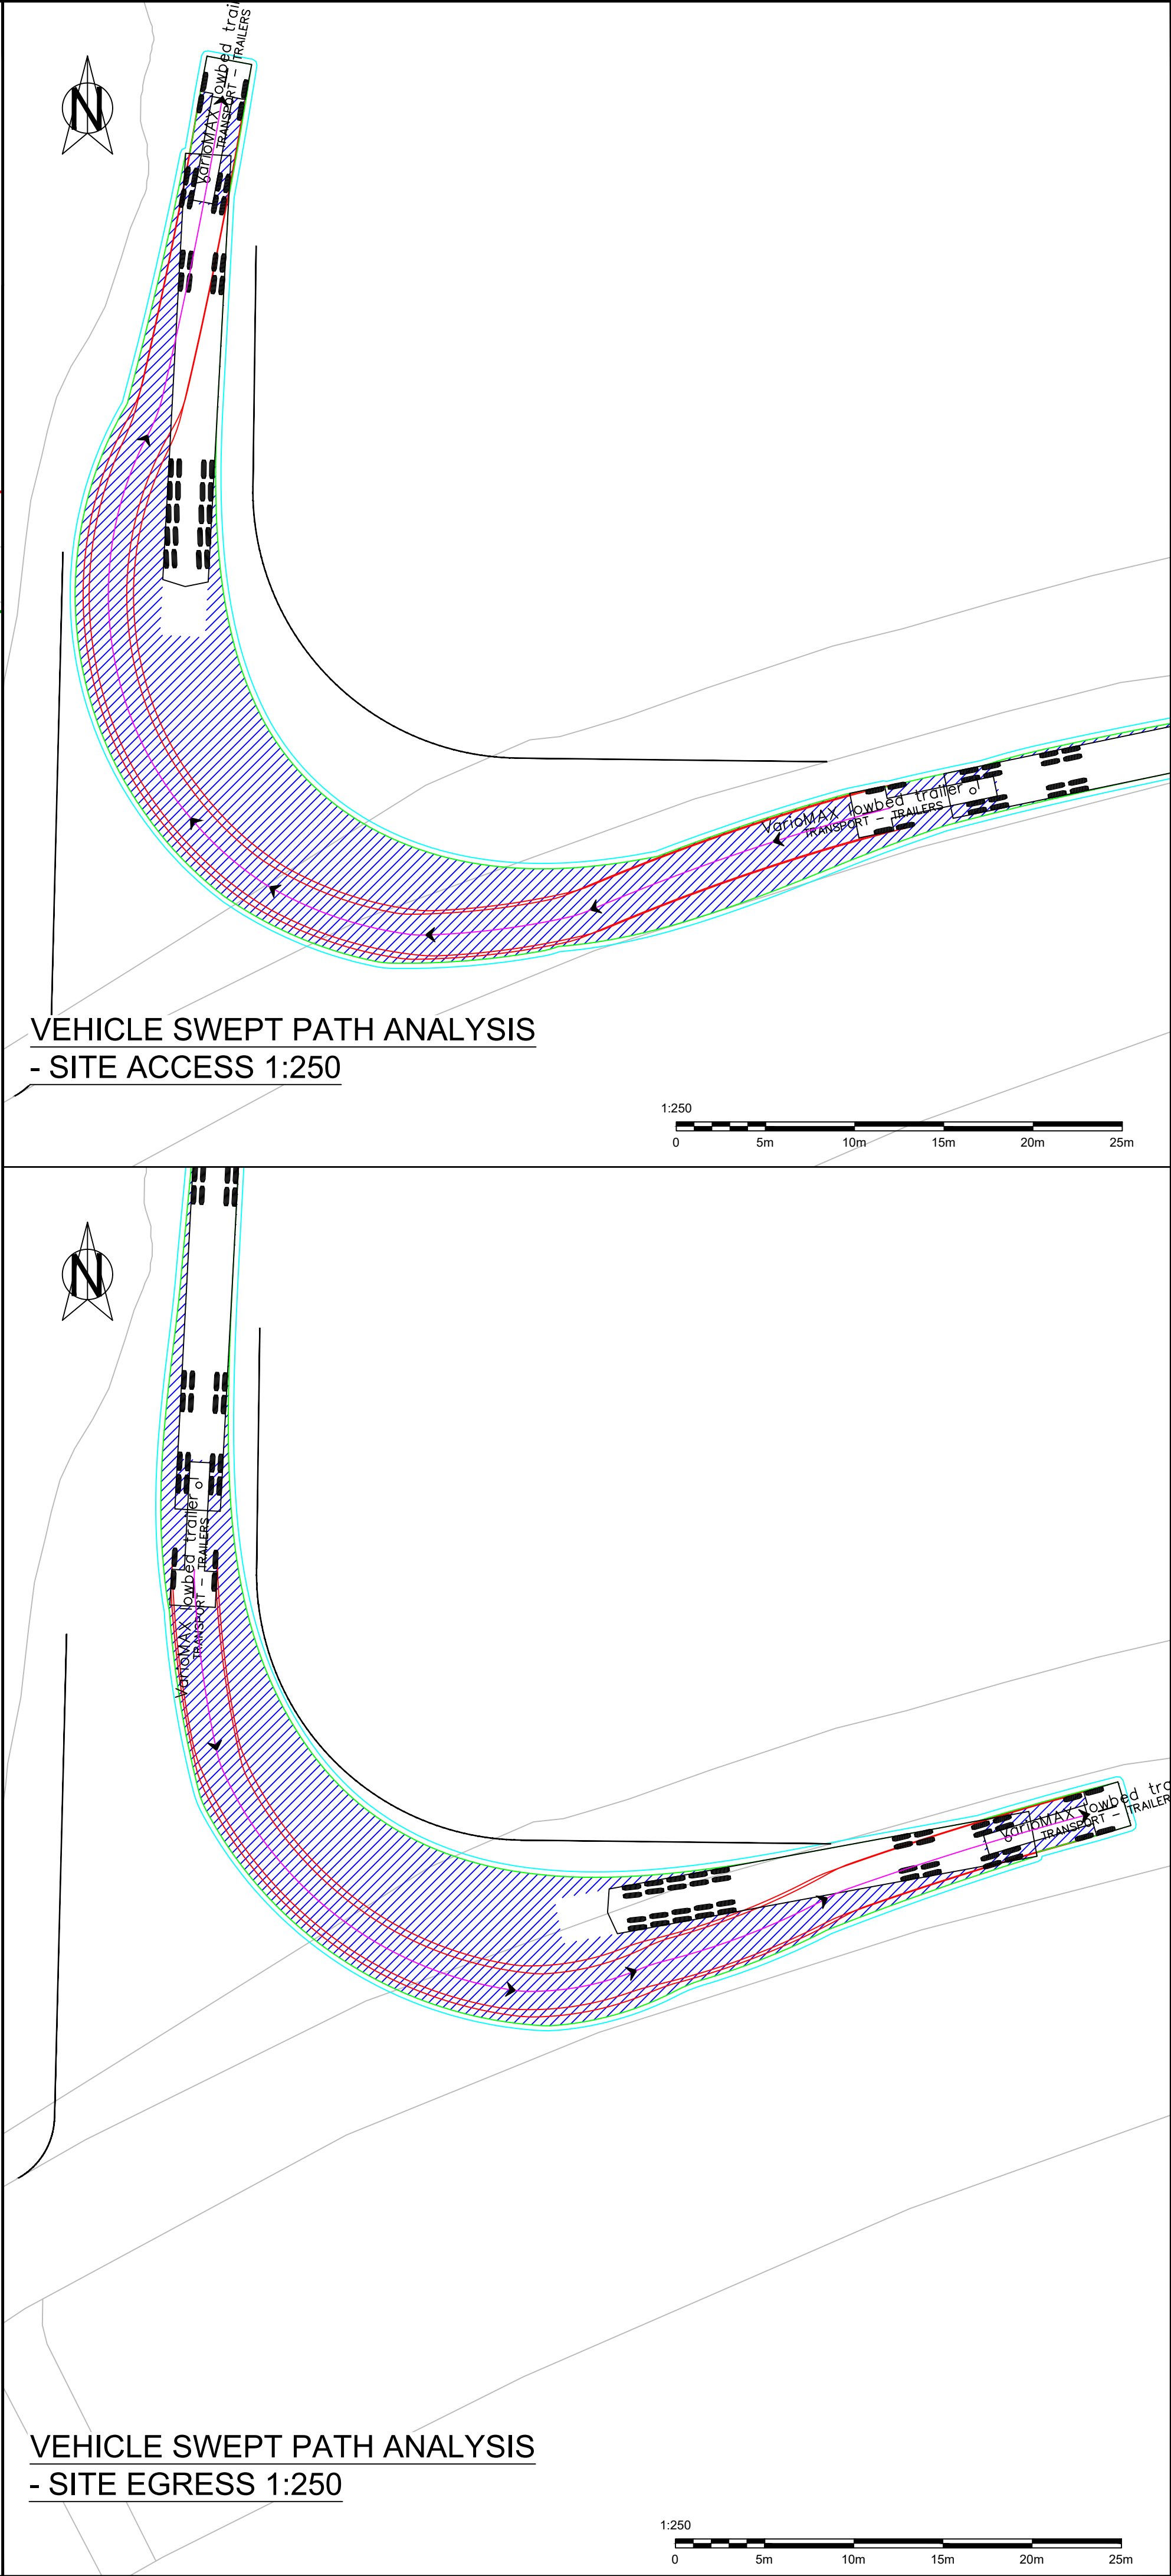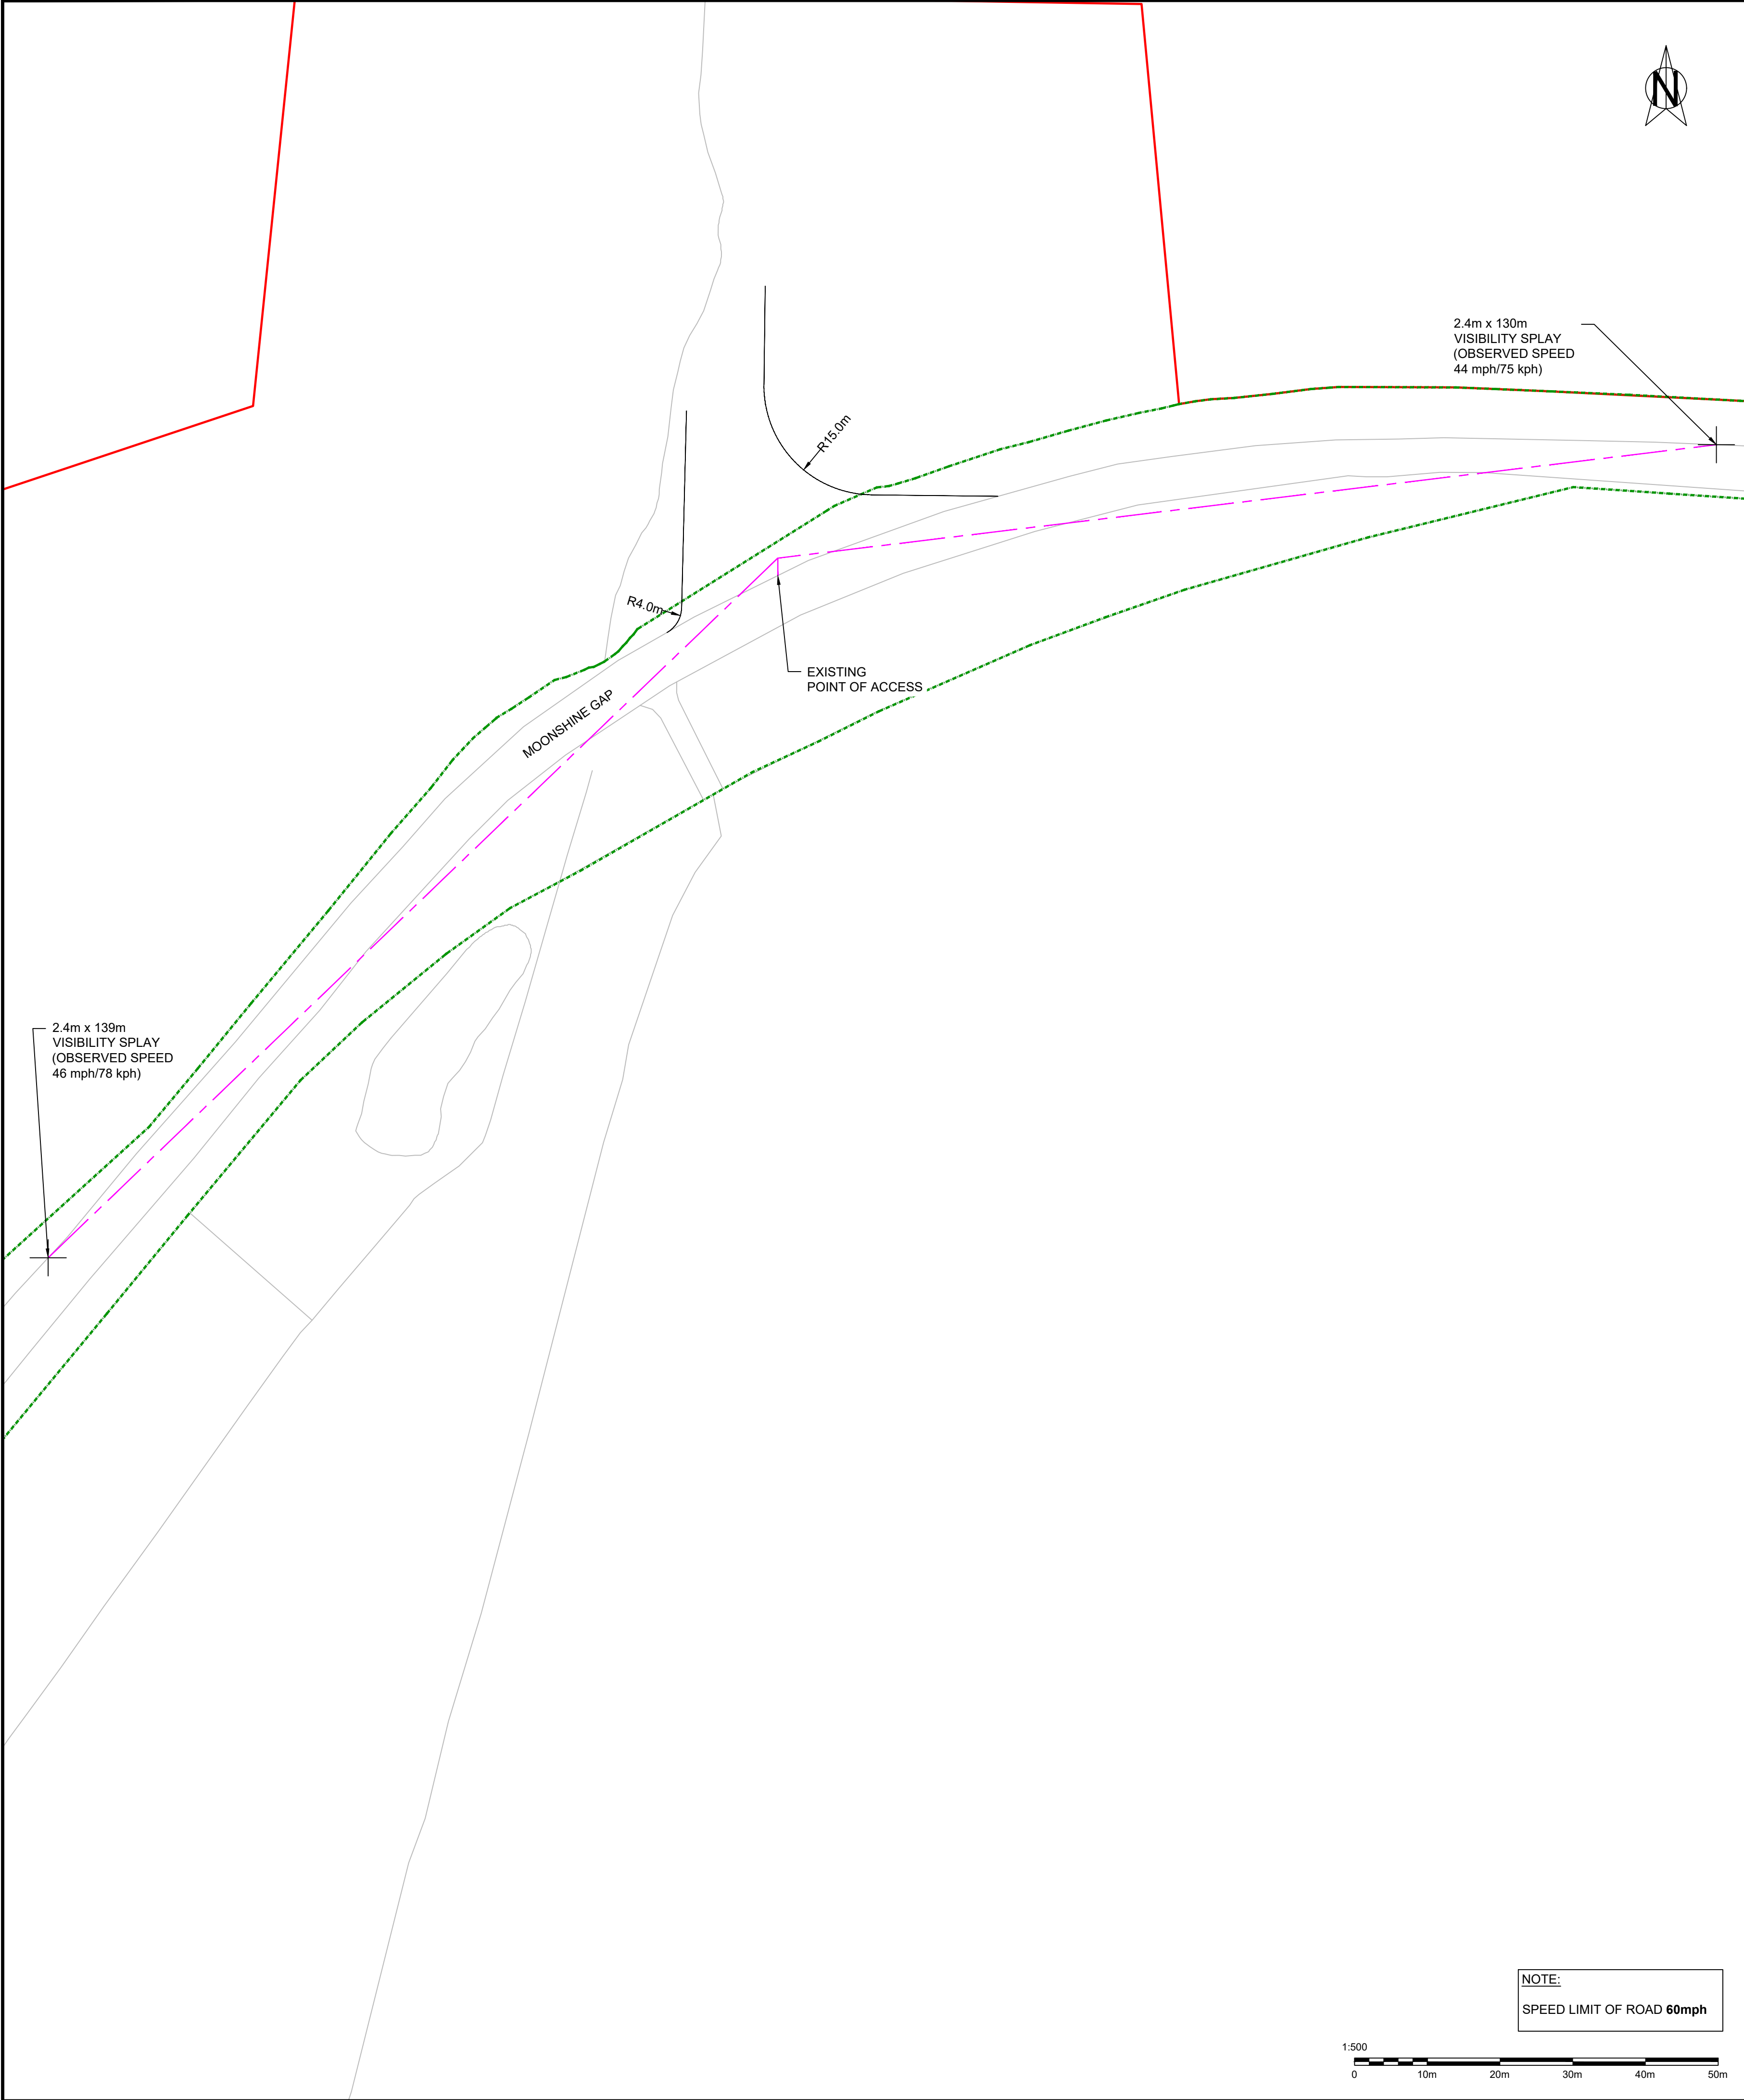

NOTES :

1. (C) This drawing is copyright.
2. All dimensions to be checked on site.
3. Do not scale from this drawing; only figured dimensions are to be worked from.
4. Any discrepancies must be reported immediately before proceeding.
5. This drawing to be read & printed in colour.
6. Ordnance Survey, (c) Crown Copyright 2024. All rights reserved. Licence number 100022432.

KEY PLAN
1:200000@A1

KEY:

- SITE BOUNDARY
- TRAFFIC SURVEY LOCATION
- HIGHWAY BOUNDARY
- VISIBILITY SPLAY EXTENT
- EXISTING LAYOUT
- PROPOSED EDGE OF ACCESS
- EXISTING VEGETATION
- EXTENT OF VEGETATION REMOVAL
- EXISTING CONTOURS

VEHICLE PROFILE:

VARIO-MAX LOWBED - 29.63m meters

TRACTOR WIDTH : 2.55

TRAILER WIDTH : 2.55

TRACTOR TRACK : 2.55

TRAILER TRACK : 2.55

LOCK TO LOCK TIME : 6.0

STEERING ANGLE : 40.0

ARTICULATING ANGLE: 70.0

VEHICLE ANALYSIS KEY:

- VEHICLE PATH & DIRECTION
- VEHICLE BODY ENVELOPE
- VEHICLE FRONT WHEEL PATH
- 0.3m VEHICLE BUFFER ZONE AROUND TRACKING

D	03.12.2025	Drawing updated as per client comments	CS	OW	SM
C	19.05.2025	Boundary removed	CS	OW	SM
B	10.04.2025	Boundary updated, Drawing combined	CS	OW	SM
A	11.03.2025	Preliminary issue	CS	LF	SM

REV	DATE	DESCRIPTION	DRN	CHKD	APRD

Issue Status

<input type="checkbox"/> CONCEPT	<input type="checkbox"/> CONSTRUCTION
<input type="checkbox"/> PRELIMINARY	<input type="checkbox"/> AS BUILT
<input type="checkbox"/> TENDER	<input type="checkbox"/> HAS FILE ISSUE

Client:
GREEN HILL SOLAR FARM LTD




Project:
GREEN HILL SOLAR FARM

Drawing Title
CABLE ROUTE ACCESS 6
GENERAL ARRANGEMENT & VEHICLE TRACKING

Scale @ A1	Drawn	CS	Chkd	OW
As shown	Aprd	SM	Date	APR 2025

Drawing Ref	Rev
23061-KMC-XX-CR6-DR-CH-0001	D

kmc
transport planning

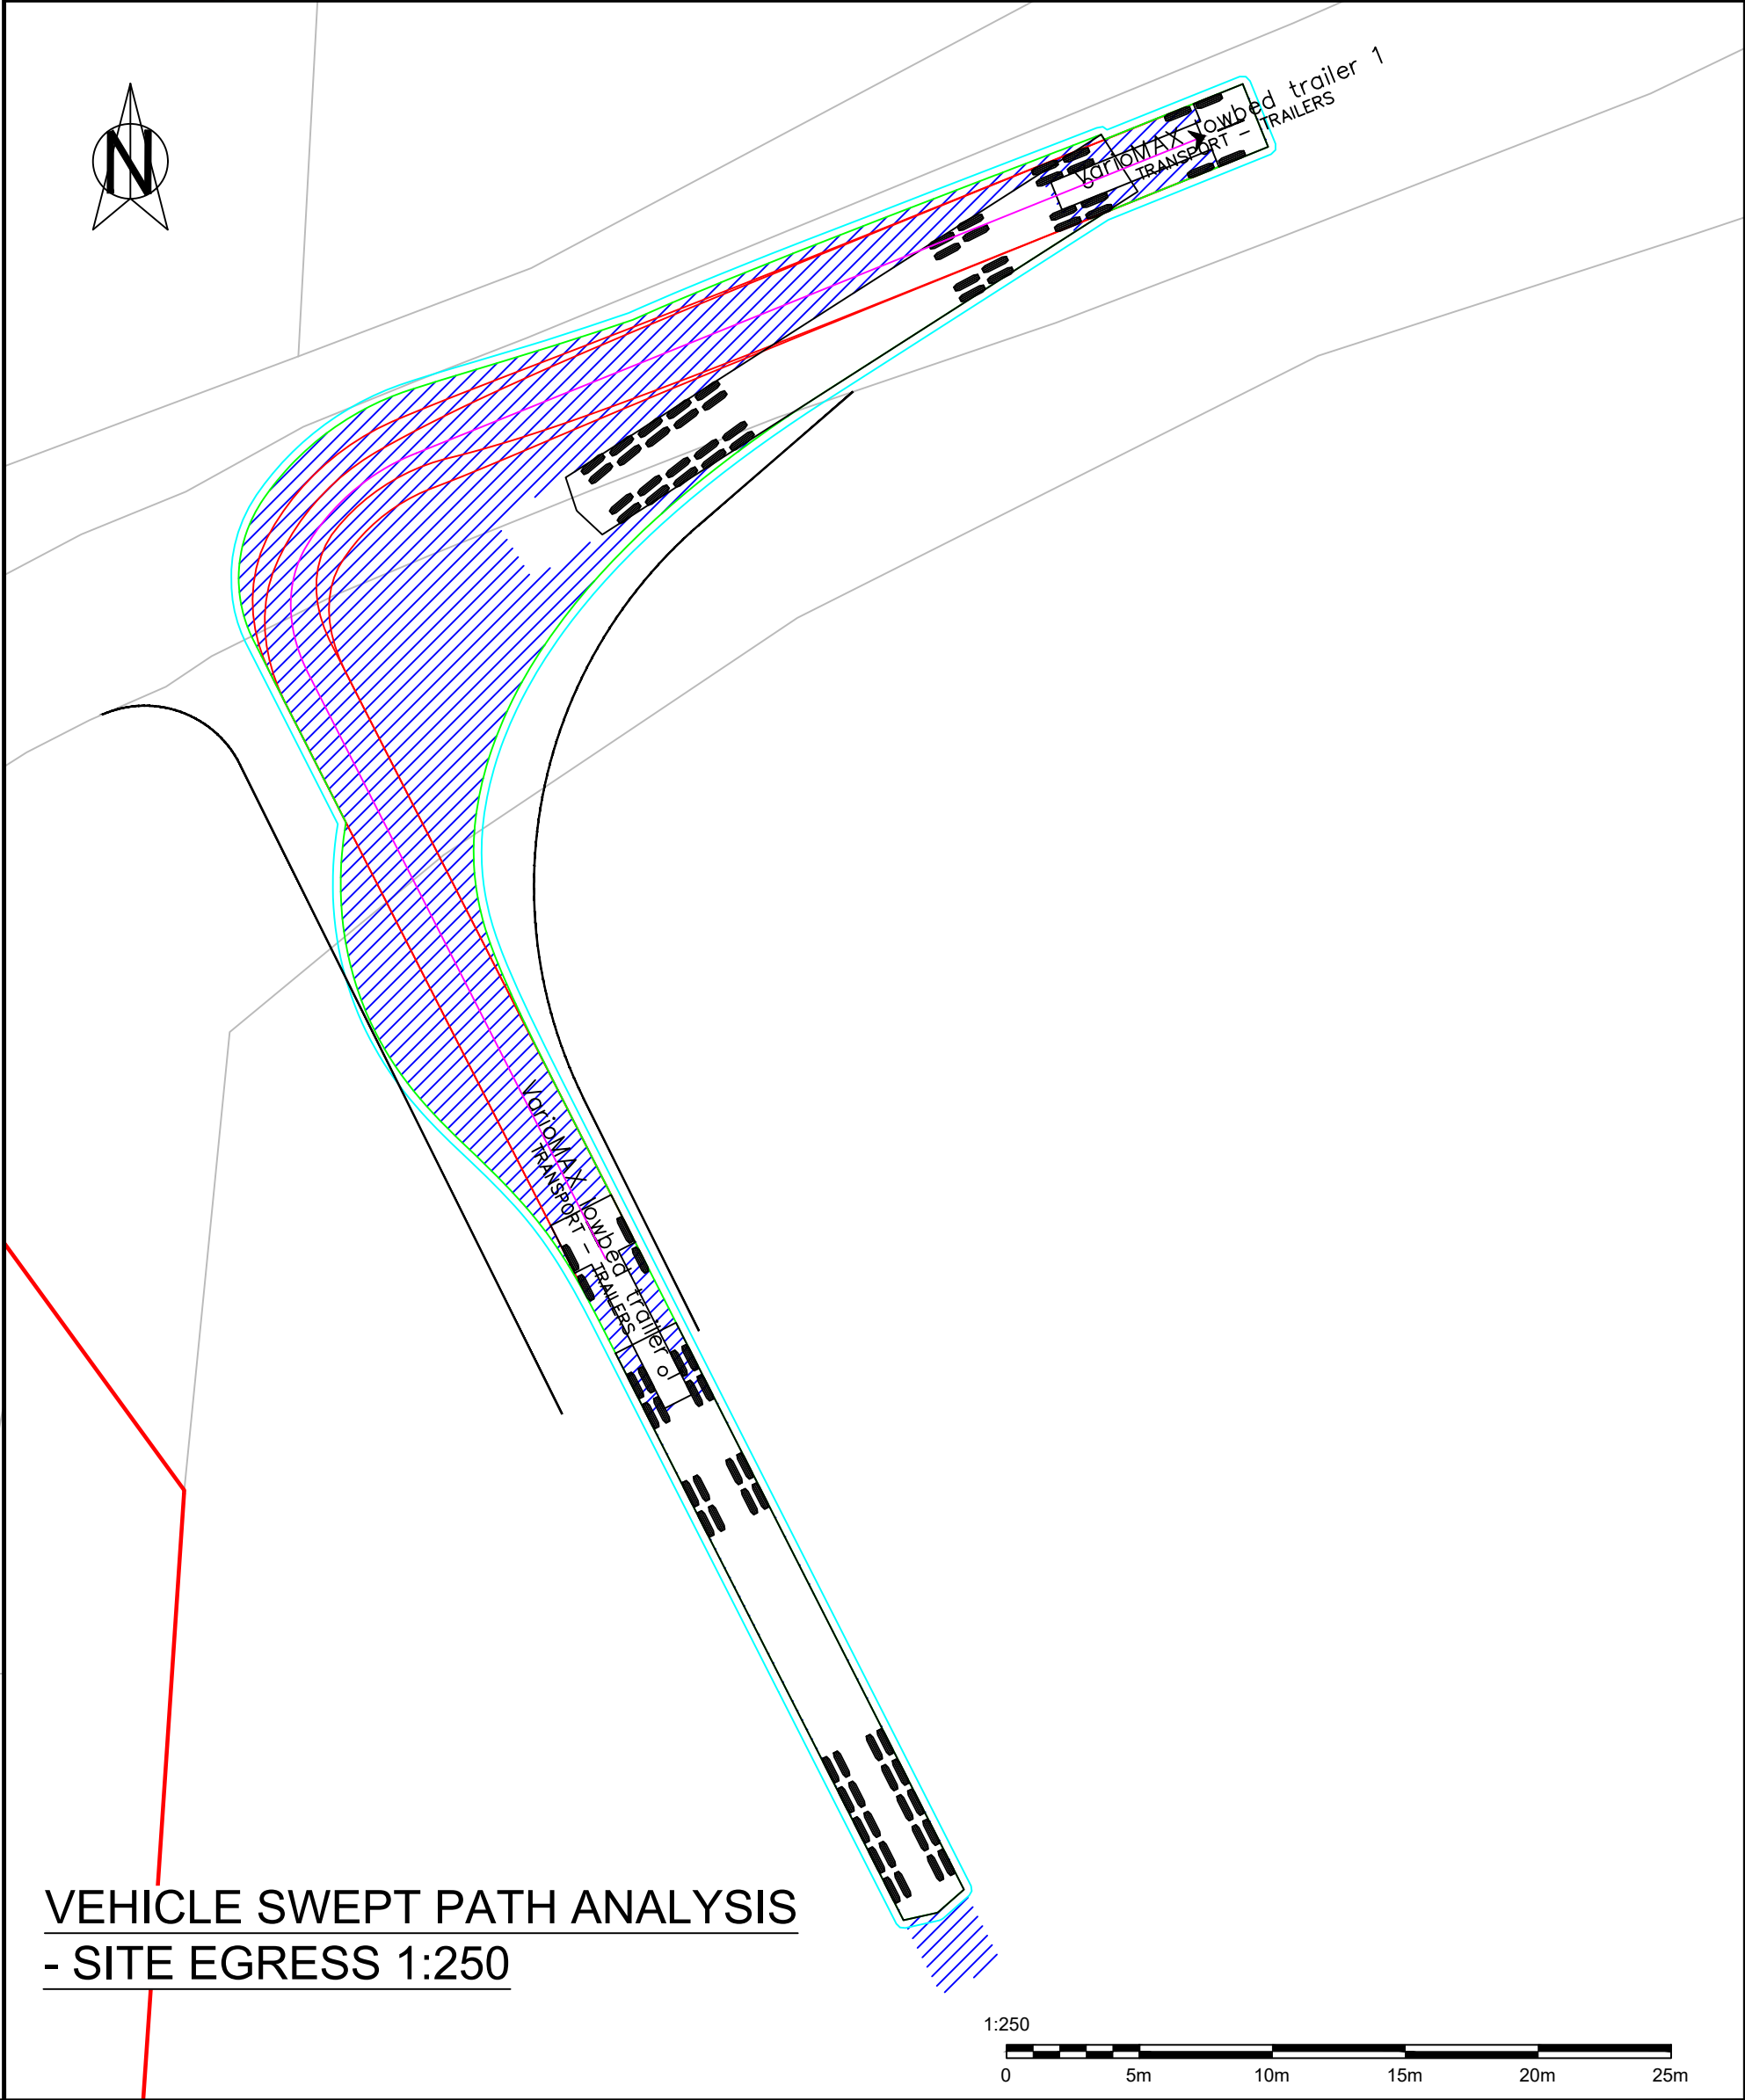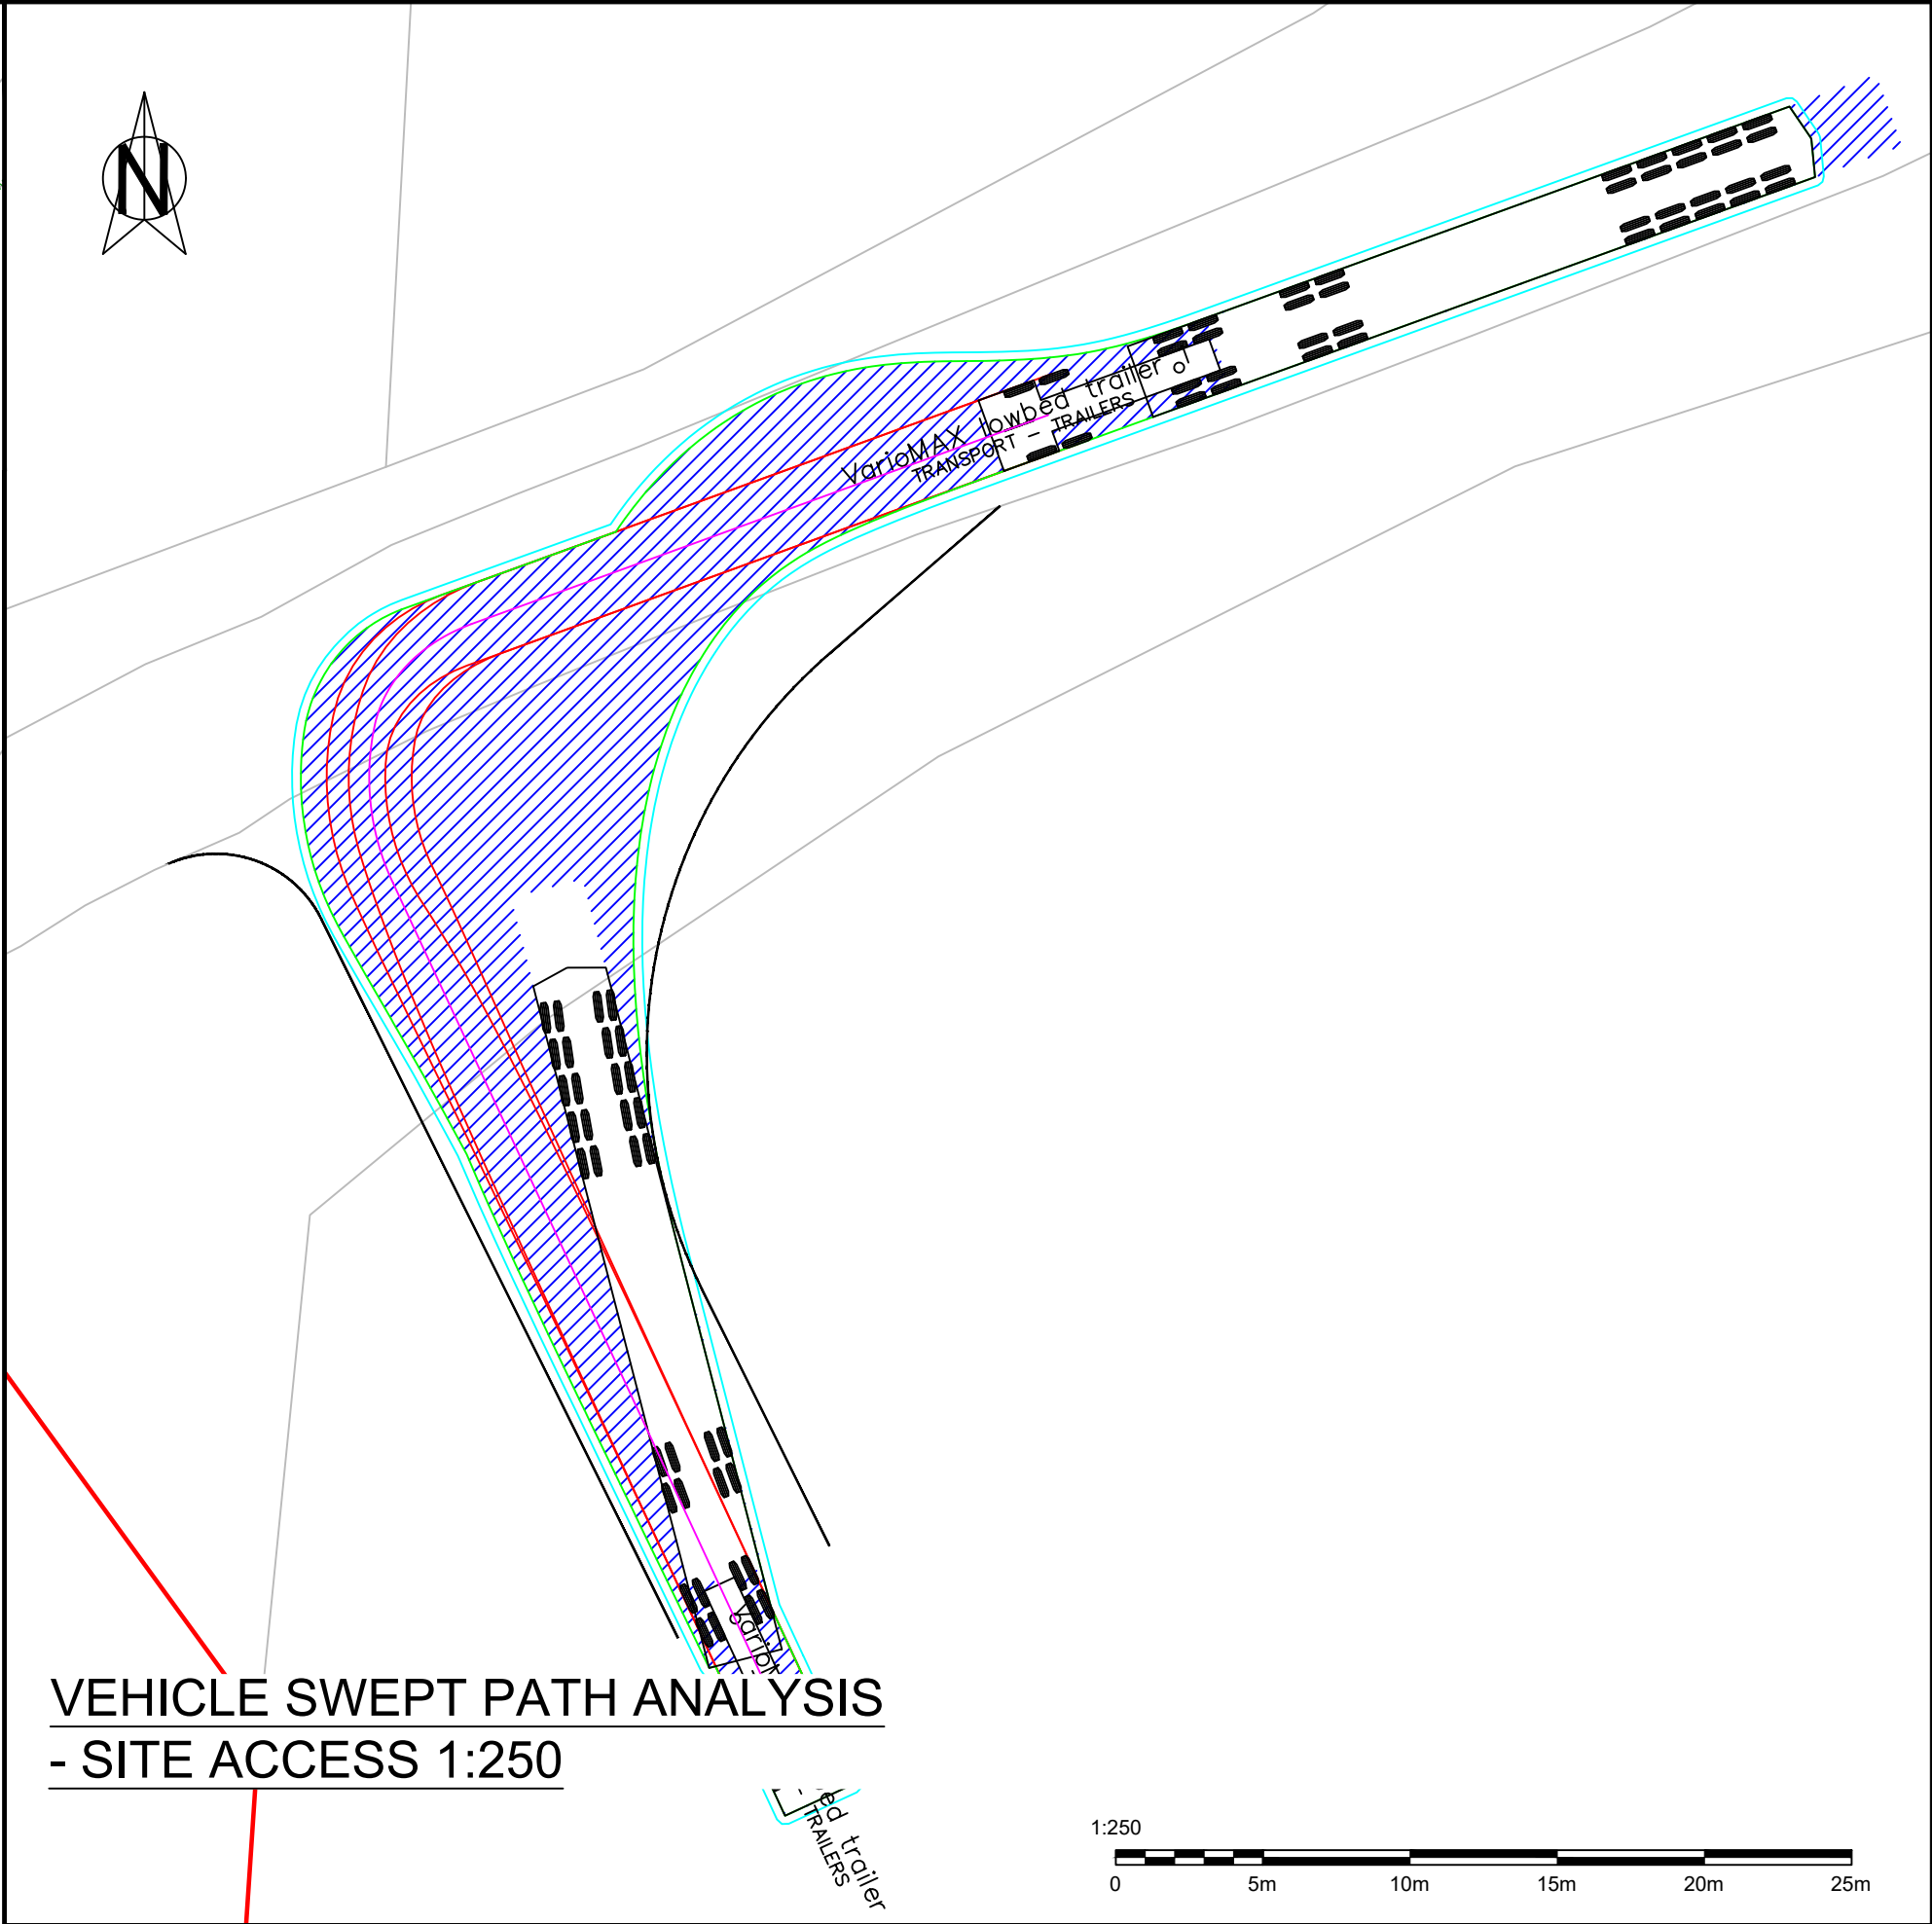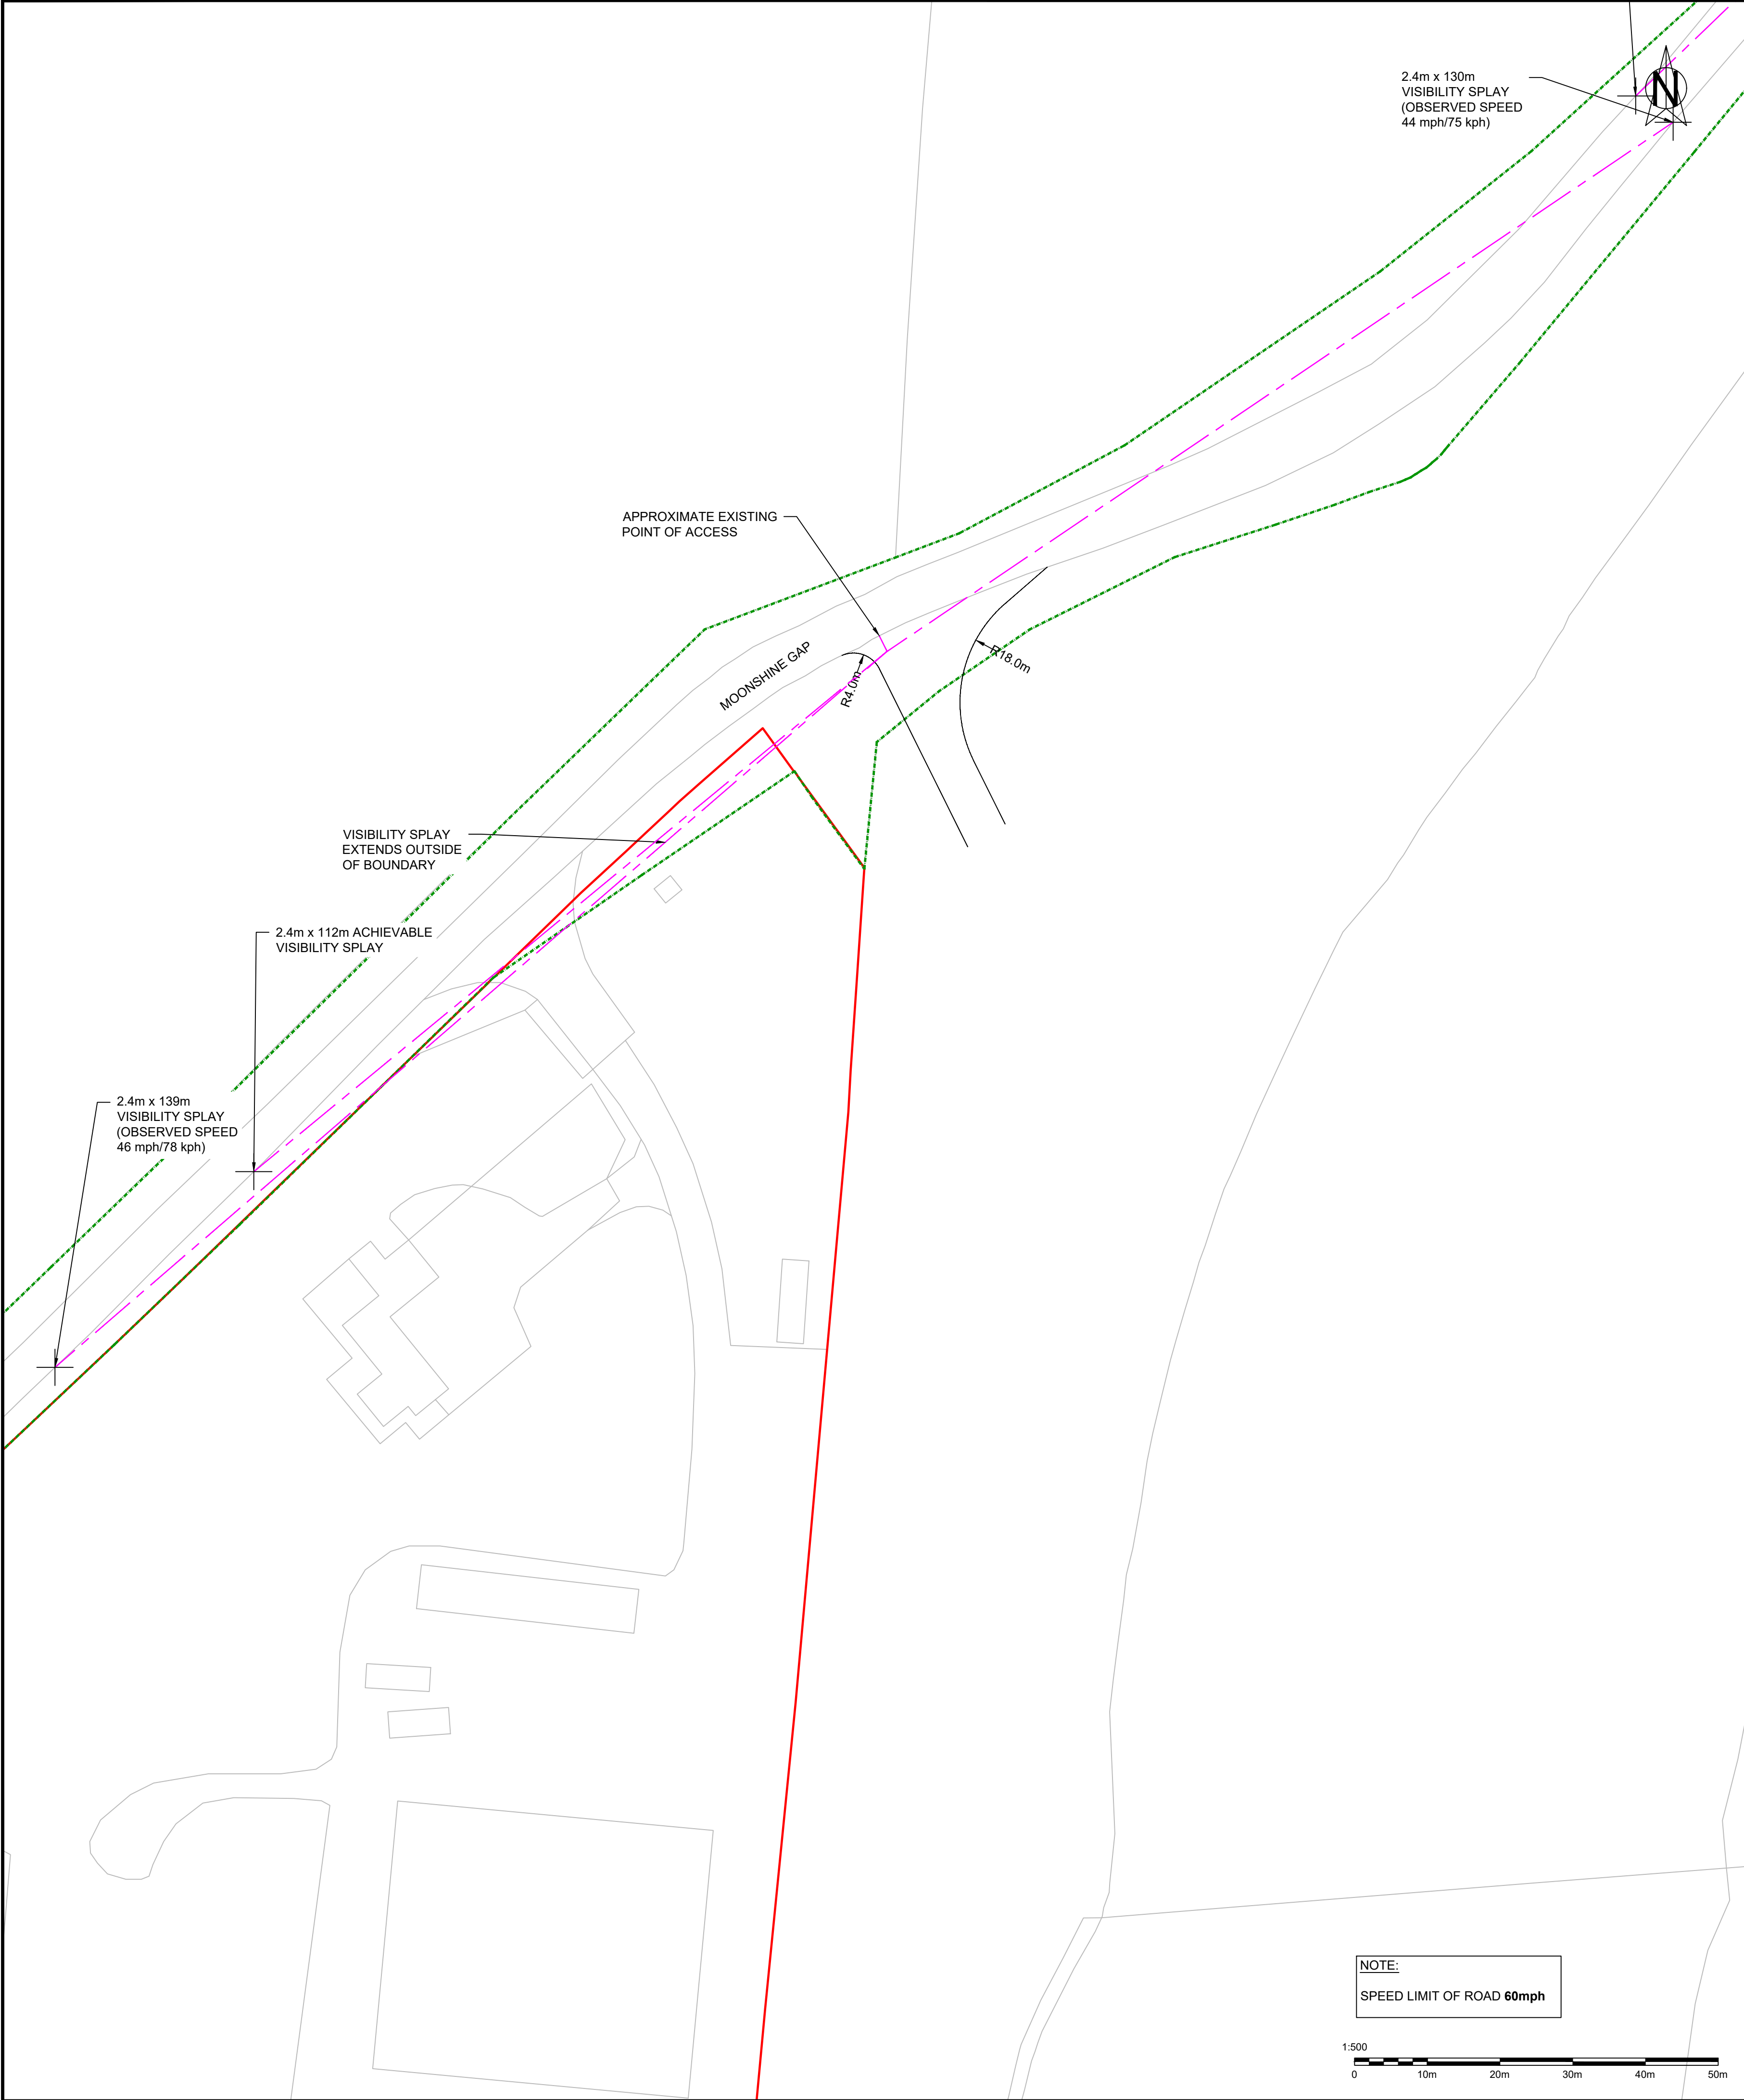

NOTES :

1. (C) This drawing is copyright.
2. All dimensions to be checked on site.
3. Do not scale from this drawing; only figured dimensions are to be worked from.
4. Any discrepancies must be reported immediately before proceeding.
5. This drawing to be read & printed in colour.
6. Ordnance Survey, (c) Crown Copyright 2024. All rights reserved. Licence number 100022432.

KEY PLAN
1:200000@A1

KEY:

- SITE BOUNDARY
- TRAFFIC SURVEY LOCATION
- HIGHWAY BOUNDARY
- VISIBILITY SPLAY EXTENT
- EXISTING LAYOUT
- PROPOSED EDGE OF ACCESS
- EXISTING VEGETATION
- EXTENT OF VEGETATION REMOVAL
- EXISTING CONTOURS

VEHICLE PROFILE:

VARIO-MAX LOWBED - 29.63m meters

TRACTOR WIDTH	: 2.55
TRAILER WIDTH	: 2.55
TRACTOR TRACK	: 2.55
TRAILER TRACK	: 2.55
LOCK TO LOCK TIME	: 6.0
STEERING ANGLE	: 40.0
ARTICULATING ANGLE	: 70.0

VEHICLE ANALYSIS KEY:

- VEHICLE PATH & DIRECTION
- VEHICLE BODY ENVELOPE
- VEHICLE FRONT WHEEL PATH
- 0.3m VEHICLE BUFFER ZONE AROUND TRACKING

C	03.12.2025	Drawing updated as per client comments	CS	OW	SM
B	19.05.2025	Boundary removed	CS	OW	SM
A	10.04.2025	Preliminary issue	CS	OW	SM

REV	DATE	DESCRIPTION	DRN	CHKD	APRD

Issue Status

<input type="checkbox"/> CONCEPT	<input type="checkbox"/> CONSTRUCTION
<input checked="" type="checkbox"/> PRELIMINARY	<input type="checkbox"/> AS BUILT
<input type="checkbox"/> TENDER	<input type="checkbox"/> HAS FILE ISSUE




Client
GREEN HILL SOLAR FARM LTD

Project
GREEN HILL SOLAR FARM

Drawing Title
CABLE ROUTE ACCESS 7
GENERAL ARRANGEMENT & VEHICLE TRACKING

Scale @ A1	Drawn	CS	Chkd	OW
As shown	Aprd	SM	Date	APR 2025

Drawing Ref	Rev
23061-KMC-XX-CR7-DR-CH-0001	C

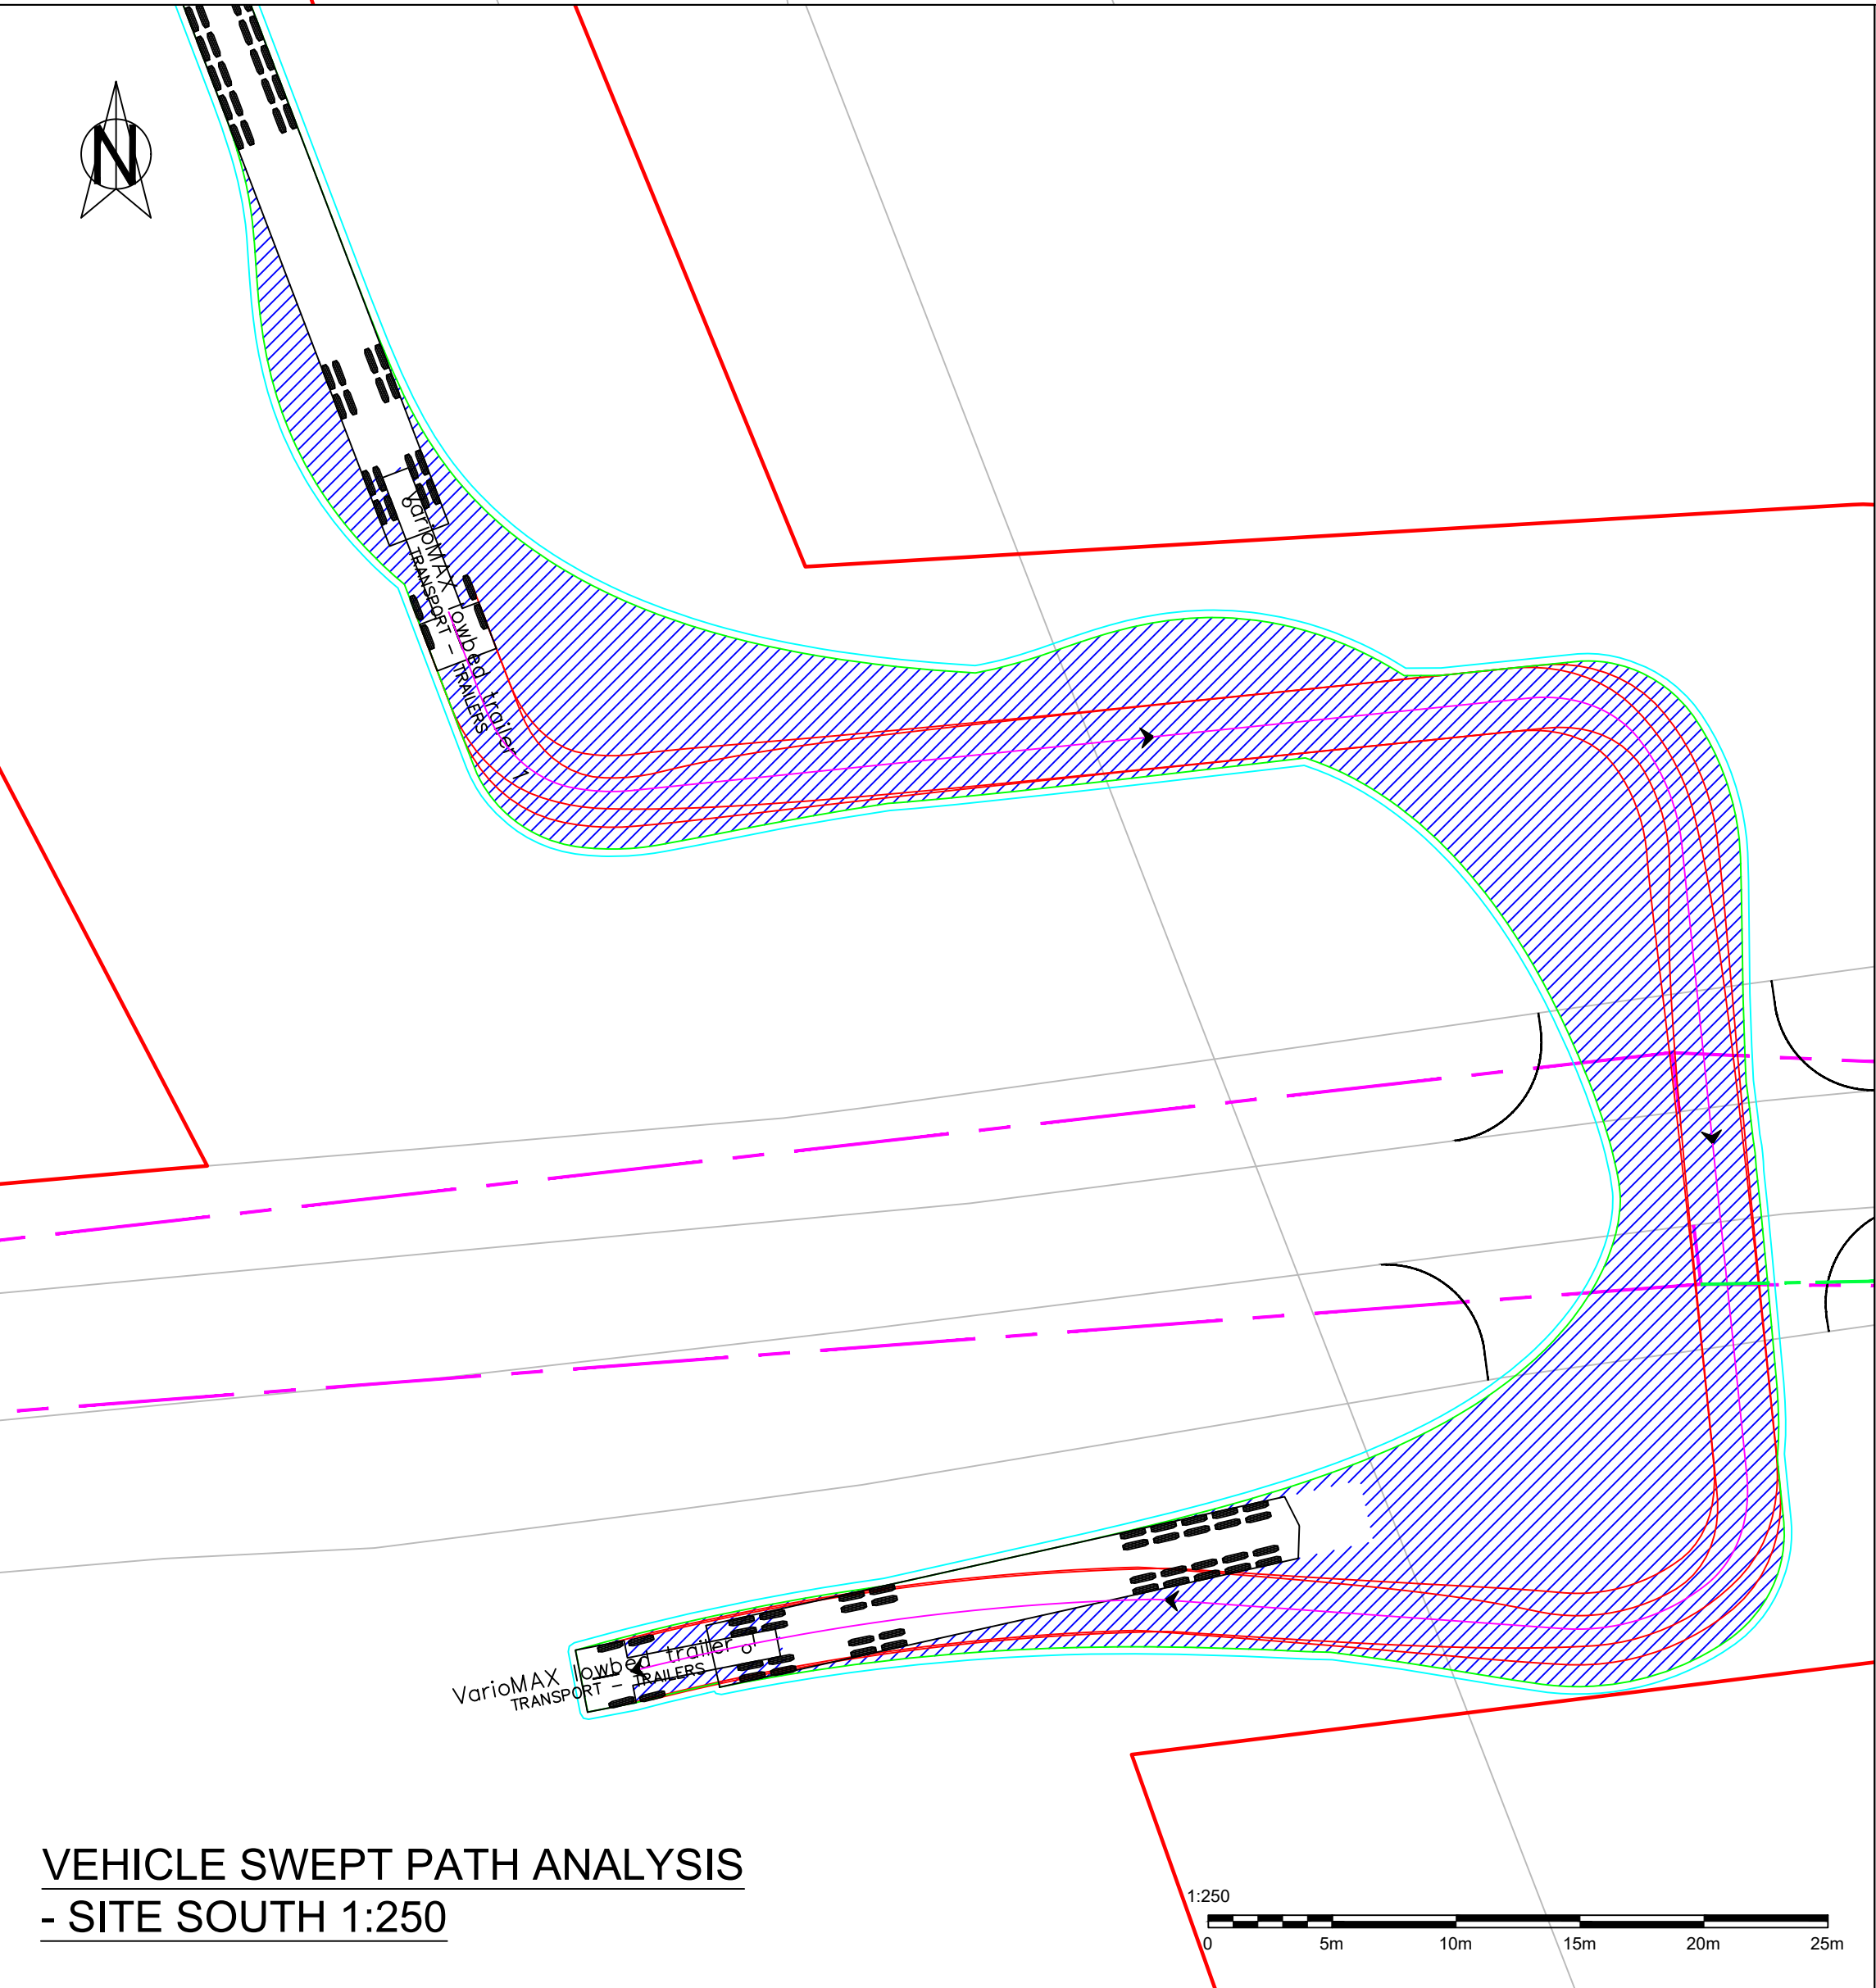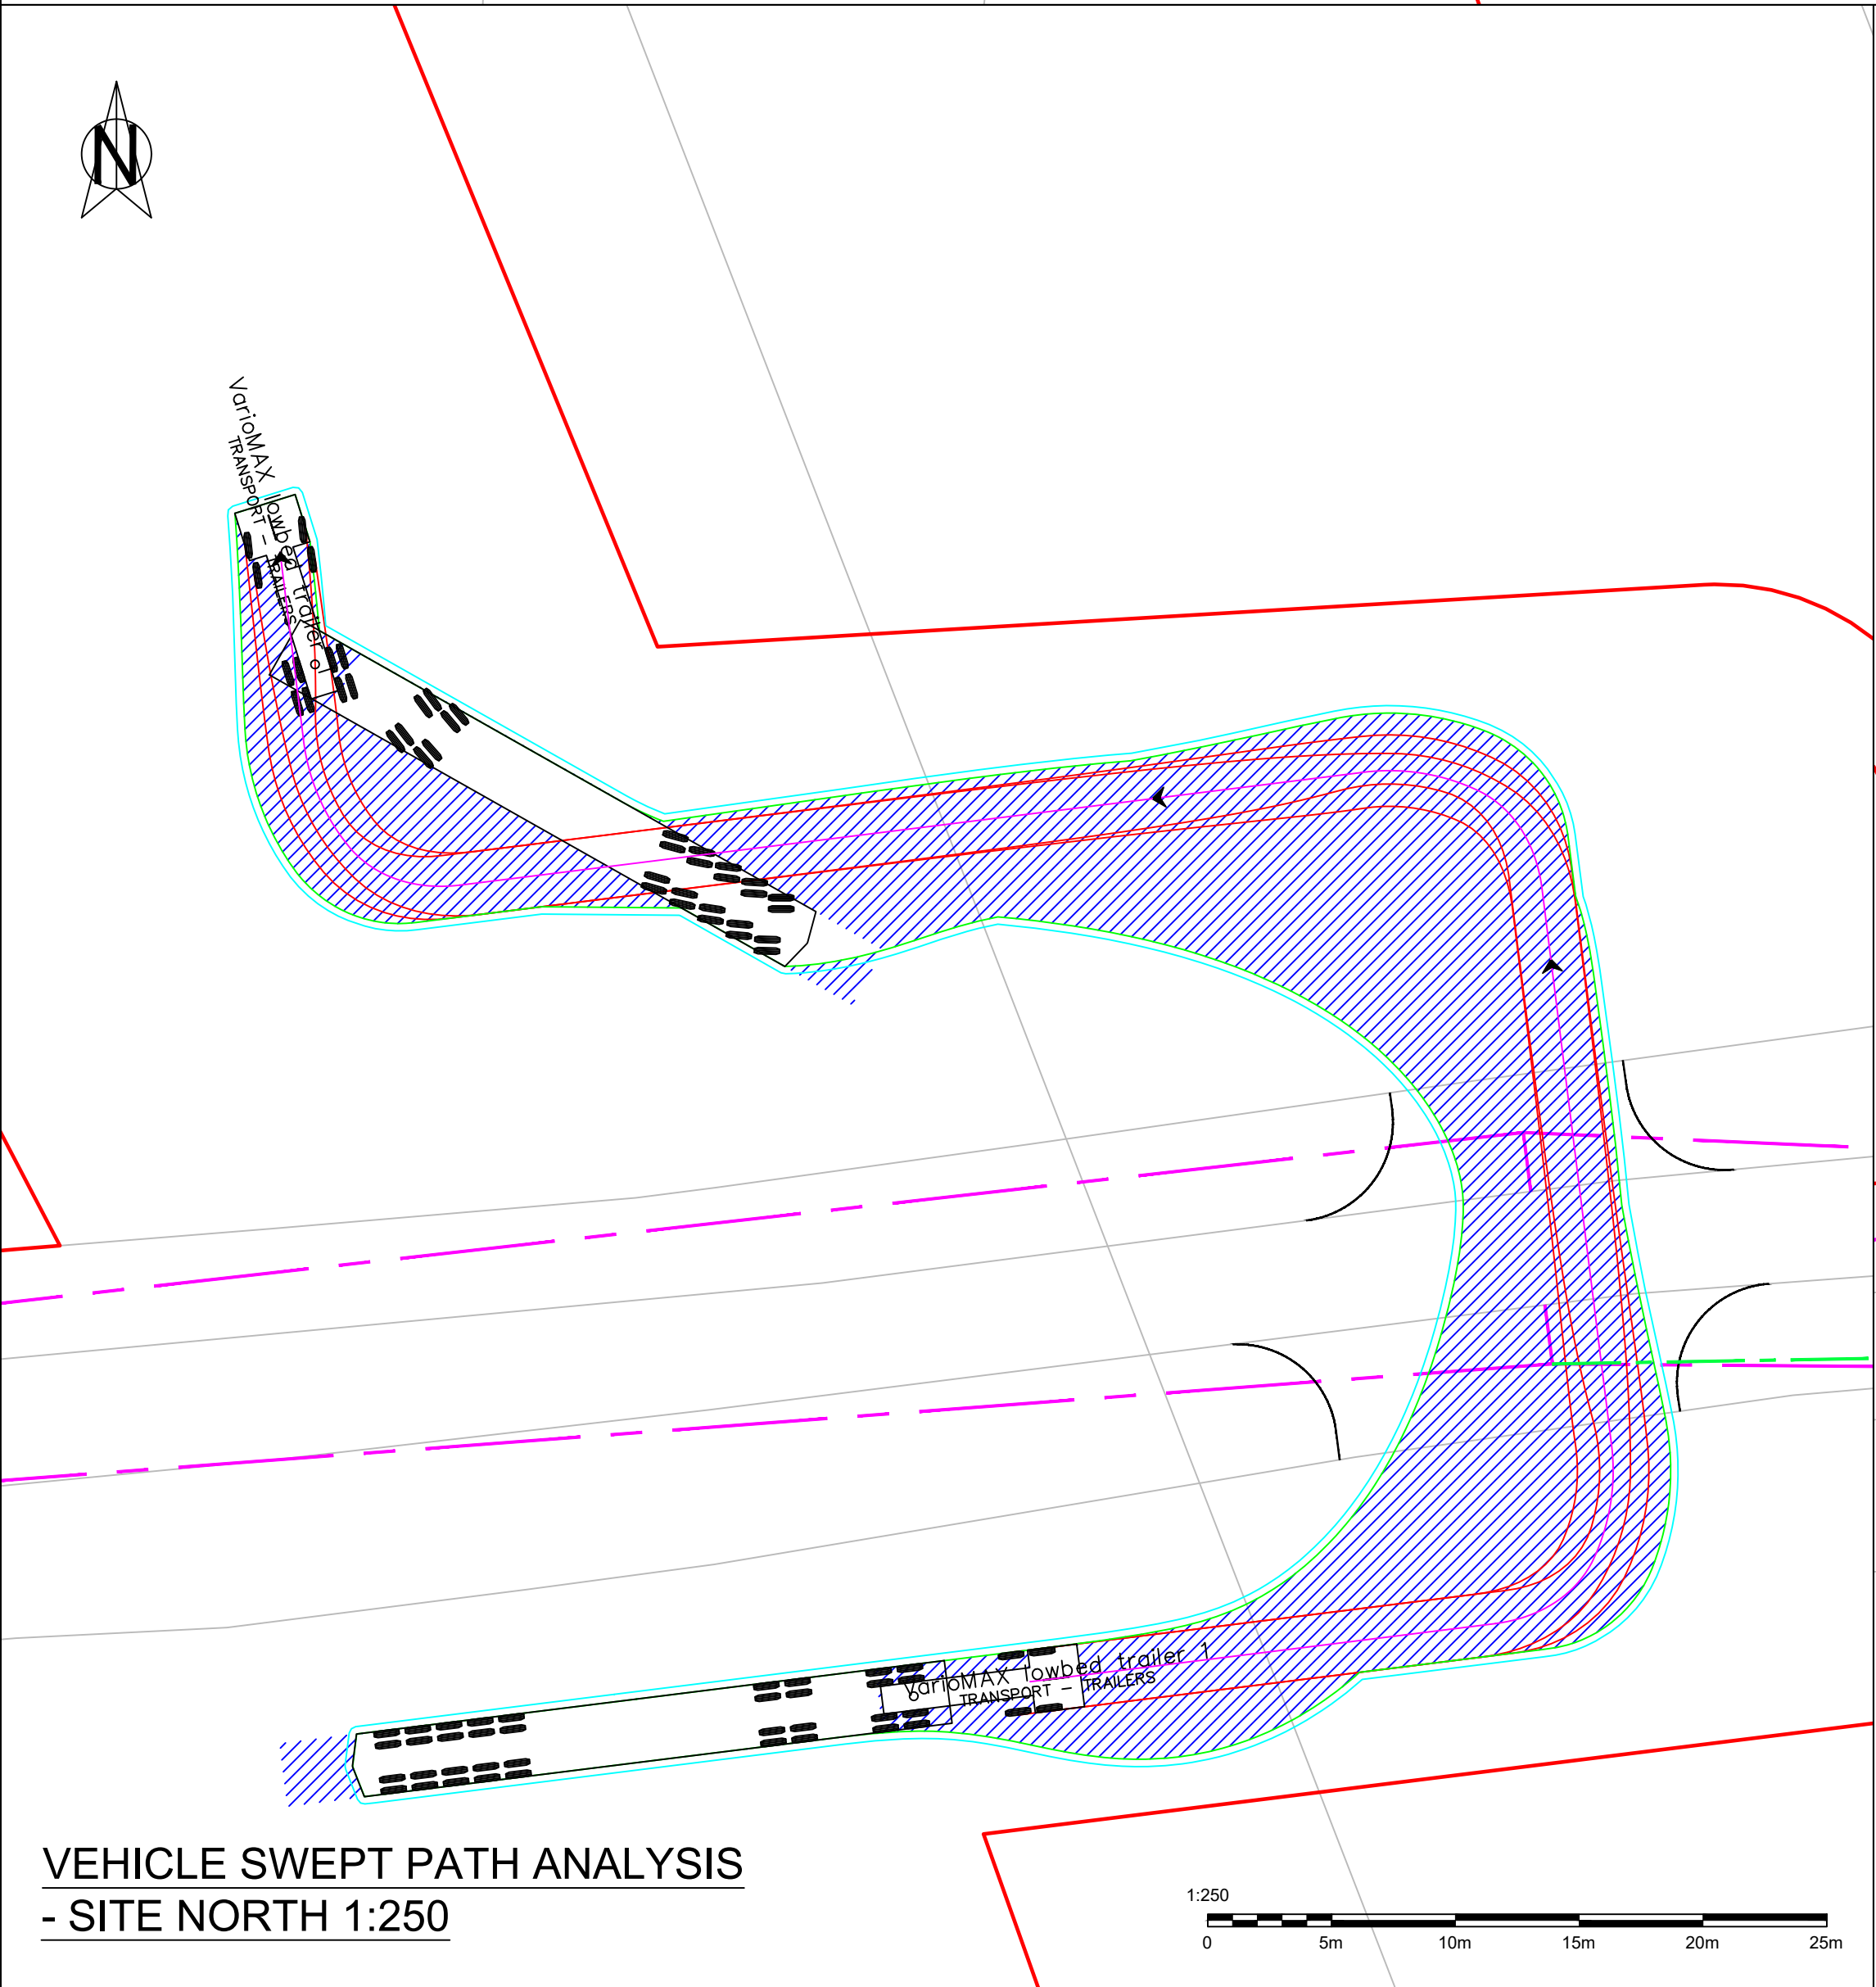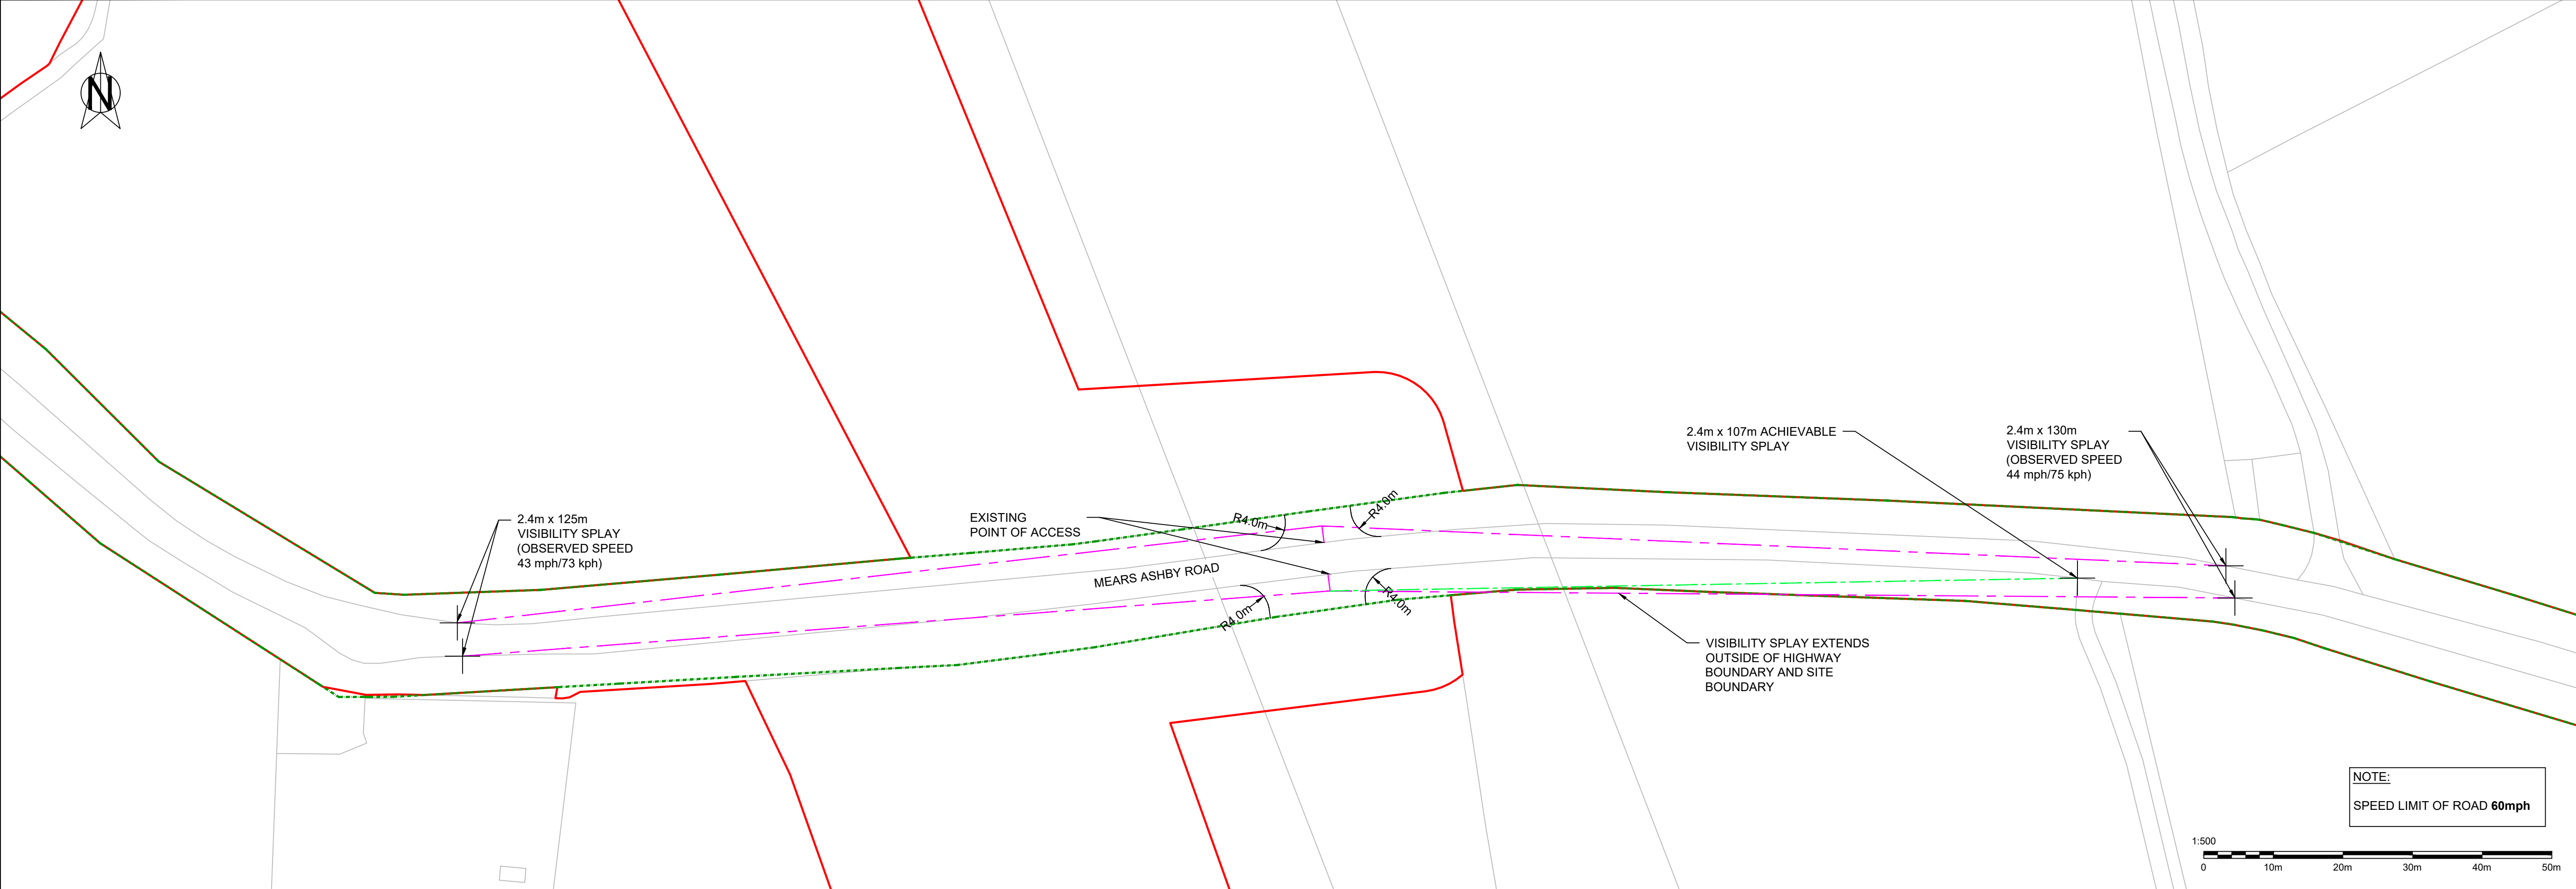

NOTES :

1. (C) This drawing is copyright.
2. All dimensions to be checked on site.
3. Do not scale from this drawing; only figured dimensions are to be worked from.
4. Any discrepancies must be reported immediately before proceeding.
5. This drawing to be read & printed in colour.
6. Ordnance Survey, (c) Crown Copyright 2024. All rights reserved. Licence number 100022432.

KEY:

- SITE BOUNDARY
- TRAFFIC SURVEY LOCATION
- HIGHWAY BOUNDARY
- VISIBILITY SPLAY EXTENT
- EXISTING LAYOUT
- PROPOSED EDGE OF ACCESS
- EXISTING VEGETATION
- EXTENT OF VEGETATION REMOVAL
- EXISTING CONTOURS

VEHICLE PROFILE:

VARIO-MAX LOWBED - 29.63m meters

TRACTOR WIDTH	: 2.55
TRAILER WIDTH	: 2.55
TRACTOR TRACK	: 2.55
TRAILER TRACK	: 2.55
LOCK TO LOCK TIME	: 6.0
STEERING ANGLE	: 40.0
ARTICULATING ANGLE	: 70.0

VEHICLE ANALYSIS KEY:

- VEHICLE PATH & DIRECTION
- VEHICLE BODY ENVELOPE
- VEHICLE FRONT WHEEL PATH
- 0.3m VEHICLE BUFFER ZONE AROUND TRACKING

D	03.12.2025	Drawing updated as per client comments	CS	OW	SM
C	19.05.2025	Achievable splay added	CS	OW	SM
B	10.04.2025	Boundary updated, Drawing combined	CS	OW	SM
A	10.04.2025	Preliminary issue	CS	OW	SM

REV	DATE	DESCRIPTION	DRN	CHKD	APRD

Issue Status

<input type="checkbox"/> CONCEPT	<input type="checkbox"/> CONSTRUCTION
<input checked="" type="checkbox"/> PRELIMINARY	<input type="checkbox"/> AS BUILT
<input type="checkbox"/> TENDER	<input type="checkbox"/> HAS FILE ISSUE

Client:

GREEN HILL SOLAR FARM LTD

Project:


GREEN HILL SOLAR FARM

Drawing Title:


CABLE ROUTE ACCESS 8 & 9
GENERAL ARRANGEMENT & VEHICLE TRACKING

Scale @ A1	Drawn	CS	Chkd	OW
As shown	Aprd	SM	Date	APR 2025


Drawing Ref	Rev
23061-KMC-XX-CR8-9-DR-CH-0001	D

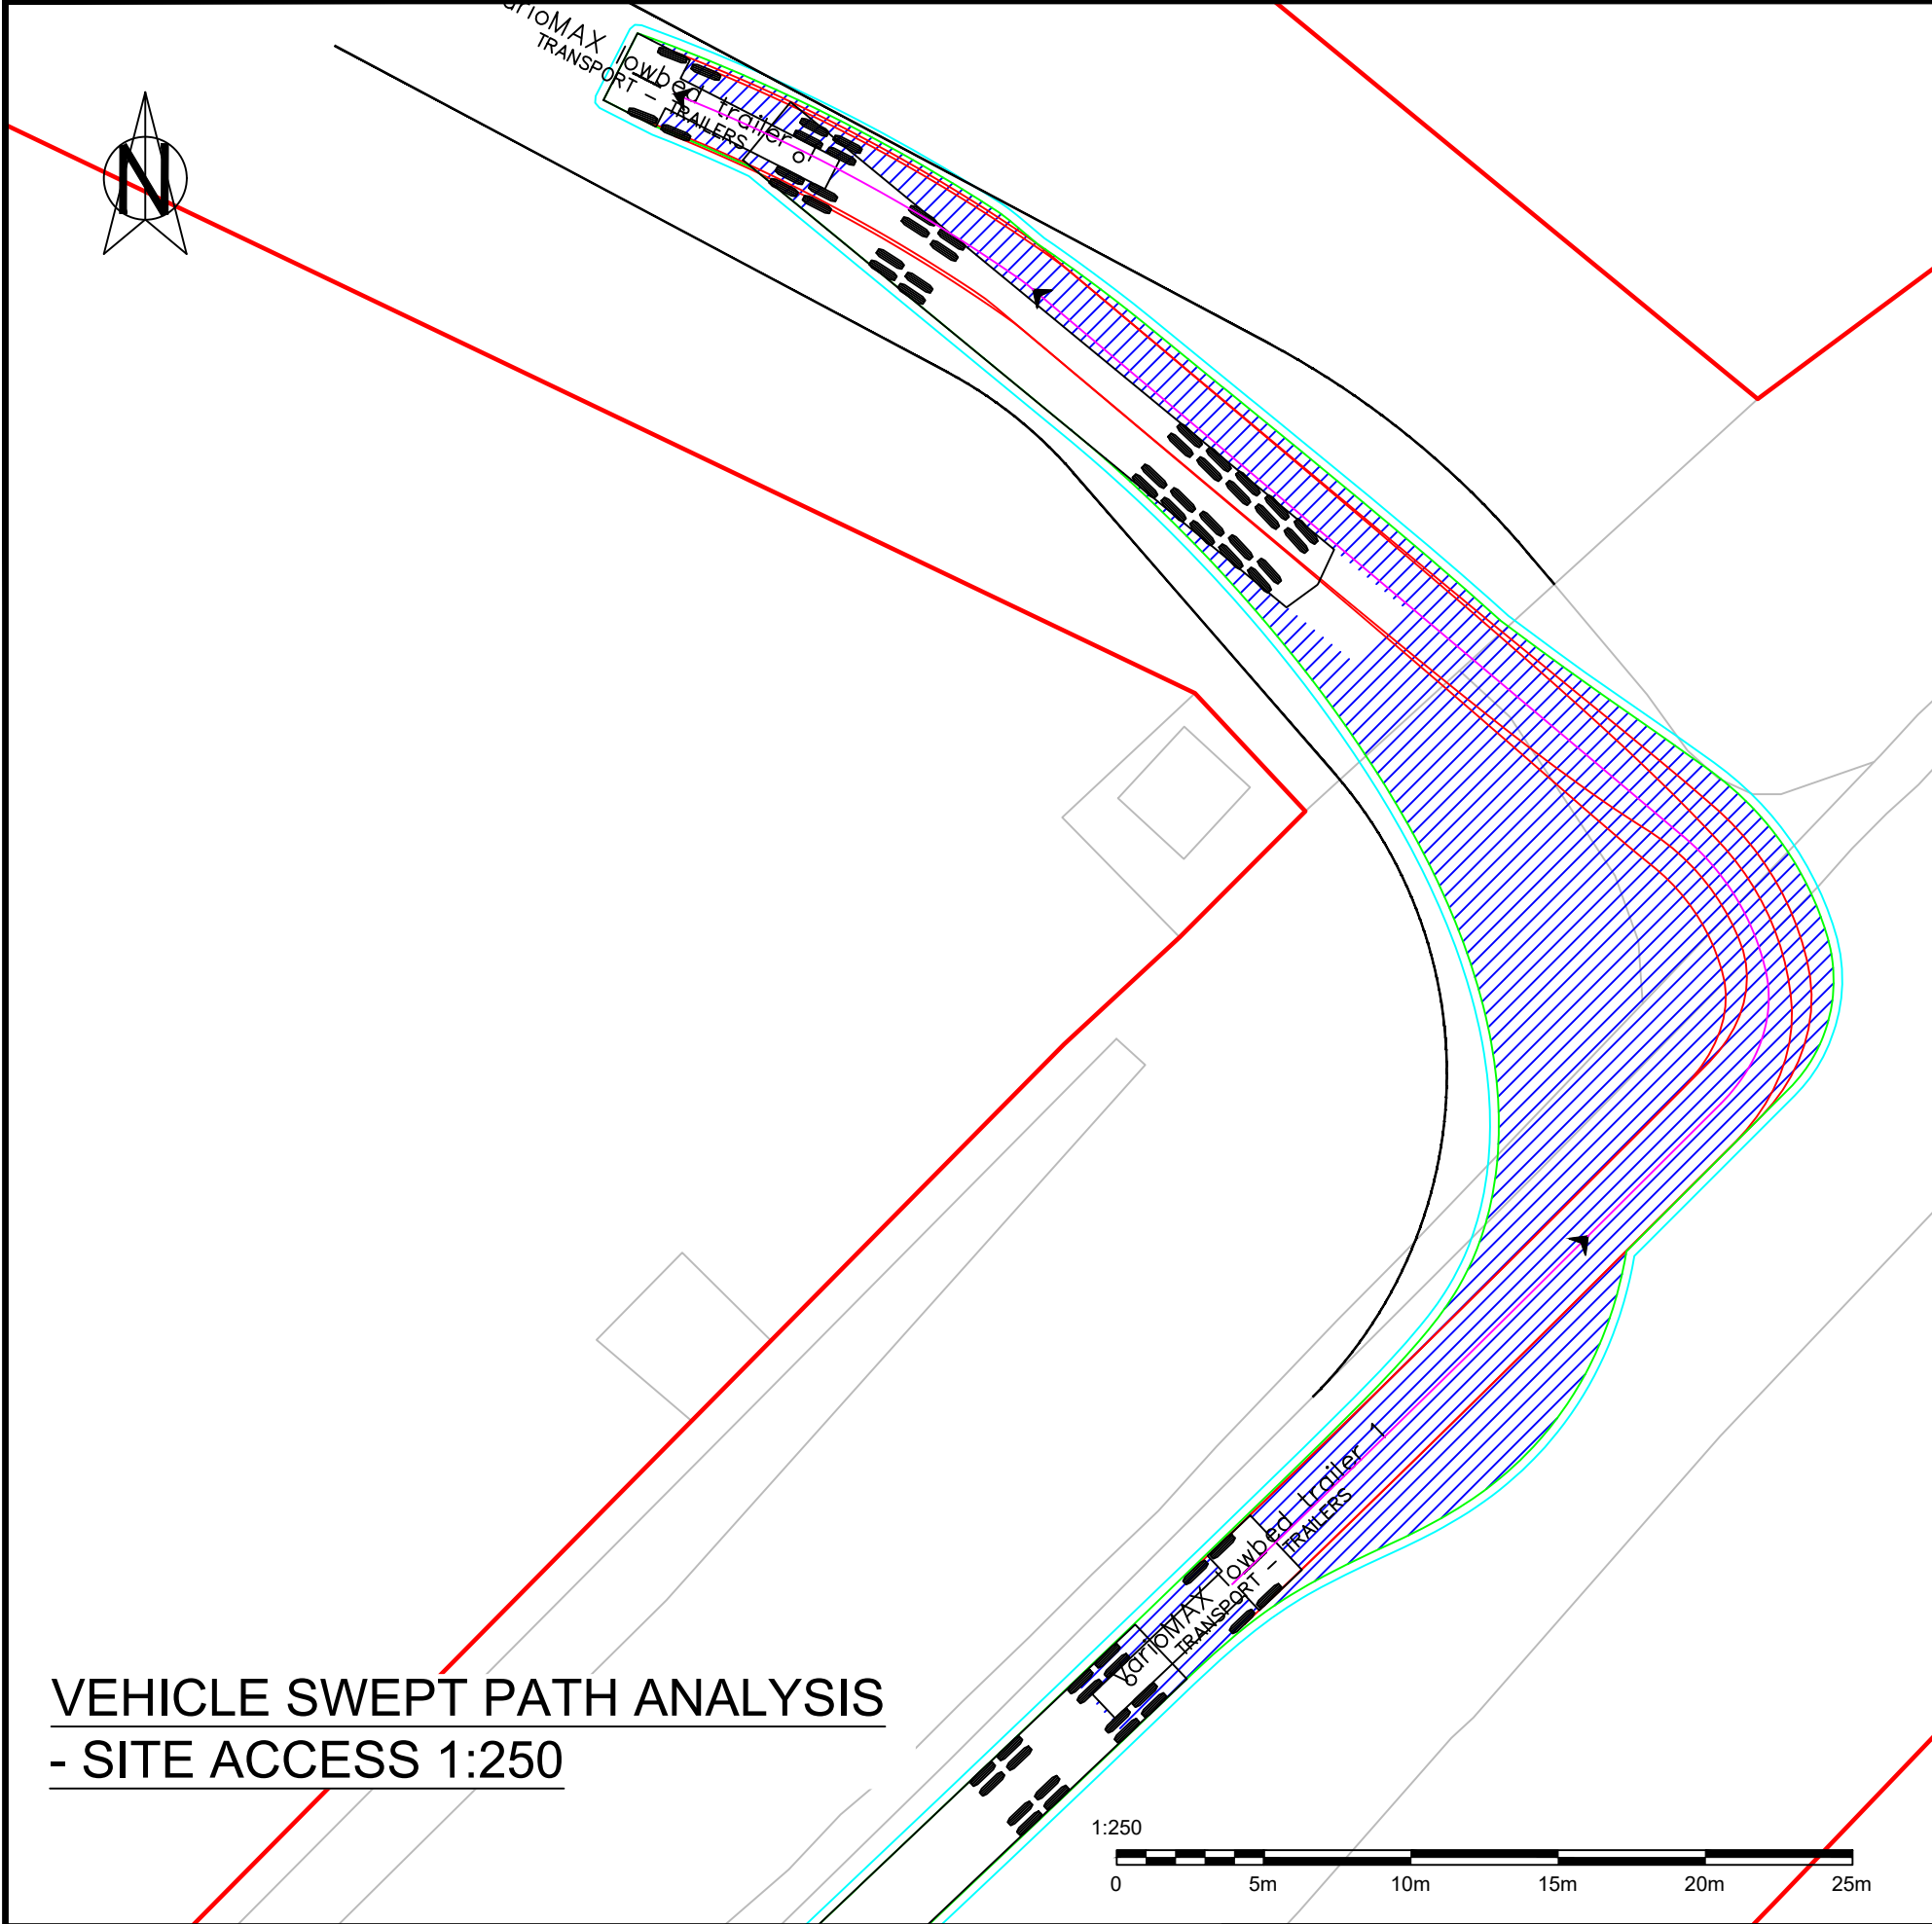

VEHICLE SWEEP PATH ANALYSIS
- SITE ACCESS 1:250

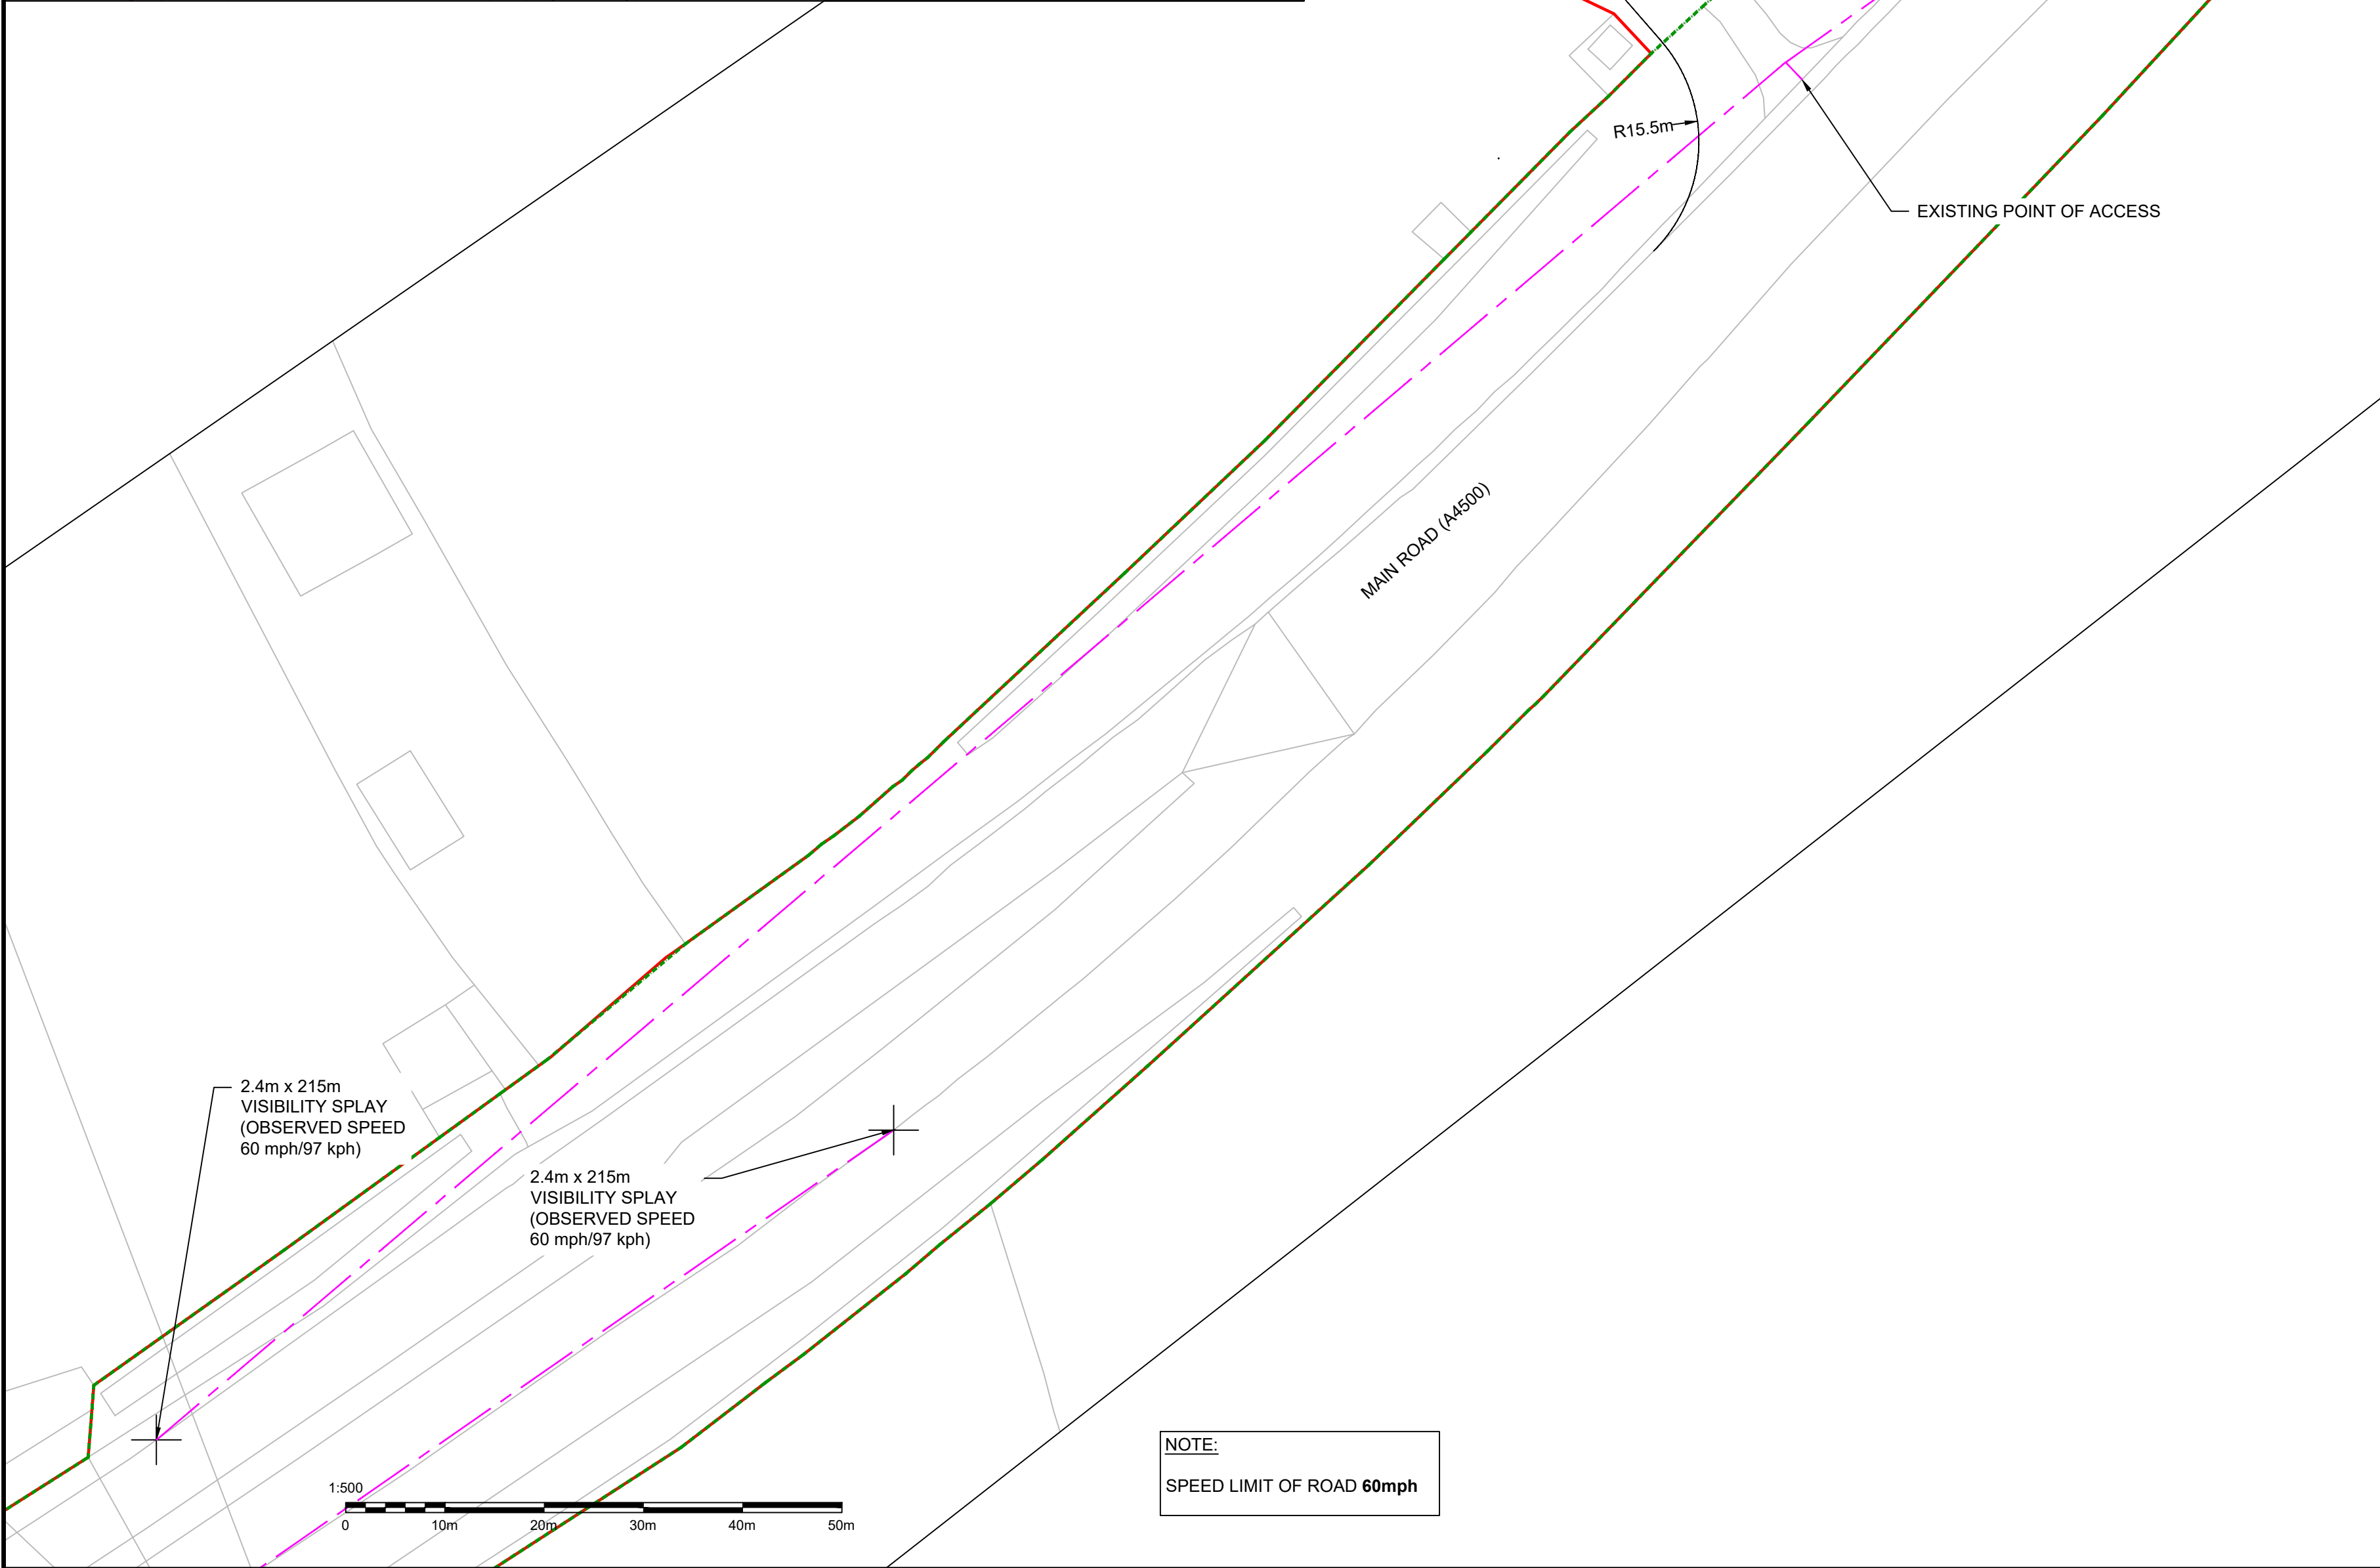

VEHICLE SWEEP PATH ANALYSIS
- SITE EGRESS 1:250

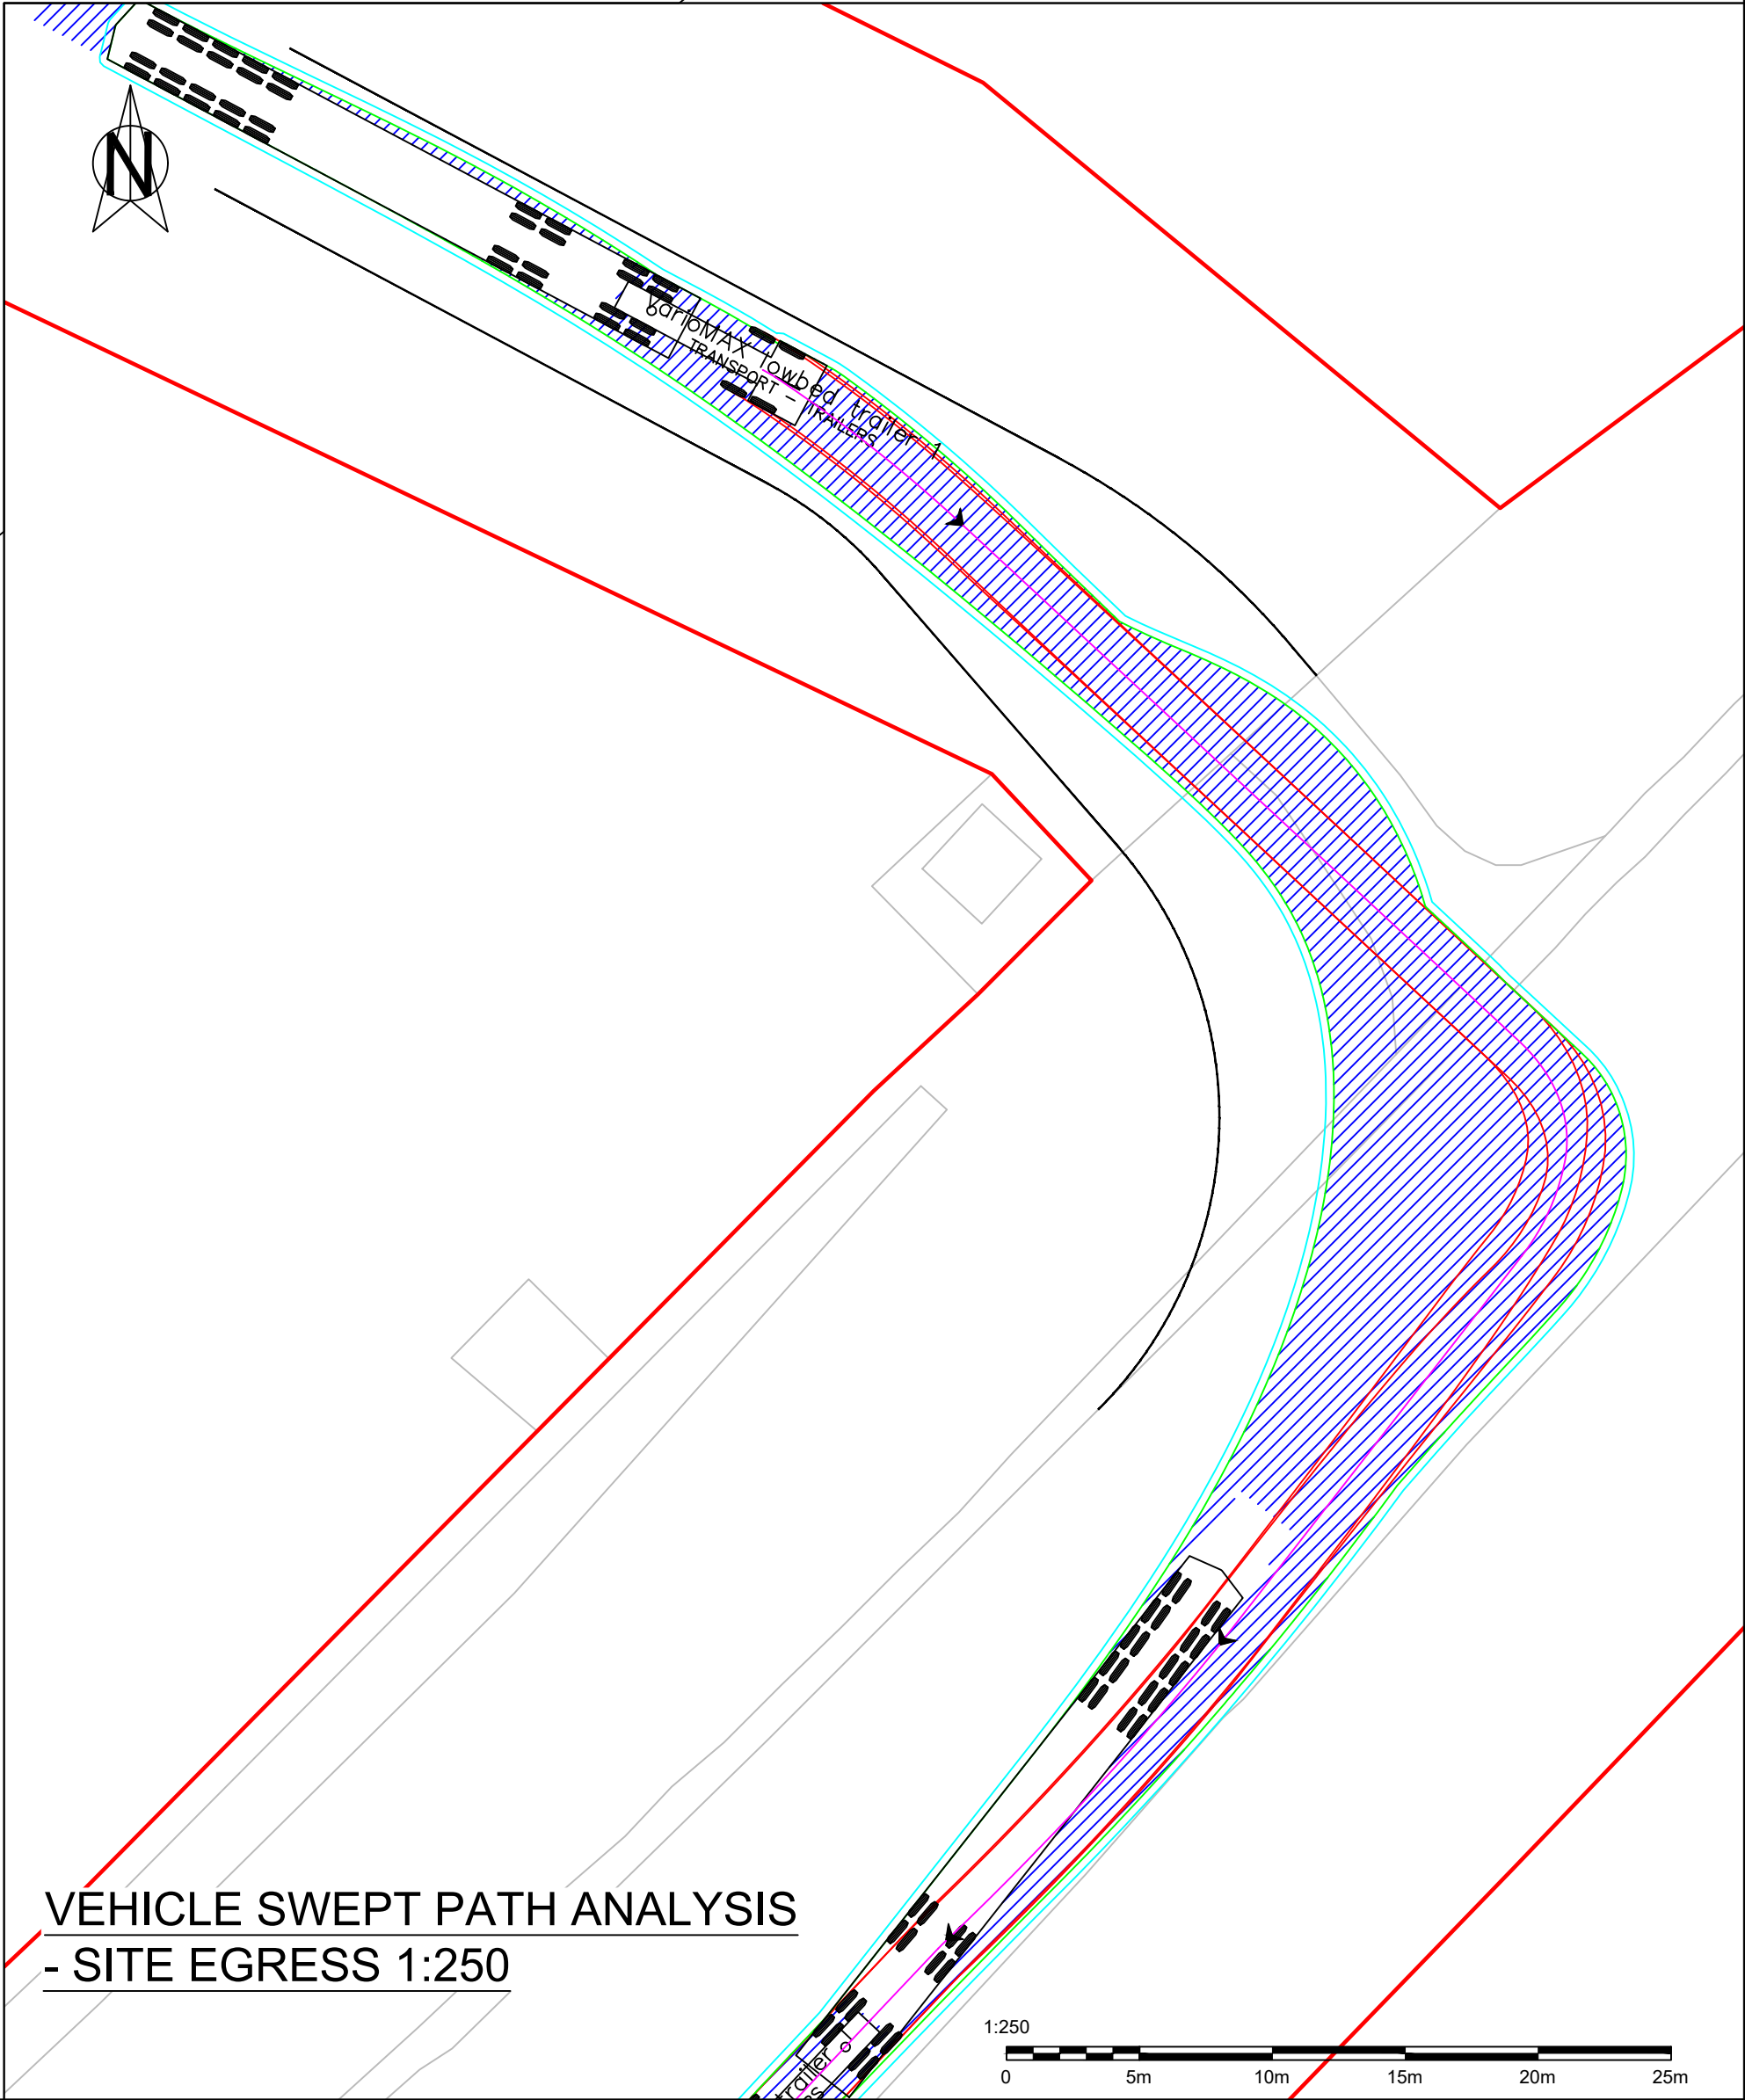

NOTES :

1. (C) This drawing is copyright.
2. All dimensions to be checked on site.
3. Do not scale from this drawing; only figured dimensions are to be worked from.
4. Any discrepancies must be reported immediately before proceeding.
5. This drawing to be read & printed in colour.
6. Ordnance Survey, (c) Crown Copyright 2024. All rights reserved. Licence number 100022432.

KEY PLAN
1:200000@A1

KEY:

- SITE BOUNDARY
- - - TRAFFIC SURVEY LOCATION
- - - HIGHWAY BOUNDARY
- - - VISIBILITY SPLAY EXTENT
- - - EXISTING LAYOUT
- - - PROPOSED EDGE OF ACCESS
- - - EXISTING VEGETATION
- - - EXTENT OF VEGETATION REMOVAL
- - - EXISTING CONTOURS

VEHICLE PROFILE:

VEHICLE PROFILE:

VARIO-MAX LOWBED - 29.63m meters

TRACTOR WIDTH	: 2.55
TRAILER WIDTH	: 2.55
TRACTOR TRACK	: 2.55
TRAILER TRACK	: 2.55
LOCK TO LOCK TIME	: 6.0
STEERING ANGLE	: 40.0
ARTICULATING ANGLE	: 70.0

VEHICLE ANALYSIS KEY:

- VEHICLE PATH & DIRECTION
- ▨ VEHICLE BODY ENVELOPE
- VEHICLE FRONT WHEEL PATH
- ▭ 0.3m VEHICLE BUFFER ZONE AROUND TRACKING

D	03.12.2025	Drawing updated as per client comments	CS	OW	SM
C	19.05.2025	Boundary removed	CS	OW	SM
B	10.04.2025	Boundary updated, Drawing combined	CS	OW	SM
A	11.03.2025	Preliminary issue	CS	LF	SM
REV	DATE	DESCRIPTION	DRN	CHKD	APRD

Issue Status

<input type="checkbox"/> CONCEPT	<input type="checkbox"/> CONSTRUCTION
<input checked="" type="checkbox"/> PRELIMINARY	<input type="checkbox"/> AS BUILT
<input type="checkbox"/> TENDER	<input type="checkbox"/> HAS FILE ISSUE

Client
GREEN HILL SOLAR FARM LTD



Project
GREEN HILL SOLAR FARM



Drawing Title
CABLE ROUTE ACCESS 10
GENERAL ARRANGEMENT & VEHICLE TRACKING

Scale @ A1	Drawn	CS	Chkd	OW
As shown	Aprd	SM	Date	MAR 2025

Drawing Ref	Rev
23061-KMC-XX-CR10-DR-CH-0001	D

kmc
transport planning

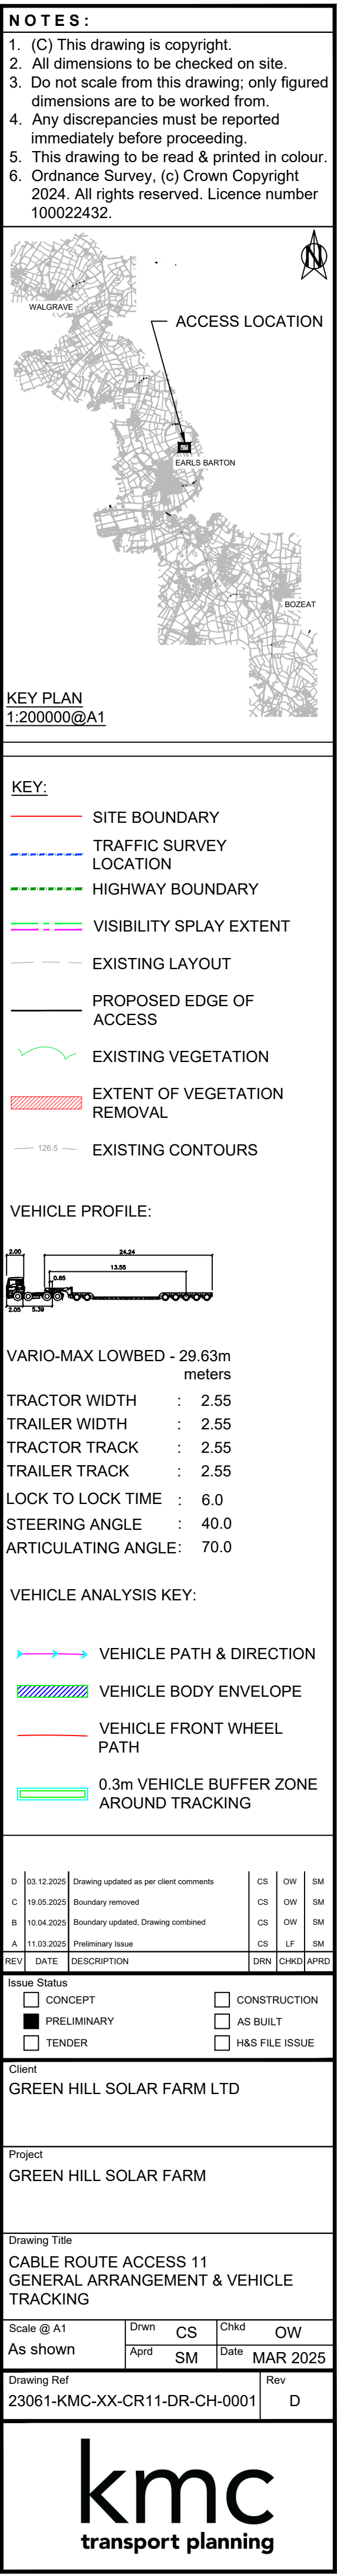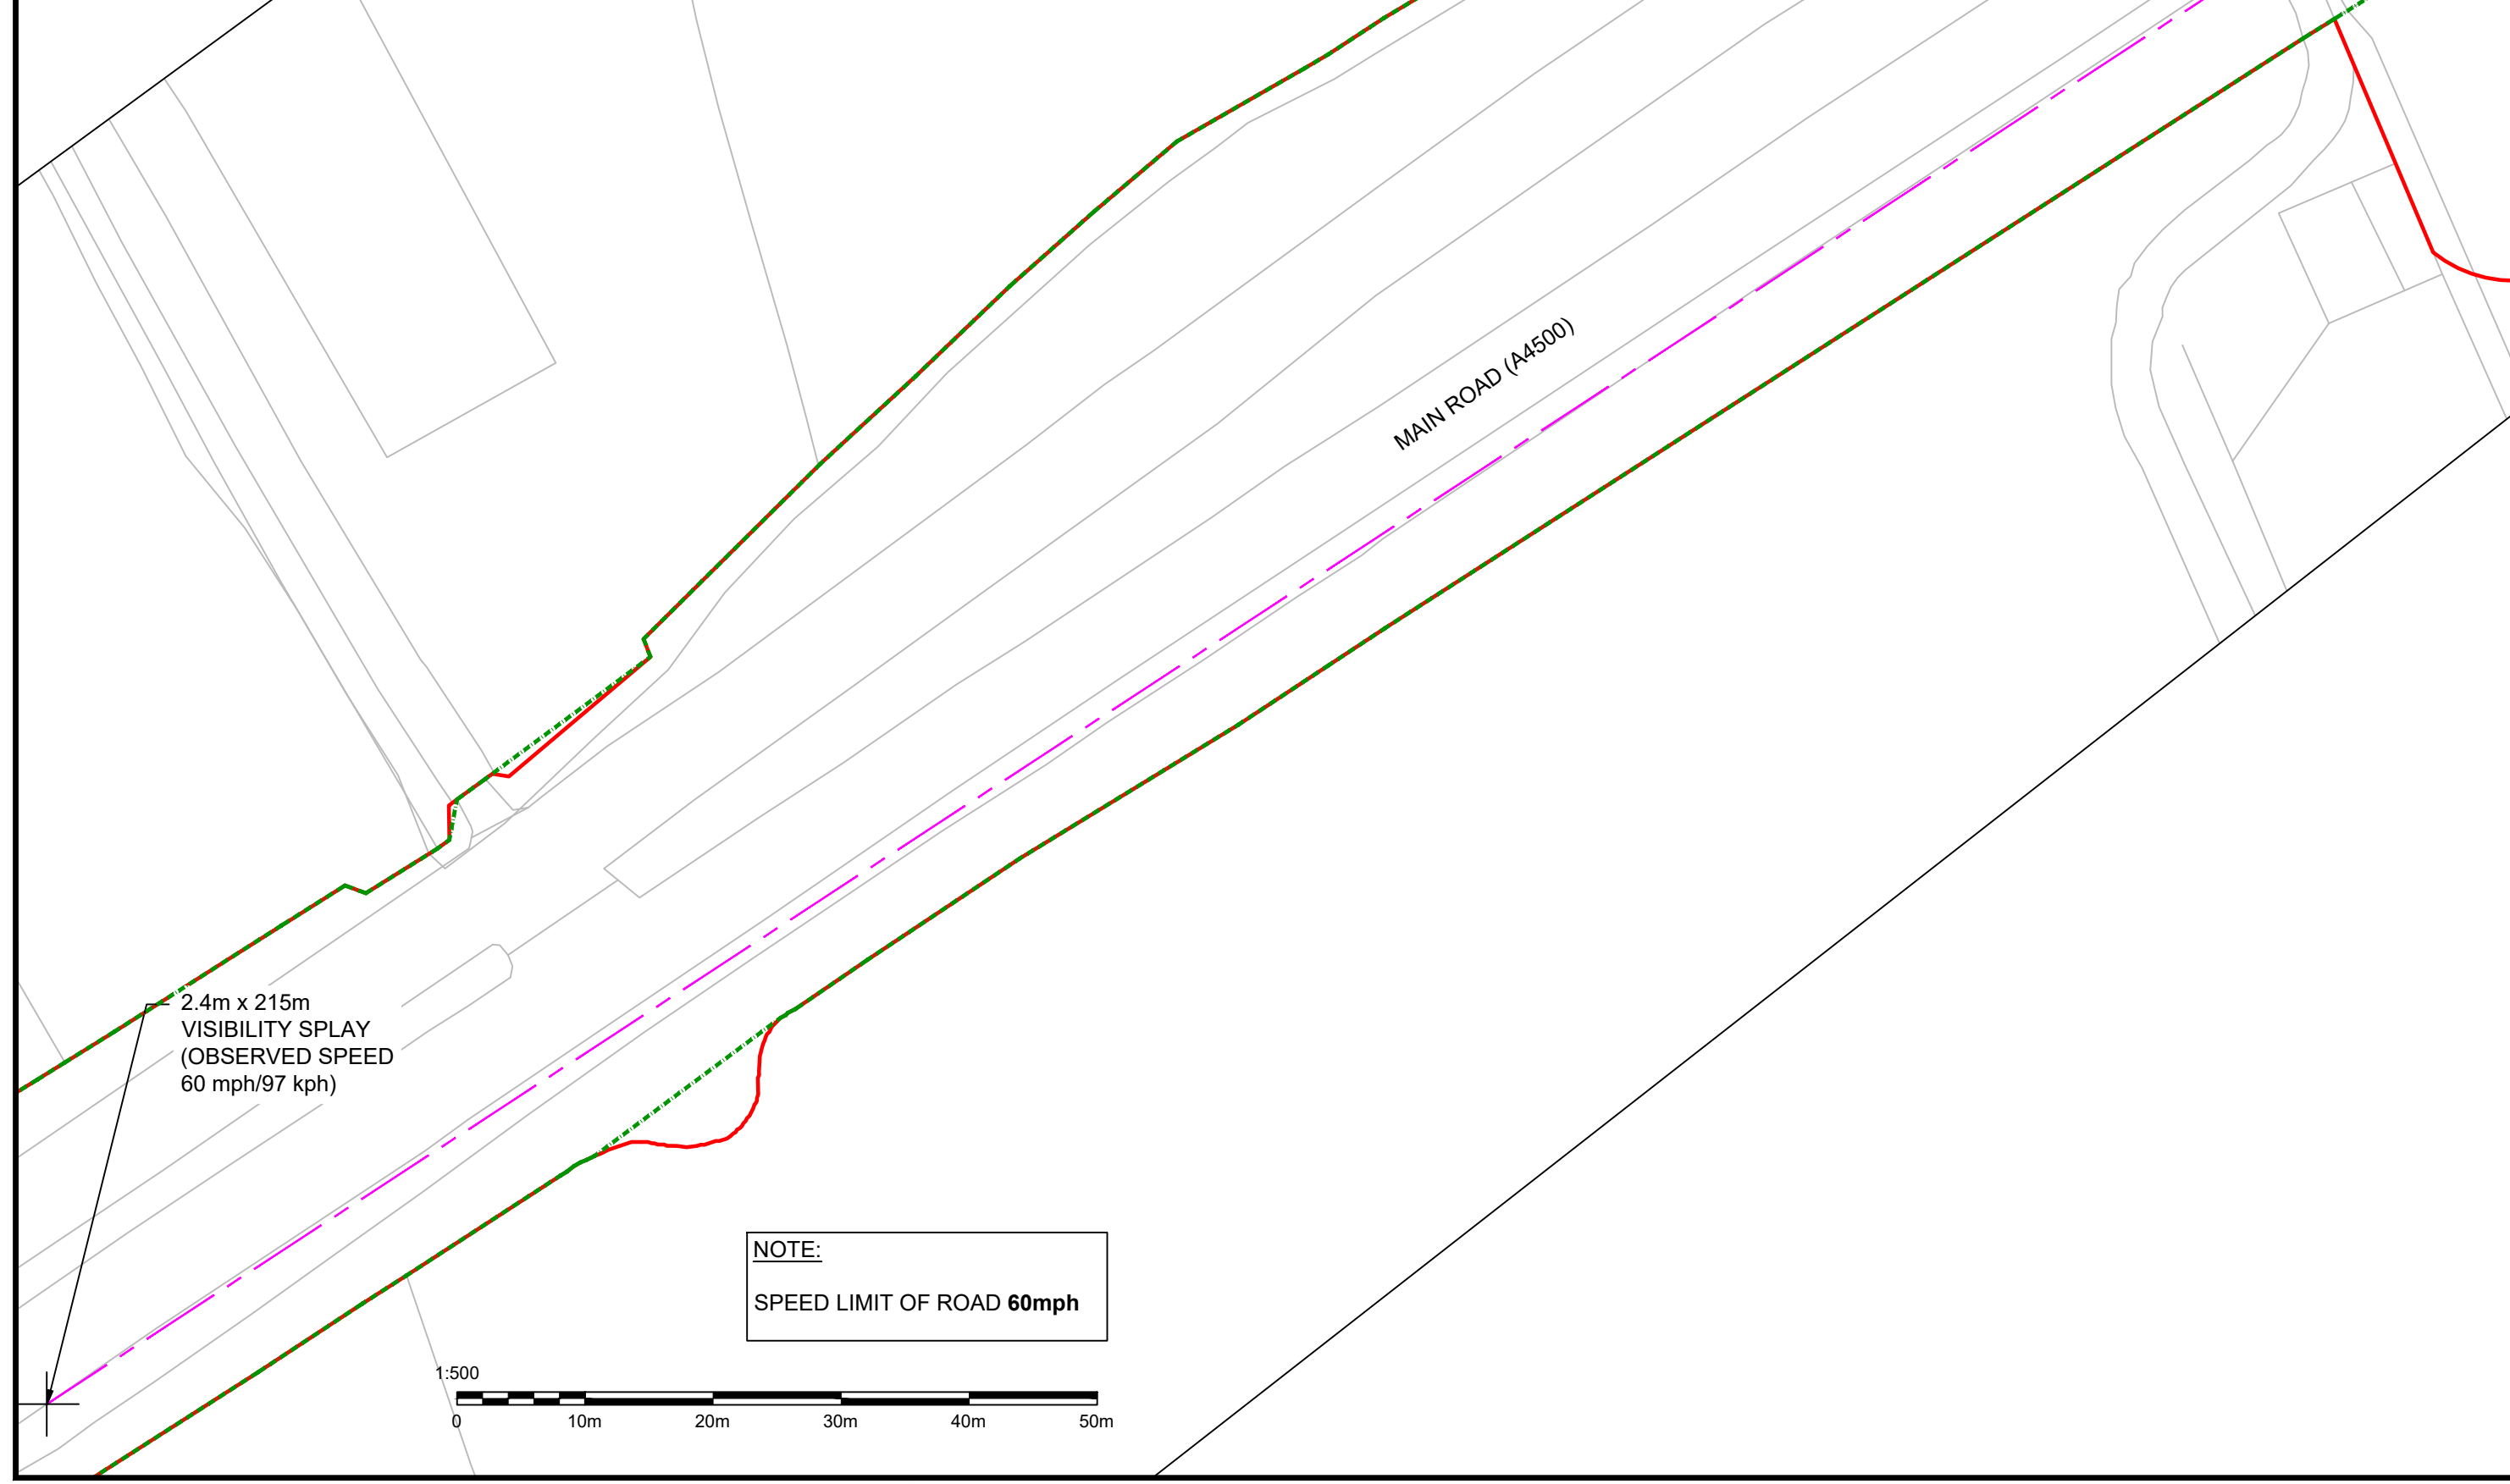

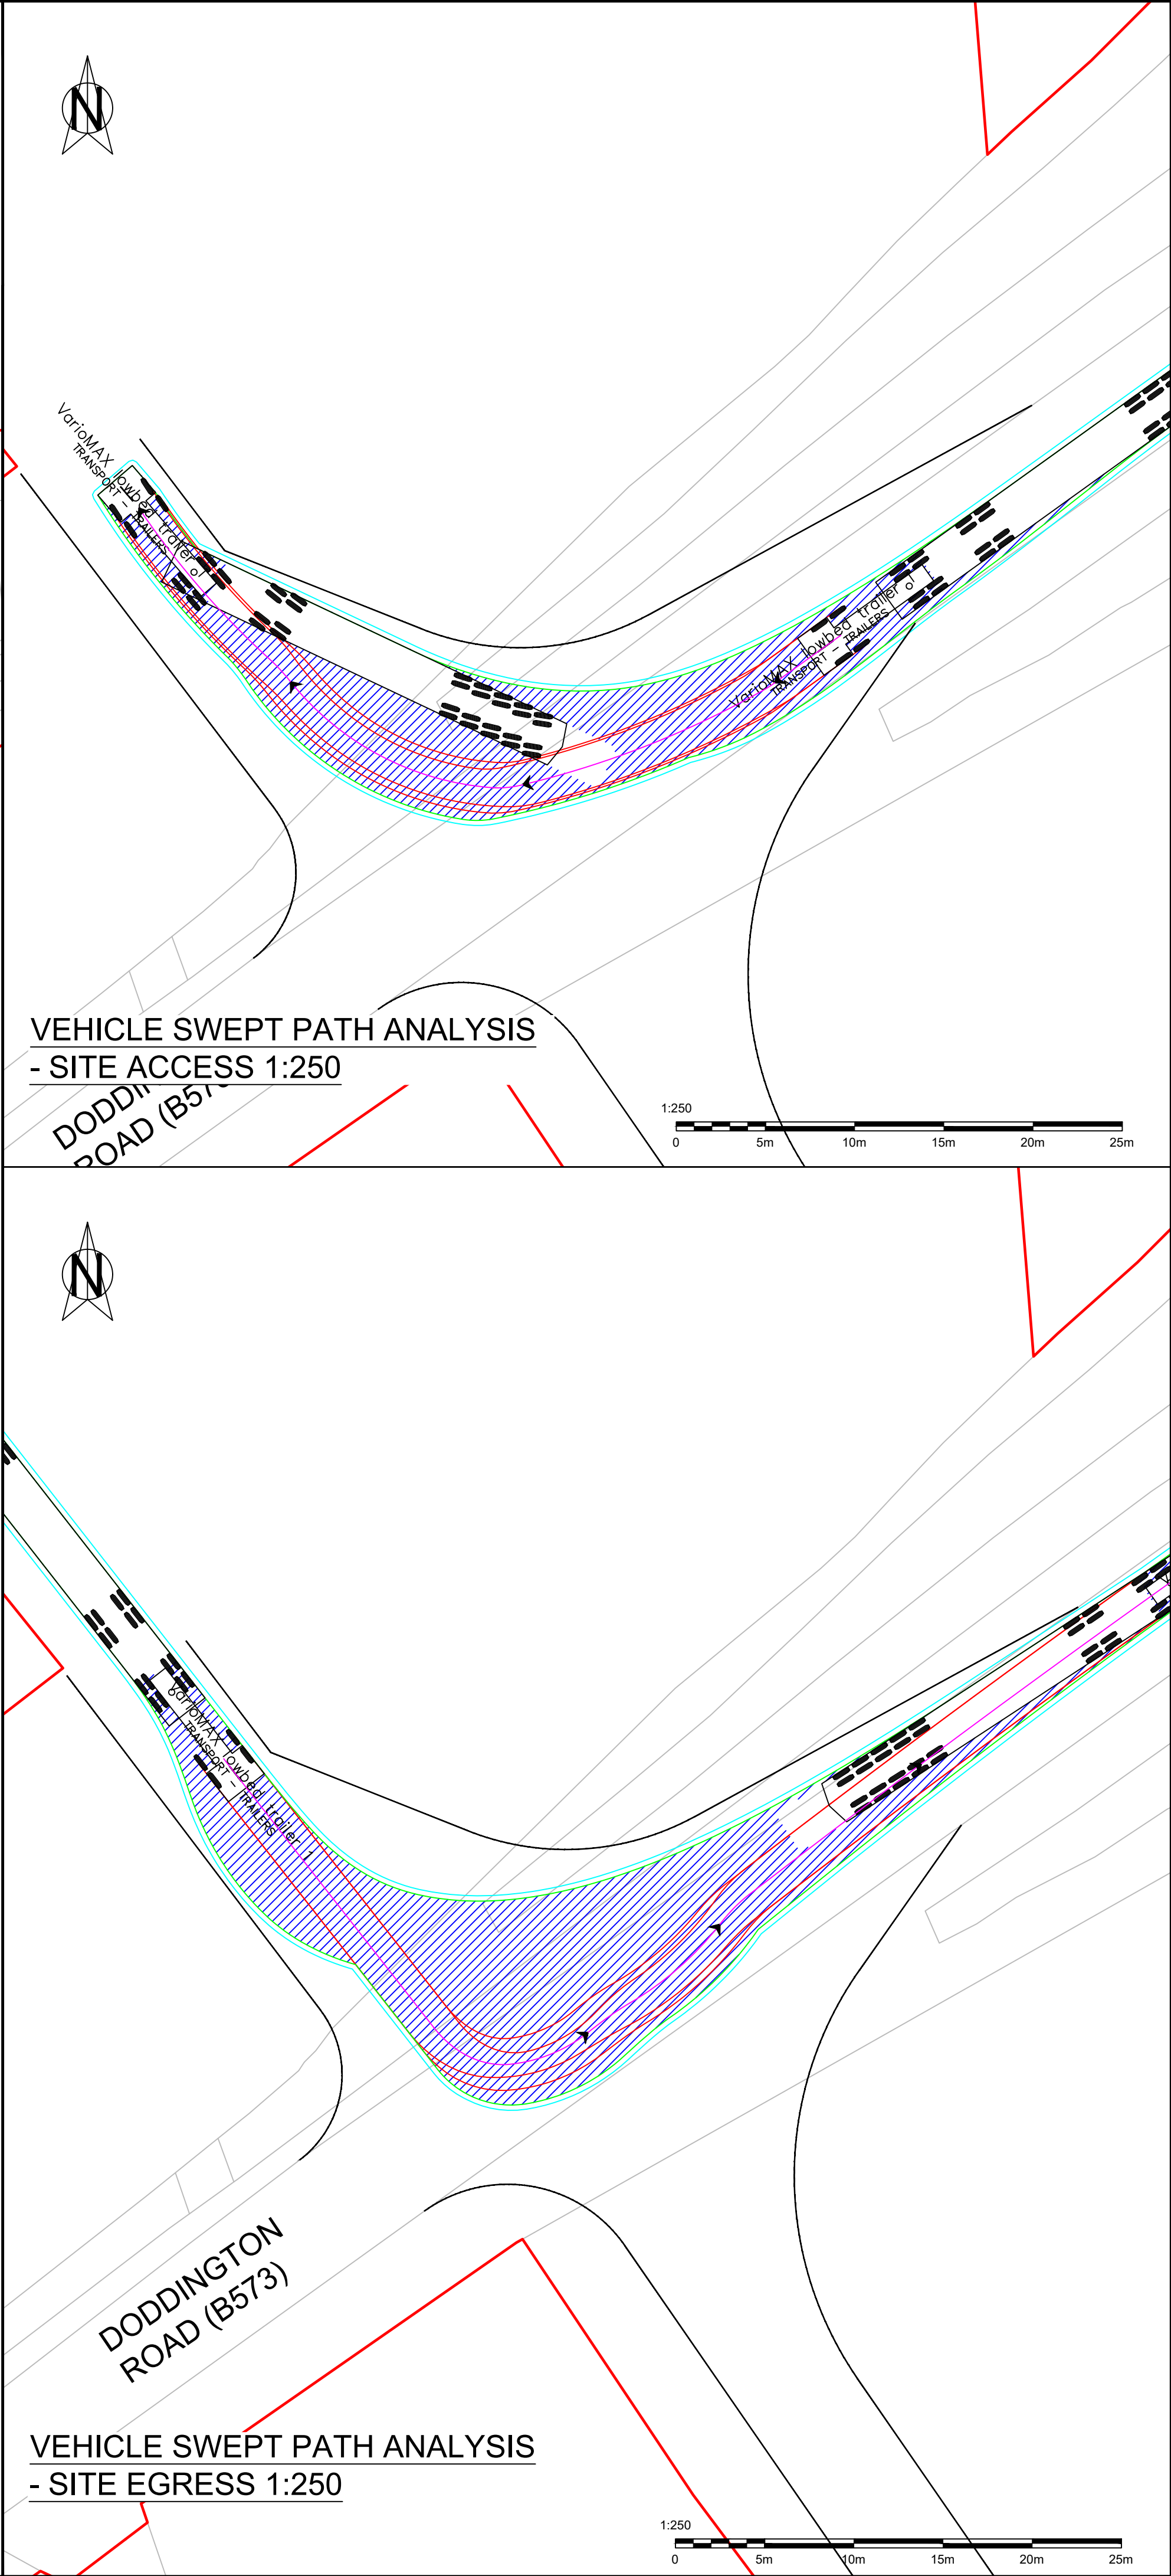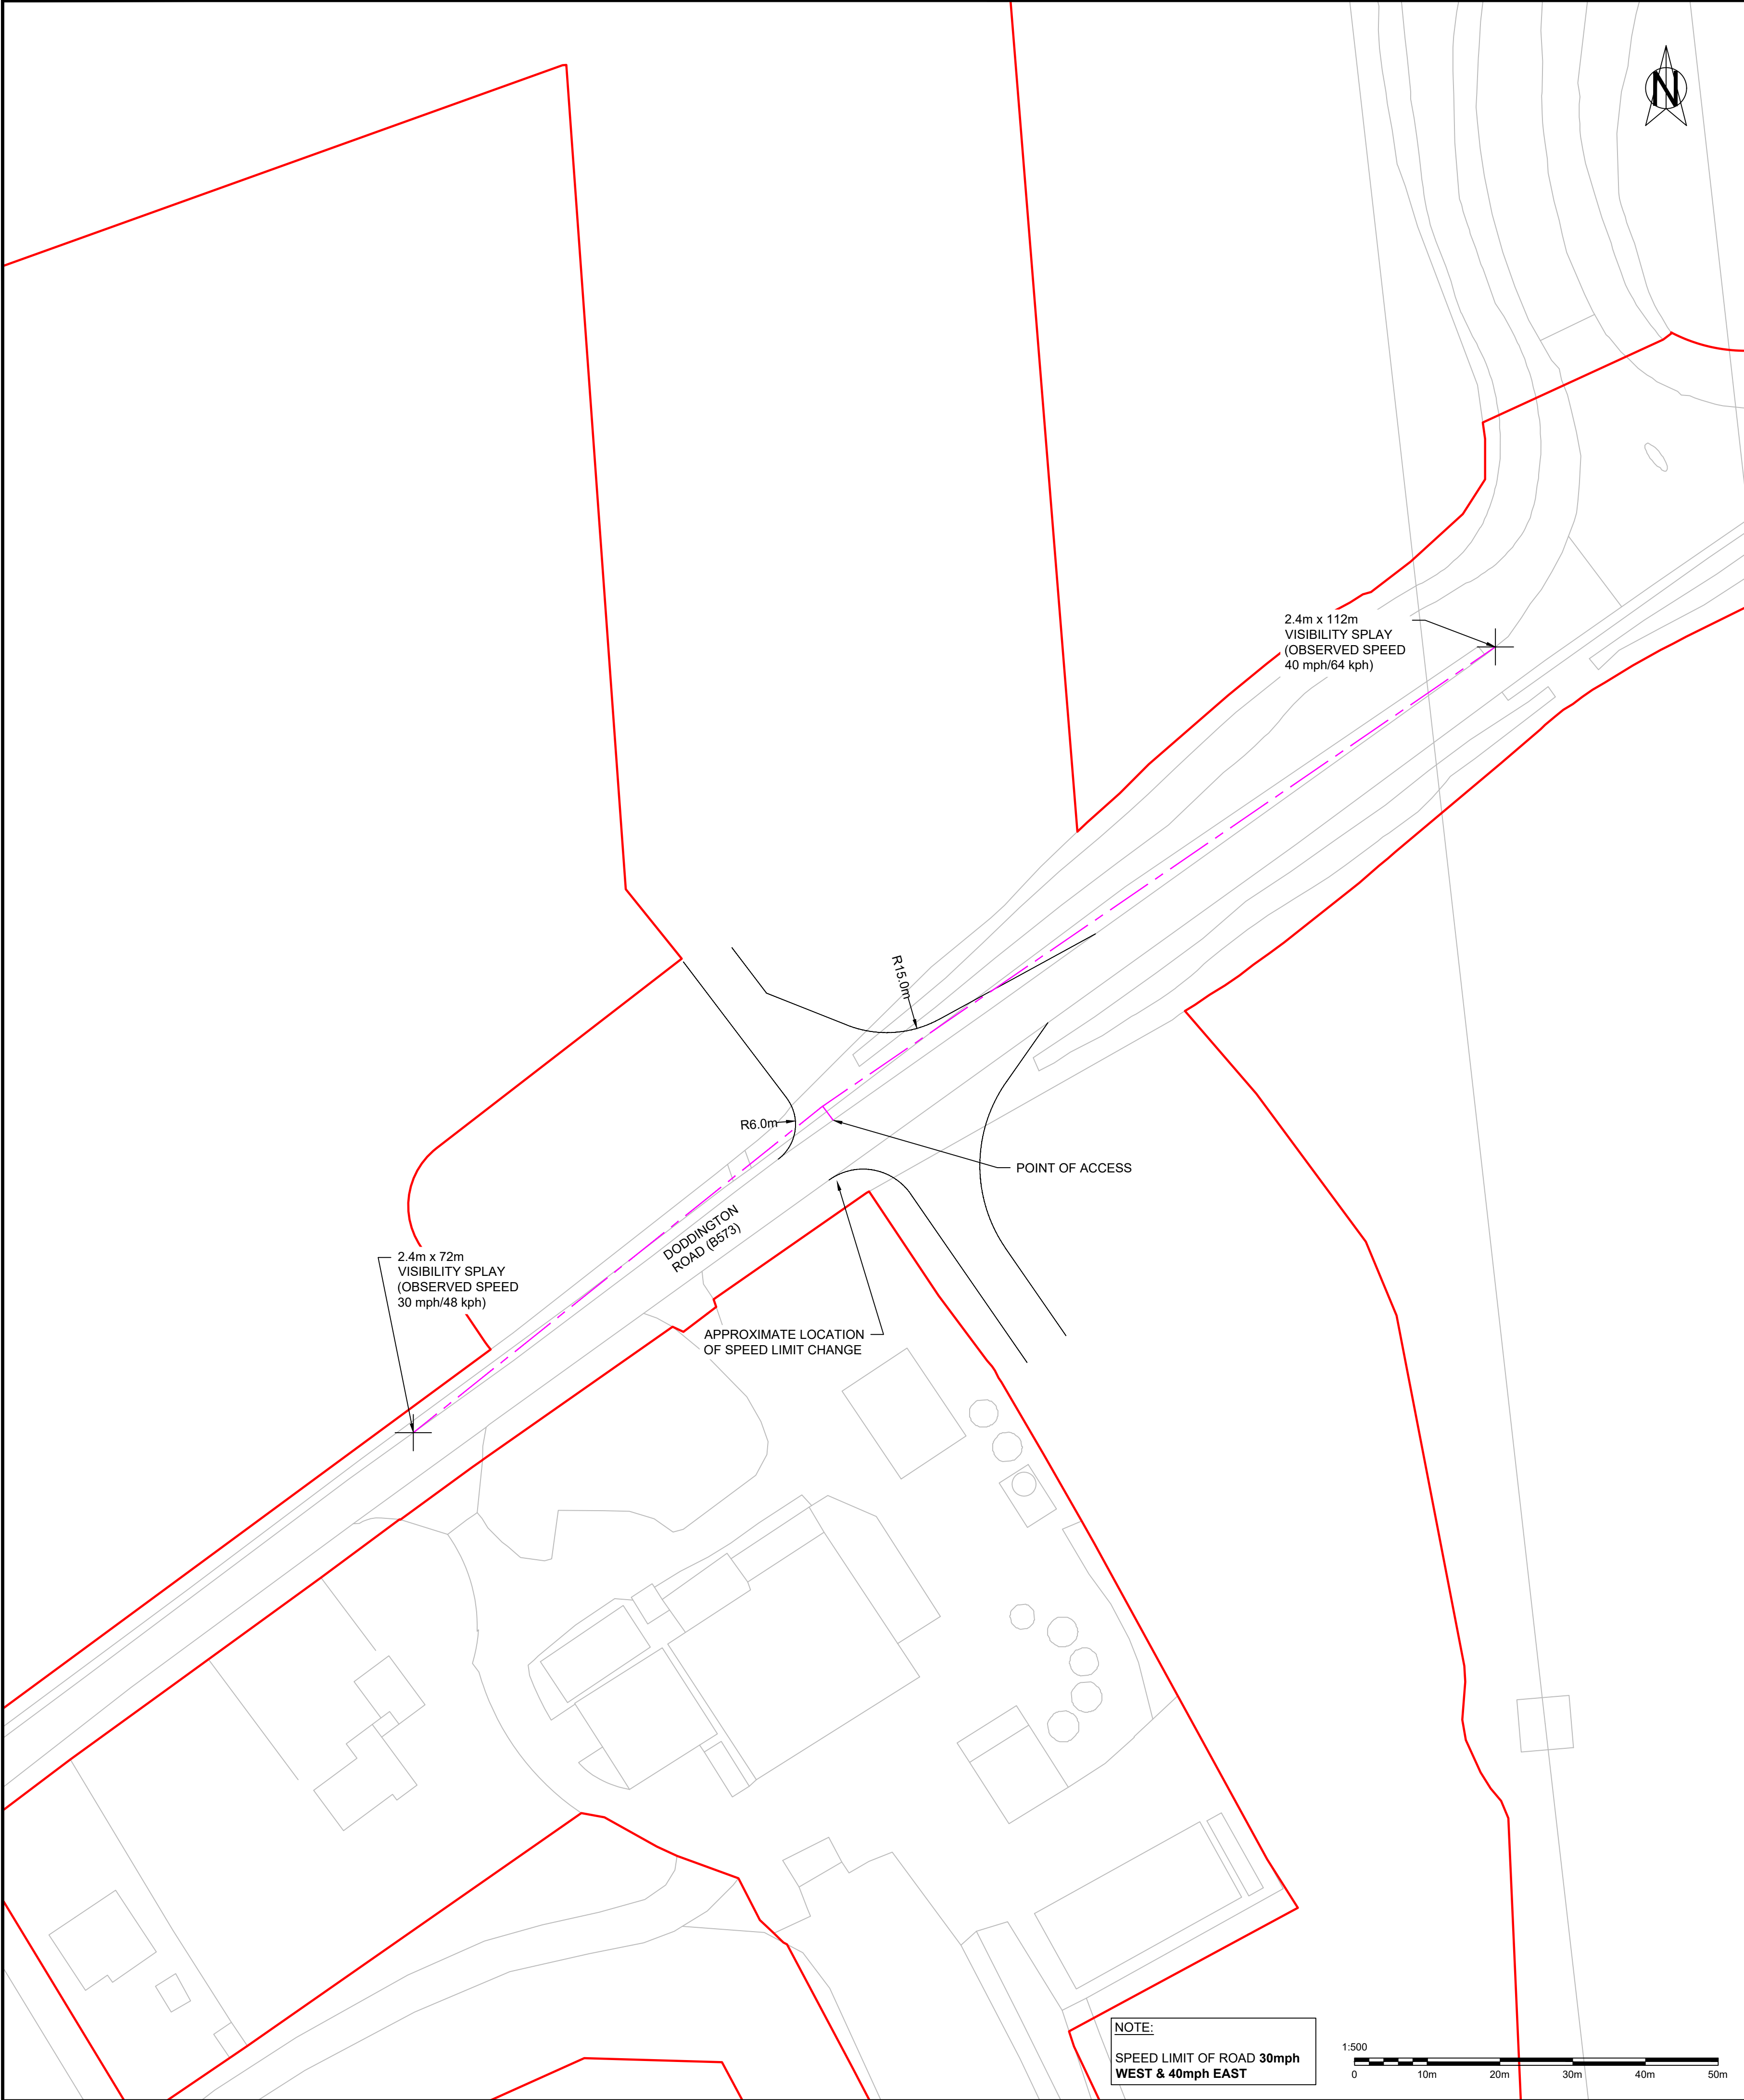

NOTES :

1. (C) This drawing is copyright.
2. All dimensions to be checked on site.
3. Do not scale from this drawing; only figured dimensions are to be worked from.
4. Any discrepancies must be reported immediately before proceeding.
5. This drawing to be read & printed in colour.
6. Ordnance Survey, (c) Crown Copyright 2024. All rights reserved. Licence number 100022432.

KEY PLAN
1:200000@A1

KEY:

- SITE BOUNDARY
- - - TRAFFIC SURVEY LOCATION
- - - HIGHWAY BOUNDARY
- - - VISIBILITY SPLAY EXTENT
- - - EXISTING LAYOUT
- PROPOSED EDGE OF ACCESS
- EXISTING VEGETATION
- EXTENT OF VEGETATION REMOVAL
- EXISTING CONTOURS

VEHICLE PROFILE:

VARIO-MAX LOWBED - 29.63m meters

TRACTOR WIDTH : 2.55
TRAILER WIDTH : 2.55
TRACTOR TRACK : 2.55
TRAILER TRACK : 2.55
LOCK TO LOCK TIME : 6.0
STEERING ANGLE : 40.0
ARTICULATING ANGLE: 70.0

VEHICLE ANALYSIS KEY:

- VEHICLE PATH & DIRECTION
- VEHICLE BODY ENVELOPE
- VEHICLE FRONT WHEEL PATH
- 0.3m VEHICLE BUFFER ZONE AROUND TRACKING

D	03.12.2025	Drawing updated as per client comments	CS	OW	SM
C	19.05.2025	Boundary removed	CS	OW	SM
B	10.04.2025	Boundary updated, Drawing combined	CS	OW	SM
A	11.03.2025	Preliminary issue	CS	LF	SM

REV	DATE	DESCRIPTION	DRN	CHKD	APRD

Issue Status

<input type="checkbox"/> CONCEPT	<input type="checkbox"/> CONSTRUCTION
<input type="checkbox"/> PRELIMINARY	<input type="checkbox"/> AS BUILT
<input type="checkbox"/> TENDER	<input type="checkbox"/> HAS FILE ISSUE

Client
GREEN HILL SOLAR FARM LTD



Project
GREEN HILL SOLAR FARM

Drawing Title
CABLE ROUTE ACCESS 12
GENERAL ARRANGEMENT & VEHICLE TRACKING

Scale @ A1	Drawn	CS	Chkd	OW
As shown	Aprd	SM	Date	MAR 2025

Drawing Ref	Rev
23061-KMC-XX-CR12-DR-CH-0001	D

kmc
transport planning

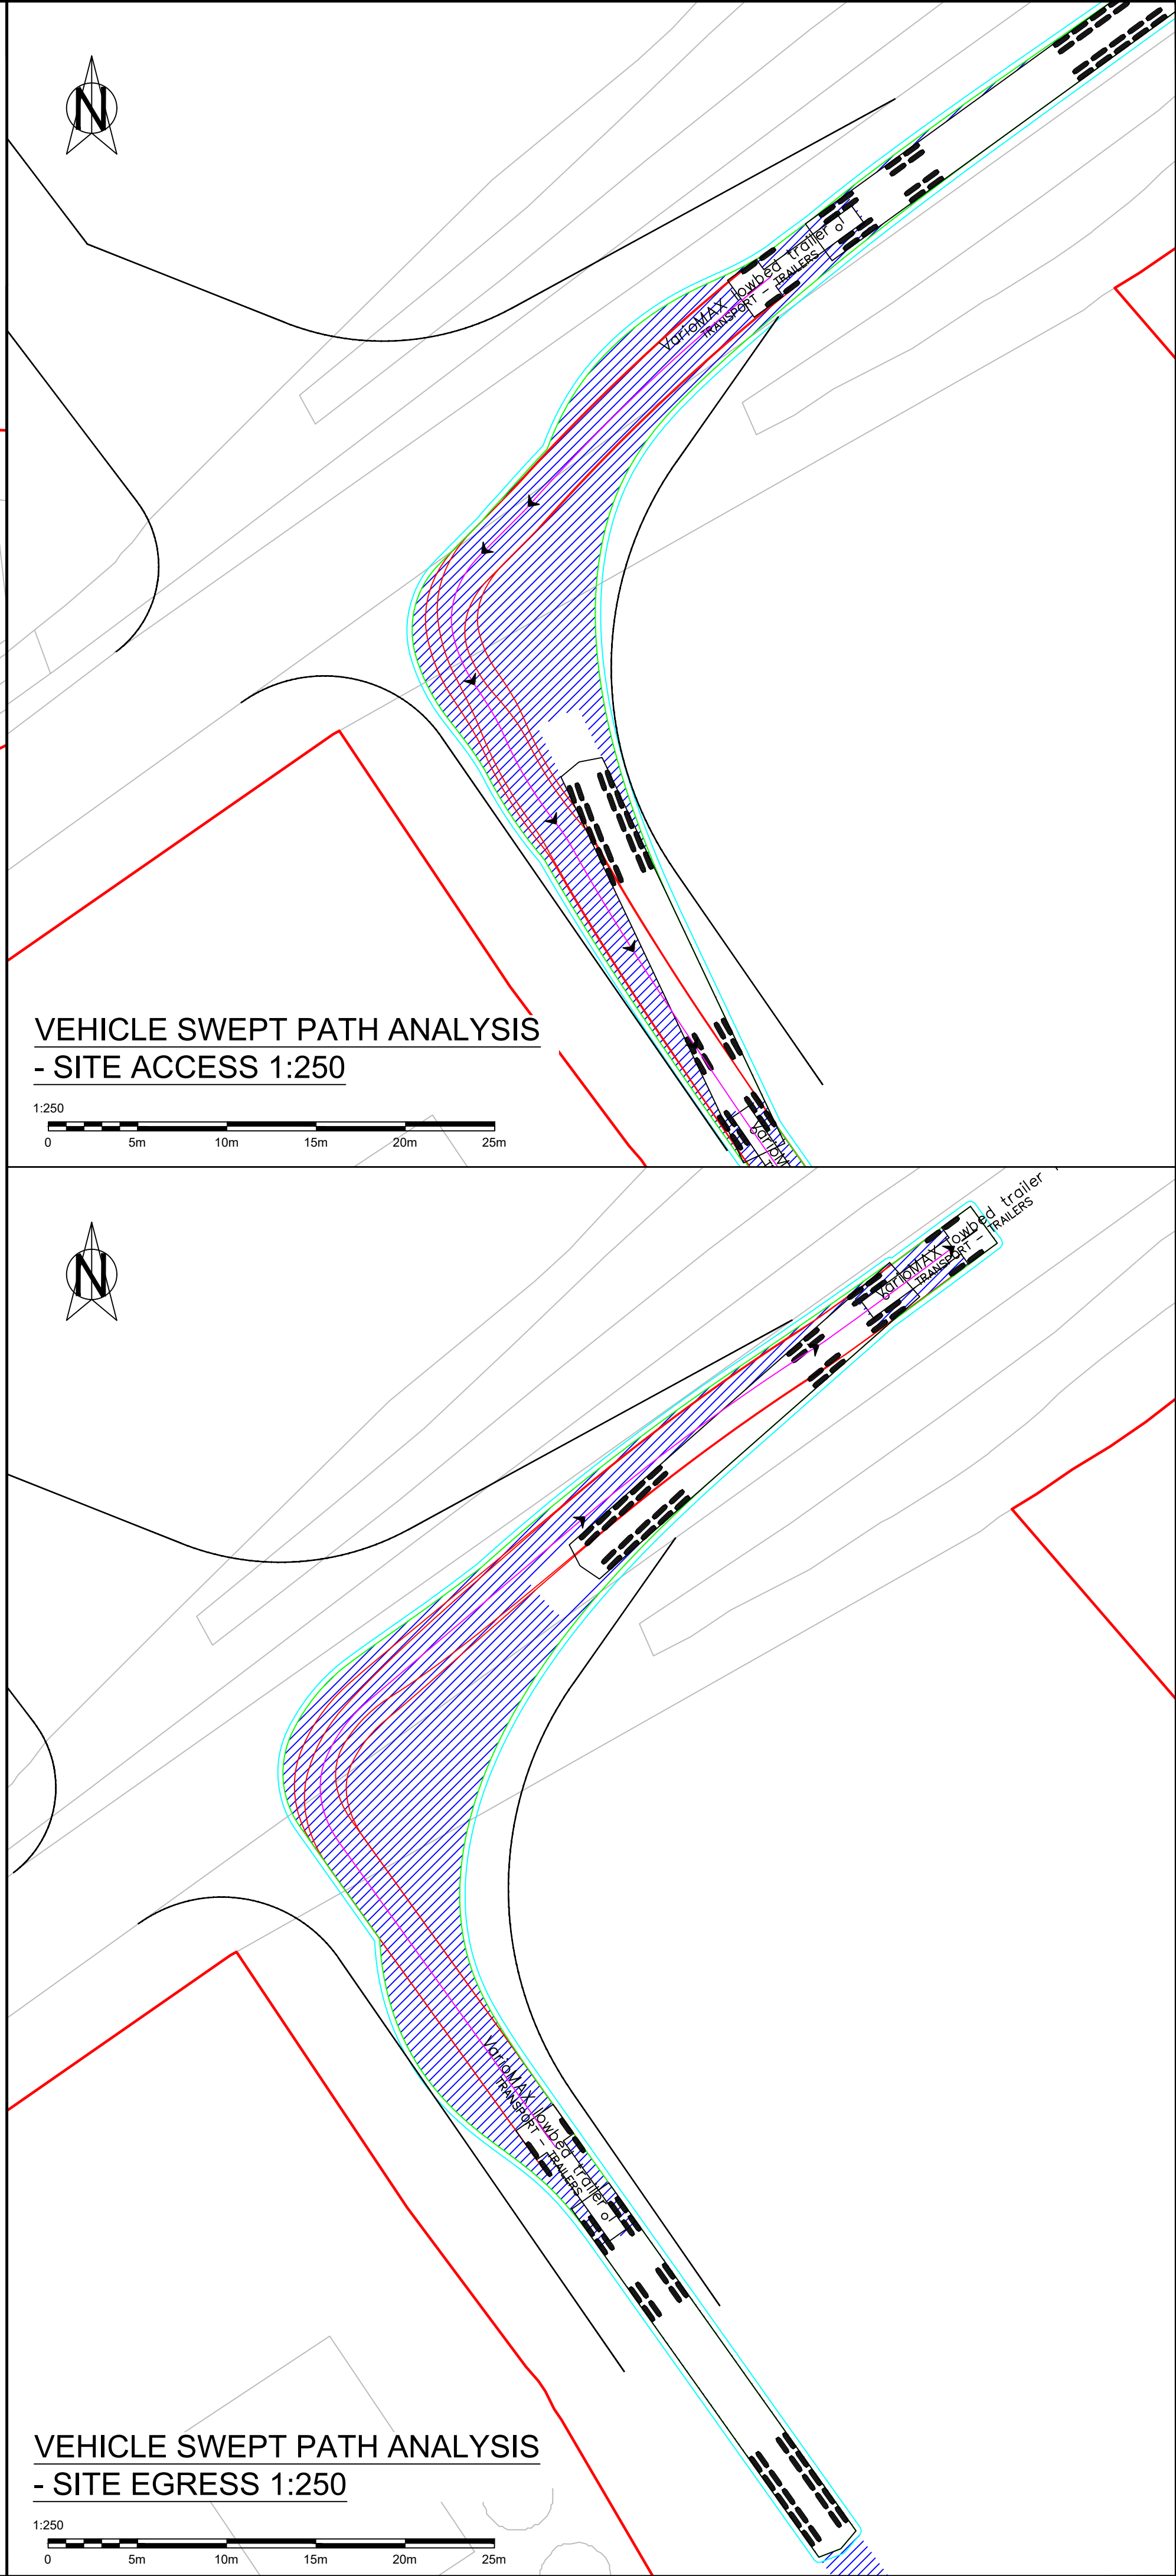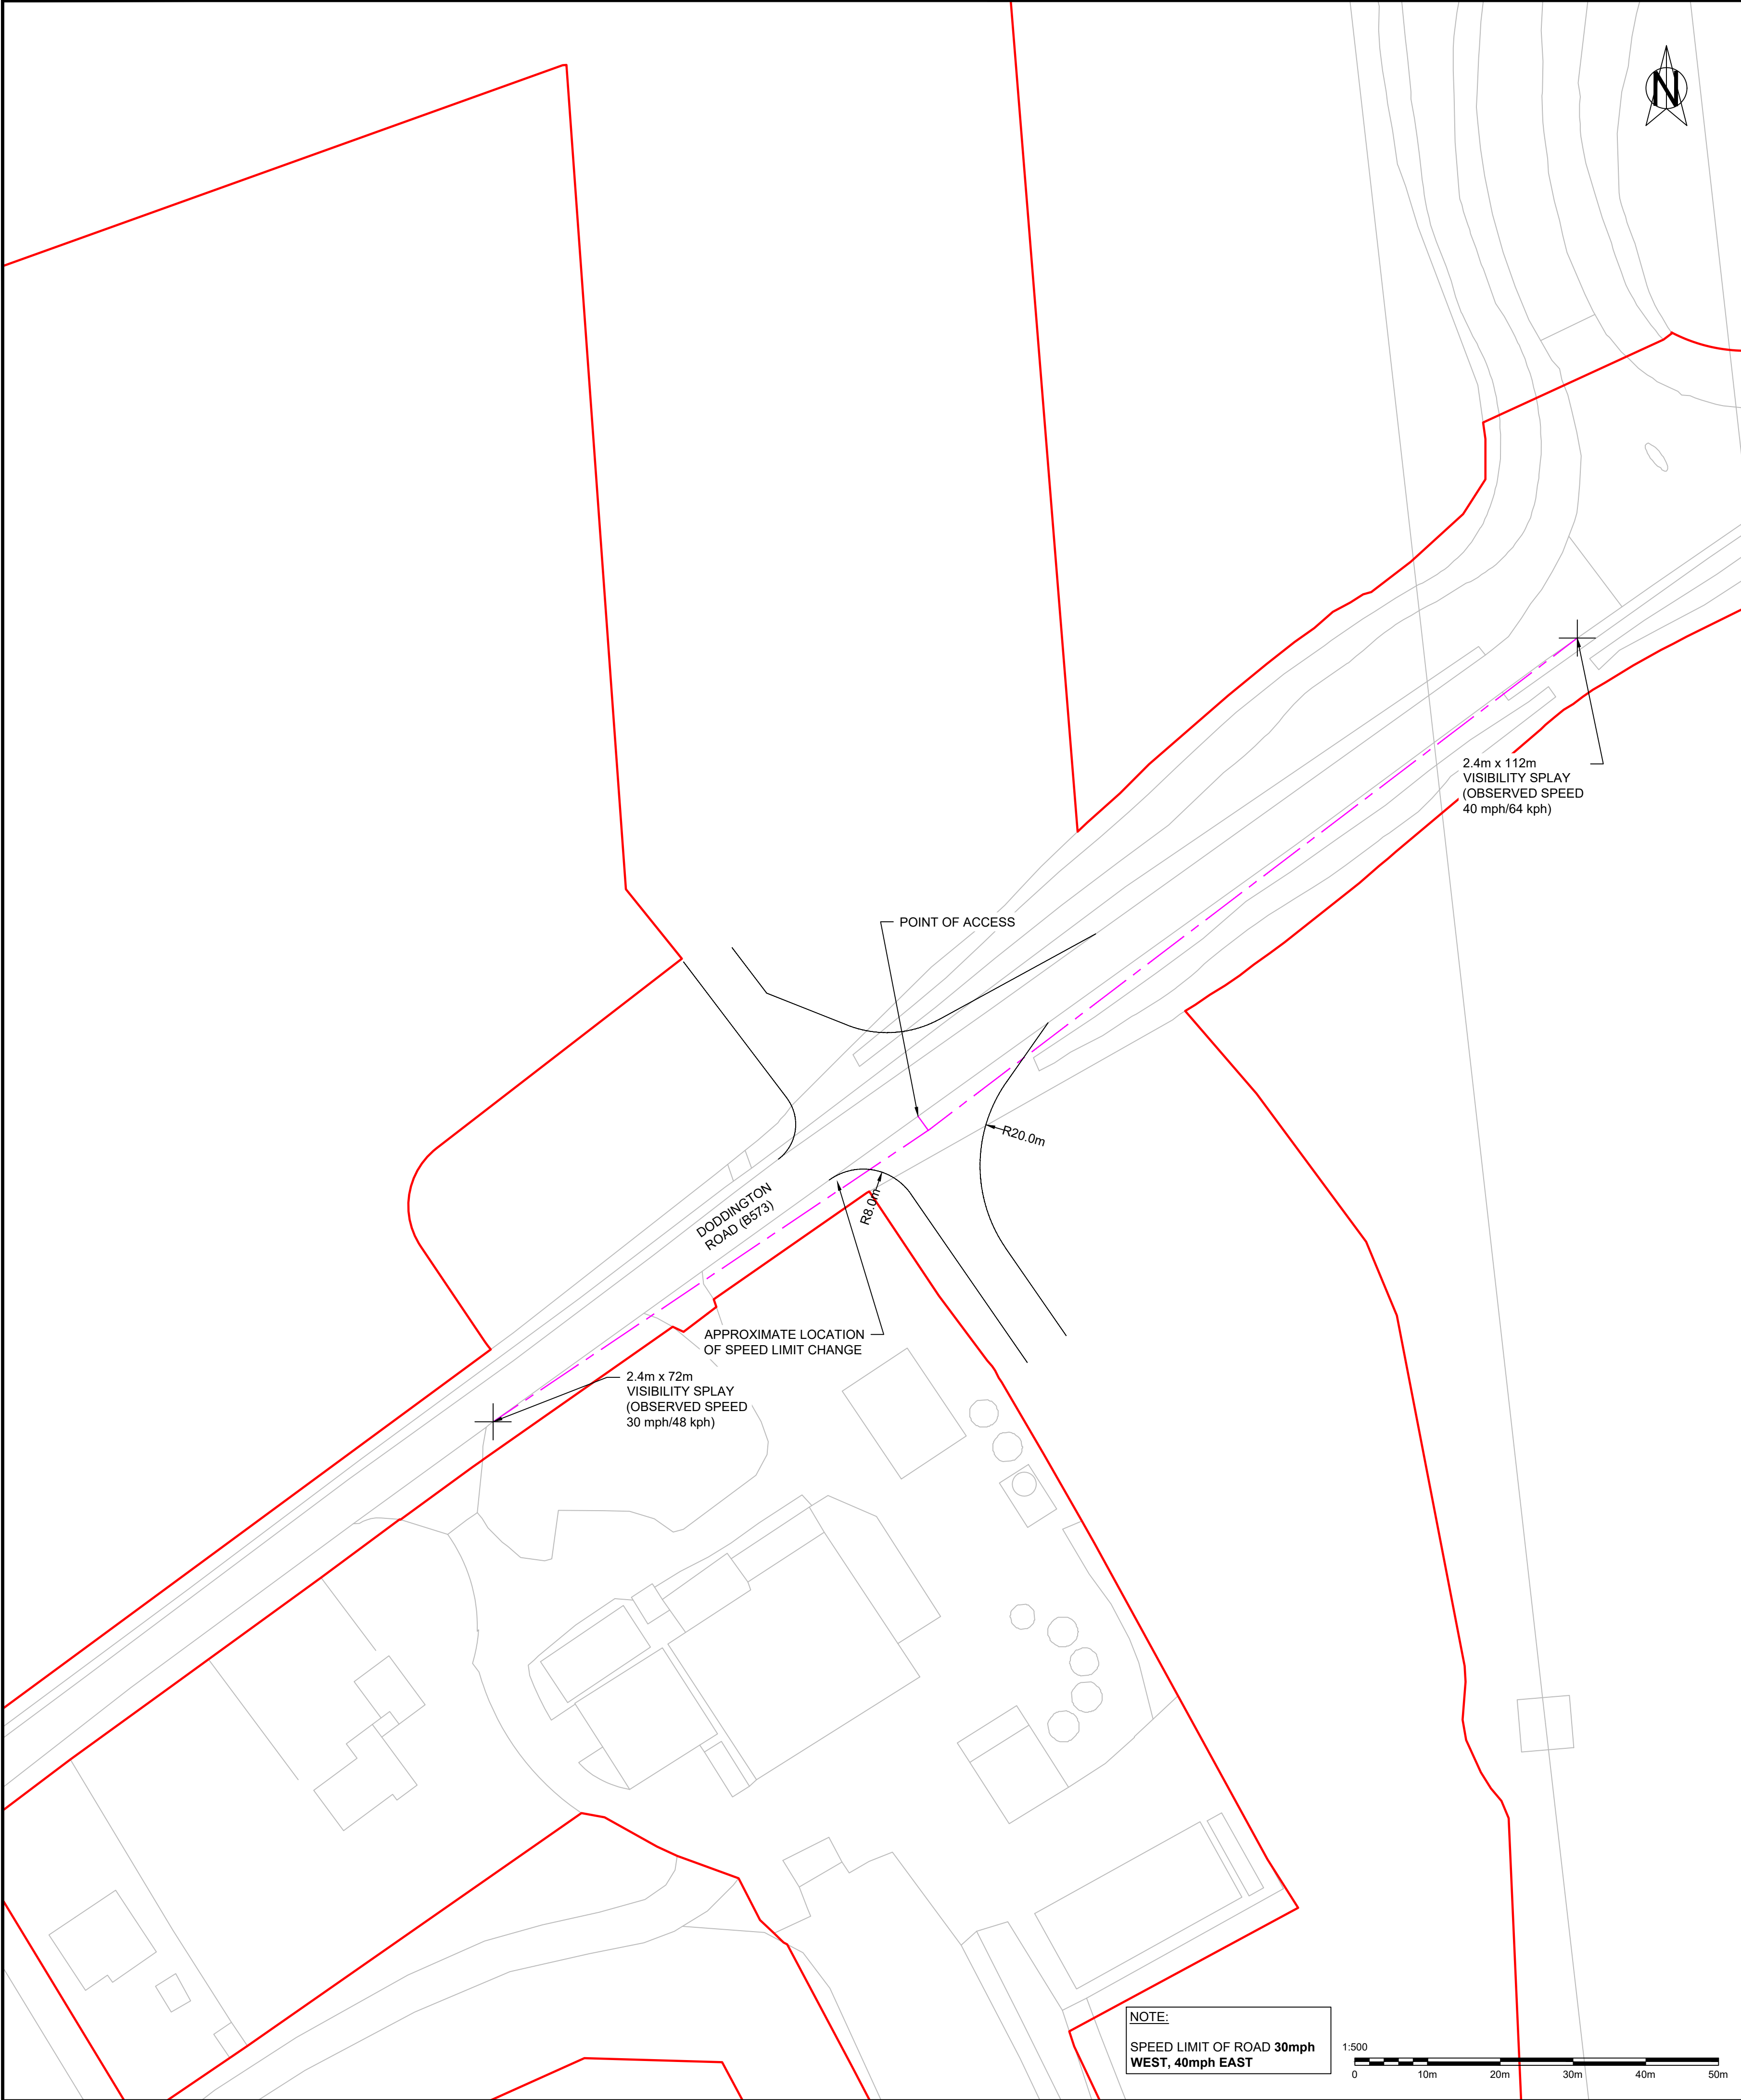

NOTES :

1. (C) This drawing is copyright.
2. All dimensions to be checked on site.
3. Do not scale from this drawing; only figured dimensions are to be worked from.
4. Any discrepancies must be reported immediately before proceeding.
5. This drawing to be read & printed in colour.
6. Ordnance Survey, (c) Crown Copyright 2024. All rights reserved. Licence number 100022432.

KEY PLAN
1:200000@A1

ACCESS LOCATION

KEY:

- SITE BOUNDARY
- TRAFFIC SURVEY LOCATION
- HIGHWAY BOUNDARY
- VISIBILITY SPLAY EXTENT
- EXISTING LAYOUT
- PROPOSED EDGE OF ACCESS
- EXISTING VEGETATION
- EXTENT OF VEGETATION REMOVAL
- EXISTING CONTOURS

VEHICLE PROFILE:

VARIO-MAX LOWBED - 29.63m meters

TRACTOR WIDTH : 2.55
TRAILER WIDTH : 2.55
TRACTOR TRACK : 2.55
TRAILER TRACK : 2.55
LOCK TO LOCK TIME : 6.0
STEERING ANGLE : 40.0
ARTICULATING ANGLE: 70.0

VEHICLE ANALYSIS KEY:

- VEHICLE PATH & DIRECTION
- VEHICLE BODY ENVELOPE
- VEHICLE FRONT WHEEL PATH
- 0.3m VEHICLE BUFFER ZONE AROUND TRACKING

D	03.12.2025	Drawing updated as per client comments	CS	OW	SM
C	19.05.2025	Boundary removed	CS	OW	SM
B	10.04.2025	Boundary updated, Drawing combined	CS	OW	SM
A	11.03.2025	Preliminary issue	CS	LF	SM

REV	DATE	DESCRIPTION	DRN	CHKD	APRD
<input type="checkbox"/>	CONCEPT	<input type="checkbox"/>	CONSTRUCTION		
<input checked="" type="checkbox"/>	PRELIMINARY	<input type="checkbox"/>	AS BUILT		
<input type="checkbox"/>	TENDER	<input type="checkbox"/>	HAS FILE ISSUE		

Client
GREEN HILL SOLAR FARM LTD


Project
GREEN HILL SOLAR FARM

Drawing Title
CABLE ROUTE ACCESS 13
GENERAL ARRANGEMENT & VEHICLE TRACKING

Scale @ A1	Drawn	CS	Chkd	OW
As shown	Aprd	SM	Date	MAR 2025

Drawing Ref	Rev
23061-KMC-XX-CR13-DR-CH-0001	D

kmc
transport planning

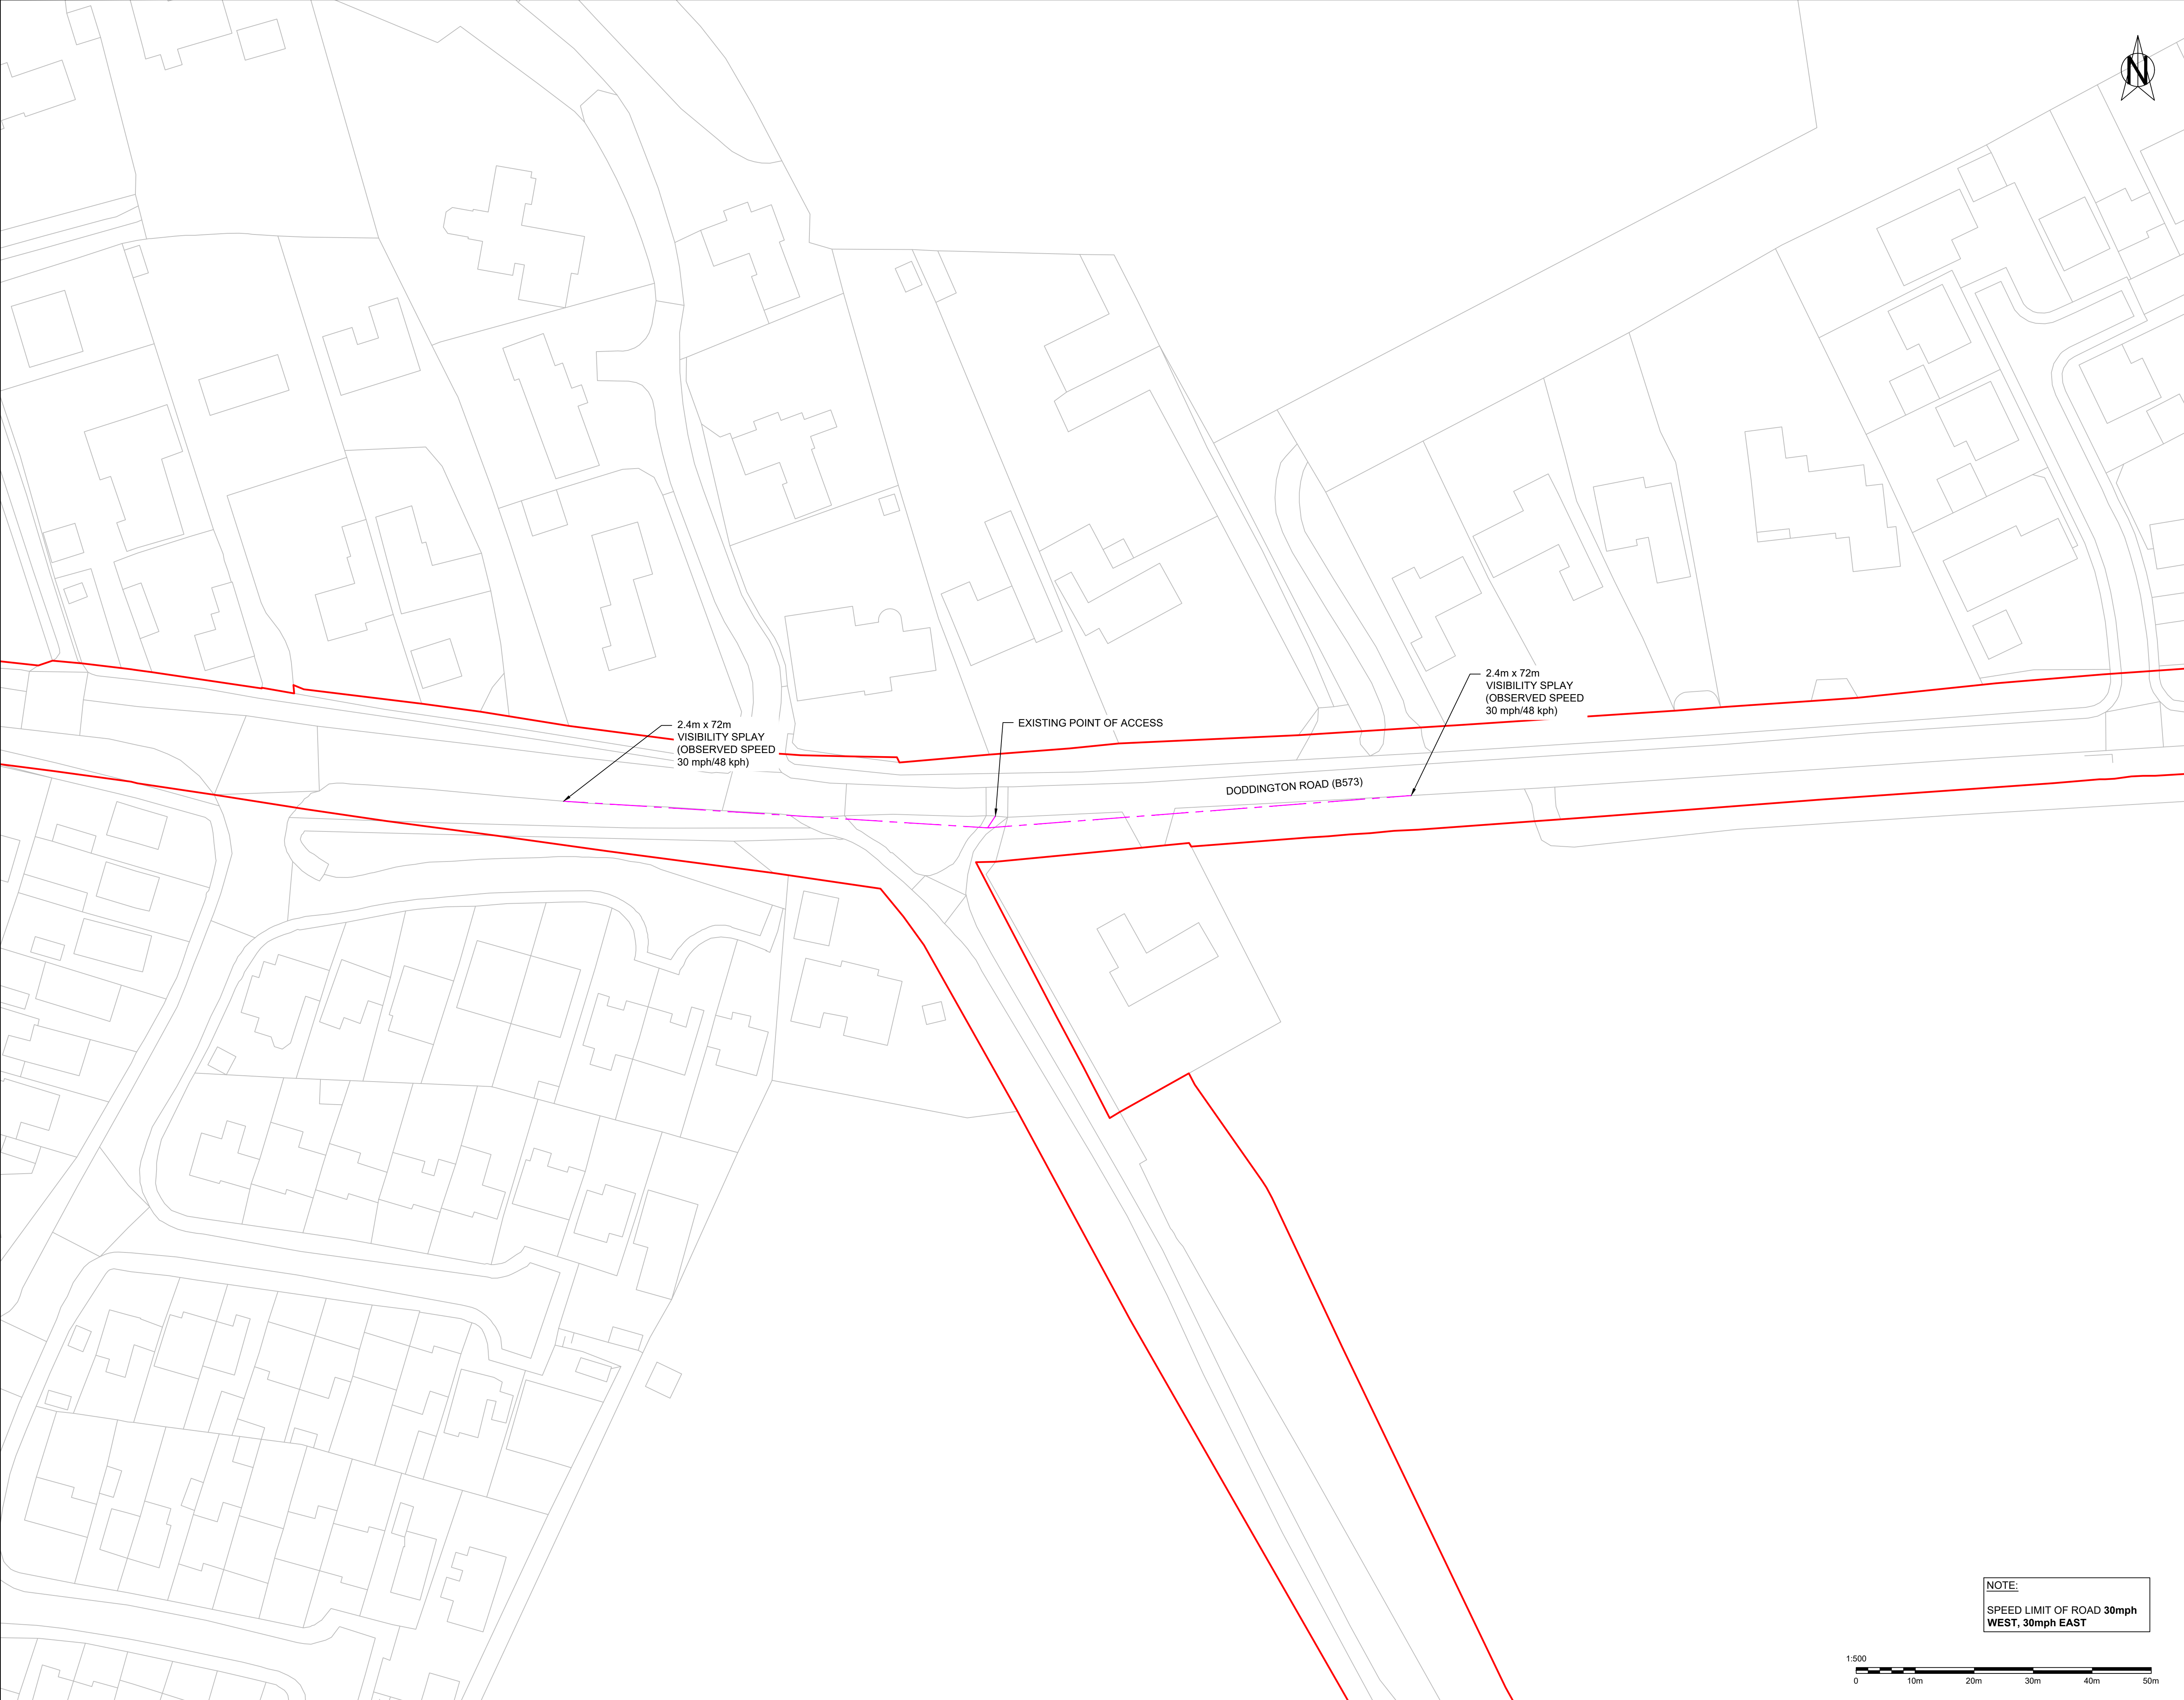

- NOTES :**
1. (C) This drawing is copyright.
 2. All dimensions to be checked on site.
 3. Do not scale from this drawing; only figured dimensions are to be worked from.
 4. Any discrepancies must be reported immediately before proceeding.
 5. This drawing to be read & printed in colour.
 6. Ordnance Survey, (c) Crown Copyright 2024. All rights reserved. Licence number 100022432.



KEY PLAN
1:200000@A1

- KEY:**
- SITE BOUNDARY
 - - - - - TRAFFIC SURVEY LOCATION
 - - - - - HIGHWAY BOUNDARY
 - - - - - VISIBILITY SPLAY EXTENT
 - - - - - EXISTING LAYOUT
 - PROPOSED EDGE OF ACCESS
 - EXISTING VEGETATION
 - ▨ EXTENT OF VEGETATION REMOVAL
 - 100.0 — EXISTING CONTOURS

D	03.12.2025	Drawing updated as per client comments	CS	OW	SM
C	19.05.2025	Tracking removed, Boundary removed	CS	OW	SM
B	10.04.2025	Boundary updated, Drawing continued	CS	OW	SM
A	11.03.2025	Preliminary issue	CS	LF	SM
REV	DATE	DESCRIPTION	DRN	CHKD	APRD

<input type="checkbox"/> CONCEPT	<input type="checkbox"/> CONSTRUCTION
<input checked="" type="checkbox"/> PRELIMINARY	<input type="checkbox"/> AS BUILT
<input type="checkbox"/> TENDER	<input type="checkbox"/> HAS FILE ISSUE

Client
GREEN HILL SOLAR FARM LTD

Project
GREEN HILL SOLAR FARM




Drawing Title
CABLE ROUTE ACCESS 14
GENERAL ARRANGEMENT & VEHICLE TRACKING

Scale @ A1	Drawn	CS	Chkd	OW
As shown	Aprd	SM	Date	MAR 2025

Drawing Ref	Rev
23061-KMC-XX-CR14-DR-CH-0001	D

NOTE:
SPEED LIMIT OF ROAD 30mph
WEST, 30mph EAST



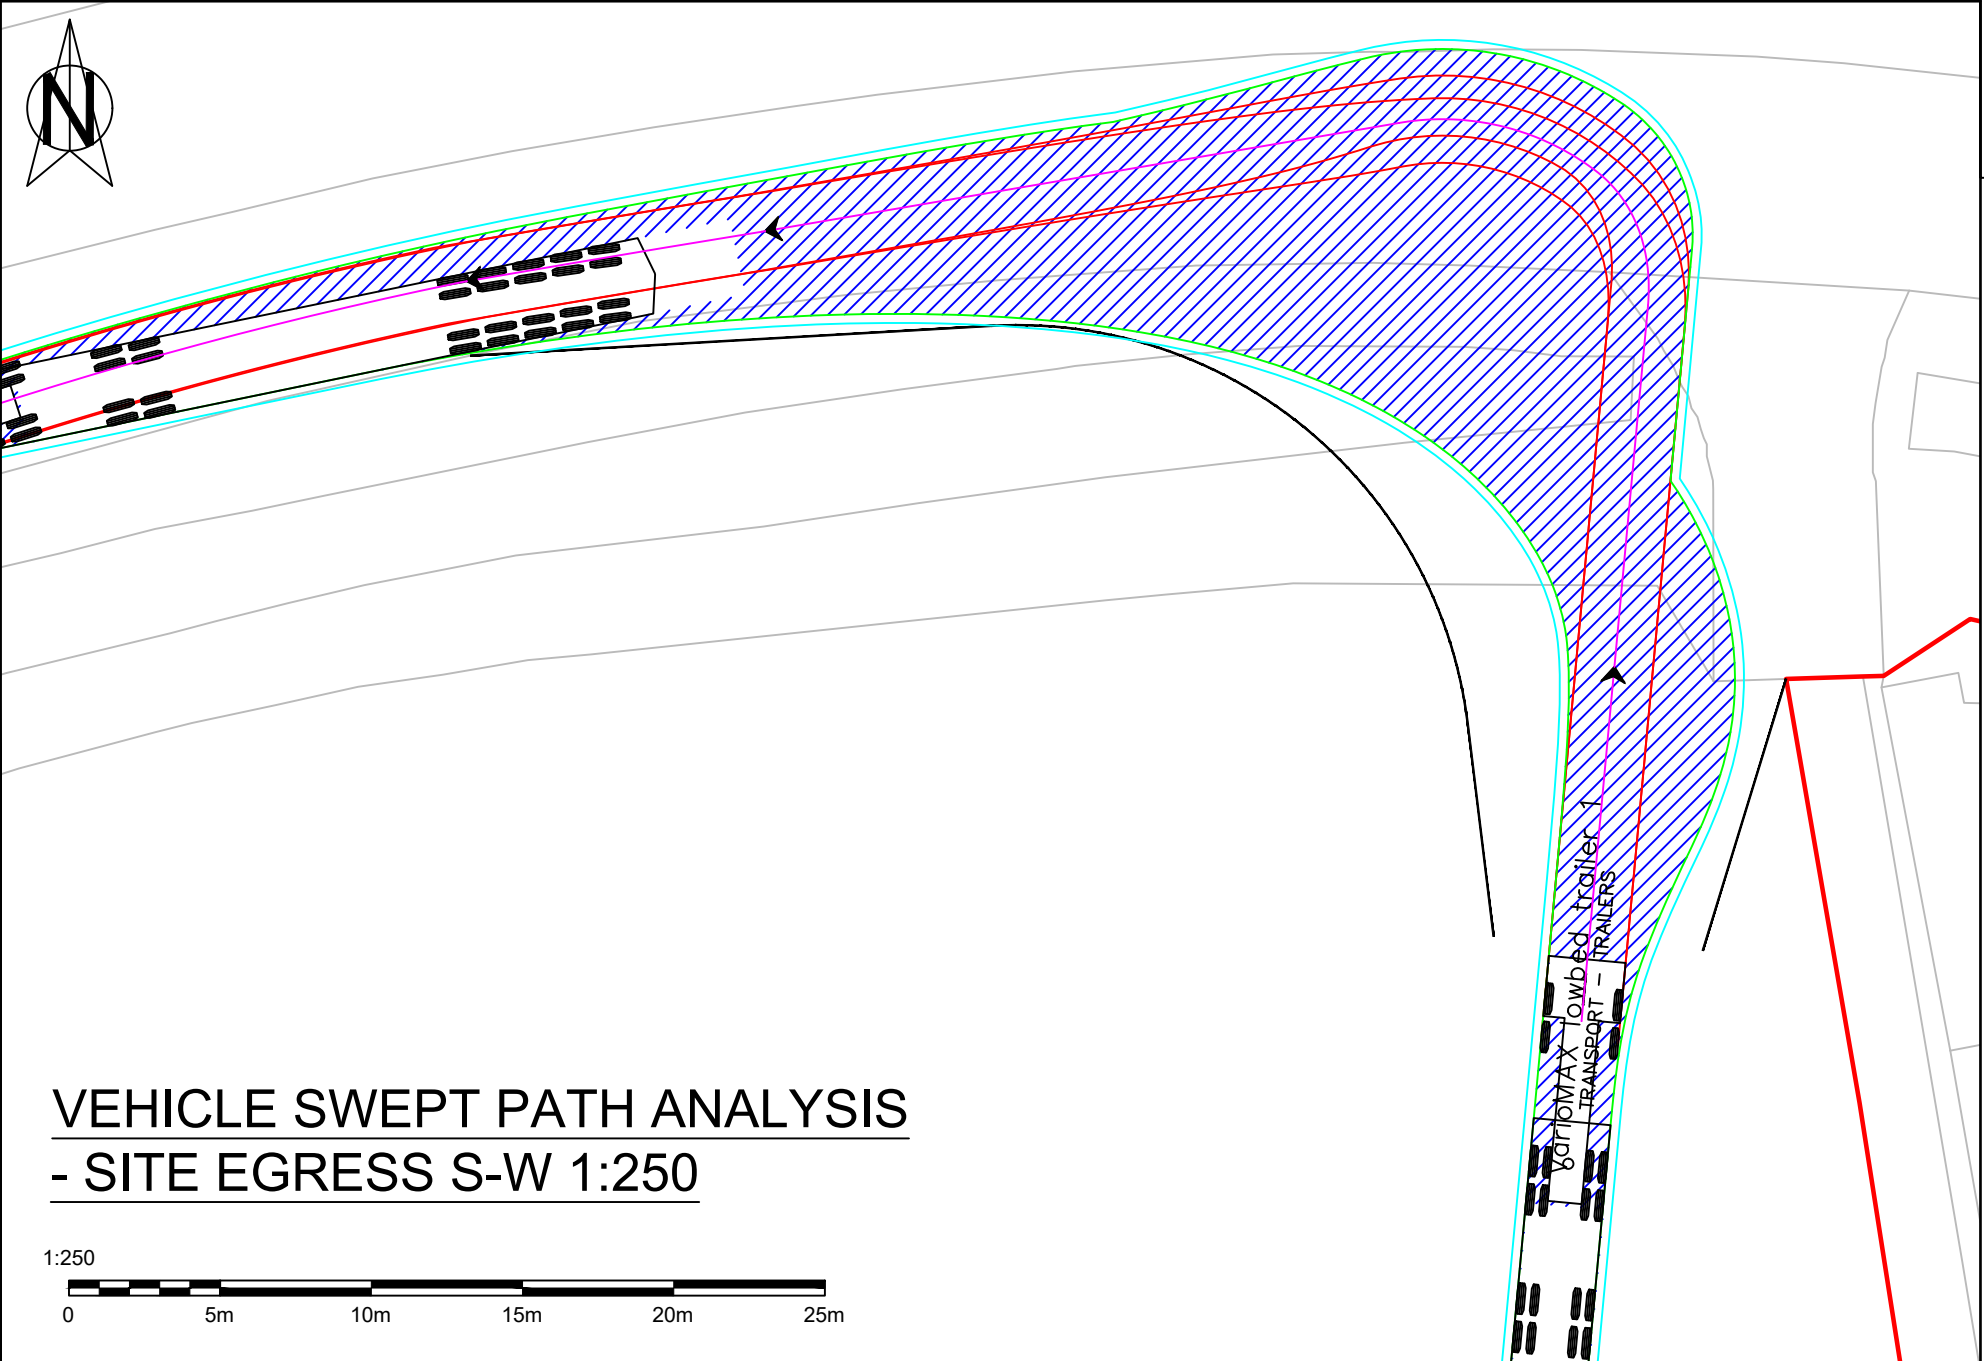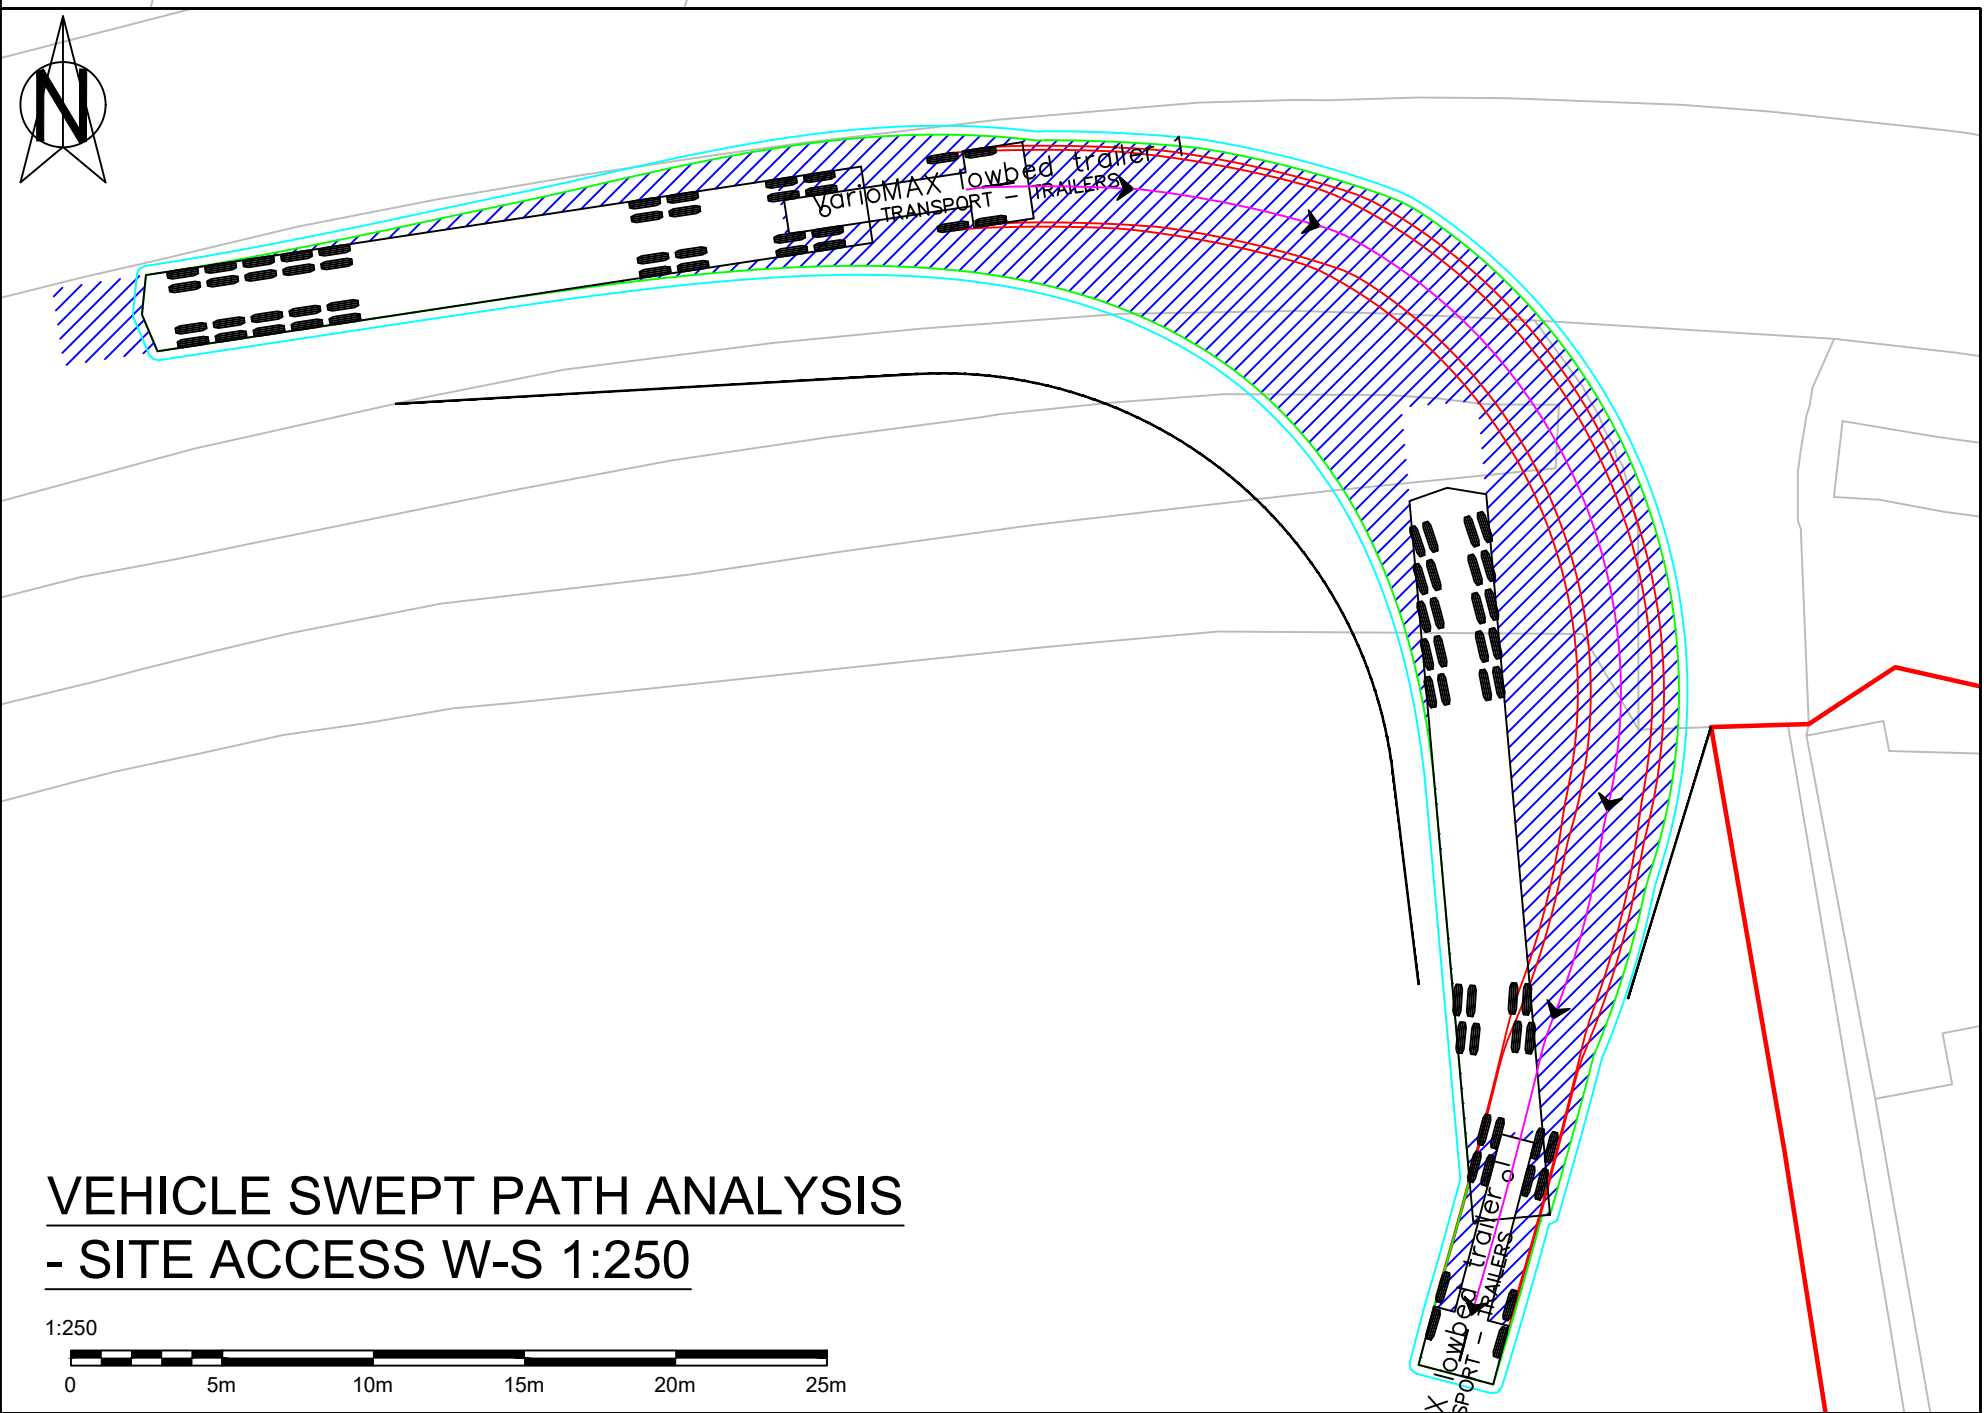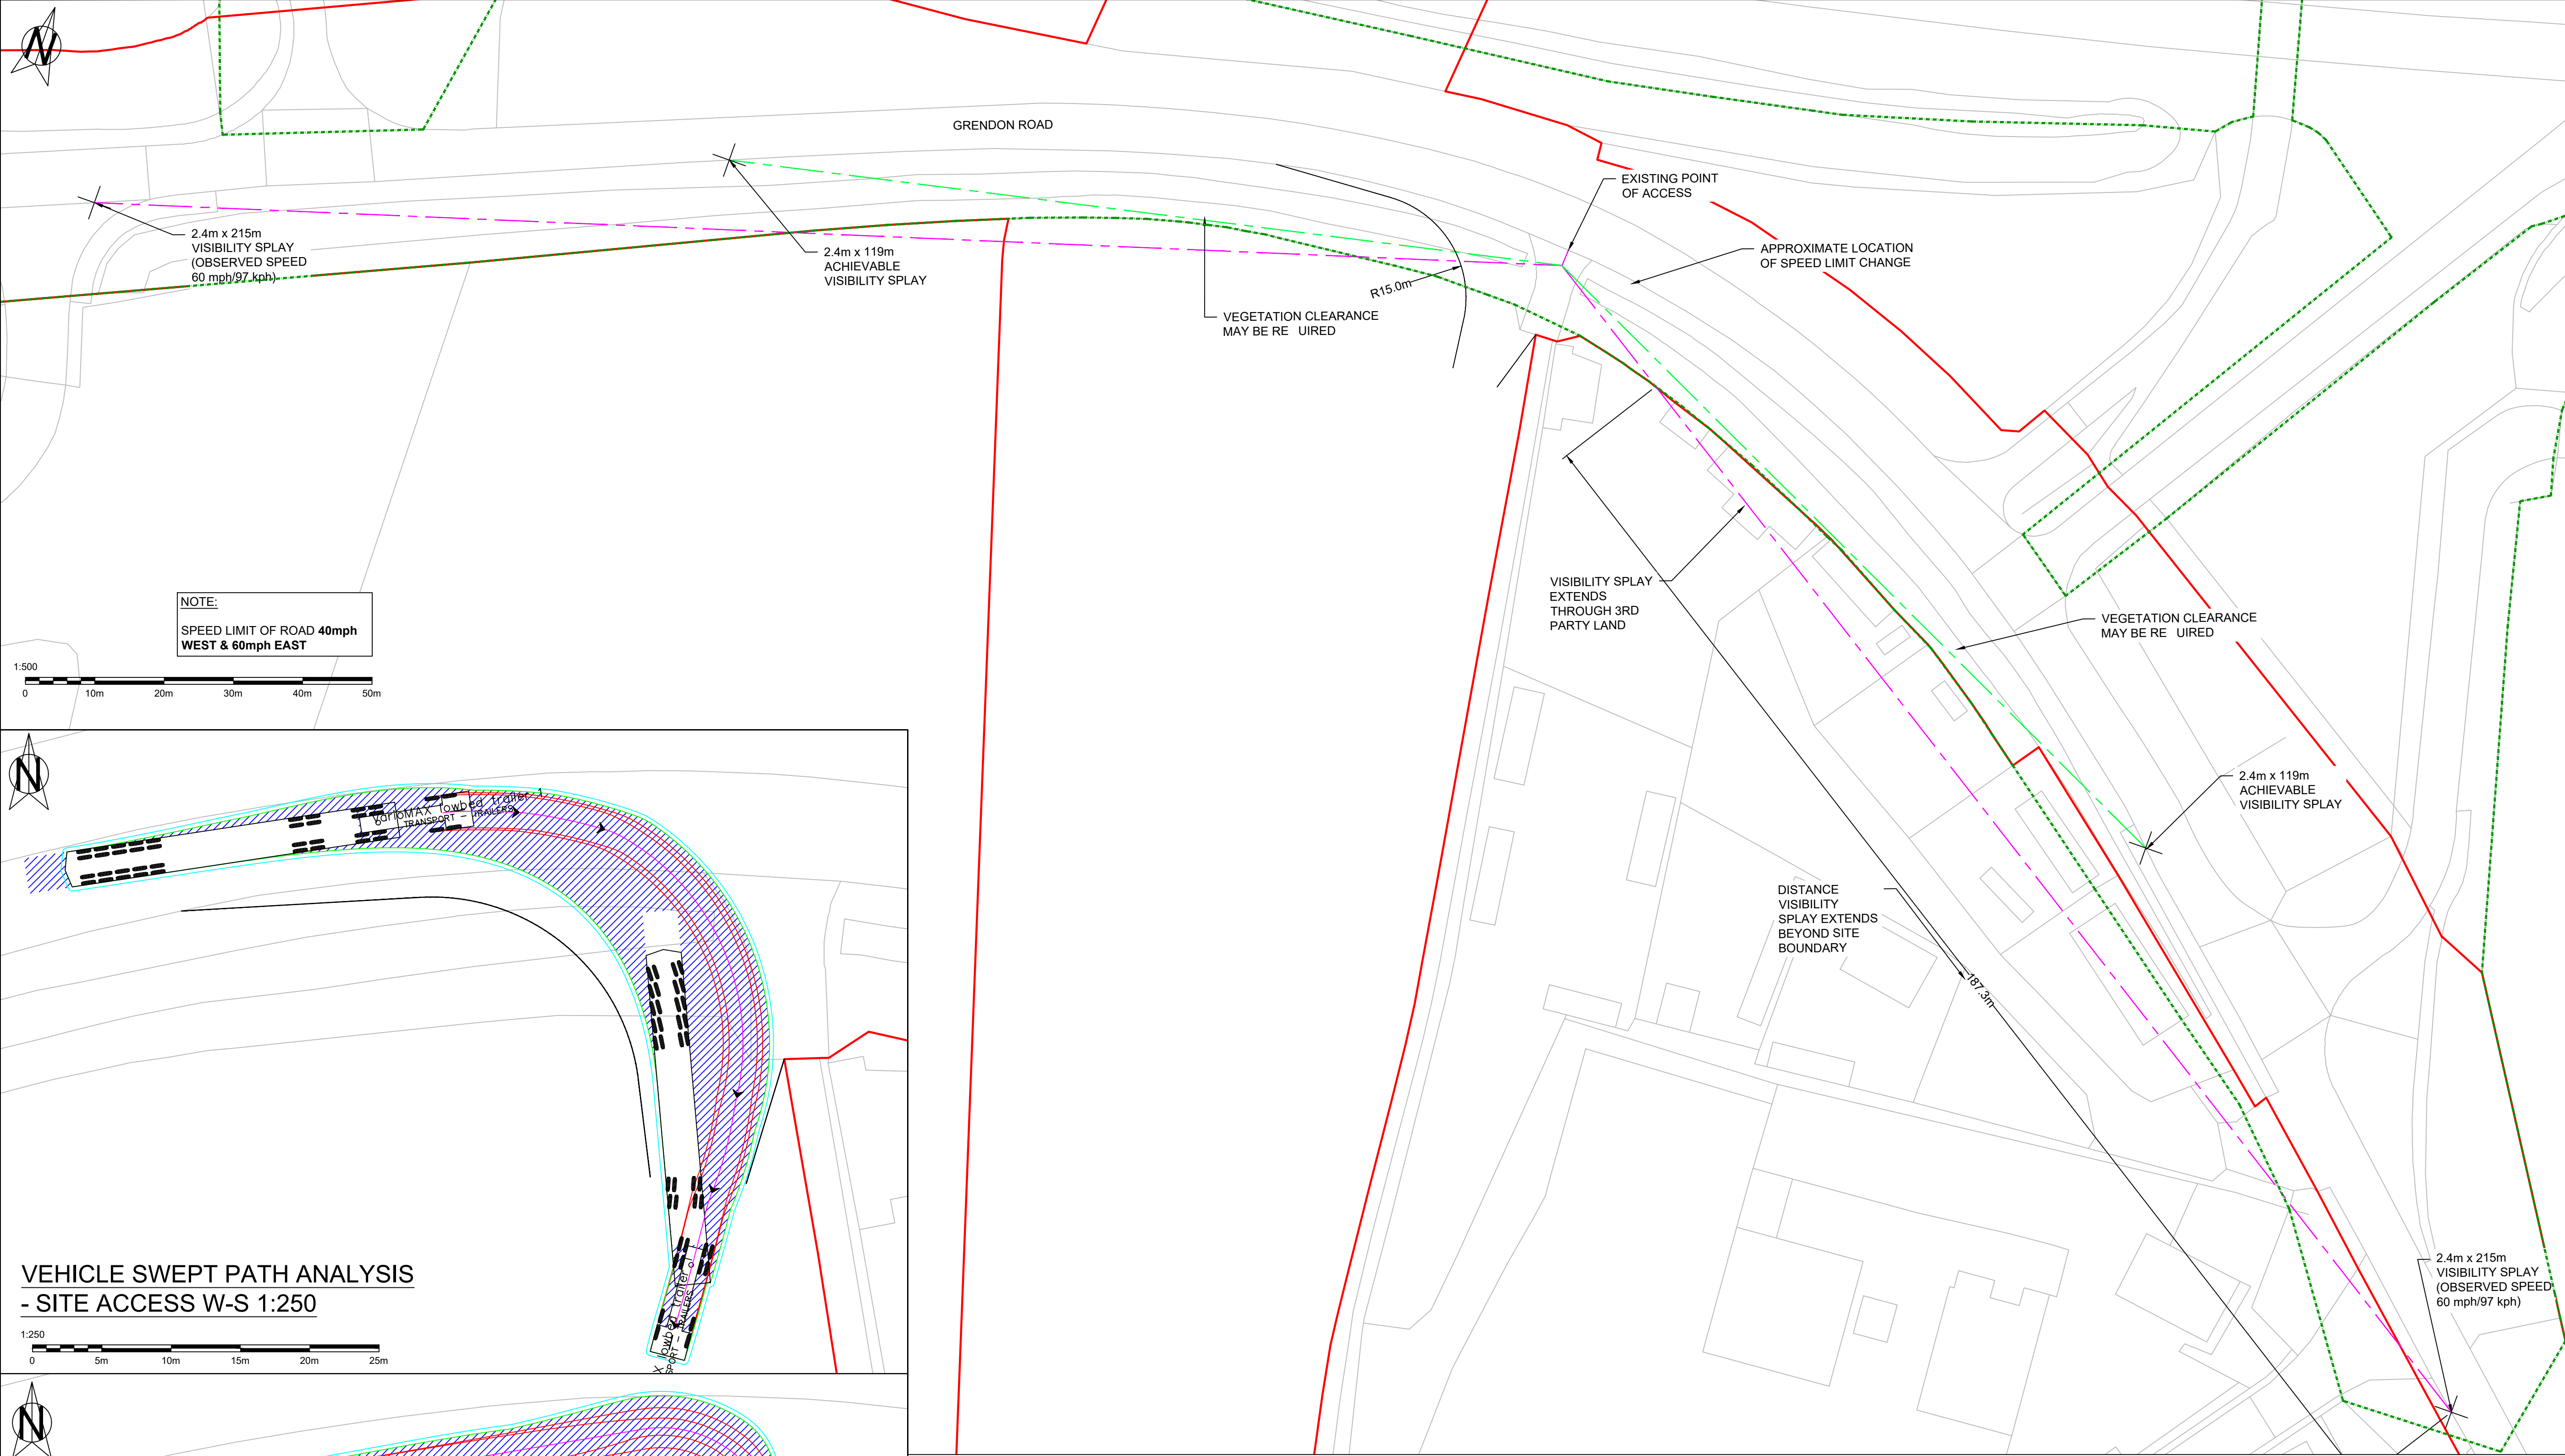

NOTES:

- (C) This drawing is copyright.
- All dimensions to be checked on site.
- Do not scale from this drawing; only figured dimensions are to be worked from.
- Any discrepancies must be reported immediately before proceeding.
- This drawing to be read & printed in colour.
- Ordnance Survey, (c) Crown Copyright 2024. All rights reserved. Licence number 100022432.

KEY PLAN
1:200000@A1

KEY:

- SITE BOUNDARY
- TRAFFIC SURVEY LOCATION
- HIGHWAY BOUNDARY
- VISIBILITY SPLAY EXTENT
- EXISTING LAYOUT
- PROPOSED EDGE OF ACCESS
- EXISTING VEGETATION
- EXTENT OF VEGETATION REMOVAL
- EXISTING CONTOURS

VEHICLE PROFILE:

VARIO-MAX LOWBED - 29.63m meters

TRACTOR WIDTH : 2.55

TRAILER WIDTH : 2.55

TRACTOR TRACK : 2.55

TRAILER TRACK : 2.55

LOCK TO LOCK TIME : 6.0

STEERING ANGLE : 40.0

ARTICULATING ANGLE: 70.0

VEHICLE ANALYSIS KEY:

- VEHICLE PATH & DIRECTION
- VEHICLE BODY ENVELOPE
- VEHICLE FRONT WHEEL PATH
- 0.3m VEHICLE BUFFER ZONE AROUND TRACKING

REV	DATE	DESCRIPTION	DRN	CHKD	APRD
E	08.12.2025	Drawing updated as per council comments	CS	OW	SM
D	03.12.2025	Drawing updated as per client comments	CS	OW	SM
C	19.05.2025	Tracking updated and location plan updated	CS	OW	SM
B	10.04.2025	Boundary updated, Drawing contained	CS	OW	SM
A	11.03.2025	Preliminary issue	CS	LF	SM

Issue Status

<input type="checkbox"/> CONCEPT	<input type="checkbox"/> CONSTRUCTION
<input checked="" type="checkbox"/> PRELIMINARY	<input type="checkbox"/> AS BUILT
<input type="checkbox"/> TENDER	<input type="checkbox"/> HAS FILE ISSUE

Client
GREEN HILL SOLAR FARM LTD




Project
GREEN HILL SOLAR FARM

Drawing Title
CABLE ROUTE ACCESS 15
GENERAL ARRANGEMENT & VEHICLE TRACKING

Scale @ A1	Drawn	CS	Chkd	OW
As shown	Aprd	SM	Date	APR 2025

Drawing Ref	Rev
23061-KMC-XX-CR15-DR-CH-0001	E

kmc
transport planning

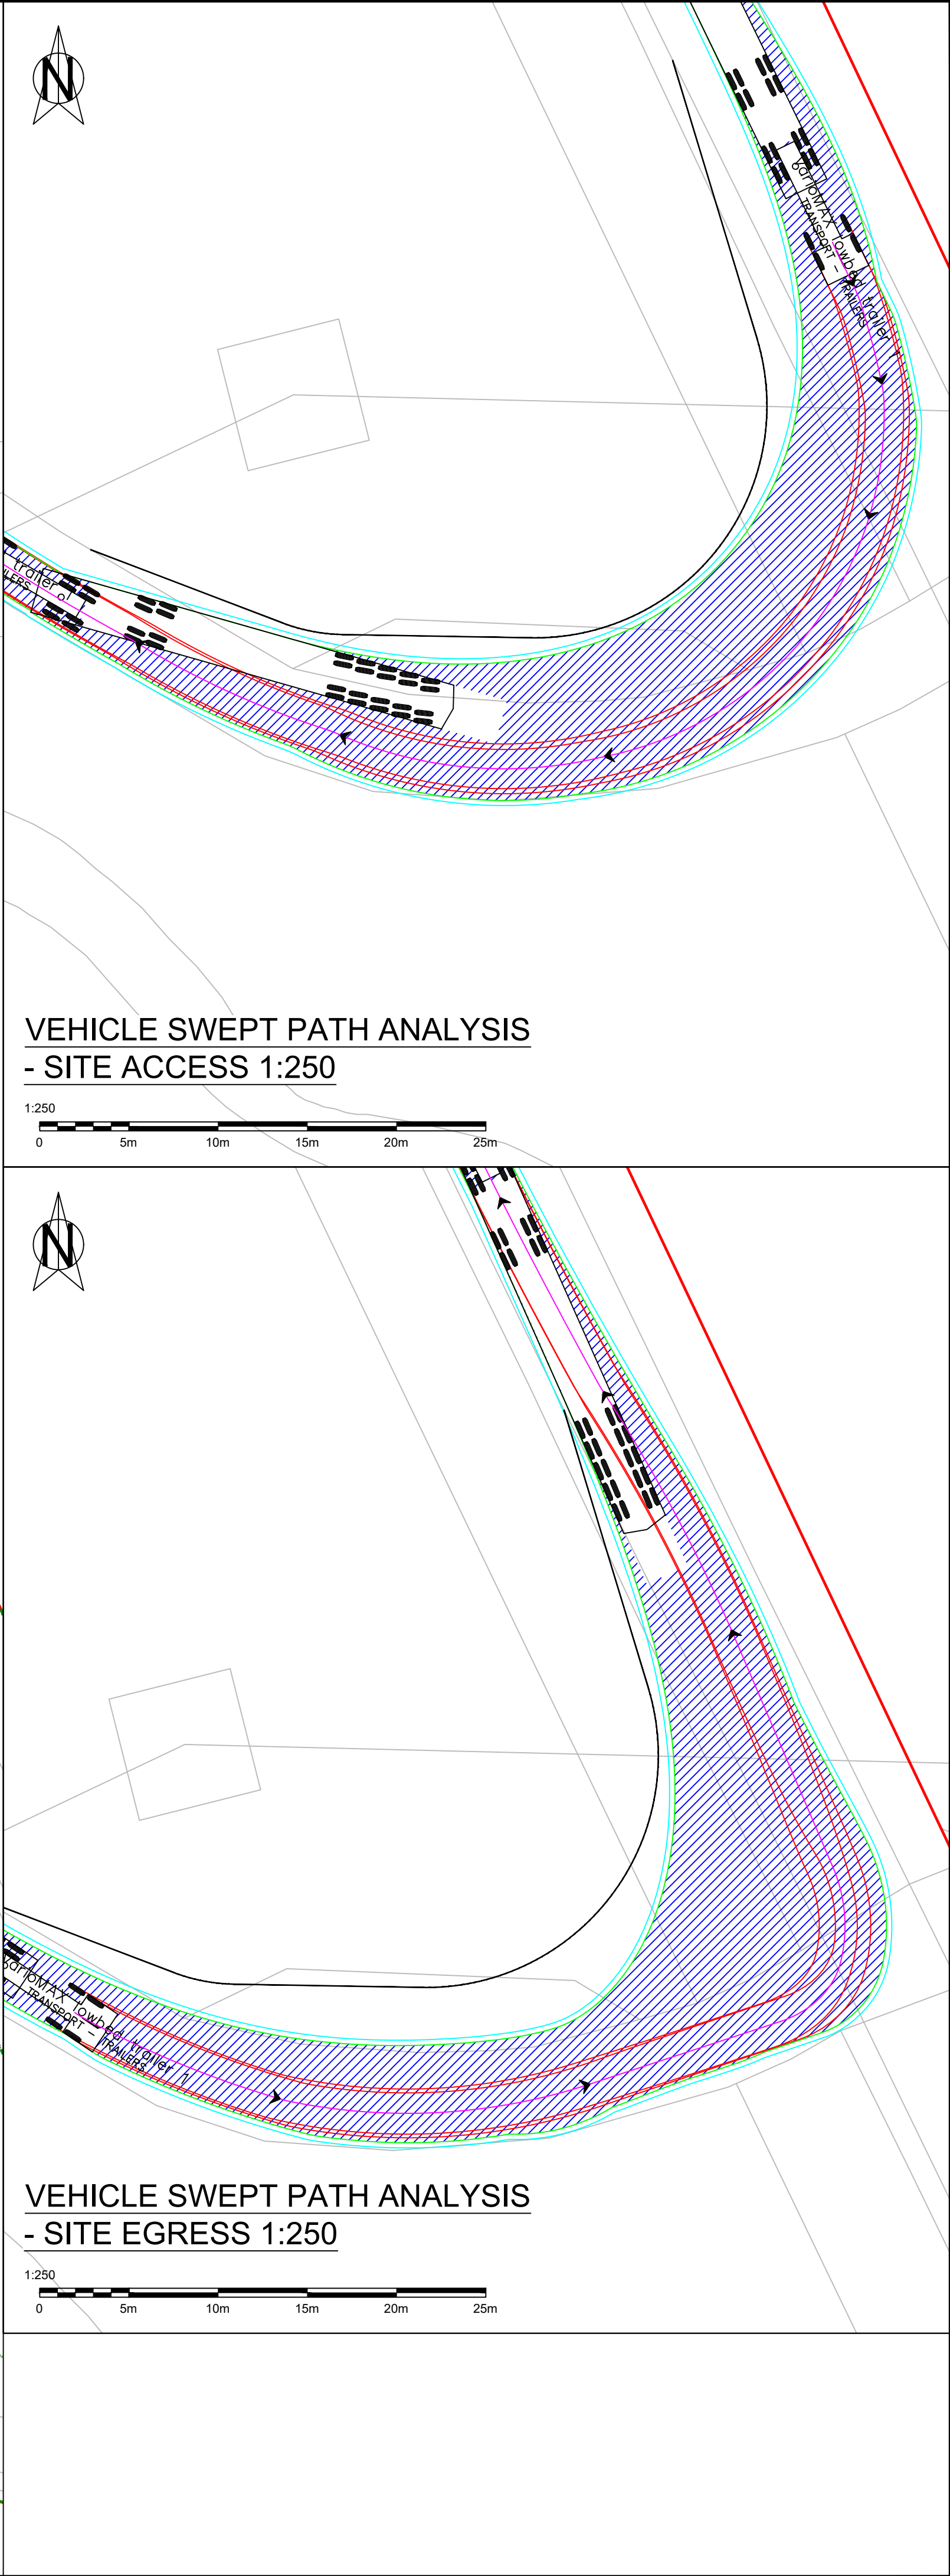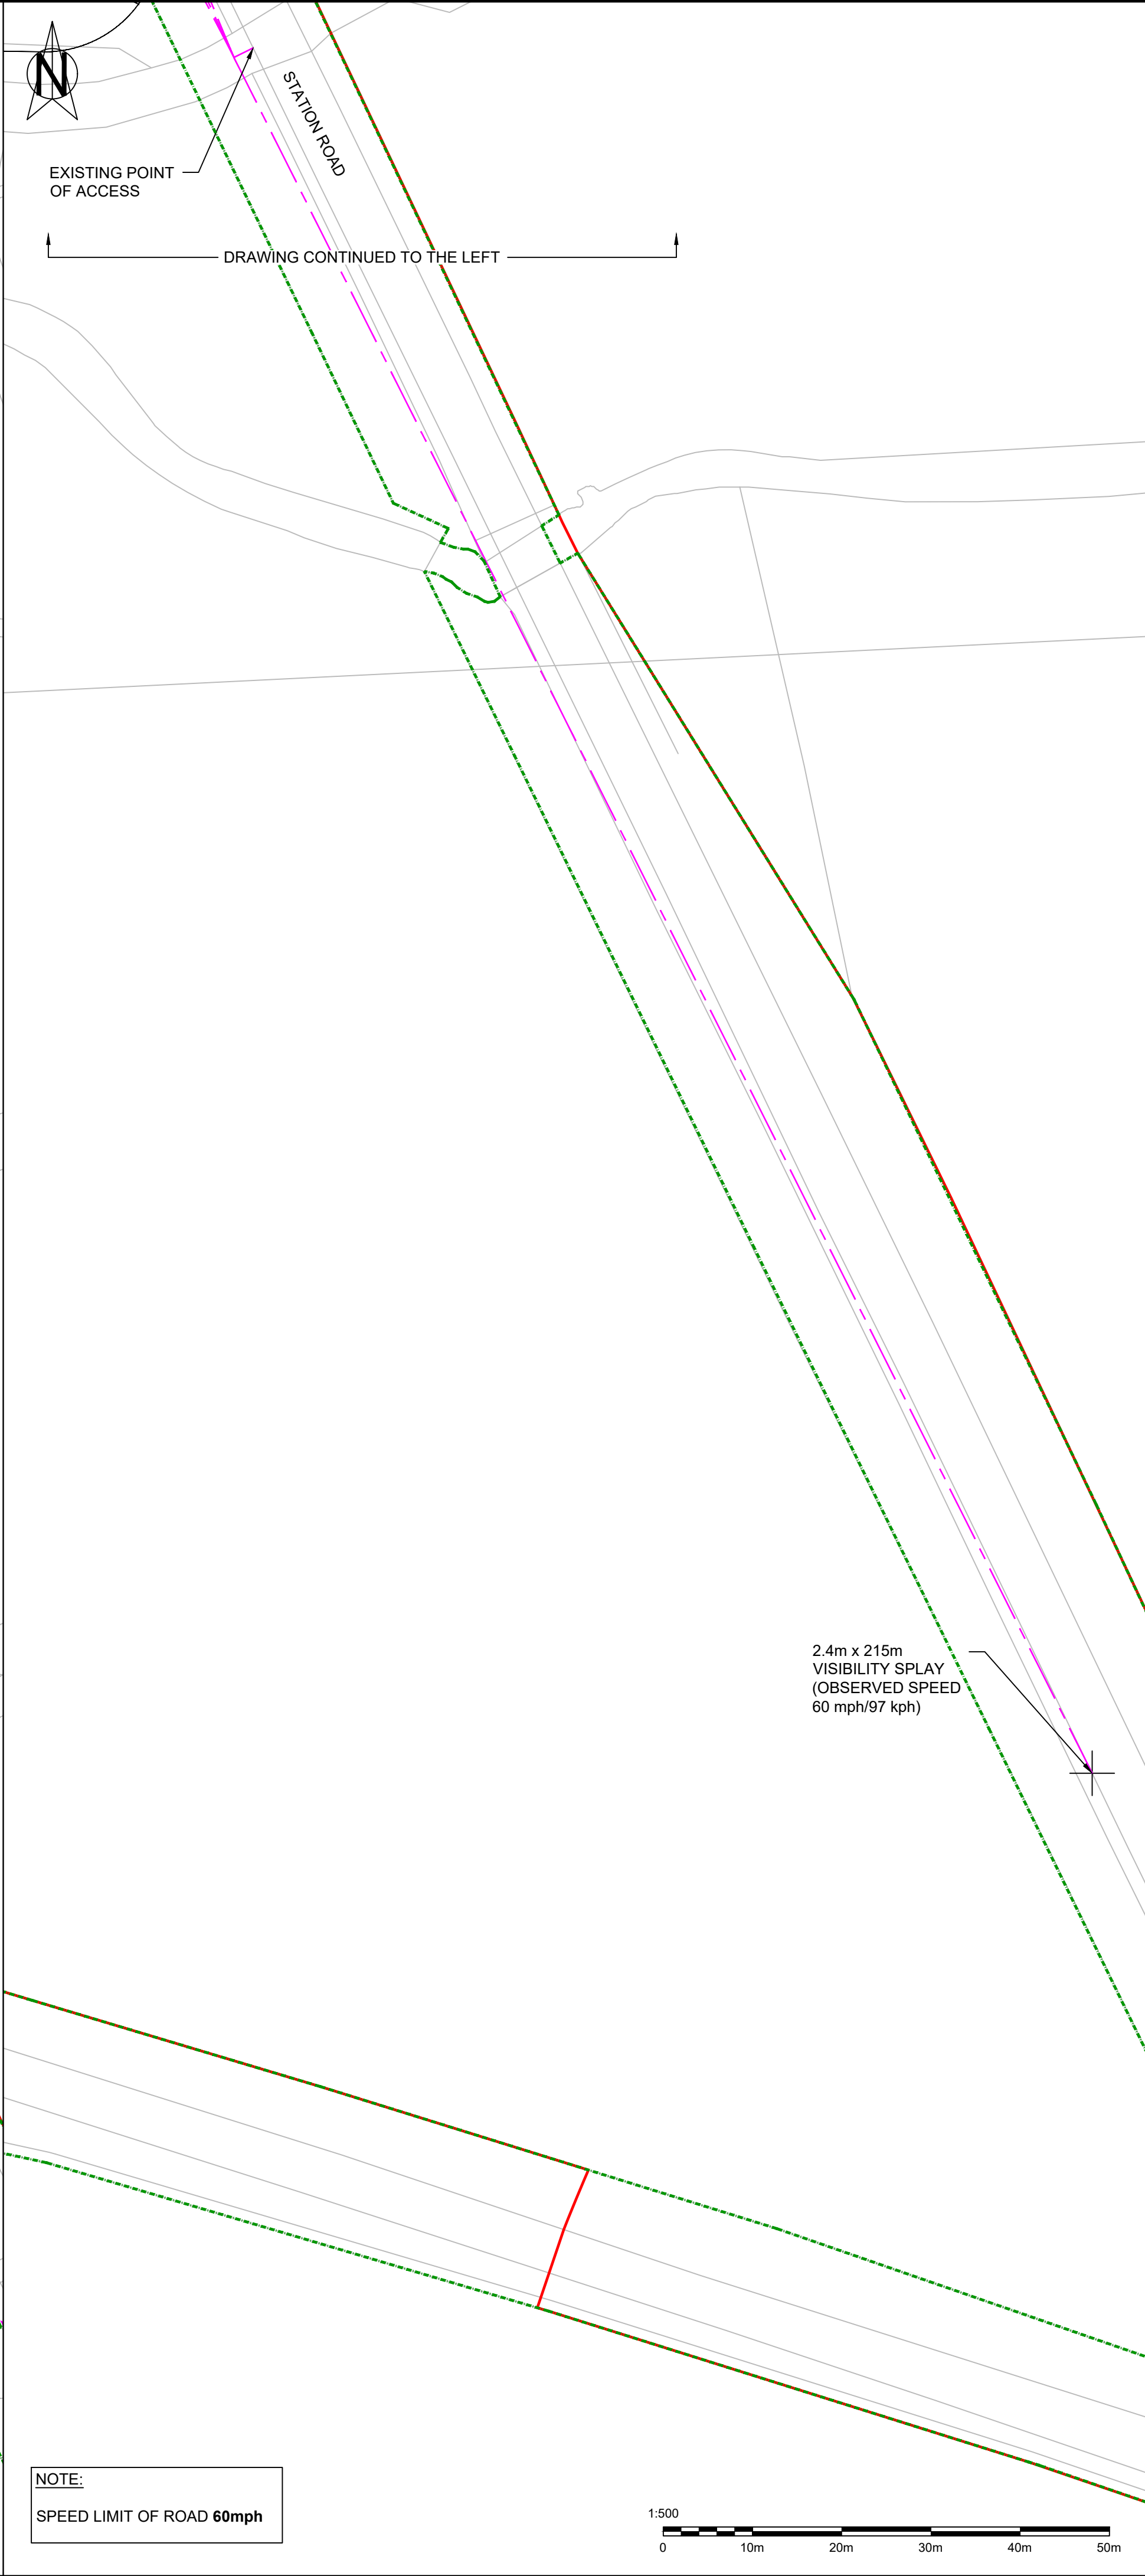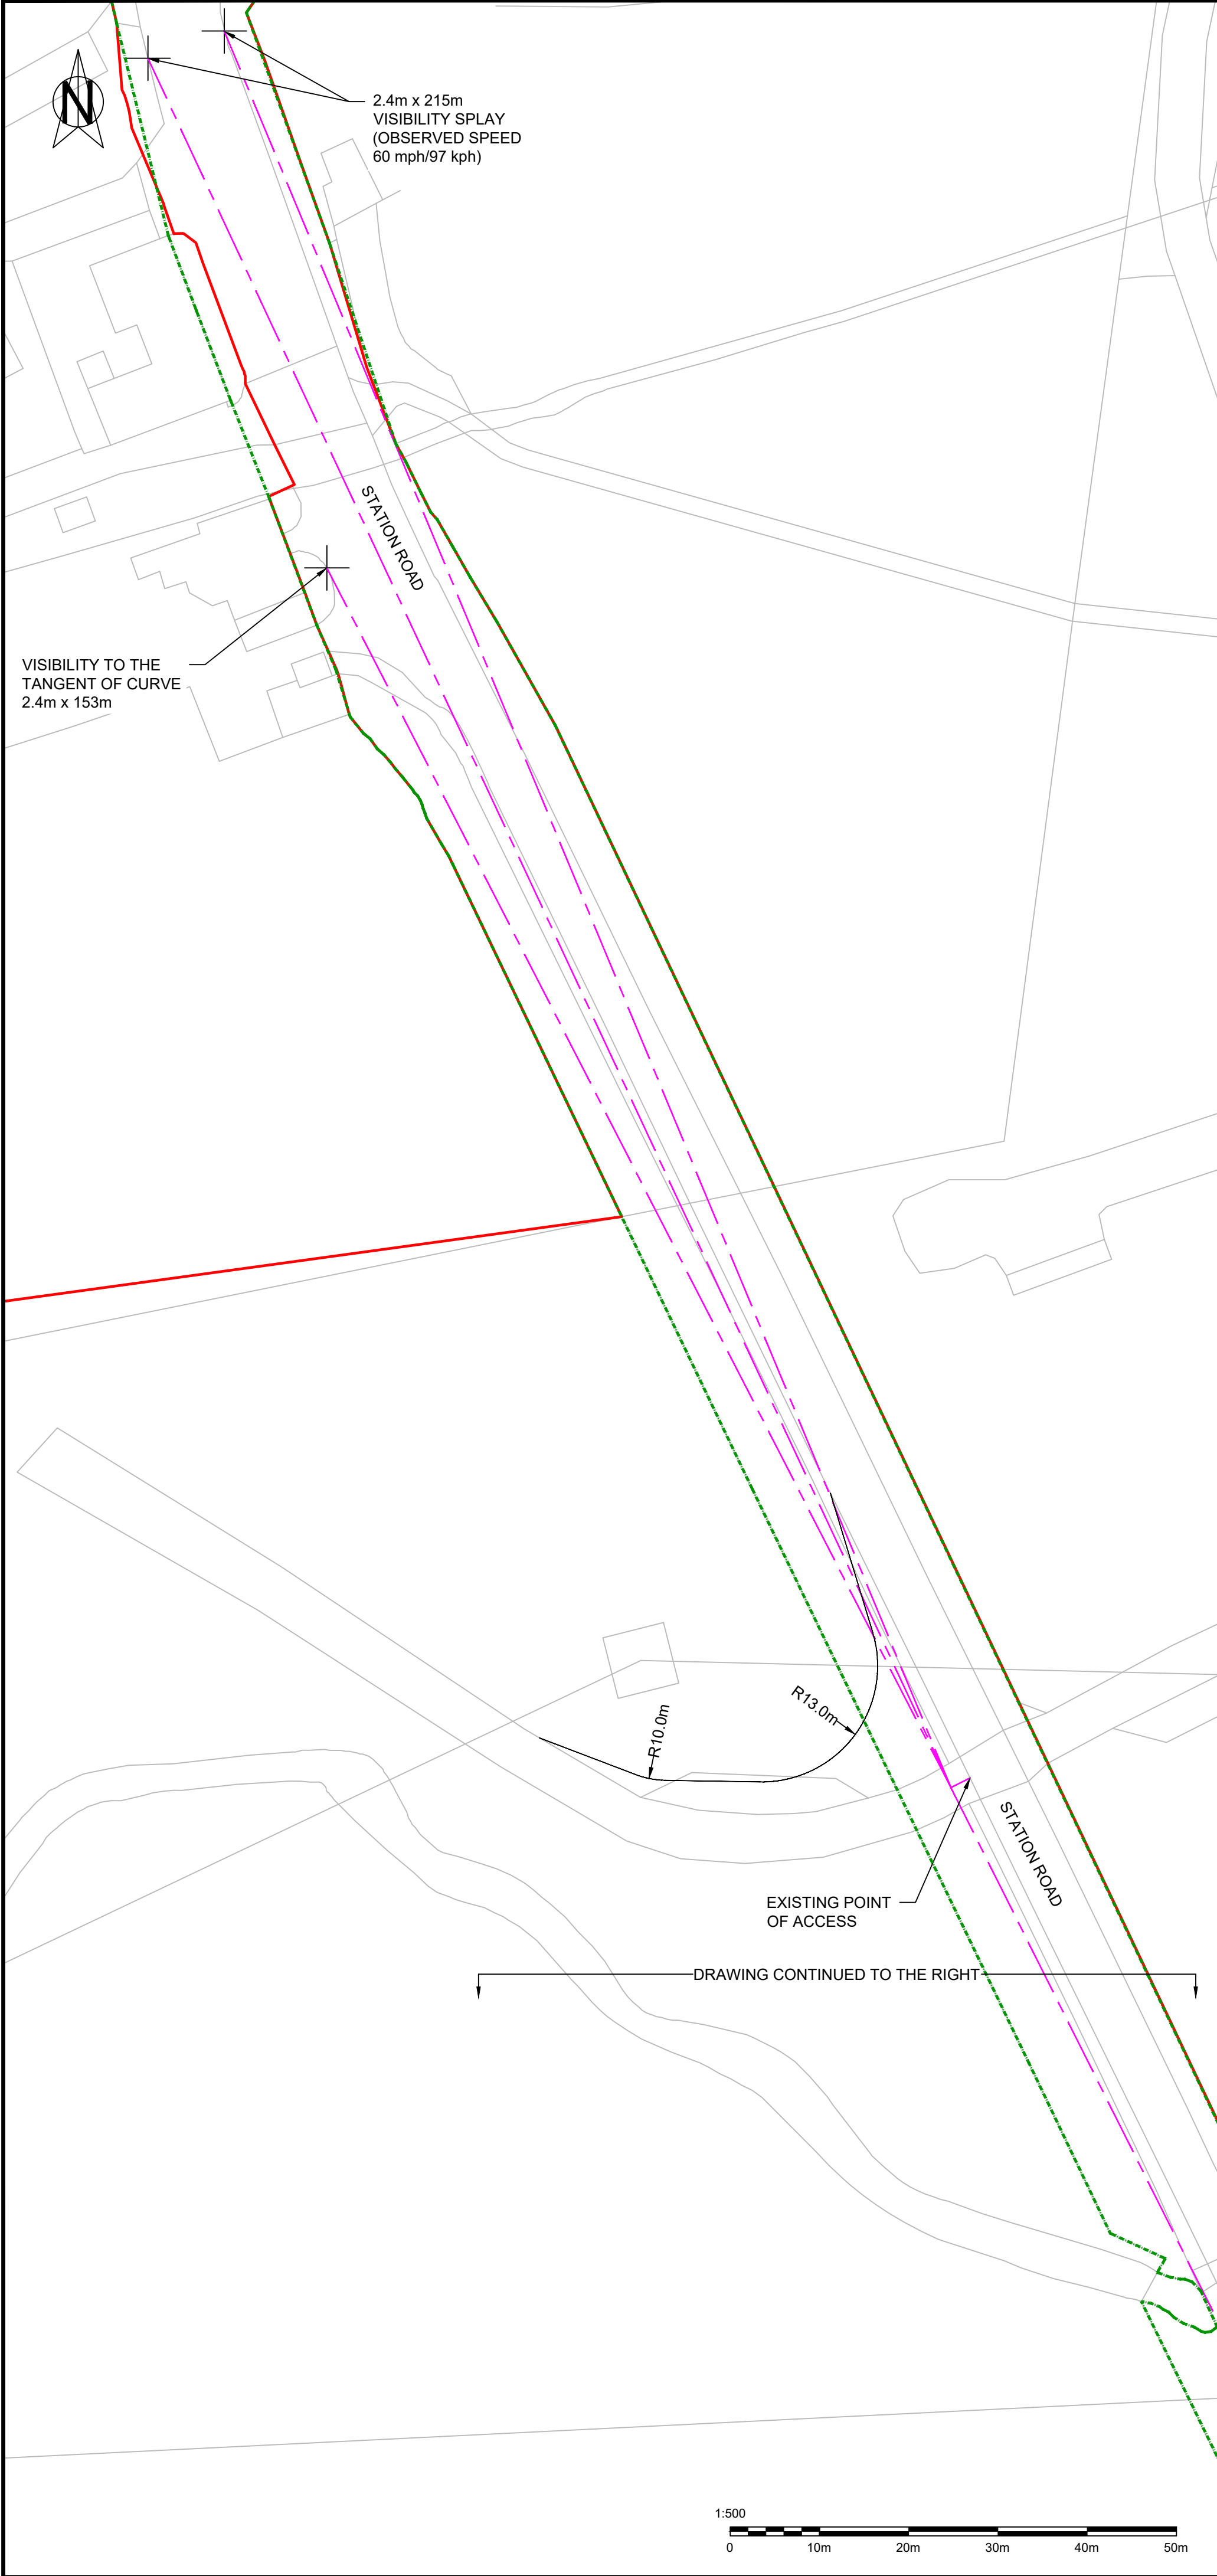

NOTES :

1. (C) This drawing is copyright.
2. All dimensions to be checked on site.
3. Do not scale from this drawing; only figured dimensions are to be worked from.
4. Any discrepancies must be reported immediately before proceeding.
5. This drawing to be read & printed in colour.
6. Ordnance Survey, (c) Crown Copyright 2024. All rights reserved. Licence number 100022432.

KEY PLAN
1:200000@A1

KEY:

- SITE BOUNDARY
- TRAFFIC SURVEY LOCATION
- HIGHWAY BOUNDARY
- VISIBILITY SPLAY EXTENT
- EXISTING LAYOUT
- PROPOSED EDGE OF ACCESS
- EXISTING VEGETATION
- EXTENT OF VEGETATION REMOVAL
- EXISTING CONTOURS

VEHICLE PROFILE:

VARIO-MAX LOWBED - 29.63m
meters

TRACTOR WIDTH : 2.55
TRAILER WIDTH : 2.55
TRACTOR TRACK : 2.55
TRAILER TRACK : 2.55
LOCK TO LOCK TIME : 6.0
STEERING ANGLE : 40.0
ARTICULATING ANGLE: 70.0

VEHICLE ANALYSIS KEY:

- VEHICLE PATH & DIRECTION
- VEHICLE BODY ENVELOPE
- VEHICLE FRONT WHEEL PATH
- 0.3m VEHICLE BUFFER ZONE AROUND TRACKING

D	03.12.2025	Drawing updated as per client comments	CS	OW	SM
C	19.05.2025	Boundary removed	CS	OW	SM
B	10.04.2025	Boundary updated, Drawing combined	CS	OW	SM
A	11.03.2025	Preliminary issue	CS	LF	SM

REV	DATE	DESCRIPTION	DRN	CHKD	APRD

Issue Status

<input type="checkbox"/> CONCEPT	<input type="checkbox"/> CONSTRUCTION
<input type="checkbox"/> PRELIMINARY	<input type="checkbox"/> AS BUILT
<input type="checkbox"/> TENDER	<input type="checkbox"/> HAS FILE ISSUE

Client
GREEN HILL SOLAR FARM LTD


Project
GREEN HILL SOLAR FARM

Drawing Title
CABLE ROUTE ACCESS 16
GENERAL ARRANGEMENT & VEHICLE TRACKING

Scale @ A1	Drawn	CS	Chkd	OW
As shown	Aprd	SM	Date	MAR 2025

Drawing Ref	Rev
23061-KMC-XX-CR16-DR-CH-0001	D

kmc
transport planning

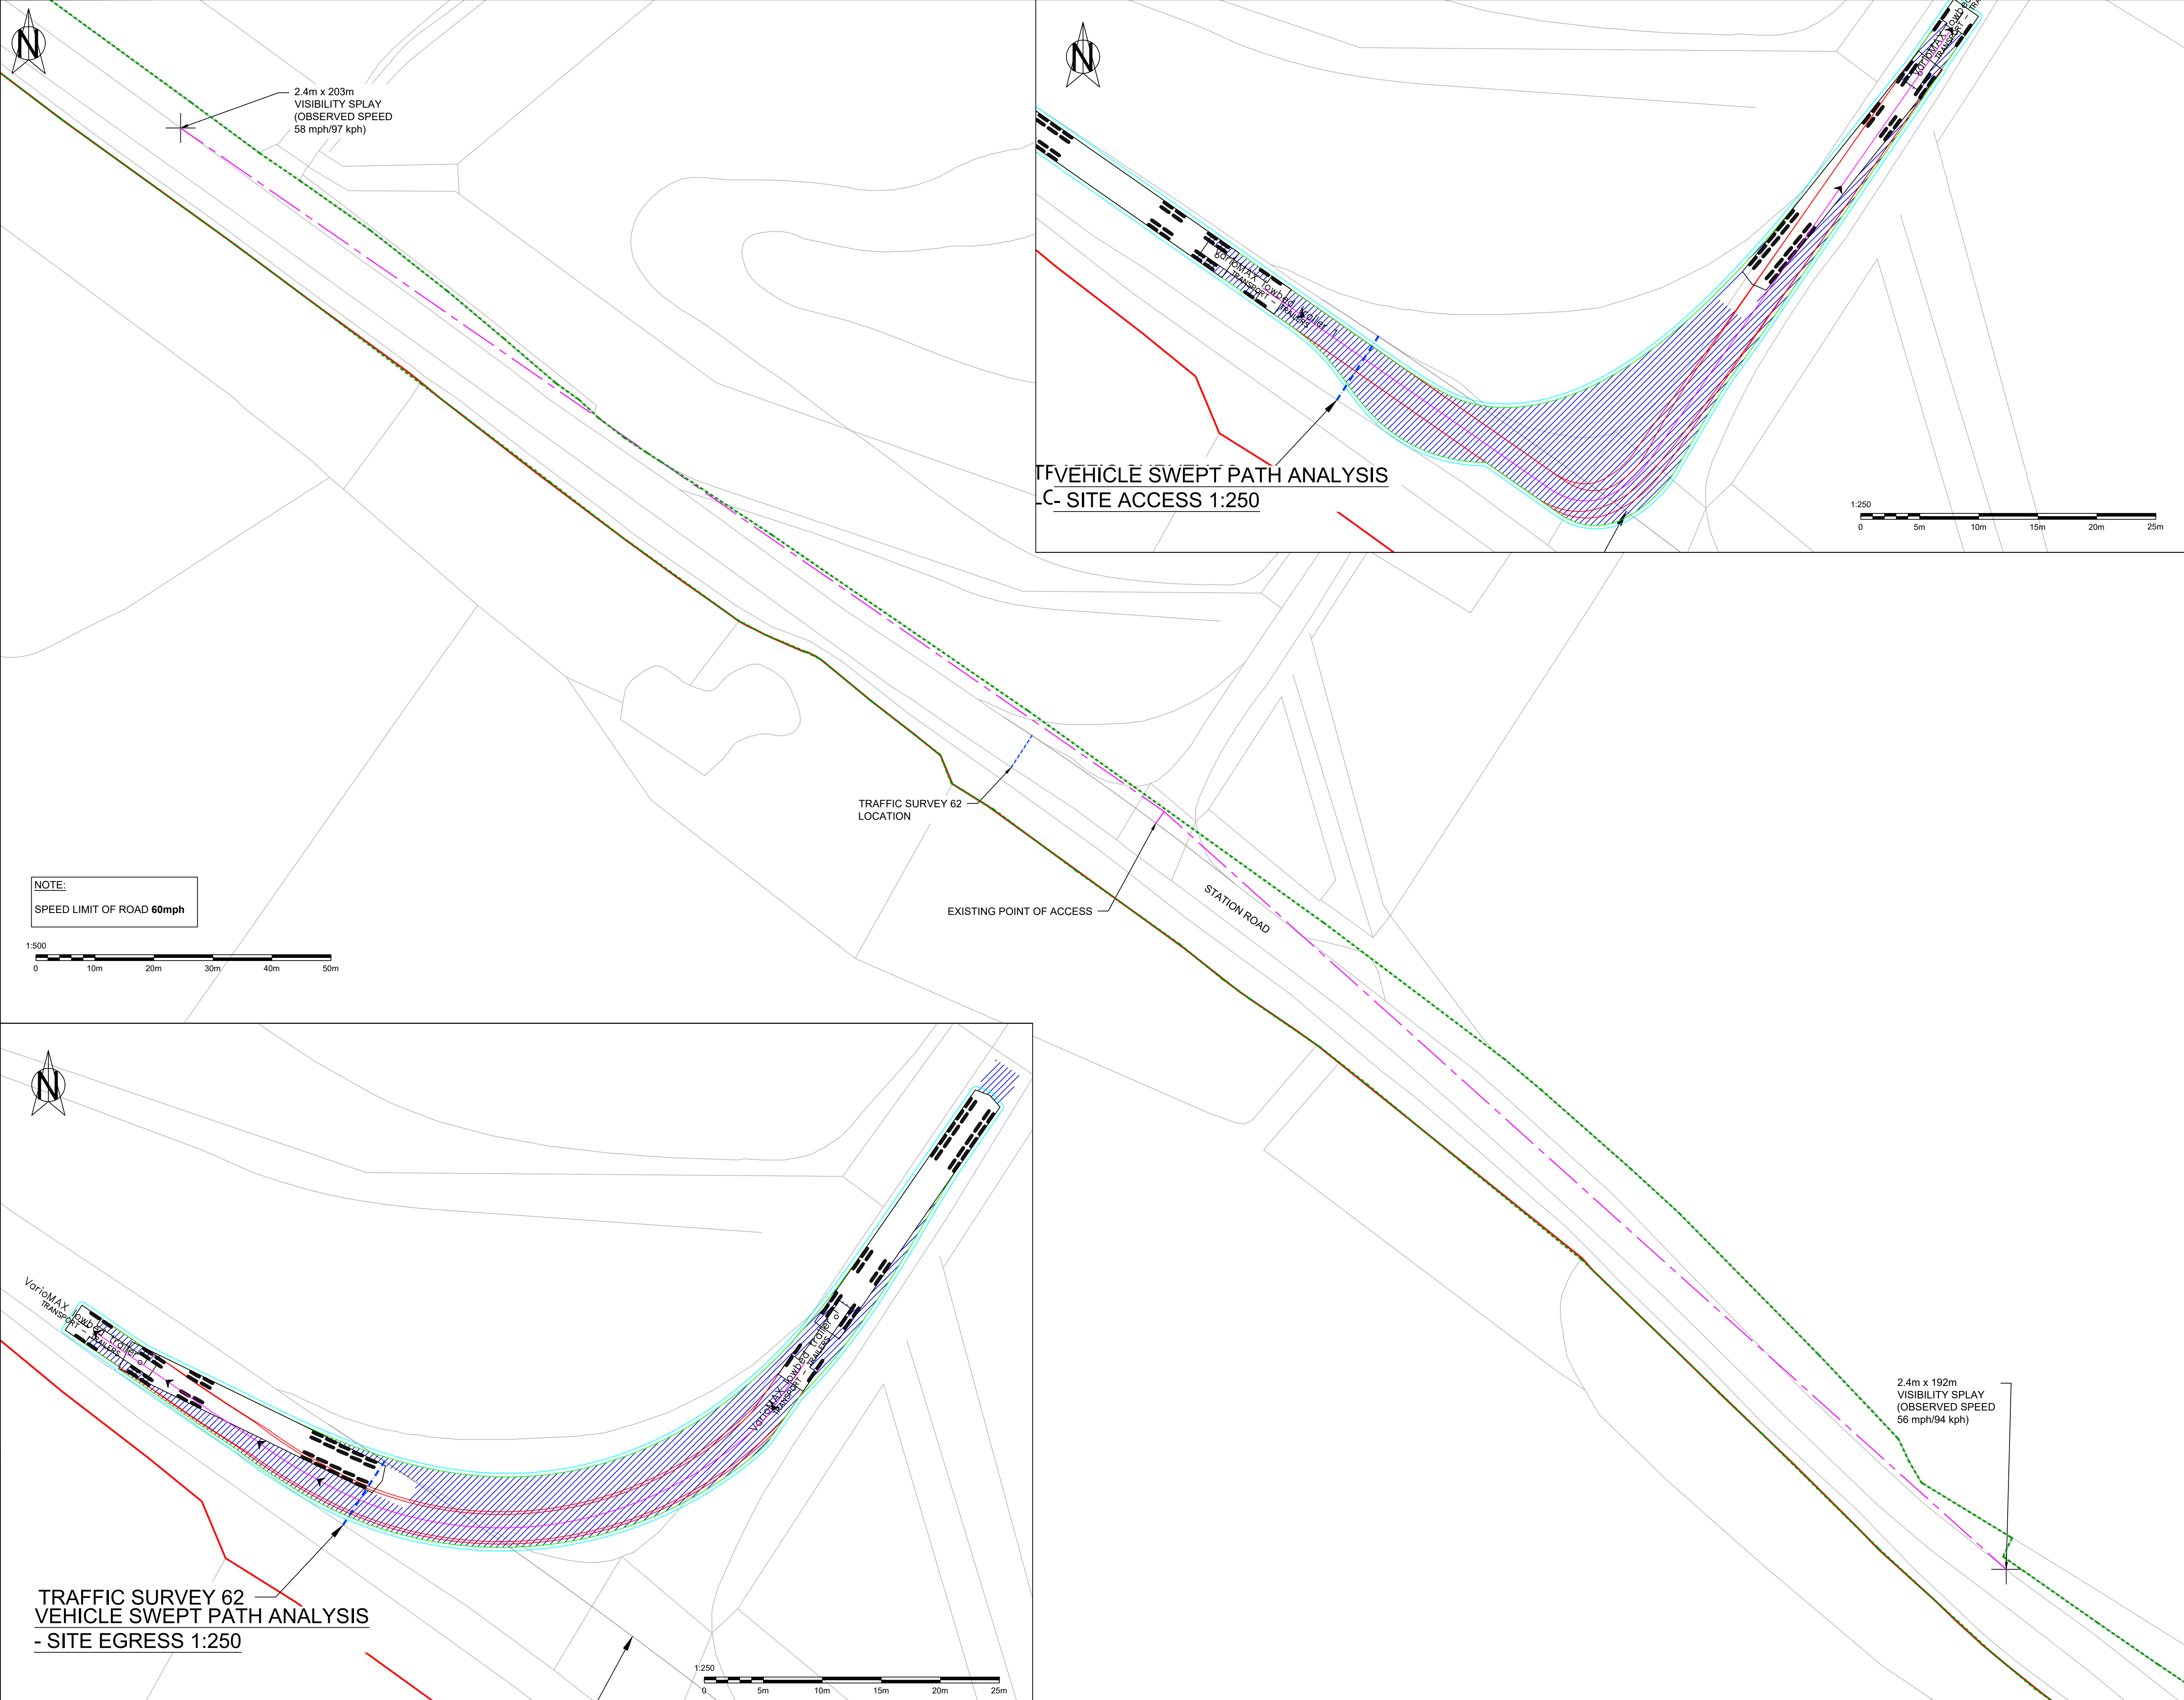

NOTES:

1. (C) This drawing is copyright.
2. All dimensions to be checked on site.
3. Do not scale from this drawing; only figured dimensions are to be worked from.
4. Any discrepancies must be reported immediately before proceeding.
5. This drawing to be read & printed in colour.
6. Ordnance Survey, (c) Crown Copyright 2024. All rights reserved. Licence number 100022432.

KEY PLAN
1:200000@A1

KEY:

- SITE BOUNDARY
- TRAFFIC SURVEY LOCATION
- HIGHWAY BOUNDARY
- VISIBILITY SPLAY EXTENT
- EXISTING LAYOUT
- PROPOSED EDGE OF ACCESS
- EXISTING VEGETATION
- EXTENT OF VEGETATION REMOVAL
- EXISTING CONTOURS

VEHICLE PROFILE:

VARIO-MAX LOWBED - 29.63m meters

TRACTOR WIDTH : 2.55

TRAILER WIDTH : 2.55

TRACTOR TRACK : 2.55

TRAILER TRACK : 2.55

LOCK TO LOCK TIME : 6.0

STEERING ANGLE : 40.0

ARTICULATING ANGLE: 70.0

VEHICLE ANALYSIS KEY:

- VEHICLE PATH & DIRECTION
- VEHICLE BODY ENVELOPE
- VEHICLE FRONT WHEEL PATH
- 0.3m VEHICLE BUFFER ZONE AROUND TRACKING

D	03.12.2025	Drawing updated as per client comments	CS	OW	SM
C	19.05.2025	Boundary removed	CS	OW	SM
B	10.04.2025	Boundary updated, Drawing combined	CS	OW	SM
A	11.03.2025	Preliminary Issue	CS	LF	SM

REV	DATE	DESCRIPTION	DRN	CHKD	APRD

Issue Status

<input type="checkbox"/> CONCEPT	<input type="checkbox"/> CONSTRUCTION
<input checked="" type="checkbox"/> PRELIMINARY	<input type="checkbox"/> AS BUILT
<input type="checkbox"/> TENDER	<input type="checkbox"/> HAS FILE ISSUE

Client
GREEN HILL SOLAR FARM LTD


Project
GREEN HILL SOLAR FARM

Drawing Title
CABLE ROUTE ACCESS 17
GENERAL ARRANGEMENT & VEHICLE TRACKING

Scale @ A1 As shown	Drawn Aprd	CS SM	Chkd Date	OW MAR 2025
------------------------	---------------	----------	--------------	----------------

Drawing Ref 23061-KMC-XX-CR17-DR-CH-0001	Rev D
---	----------

kmc
transport planning

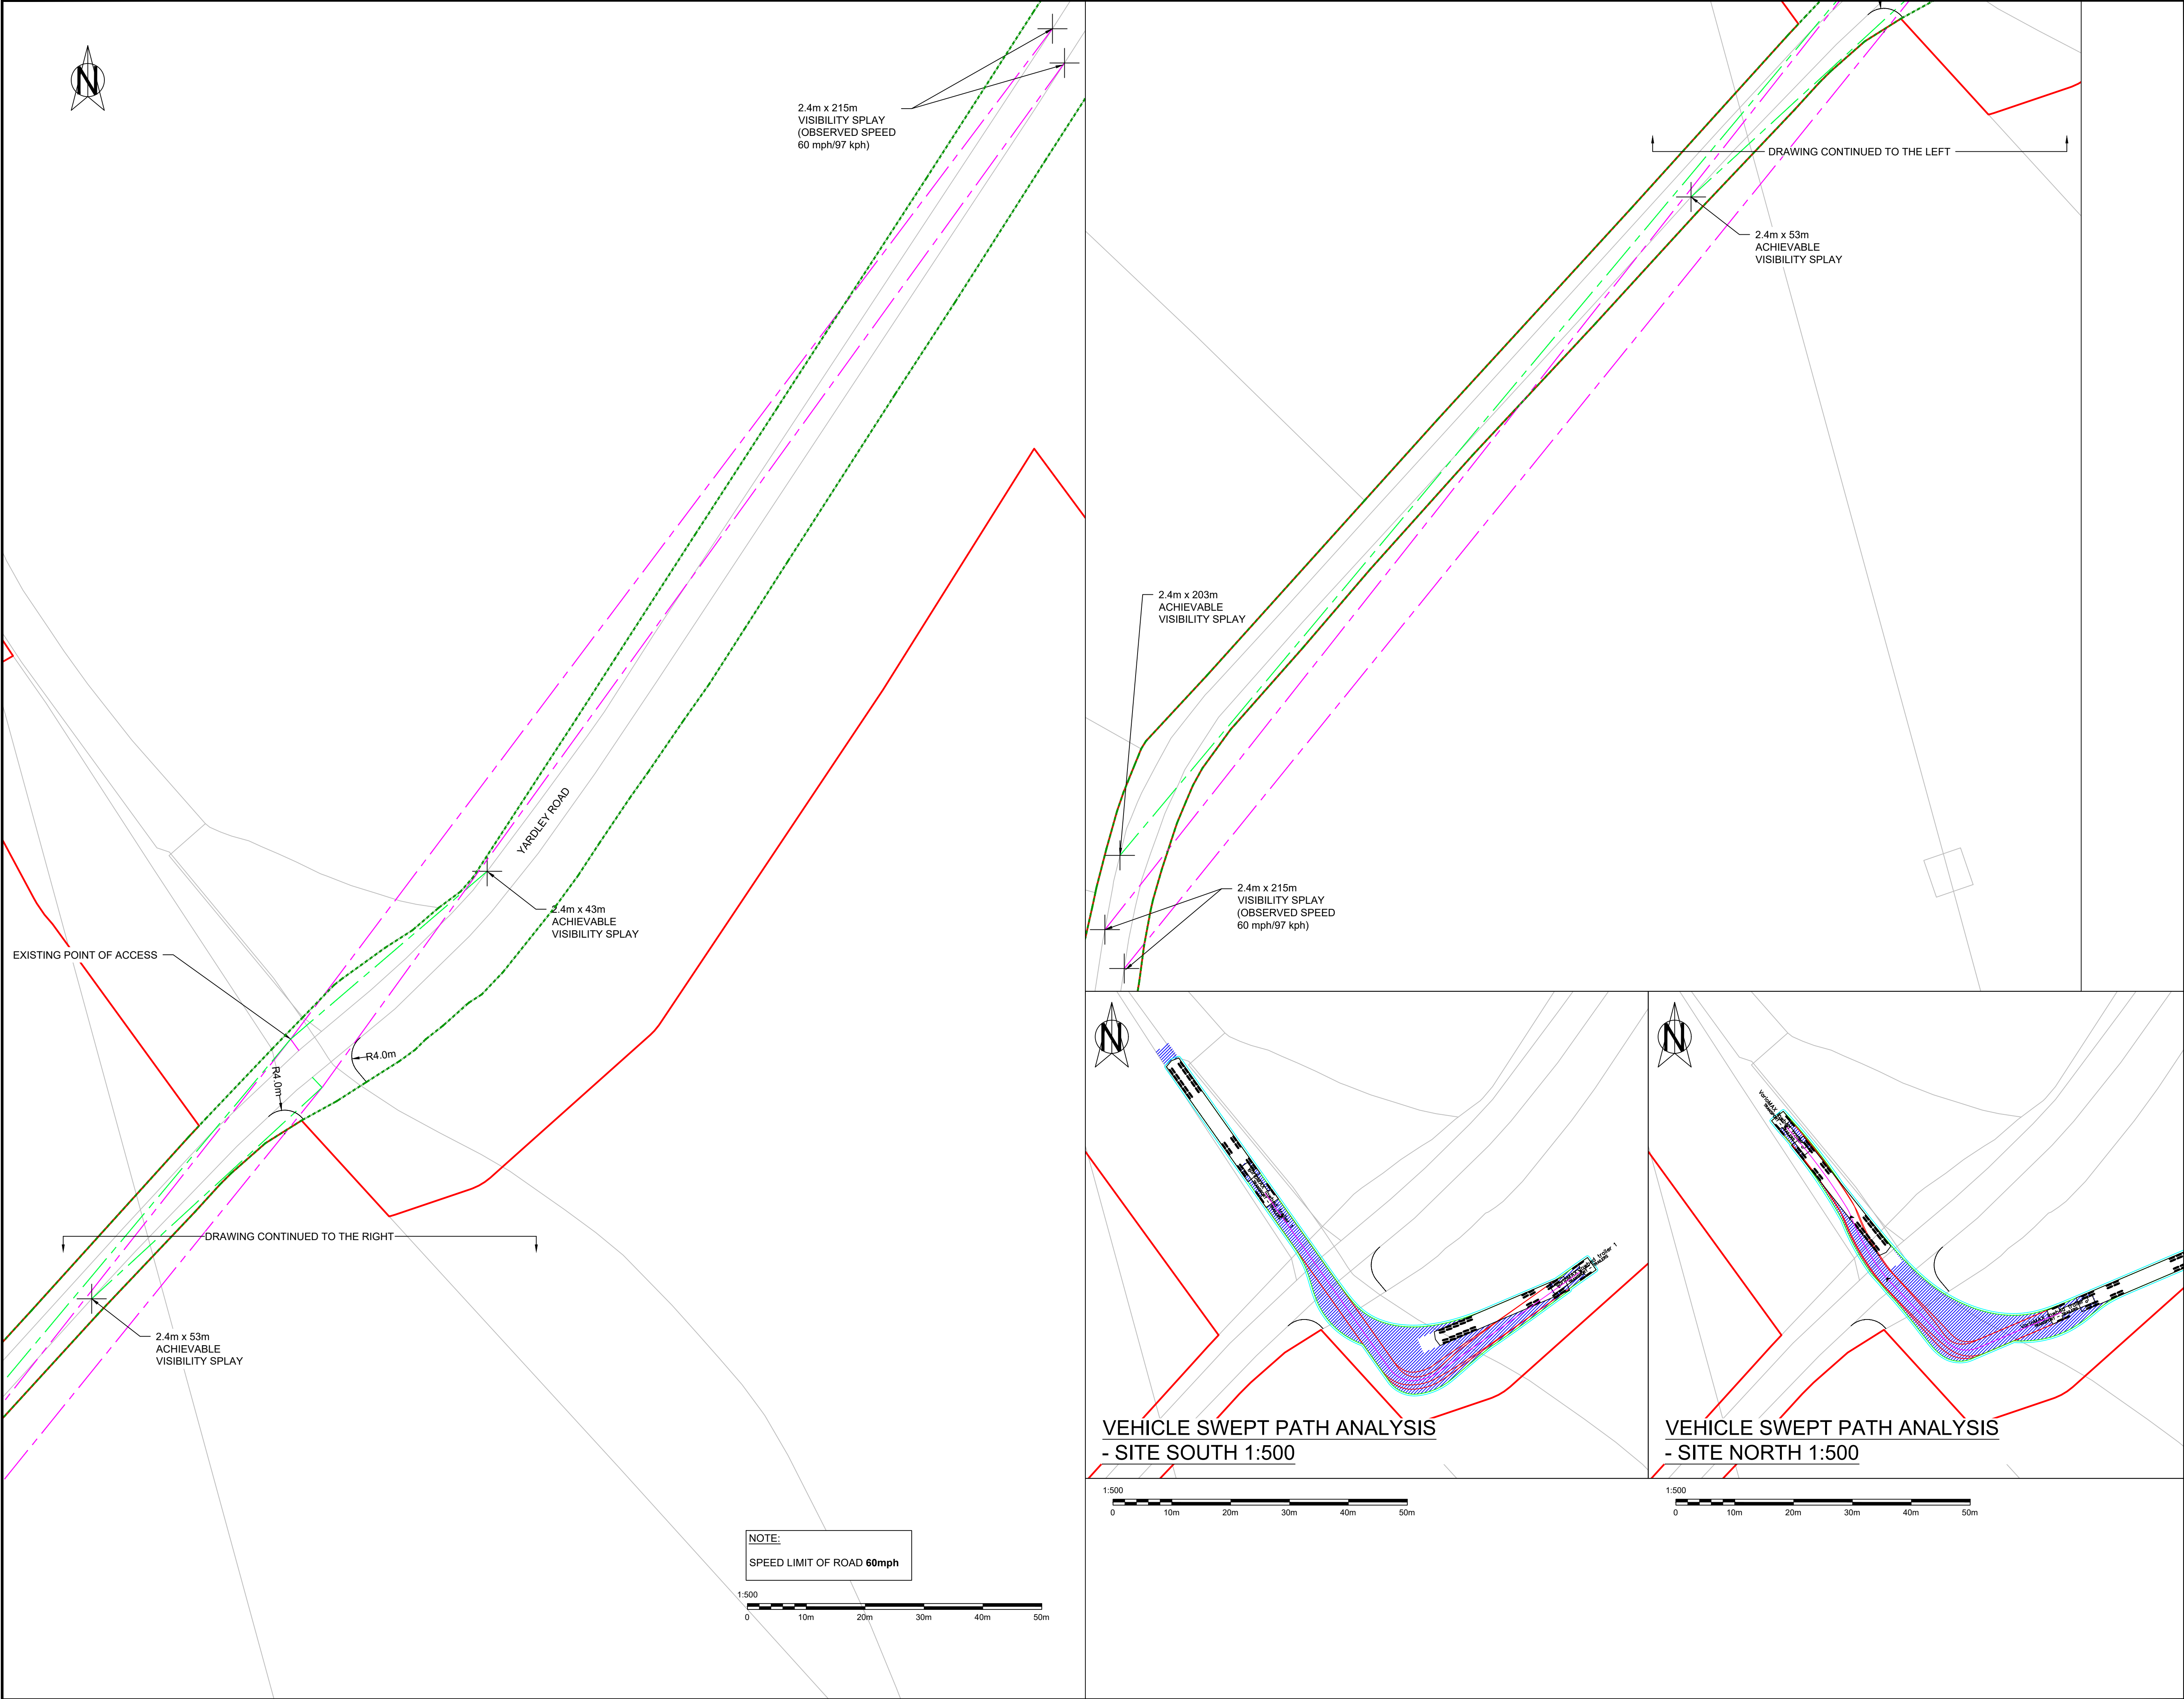

WALGRAVE










EARL'S BARTON

ACCESS LOCATION

BOZEAT

KEY PLAN
:200000@A1

KEY:

-  SITE BOUNDARY
-  TRAFFIC SURVEY LOCATION
-  HIGHWAY BOUNDARY
-  VISIBILITY SPLAY EXTENT
-  EXISTING LAYOUT
-  PROPOSED EDGE OF ACCESS
-  EXISTING VEGETATION
-  EXTENT OF VEGETATION REMOVAL
-  EXISTING CONTOURS





VEHICLE PROFILE:

Parameter	Value
Overall Length	34.24 m
Wheelbase	13.90 m
Front Overhang	6.80 m
Rear Overhang	9.54 m
Max Height	2.00 m
Min Ground Clearance	0.38 m

VARIO-MAX LOWBED - 29.63m meters

TRACTOR WIDTH :	2.55
TRAILER WIDTH :	2.55
TRACTOR TRACK :	2.55
TRAILER TRACK :	2.55
LOCK TO LOCK TIME :	6.0
STEERING ANGLE :	40.0
ARTICULATING ANGLE:	70.0

VEHICLE ANALYSIS KEY:

-  VEHICLE PATH & DIRECTION
-  VEHICLE BODY ENVELOPE
-  VEHICLE FRONT WHEEL PATH
-  0.3m VEHICLE BUFFER ZONE AROUND TRACKING

D	03.12.2025	Drawing updated as per client comments	CS	OW	SM
C	19.05.2025	Boundary removed	CS	OW	SM
B	10.04.2025	Boundary updated, Drawing combined	CS	OW	SM
A	10.04.2025	Preliminary Issue	CS	OW	SM
EV	DATE	DESCRIPTION	DRN	CHKD	APRD

Issue Status

<input type="checkbox"/> CONCEPT	<input type="checkbox"/> CONSTRUCTION
<input checked="" type="checkbox"/> PRELIMINARY	<input type="checkbox"/> AS BUILT
<input type="checkbox"/> TENDER	<input type="checkbox"/> H&S FILE ISSUE

Client
GREEN HILL SOLAR FARM LTD





Project	GREEN HILL SOLAR FARM
---------	-----------------------

Drawing Title
CABLE ROUTE ACCESS 19 & 20
GENERAL ARRANGEMENT & VEHICLE
TRACKING

Scale @ A1	Drwn CS	Chkd OW
As shown	Aprd SM	Date APR 2025

Drawing Ref	Rev
23061-KMC-XX-CR19-20-DR-CH-0001	D



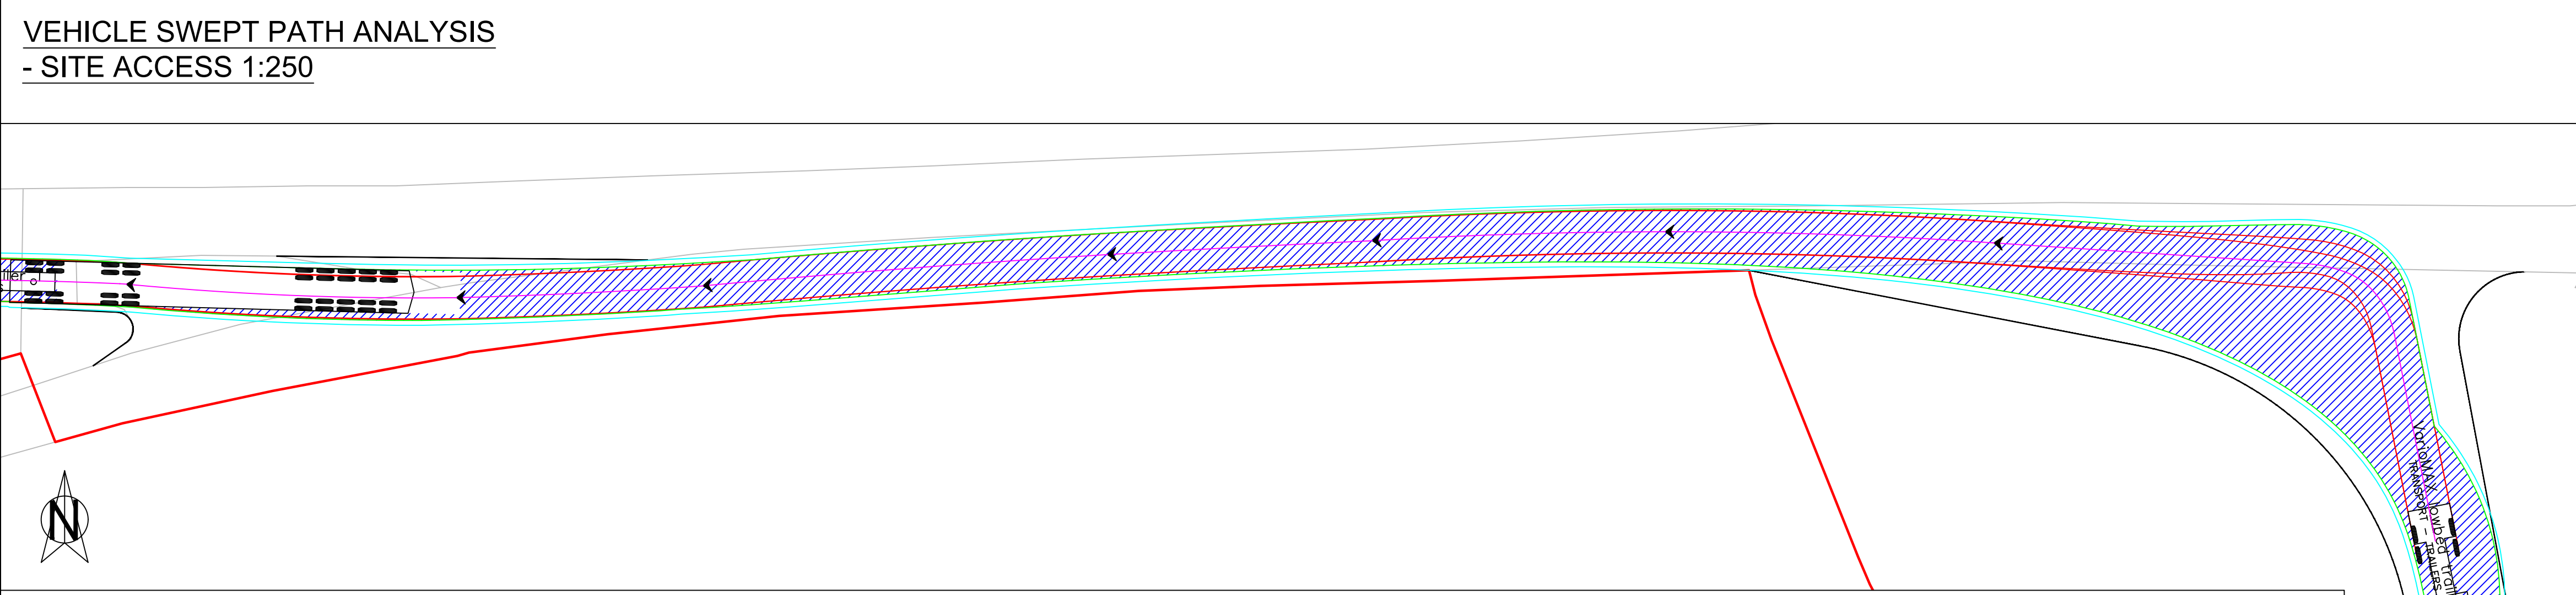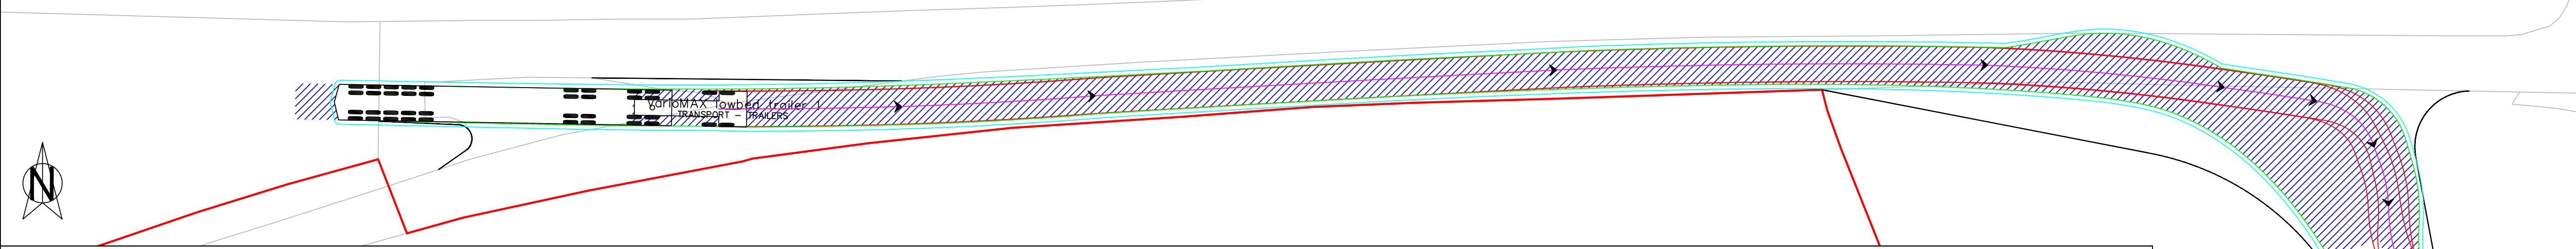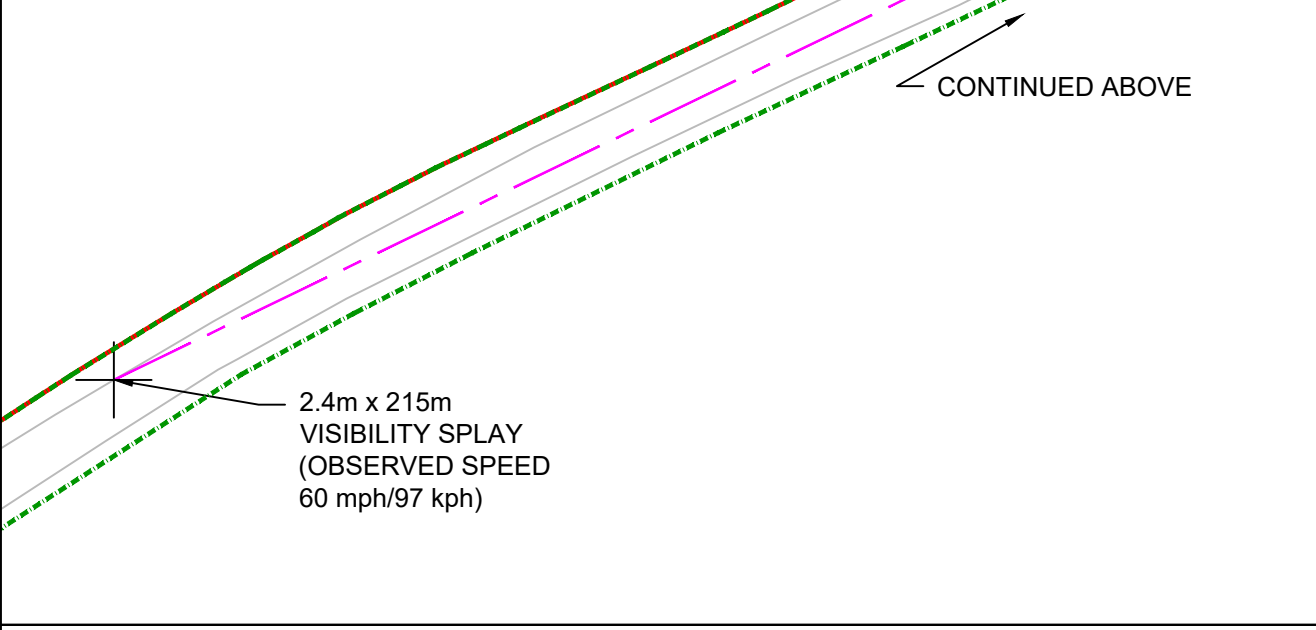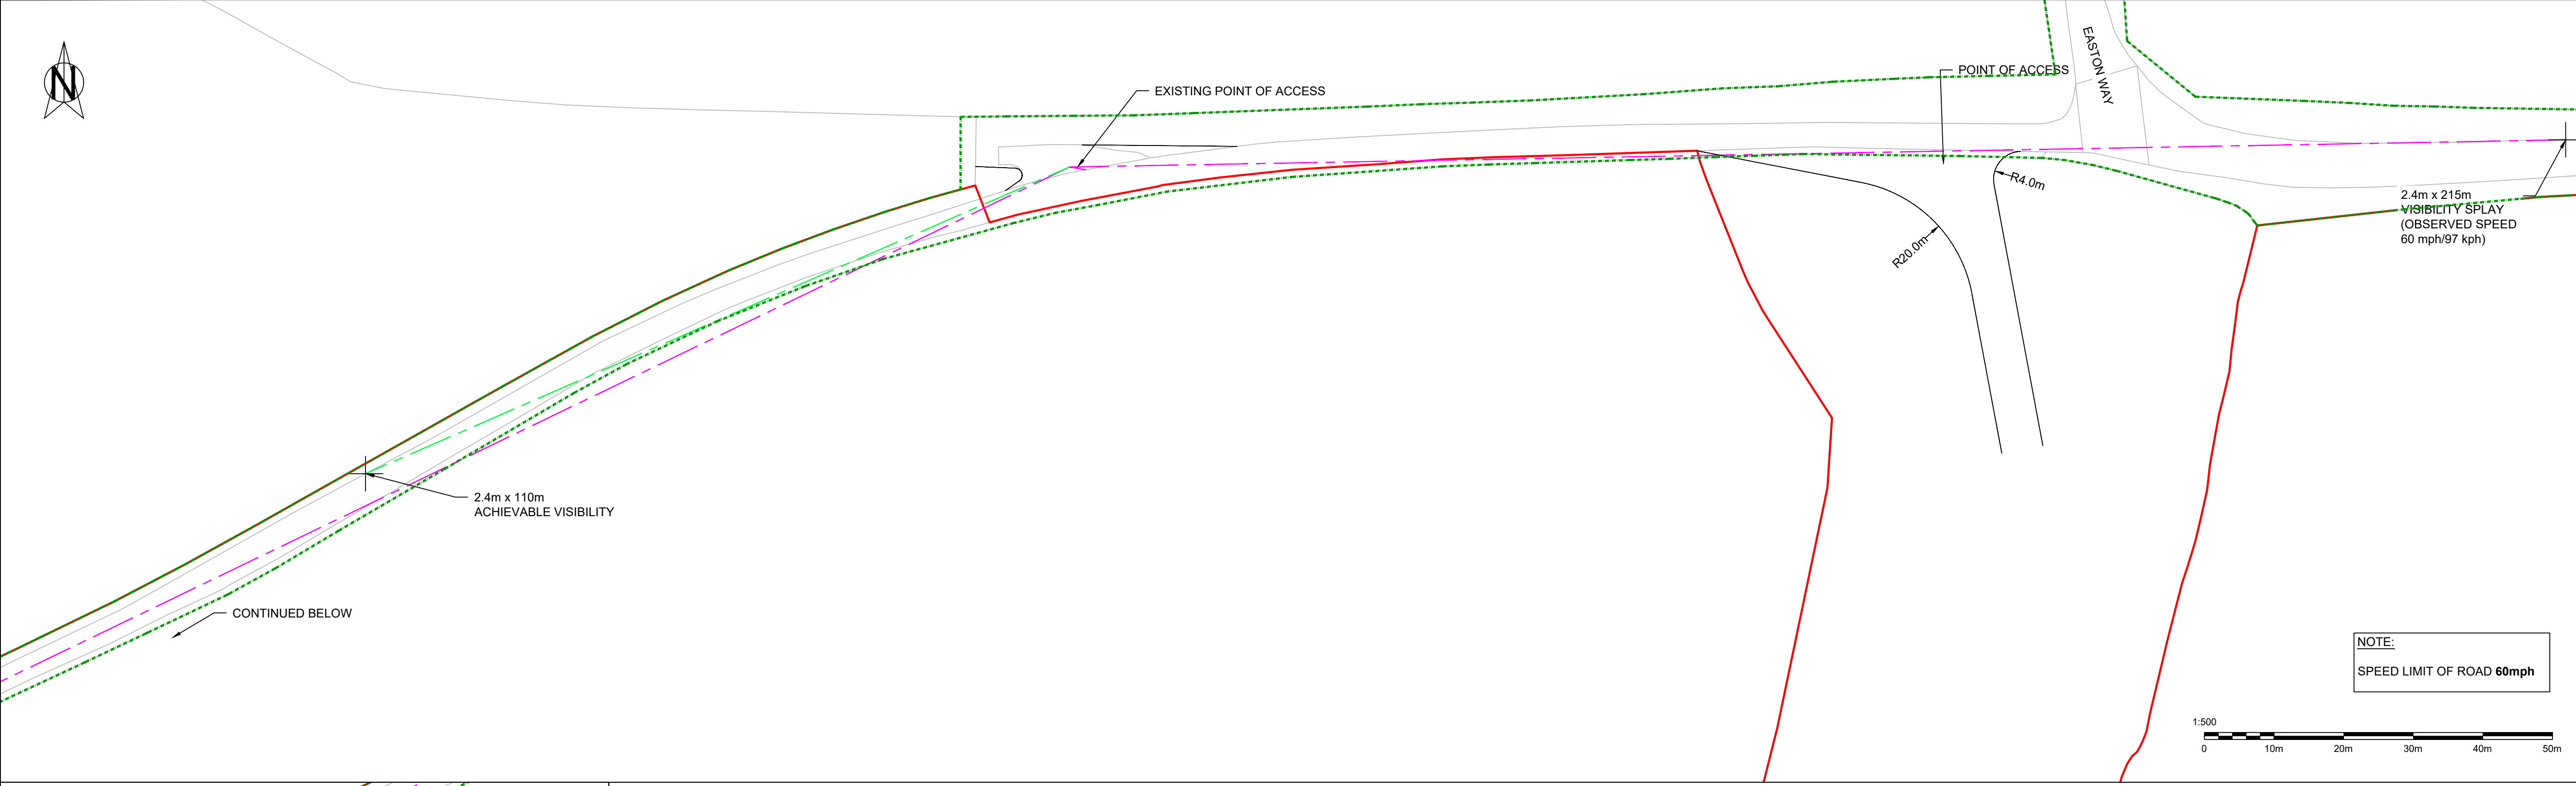

NOTES :

1. (C) This drawing is copyright.
2. All dimensions to be checked on site.
3. Do not scale from this drawing; only figured dimensions are to be worked from.
4. Any discrepancies must be reported immediately before proceeding.
5. This drawing to be read & printed in colour.
6. Ordnance Survey, (c) Crown Copyright 2024. All rights reserved. Licence number 100022432.

KEY PLAN
1:200000@A1

KEY:

- SITE BOUNDARY
- TRAFFIC SURVEY LOCATION
- HIGHWAY BOUNDARY
- VISIBILITY SPLAY EXTENT
- EXISTING LAYOUT
- PROPOSED EDGE OF ACCESS
- EXISTING VEGETATION
- EXTENT OF VEGETATION REMOVAL
- EXISTING CONTOURS

VEHICLE PROFILE:

VARIO-MAX LOWBED - 29.63m meters

TRACTOR WIDTH	: 2.55
TRAILER WIDTH	: 2.55
TRACTOR TRACK	: 2.55
TRAILER TRACK	: 2.55
LOCK TO LOCK TIME	: 6.0
STEERING ANGLE	: 40.0
ARTICULATING ANGLE	: 70.0

VEHICLE ANALYSIS KEY:

- VEHICLE PATH & DIRECTION
- VEHICLE BODY ENVELOPE
- VEHICLE FRONT WHEEL PATH
- 0.3m VEHICLE BUFFER ZONE AROUND TRACKING

D	03.12.2025	Drawing updated as per client comments	CS	OW	SM
C	19.05.2025	Boundary removed	CS	OW	SM
B	10.04.2025	Boundary updated, Drawing combined	CS	OW	SM
A	11.03.2025	Preliminary issue	CS	LF	SM

REV	DATE	DESCRIPTION	DRN	CHKD	APRD

Issue Status

<input type="checkbox"/> CONCEPT	<input type="checkbox"/> CONSTRUCTION
<input type="checkbox"/> PRELIMINARY	<input type="checkbox"/> AS BUILT
<input type="checkbox"/> TENDER	<input type="checkbox"/> HAS FILE ISSUE


Client
GREEN HILL SOLAR FARM LTD

Project
GREEN HILL SOLAR FARM

Drawing Title
**CABLE ROUTE ACCESS 21 & 22
GENERAL ARRANGEMENT & VEHICLE TRACKING**

Scale @ A1	Drawn	CS	Chkd	OW
As shown	Aprd	SM	Date	MAR 2025

Drawing Ref	Rev
23061-KMC-XX-CR21-22-DR-CH-0001	D

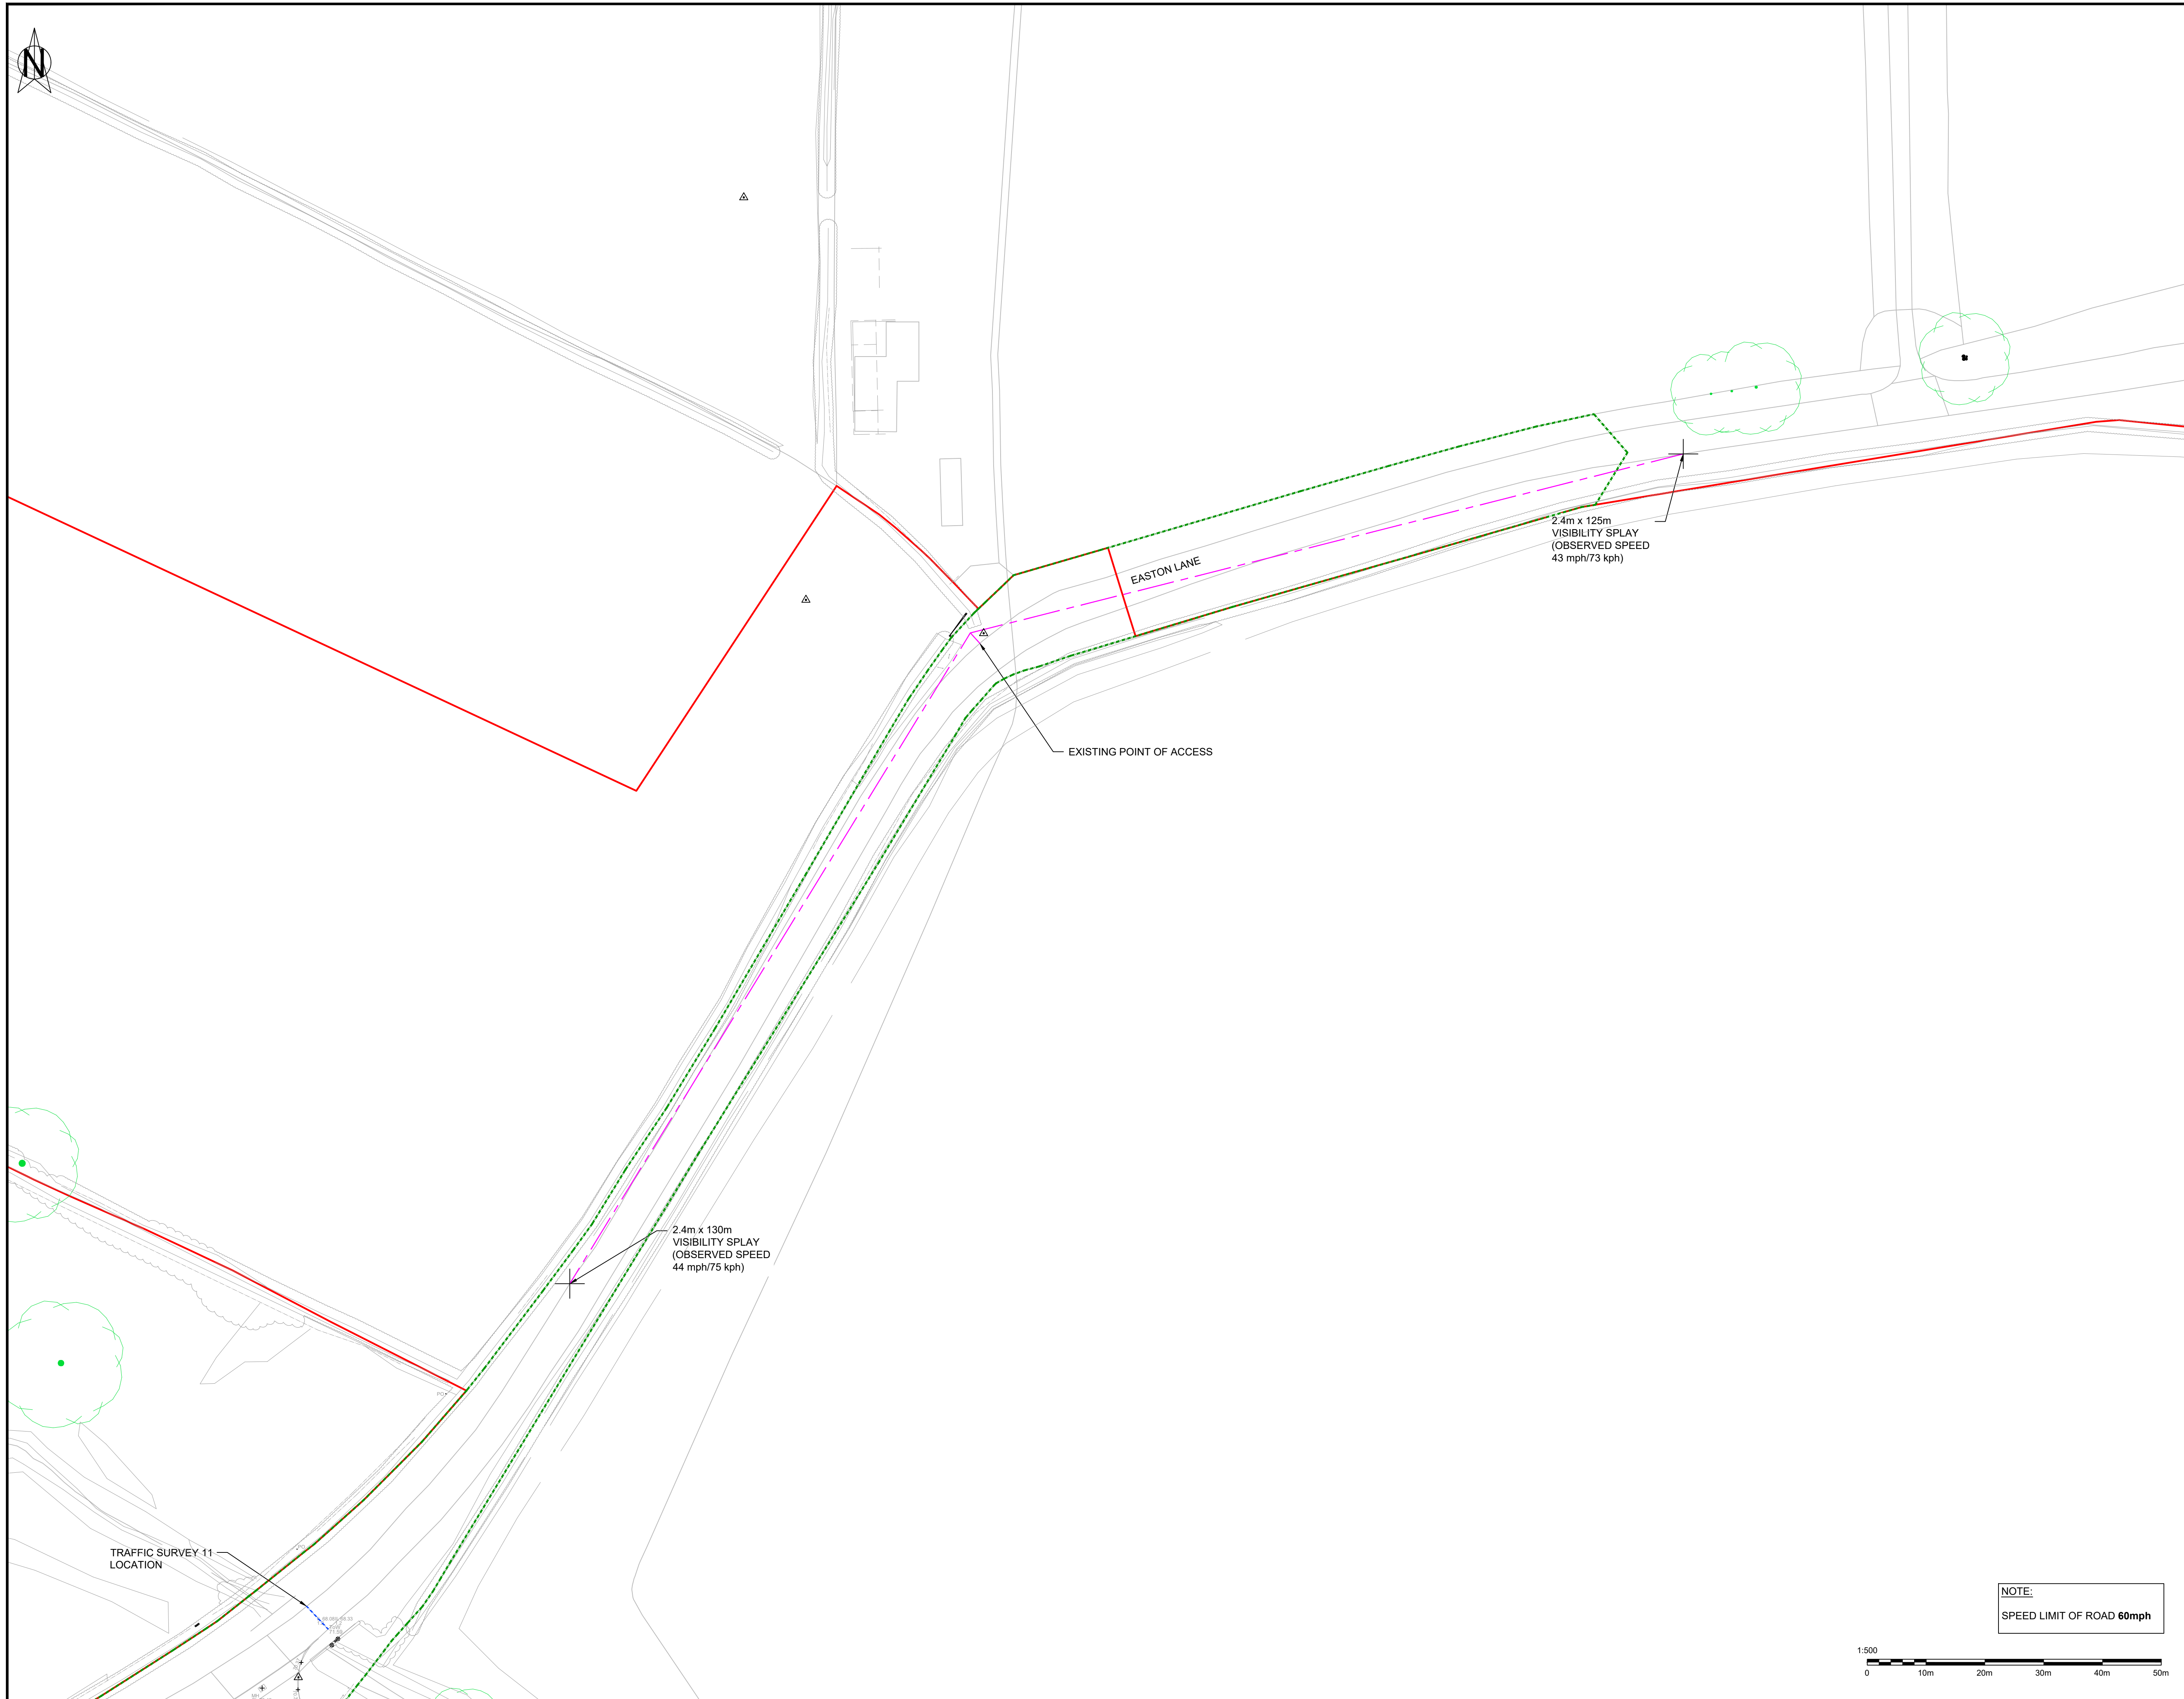

- NOTES:**
1. (C) This drawing is copyright.
 2. All dimensions to be checked on site.
 3. Do not scale from this drawing; only figured dimensions are to be worked from.
 4. Any discrepancies must be reported immediately before proceeding.
 5. This drawing to be read & printed in colour.
 6. Ordnance Survey, (c) Crown Copyright 2024. All rights reserved. Licence number 100022432.




KEY PLAN
1:200000@A1

KEY:

-
- SITE BOUNDARY
 TRAFFIC SURVEY LOCATION
 HIGHWAY BOUNDARY
 VISIBILITY SPLAY EXTENT
 EXISTING LAYOUT
 PROPOSED EDGE OF ACCESS
 EXISTING VEGETATION
 EXTENT OF VEGETATION REMOVAL
 EXISTING CONTOURS





VEHICLE PROFILE:



VARIO-MAX LOWBED - 29.63m
meters

TRACTOR WIDTH	:	2.55
TRAILER WIDTH	:	2.55
TRACTOR TRACK	:	2.55
TRAILER TRACK	:	2.55
LOCK TO LOCK TIME	:	6.0
STEERING ANGLE	:	40.0
ARTICULATING ANGLE	:	70.0

VEHICLE ANALYSIS KEY:

-  VEHICLE PATH & DIRECTION
-  VEHICLE BODY ENVELOPE
-  VEHICLE FRONT WHEEL PATH
-  0.3m VEHICLE BUFFER ZONE AROUND TRACKING

C	03.12.2025	Drawing updated as per client comments	CS	OW	SM
B	19.05.2025	Boundary removed	CS	OW	SM
A	10.04.2025	Preliminary Issue	CS	OW	SM
REV	DATE	DESCRIPTION	DRN	CHKD	APRD

Issue Status

<input type="checkbox"/> CONCEPT	<input type="checkbox"/> CONSTRUCTION
<input checked="" type="checkbox"/> PRELIMINARY	<input type="checkbox"/> AS BUILT
<input type="checkbox"/> TENDER	<input type="checkbox"/> H&S FILE ISSUE

Client
GREEN HILL SOLAR FARM LTD

Project
GREEN HILL SOLAR FARM

Drawing Title

CABLE ROUTE ACCESS 23
GENERAL ARRANGEMENT & VEHICLE
TRACKING


Scale @ A1	Drwn CS	Chkd OW
As shown	Aprd SM	Date APR 2023

Drawing Ref	Rev
23061-KMC-XX-CR23-DR-CH-0001	0


NOTE:
SPEED LIMIT OF ROAD **60mph**



kmc
transport planning

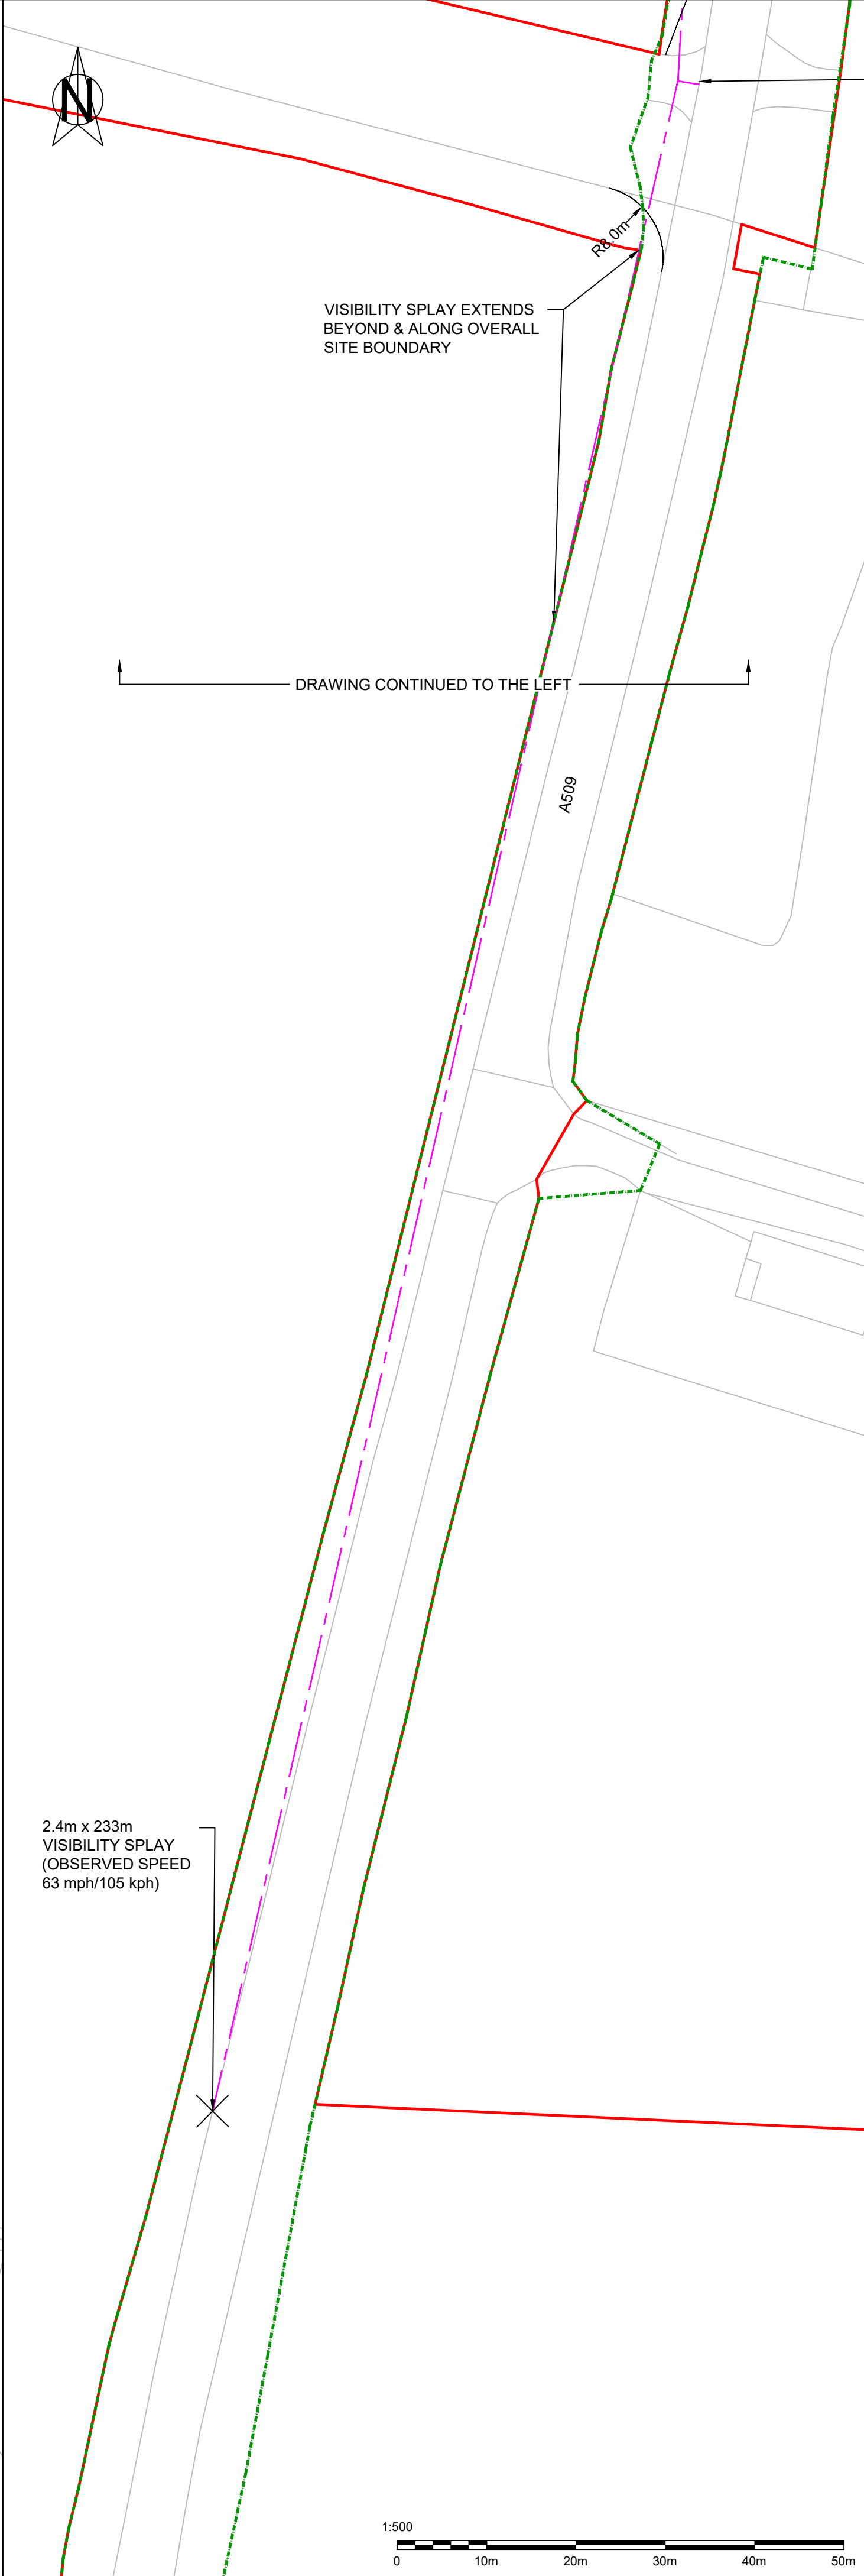

NOTE:
SPEED LIMIT OF ROAD 60mph

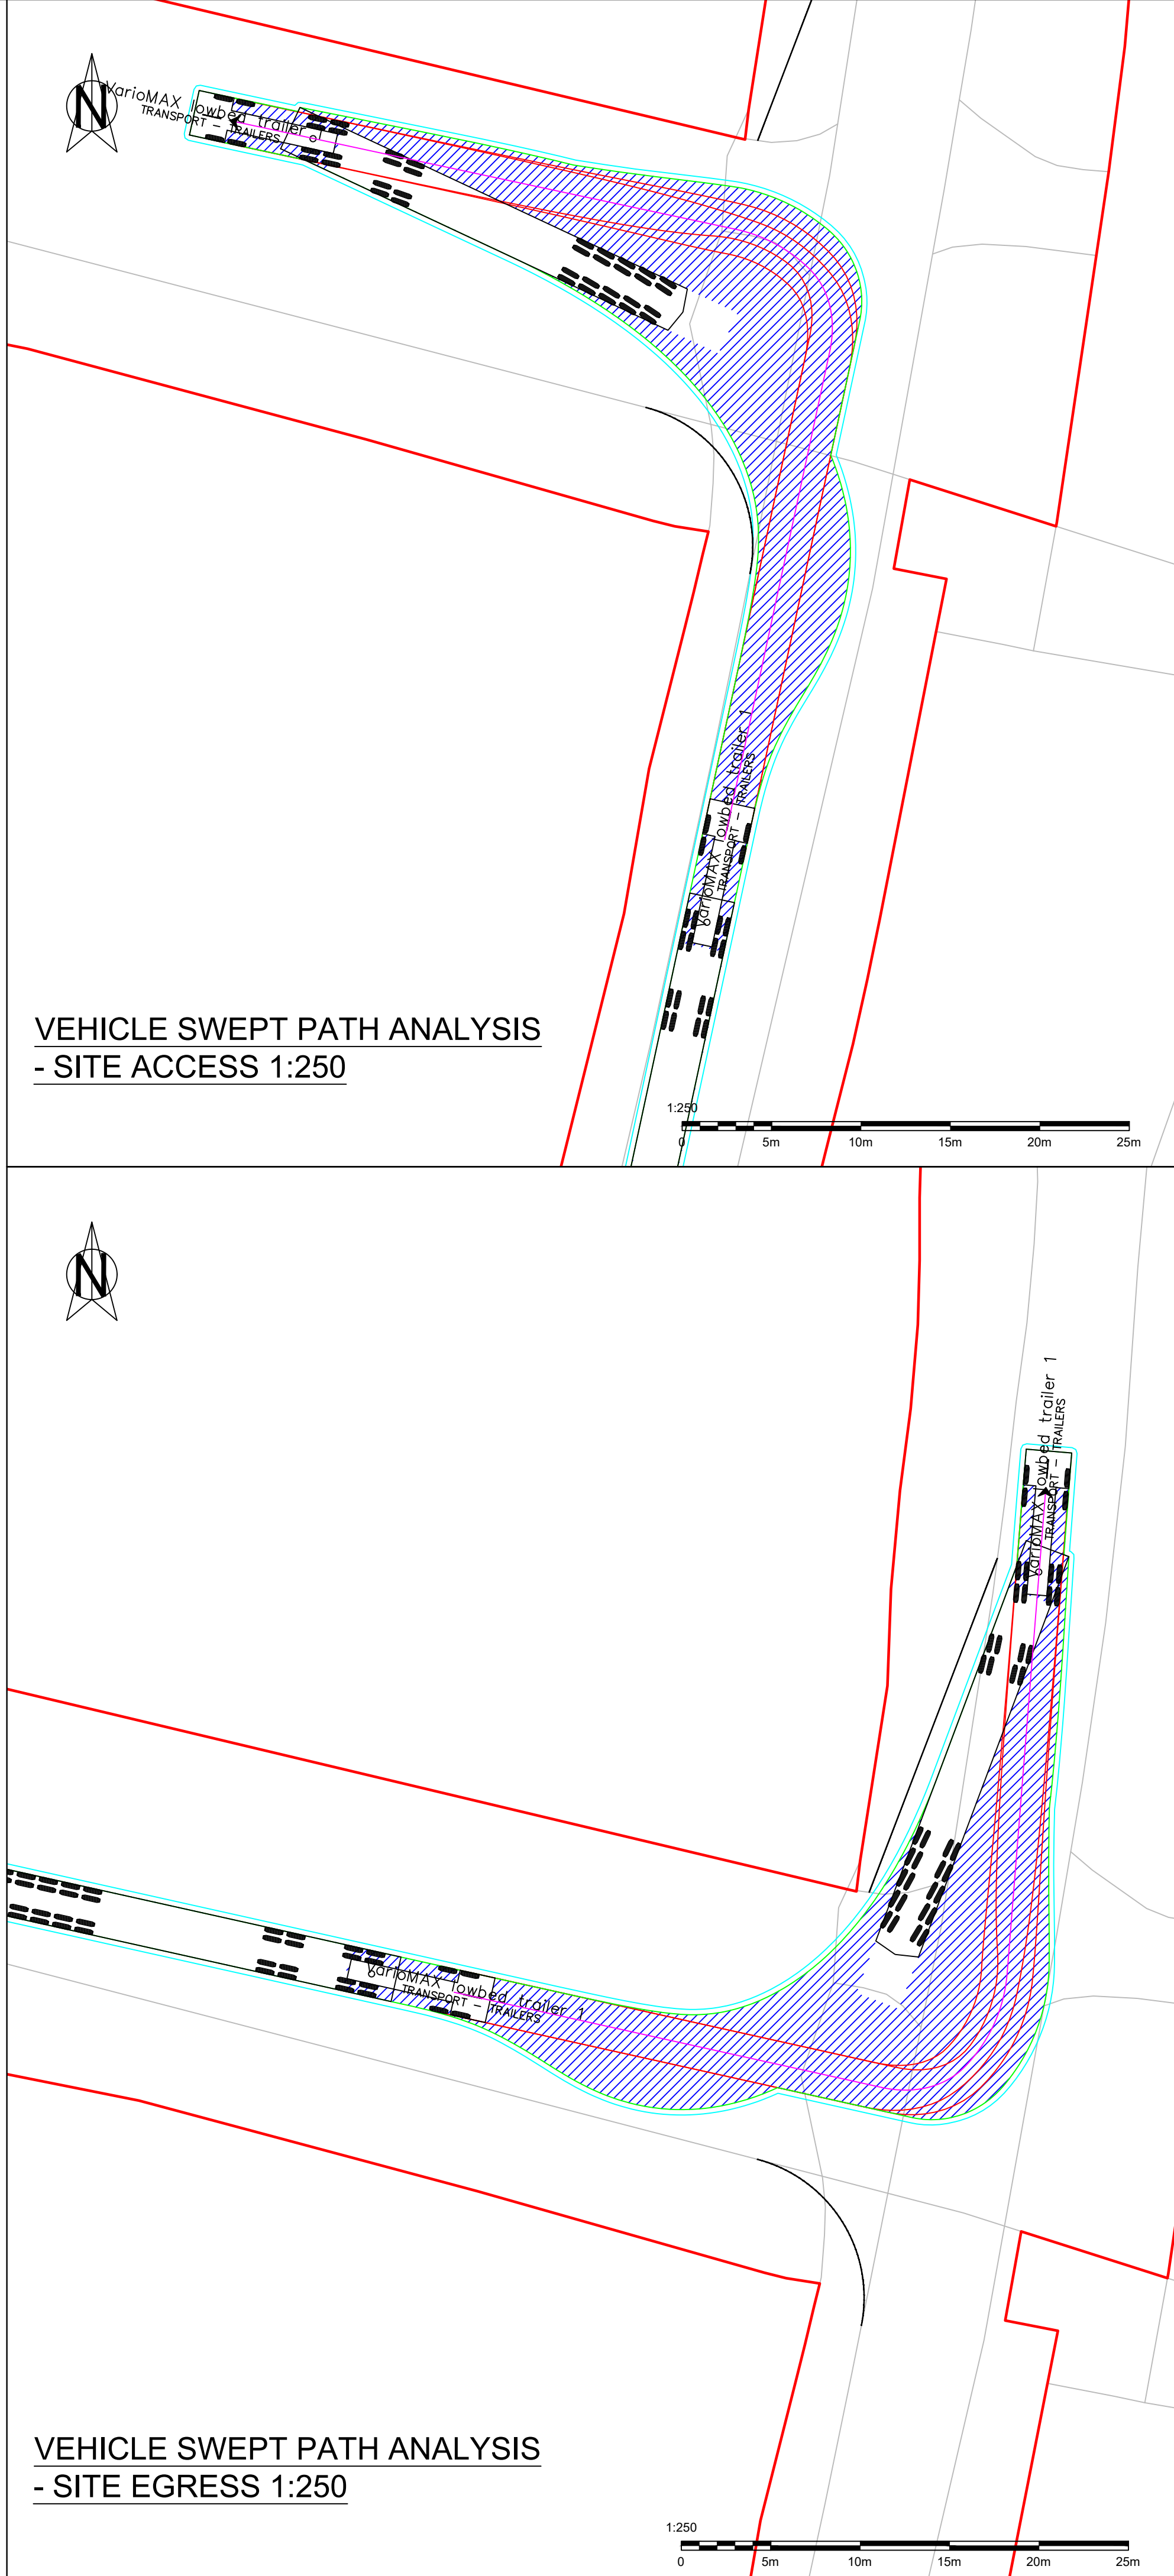

NOTES :

1. (C) This drawing is copyright.
2. All dimensions to be checked on site.
3. Do not scale from this drawing; only figured dimensions are to be worked from.
4. Any discrepancies must be reported immediately before proceeding.
5. This drawing to be read & printed in colour.
6. Ordnance Survey, (c) Crown Copyright 2024. All rights reserved. Licence number 100022432.

KEY PLAN
1:200000@A1

KEY:

- SITE BOUNDARY
- TRAFFIC SURVEY LOCATION
- HIGHWAY BOUNDARY
- VISIBILITY SPLAY EXTENT
- EXISTING LAYOUT
- PROPOSED EDGE OF ACCESS
- EXISTING VEGETATION
- EXTENT OF VEGETATION REMOVAL
- EXISTING CONTOURS

VEHICLE PROFILE:

VEHICLE ANALYSIS KEY:

- VEHICLE PATH & DIRECTION
- VEHICLE BODY ENVELOPE
- VEHICLE FRONT WHEEL PATH
- 0.3m VEHICLE BUFFER ZONE AROUND TRACKING

D	03.12.2025	Drawing updated as per client comments	CS	OW	SM
C	19.05.2025	Visibility splay updated	CS	OW	SM
B	10.04.2025	Boundary updated, Drawing continued	CS	OW	SM
A	11.03.2025	Preliminary issue	CS	LF	SM

REV	DATE	DESCRIPTION	DRN	CHKD	APRD

Issue Status

<input type="checkbox"/> CONCEPT	<input type="checkbox"/> CONSTRUCTION
<input type="checkbox"/> PRELIMINARY	<input type="checkbox"/> AS BUILT
<input type="checkbox"/> TENDER	<input type="checkbox"/> HAS FILE ISSUE

Client
GREEN HILL SOLAR FARM LTD

Project
GREEN HILL SOLAR FARM

Drawing Title
CABLE ROUTE ACCESS 24
GENERAL ARRANGEMENT & VEHICLE TRACKING

Scale @ A1	Drawn	CS	Chkd	OW
As shown	Aprd	SM	Date	MAR 2025

Drawing Ref	Rev
23061-KMC-XX-CR24-DR-CH-0001	D

kmc
transport planning

Appendix D Abnormal Load Report



Abnormal Indivisible Load Access to Green Hill Solar Project Substations – High Level Summary Document

Prepared for Island Green Power (IGP)





IGP I 23-1218 Green Hill Solar I AIL Access Summary I 17.04.25

NAME	SIGNATURE	DATE
Prepared by:		17.04.25
Checked by:		17.04.25
Approved by:		17.04.25

DISCLAIMER

Any conclusions, calculations or findings presented here should not be changed or altered.

COPYRIGHT AND NON-DISCLOSURE NOTICE

The contents and layout of this report are subject to copyright owned by Wynns Ltd save to the extent that copyright has been legally assigned by us to another party or is used by Wynns Ltd under licence. To the extent that we own the copyright in this report, it may not be copied or used without our prior written agreement for any purpose other than the purpose indicated in this report.

The methodology (if any) contained in this report is provided to you in confidence and must not be disclosed or copied to third parties without the prior written agreement of Wynns Ltd. Disclosure of that information may constitute an actionable breach of confidence or may otherwise prejudice our commercial interests. Any third party who obtains access to this report by any means will, in any event, be subject to the Third Party Disclaimer set out below.

THIRD PARTY DISCLAIMER

Any disclosure of this report to a third party is subject to this disclaimer. The report was prepared by Wynns Ltd at the instruction of, and for use by, our client named on the front of the report. It does not in any way constitute advice to any third party who is able to access it by any means. Wynns Ltd excludes to the fullest extent lawfully permitted all liability whatsoever for any loss or damage howsoever arising from reliance on the contents of this report. We do not however exclude our liability (if any) for personal injury or death resulting from our negligence, for fraud or any other matter in relation to which we cannot legally exclude liability.

DOCUMENT REVISIONS

Issue	Date	Details
<input type="checkbox"/>	17.04.25	First Issue
<input type="checkbox"/>		
<input type="checkbox"/>		

Contents

1.	Introduction	2
2.	Transport Drawings	2
3.	Green Hill Solar Project Individual Summary Reports	6
3.1.	Green Hill A (Old)	6
3.2.	Green Hill B (Holcot)	11
3.3.	Green Hill C (Sywell)	15
3.4.	Green Hill E (Mears Ashby)	20
3.5.	Green Hill F (Bozeat)	24
3.6.	Green Hill G (Warrington)	29
3.7.	Grendon BESS (Grendon)	33
3.8.	Cable Drum Highway Access Location Summary	38



1. Introduction

- 1.1. This document includes high level summary reports in respect to Abnormal Indivisible Loads (AIL) access to the proposed substations that are expected to be required for the Green Hill Solar Project.
- 1.2. This will require deliveries of transformer units to the following sites.
 - Green Hill A (Old) – 95Te Transformer
 - Green Hill B (Holcot) – 65Te Transformer
 - Green Hill C (Sywell) – 155Te and 183Te Transformers
 - Green Hill E (Mears Ashby) – 95Te Transformer
 - Green Hill F (Bozeat) – 95Te Transformer
 - Green Hill G (Warrington) – 95Te Transformer
 - Grendon BESS (Grendon) – 155Te and 183Te Transformers
- 1.3. The report considers access to the proposed onshore substation in terms of AIL transportation of the main transformers and cable drums. Wider traffic and transport for Construction and Use vehicles is not within the scope of this document which details the issues on access for heavy transformers and cable drums only.
- 1.4. The report highlights preferred AIL access routes for transformer AILs via the public road network as far as is possible to date and highlights where additional remedial works will be necessary.
- 1.5. The report includes reference to the responses of highway and structural authorities where applicable including Northamptonshire, Milton Keynes City Council, National Highways Area 7 and National Highways East Region. The high level summary is intended to inform planning documentation. A more detailed report discussing the various issues raised and routes rejected will be issued to Island Green Power (IGP) under separate cover. This will include more information on legislative requirements, route negotiability and the structural status of the routes.

2. Transport Drawings

- 2.1. The anticipated transport dimensions of the transformers for each of the substation location are shown below in Table 1 as is the indicative AIL transport arrangement that has been used for initial consultation with highway authorities that are reproduced on the following pages. These are based on standard AIL transport configuration that are generally used for transformers of the dimensions stated.
- 2.2. Drawings of indicative cable drum trailer arrangements are also included within this report.




Table 1 Transformer Transport Dimensions and Trailer Arrangements

Site	Length (mm)	Width (mm)	Height (mm)	Weight (kgs)	Transport Arrangements
A	7600	2700	4500	95,000kgs	5 bed 5 trailer as shown in drawing number 23-1218.TC03
B	7000	2600	4000	65,000kgs	5 bed 5 trailer as shown in drawing number 23-1218.TC03
C	10000	4000	4900	183,000kgs	16 axle girder frame as shown in drawing number 23-1218.TC02 and 20 axle girder frame as shown in drawing number 23-1218.TC01
E	7600	2700	4500	95,000kgs	5 bed 5 trailer as shown in drawing number 23-1218.TC03
F	7600	2700	4500	95,000kgs	5 bed 5 trailer as shown in drawing number 23-1218.TC03
G	7600	2700	4500	95,000kgs	5 bed 5 trailer as shown in drawing number 23-1218.TC03
Grendon BESS	10000	4000	4900	183,000kgs	16 axle girder frame as shown in drawing number 23-1218.TC02 and 20 axle girder frame as shown in drawing number 23-1218.TC01
Cable Drum Sites	3800	4500	4500	30,000kgs	4 axle modular reeling trailer as shown in drawing number 23-1218.TC04 and 4axle spooling trailer as shown in drawing number 23-1218.TC03




Attachment 1


Transport Arrangements

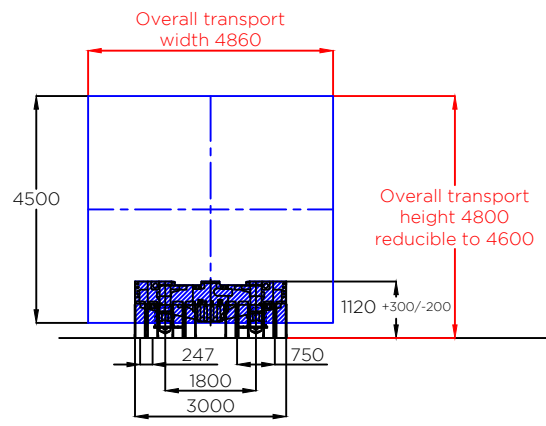


Profile view
Scale 1:150

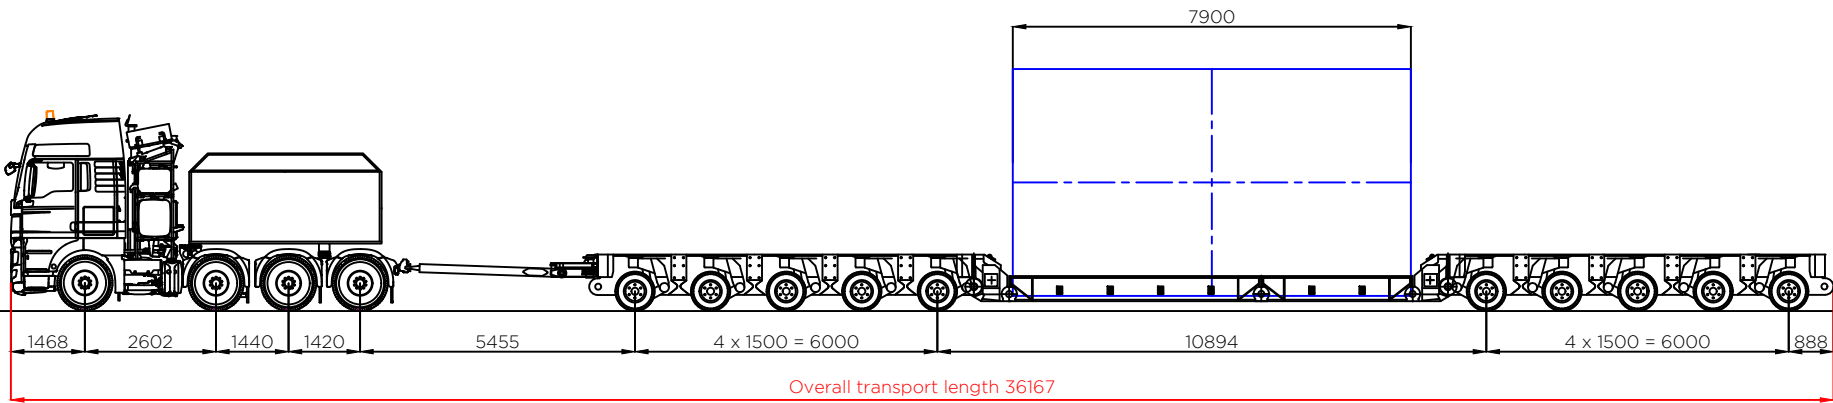


Elevation view - 5 axle bed 5 axle draw bar trailer - concept model only
Indicative 100 te transformer
Scale 1:150

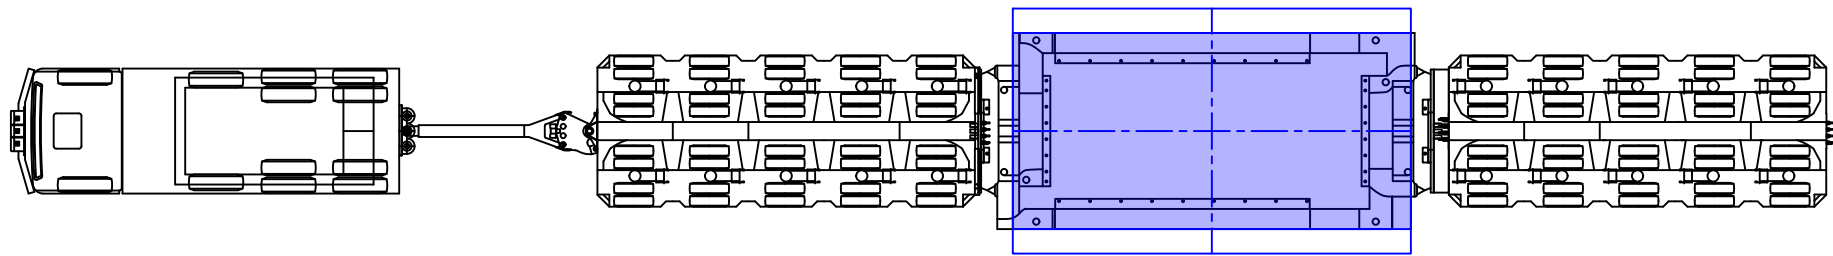

Plan view - 5 axle bed 5 axle draw bar trailer - concept model only
Indicative 100 te transformer
Scale 1:150



Vertical curve negotiability
information based on
hauliers literature
Scale 1:600

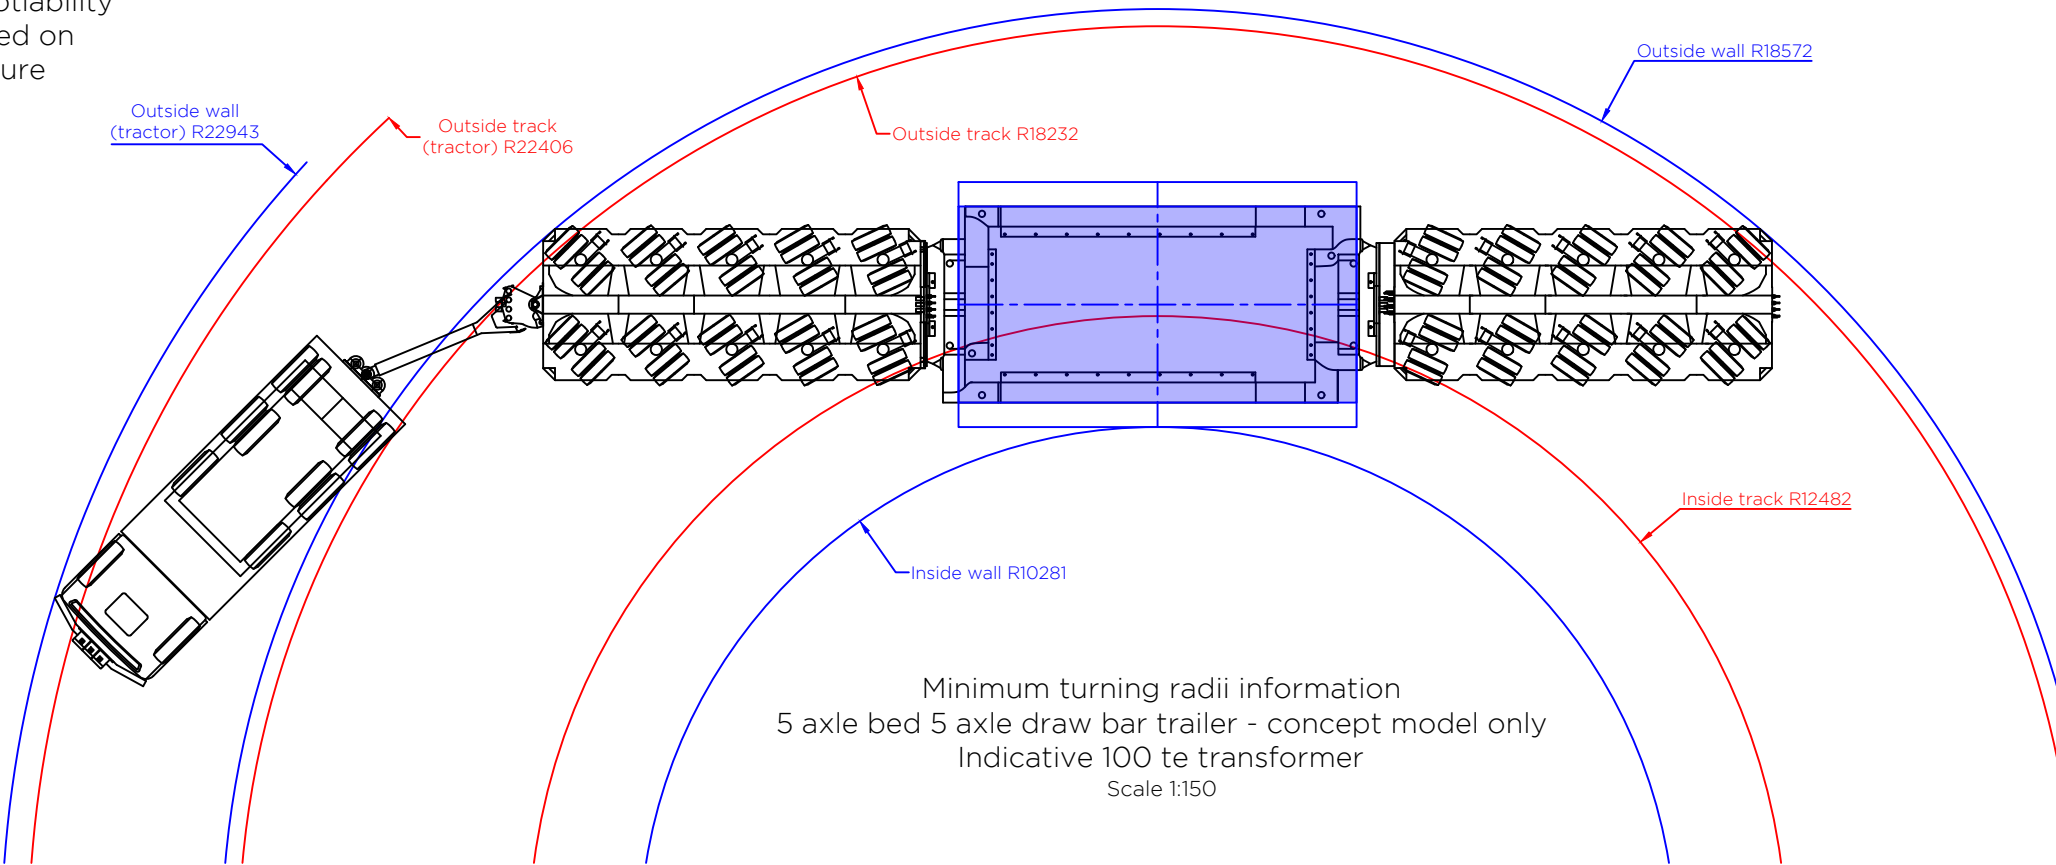


Minimum turning radii information
5 axle bed 5 axle draw bar trailer - concept model only
Indicative 100 te transformer
Scale 1:150

Load table	
5 axle bed 5 axle draw bar trailer	
Self weight of transformer	100.0 te
Self weight of trailer	Say 46.0 te
Self weight of aux. steelwork (for L&S)	0.0 te
Total combined weight	146.0 te
Load per axle line	14.6 te
Load per axle	7.3 te
Load per wheel (4 per axle)	1.83 te
Overall ground bearing pressure	4.06 te/m ²
Tractor (40 te)	
Front axle	7.0 te
Second steer	7.0 te
Rear axle	13.0 te
Rear axle	13.0 te

- Notes:
- [1] The figures shown above are representative of the transport configuration portrayed. However as tractor and trailer arrangements vary then the loads and dimensions indicated should be treated as probable values.
- [2] Actual dimensions, including axle spacing and mean running height, may vary slightly depending on manufacturer of trailer deployed.
- [3] All linear measures in millimetres unless stated otherwise.
- [4] Indicative transformer shown only.
- [5] Running height dependent upon tank base and transport lug arrangement.

1		
0	14.03.23	Issued for comment
Rev.	Date	Amendments
Revisions		

Prepared by:



Shaftesbury House, 2 High Street,
Eccleshall, Stafford, ST21 6BZ
Tel: (01785) 850411

Independent Transportation Engineers

Client:



Project:

Solar Farm Northampton (Grendon)


Title:

Indicative transport configuration
Indicative 100.0 te transformer carried on
5 axle bed 5 axle draw bar trailer
showing minimum turning radii


Drawing status:		
Final report		
Scale (A3): As shown	Drawn By: MTO	Checked By: ---
Dwg. no: 23-1218.TC03	Sheet: 1 of 1	Rev: 0

© Wynns Limited. This drawing is not to be reproduced in whole or in part, in any form or by any means, without prior written consent.


P:\Clients\Existing Clients\Island Green Power\23-1218 Solar Farm in Northamptonshire (Grendon)\Transport Configurations\23-1218.TC03 Solar Farm Northampton (Grendon) 100 te transformer 5 bed 5 R0.dwg

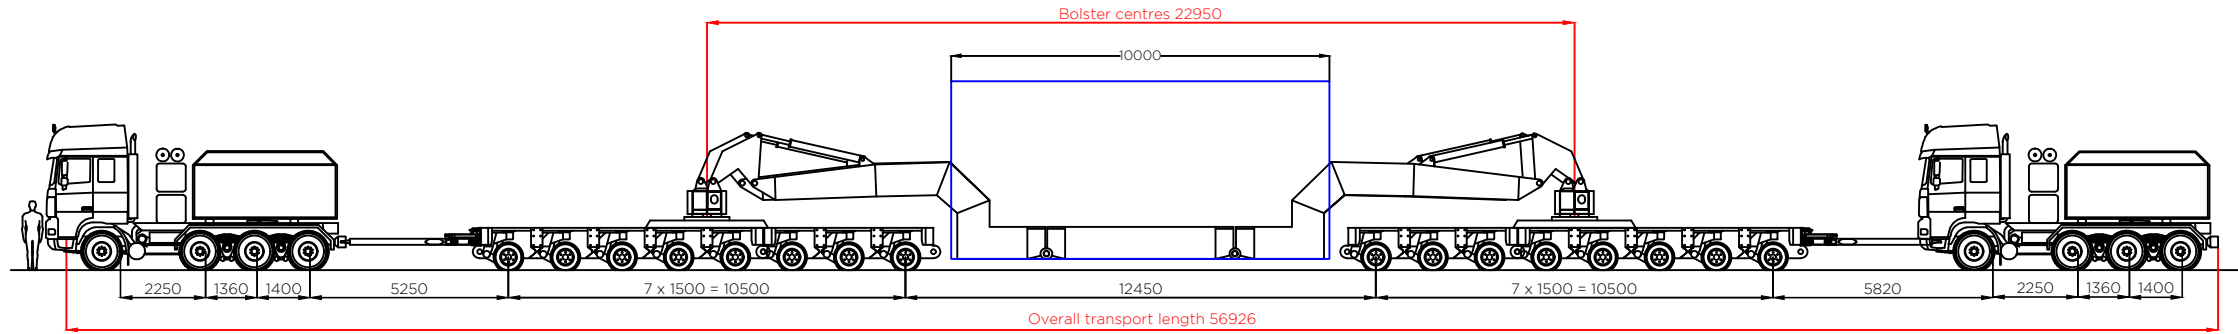

Side Elevation - 16 axle girder frame trailer - concept model only
Indicative 183 te transformer
Scale 1:200





Plan View - 16 axle girder frame trailer - concept model only
Indicative 183 te transformer
Scale 1:200

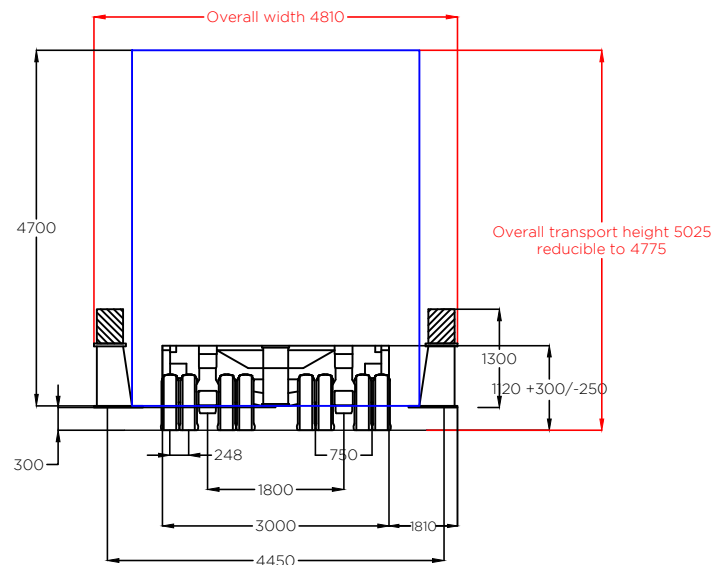


Profile view
Indicative 183 te transformer
Scale 1:100

NOTE: Final Design/Transport Arrangement to be Determined.
Detail is Illustrative Only.



Vertical curve negotiability information
based on manufacturers literature
(Scale 1:200)

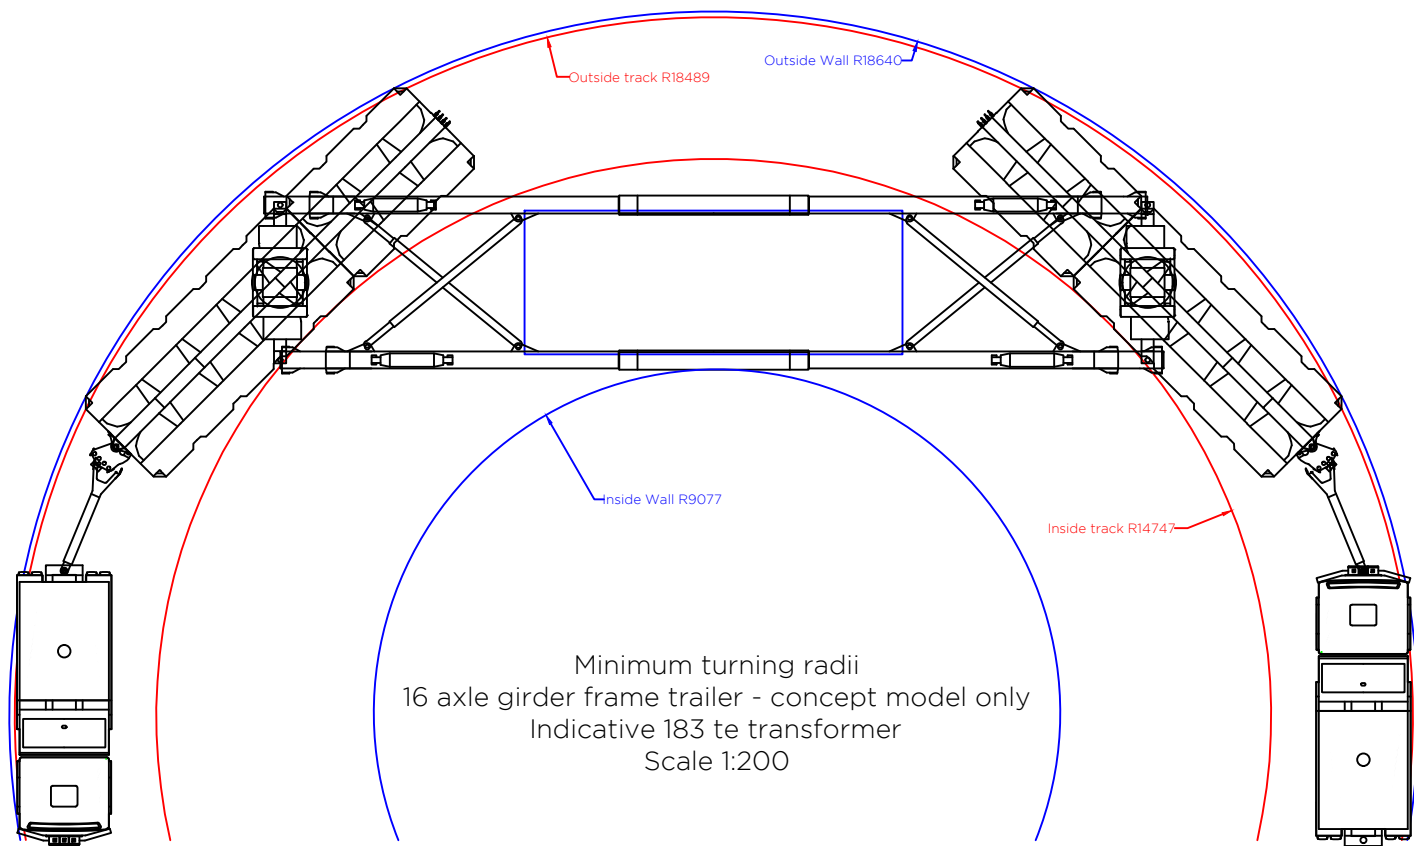

Minimum turning radii
16 axle girder frame trailer - concept model only
Indicative 183 te transformer
Scale 1:200

Load Table

16 axle girder frame trailer

Self weight of load	183.0 te
Self weight of trailer	86.8 te
Self weight of aux. steelwork (for L&S)	0.0 te
Total combined weight	269.6 te
Load per trailer	134.8 te
Load per axle line (2 axles per line)	16.85 te
Load per wheel (4 wheels per axle)	2.11 te
Overall ground bearing pressure	4.28 te/m ²

Tractors x2 (42 te)

Front axle	8.0 te
Second steer	10.0 te
Rear axle	12.0 te
Rear axle	12.0 te

Notes:-

[1] The figures shown above are representative of the transport configuration portrayed. However as tractor and trailer arrangements vary then the loads and dimensions indicated should be treated as probable values.

[2] Actual dimensions, including axle spacing and mean running height, may vary slightly depending on manufacturer of trailer deployed.


[3] All linear measures in millimeters unless stated otherwise.

[4] Transformer drawing indicative only.

1		
0	03.12.24	Issued for comment
Rev.	Date	Amendments

Revisions

Prepared By:



Shaftesbury House, 2 High Street,
Eccleshall, Stafford, ST21 6BZ
Tel: (01785) 850411

Independent Transportation Engineers

Client:



Project:

Solar Farm Northamptonshire (Grendon)

Title:

Indicative Transport Configuration
183 te transformer carried within
16 axle girder frame trailer
showing minimum turning radii





Drawing Status:

Final Report

Scale (A3): As shown	Drawn By: MTO	Checked By: ---
DWG. No: 23-1218.TC02	Sheet: 1 of 1	Rev: 0

Wynns Limited. This drawing is not to be reproduced in whole or in part, in any form or by any means, without prior written consent.

P:\Clients\Existing Clients\Island Green Power\23-1218 Solar Farm in Northamptonshire (Grendon)\Transport Configurations\23-1218.TC02 Solar Farm Northampton (Grendon) 183te transformer 16 Axle Girder Frame.R0.dwg

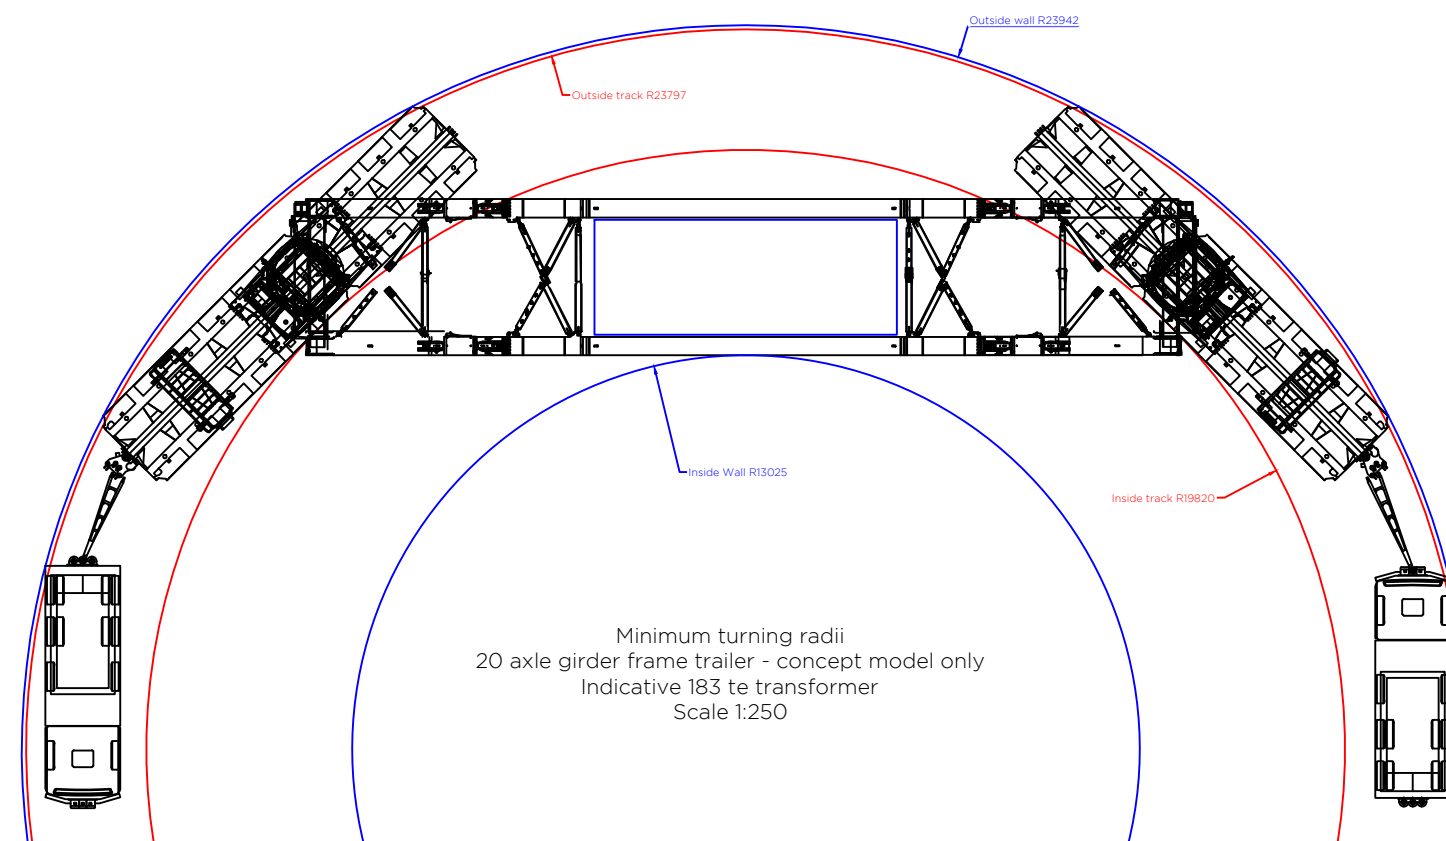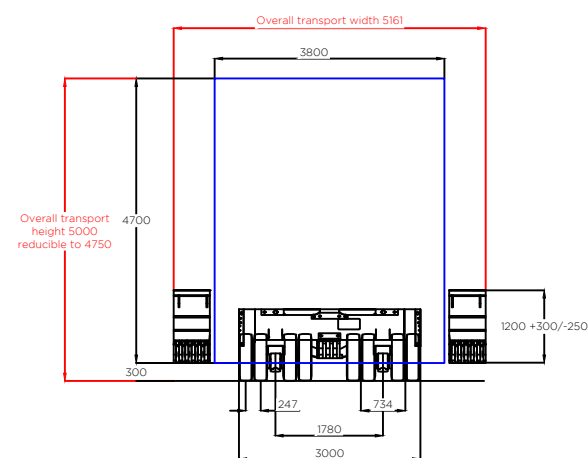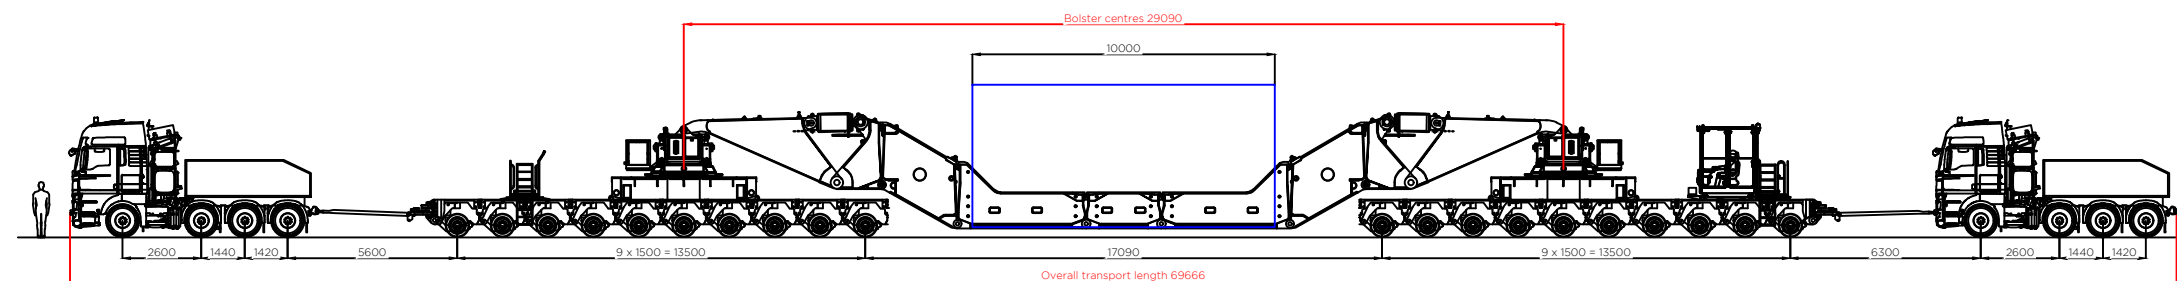

Load table	
20 axle girder frame trailer	
Self weight of transformer	183.0 te
Self weight of trailer	134.0 te
Self weight of aux. steelwork (for L&S)	0.0 te
Total combined weight	317.0 te
Load per trailer	158.50 te
Load per axle line	15.85 te
Load per axle	7.92 te
Load per wheel (4 per axle)	1.98 te
Overall ground bearing pressure	3.91 te/m ²
Tractor(s) (42 te)	
Front axle	7.0 te
Second steer	8.0 te
Rear axle	13.5 te
Rear axle	13.5 te

Notes:-

[1] The figures shown above are representative of the transport configuration portrayed. However as tractor and trailer arrangements vary then the loads and dimensions indicated should be treated as probable values.

[2] Actual dimensions, including axle spacing and mean running height, may vary slightly depending on manufacturer of trailer deployed.

[3] All linear measures in millimeters unless stated otherwise.

[4] Transformer drawing indicative only.

1		
0	03.12.24	Issued for comment
Rev.	Date	Amendments

Prepared by:



Shaftesbury House, 2 High Street,
Eccleshall, Stafford, ST21 6BZ
Tel: (01785) 850411

Independent Transportation Engineers

Client:



Project:

Solar Farm Northamptonshire (Grendon)

Title:

Indicative Transport Configuration
183 te transformer carried within
20 axle girder frame trailer
showing minimum turning radii


Drawing status:

Final Report

Scale (A3): As shown	Drawn By: MTO	Checked By: ---
Dwg. no: 23-1218.TC01	Sheet: 1 of 1	Rev: 0


© Wynns Limited. This drawing is not to be reproduced in whole or in part, in any form or by any means, without prior written consent.

P:\Clients\Existing Clients\Island Green Power\23-1218 Solar Farm in Northamptonshire (Grendon)\Transport Configurations\23-1218.TC01 Solar Farm Northampton (Grendon) 183te transformer 20 Axle Girder Frame.R0.dwg

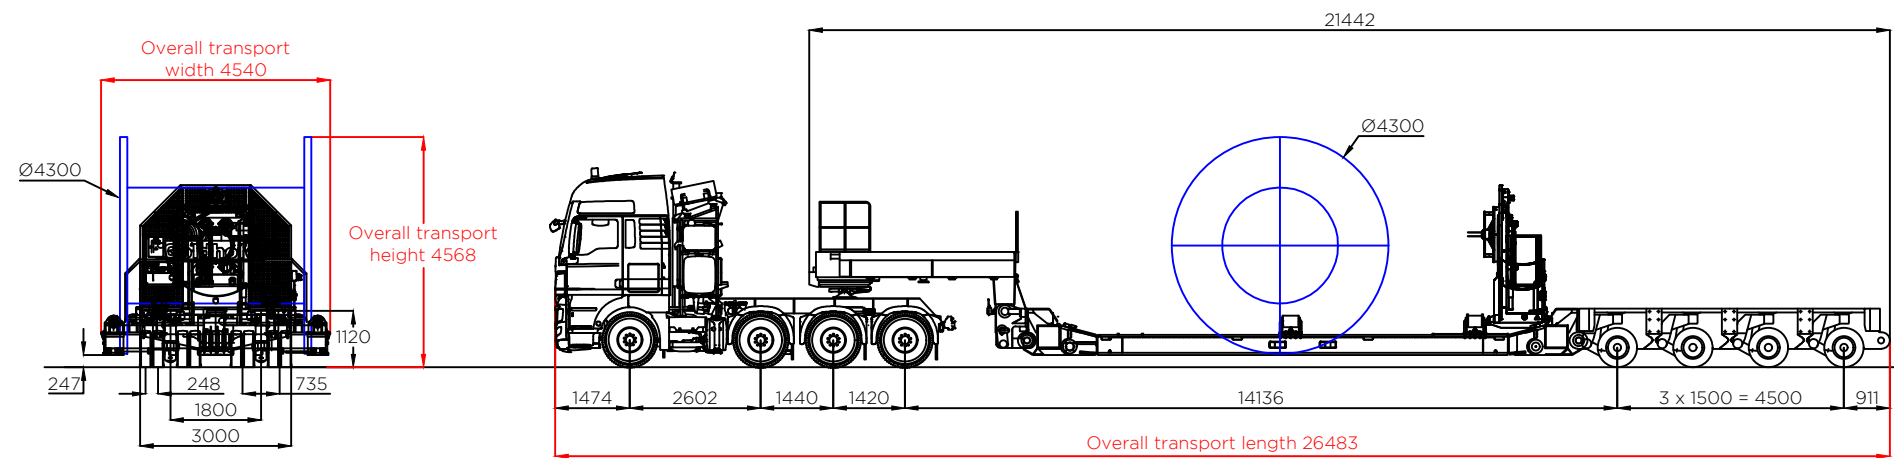


Profile view

Elevation view - 4 axle modular reeling trailer - concept model only
Indicative 30 te cable drum
Scale 1:150



Plan view - 4 axle modular reeling trailer - concept model only
Indicative 30 te cable drum
Scale 1:150

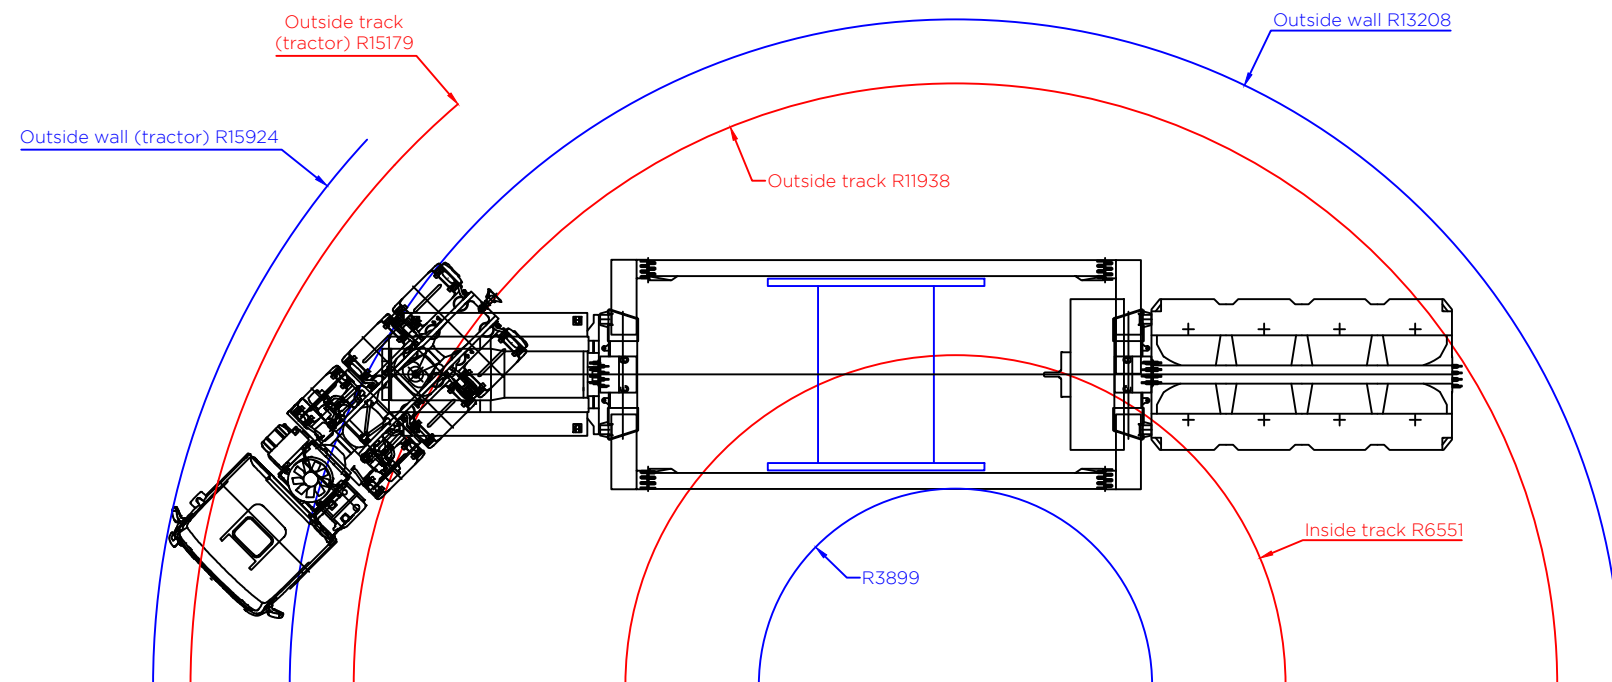

Minimum turning radii information
4 axle modular reeling trailer - concept model only
Indicative 30 te cable drum
Scale 1:150

Load table

4 axle modular reeling trailer

Self weight of cable drum	30.0 te
Self weight of trailer	33.3 te
Self weight of tractor	15.0 te
Total combined weight	78.3 te
Load per axle line (trailer)	10.55 te
Load per axle	5.28 te
Load per wheel (4 per axle)	1.32 te
Overall ground bearing pressure	3.13 te/m ²

Tractor (15 te)

Front axle	7.0 te
Second steer	8.0 te
Rear axle	10.55 te
Rear axle	10.55 te

Notes:

[1] The figures shown above are representative of the transport configuration portrayed. However as tractor and trailer arrangements vary then the loads and dimensions indicated should be treated as probable values.

[2] Actual dimensions, including axle spacing and mean running height, may vary slightly depending on manufacturer of trailer deployed.

[3] All linear measures in millimetres unless stated otherwise.

1		
0	14.04.25	Issued for comment
Rev.	Date	Amendments

Revisions

Prepared by:



Shaftesbury House, 2 High Street,
Eccleshall, Stafford, ST21 6BZ
Tel: (01785) 850411

Independent Transportation Engineers

Client:



Project:

Solar Farm Northampton (Grendon)

Title:

Indicative transport configuration
Indicative 30.0 te cable drum carried on
4 axle modular reeling trailer
showing minimum turning radii


Drawing status:

Final report

Scale (A3):	Drawn By:	Checked By:
As shown	MTO	ARP
Dwg. no:	Sheet:	Rev:
23-1218.TC04	1 of 1	0


© Wynns Limited. This drawing is not to be reproduced in whole or in part, in any form or by any means, without prior written consent.

P:\Clients\Existing Clients\Island Green Power\23-1218 Solar Farm in Northamptonshire (Grendon)\Transport Configurations\23-1218.TC05 Solar Farm Northampton 30t Cable Drum 4 Axle reeling trailer R0 - Copy.dwg

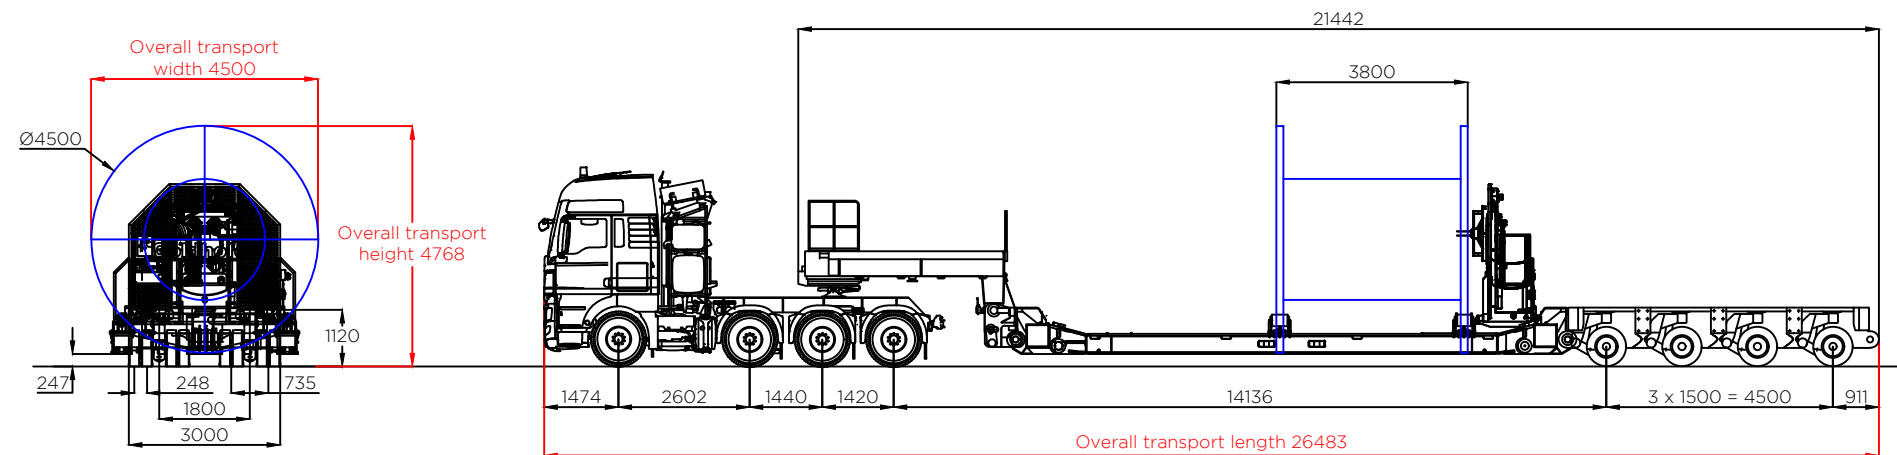


Profile view

Elevation view - 4 axle modular spooling trailer - concept model only
Indicative 30 te cable drum Scale 1:150



Plan view - 4 axle modular spooling trailer - concept model only
Indicative 30 te cable drum
Scale 1:150

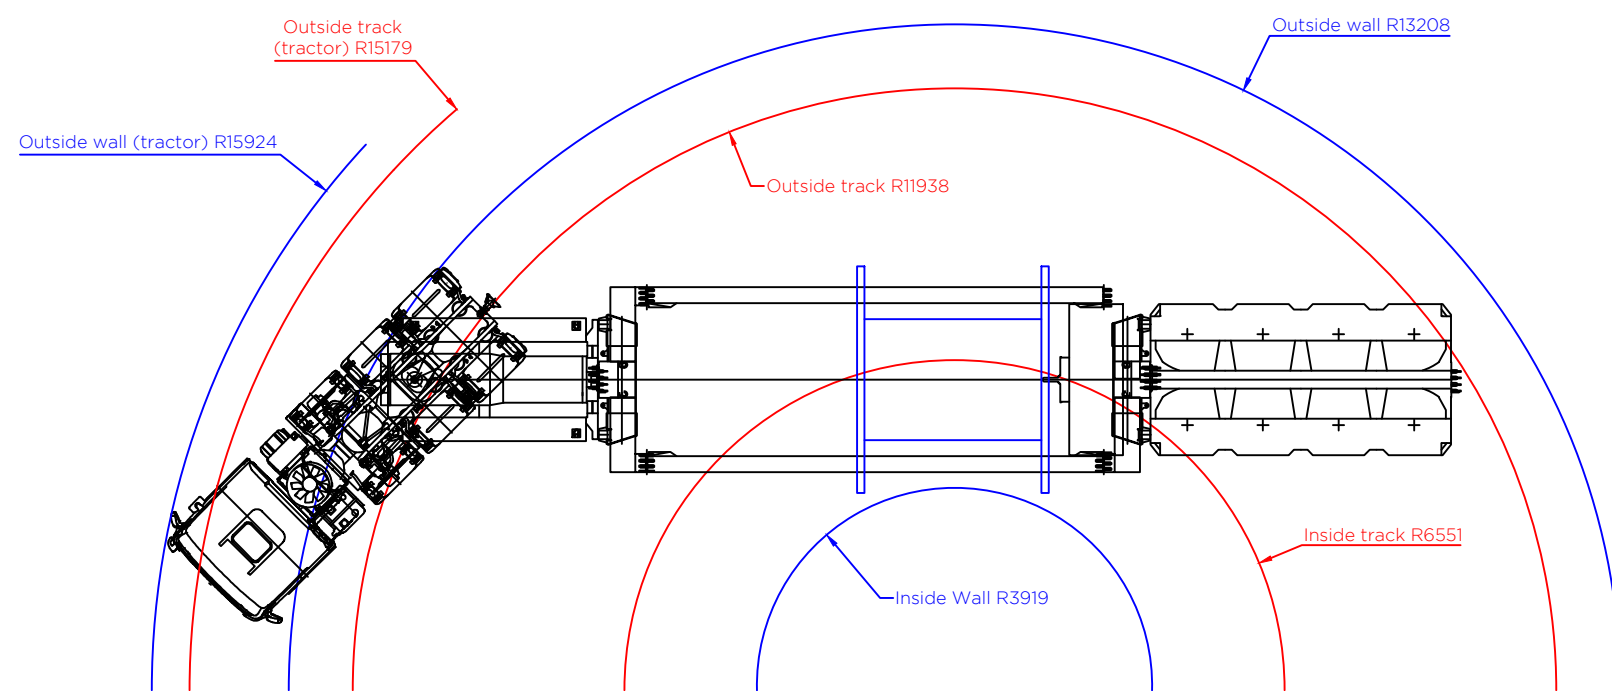

Minimum turning radii information
4 axle modular spooling trailer - concept model only
Indicative 30 te cable drum
Scale 1:150

Load table

4 axle modular spooling trailer

Self weight of cable drum	30.0 te
Self weight of trailer	33.3 te
Self weight of tractor	15.0 te
Total combined weight	78.3 te
Load per axle line (trailer)	10.55 te
Load per axle	5.28 te
Load per wheel (4 per axle)	1.32 te
Overall ground bearing pressure	3.13 te/m ²

Tractor (15 te)

Front axle	7.0 te
Second steer	8.0 te
Rear axle	10.55 te
Rear axle	10.55 te

Notes:

[1] The figures shown above are representative of the transport configuration portrayed. However as tractor and trailer arrangements vary then the loads and dimensions indicated should be treated as probable values.

[2] Actual dimensions, including axle spacing and mean running height, may vary slightly depending on manufacturer of trailer deployed.

[3] All linear measures in millimetres unless stated otherwise.

1		
0	14.04.25	Issued for comment
Rev.	Date	Amendments

Revisions

Prepared by:



Shaftesbury House, 2 High Street,
Eccleshall, Stafford, ST21 6BZ
Tel: (01785) 850411

Independent Transportation Engineers

Client:



Project:

Solar Farm Northampton (Grendon)

Title:

Indicative transport configuration
Indicative 30.0 te cable drum carried on
4 axle modular spooling trailer
showing minimum turning radii

Drawing status:

Final report

Scale (A3):	Drawn By:	Checked By:
As shown	MTO	ARP
Dwg. no:	Sheet:	Rev:
23-1218.TC04	1 of 1	0


© Wynns Limited. This drawing is not to be reproduced in whole or in part, in any form or by any means, without prior written consent.








P:\Clients\Existing Clients\Island Green Power\23-1218 Solar Farm in Northamptonshire (Grendon)\Transport Configurations\23-1218.TC04 Solar Farm Northampton 30t Cable Drum 4 Axle spooling trailer R0.dwg

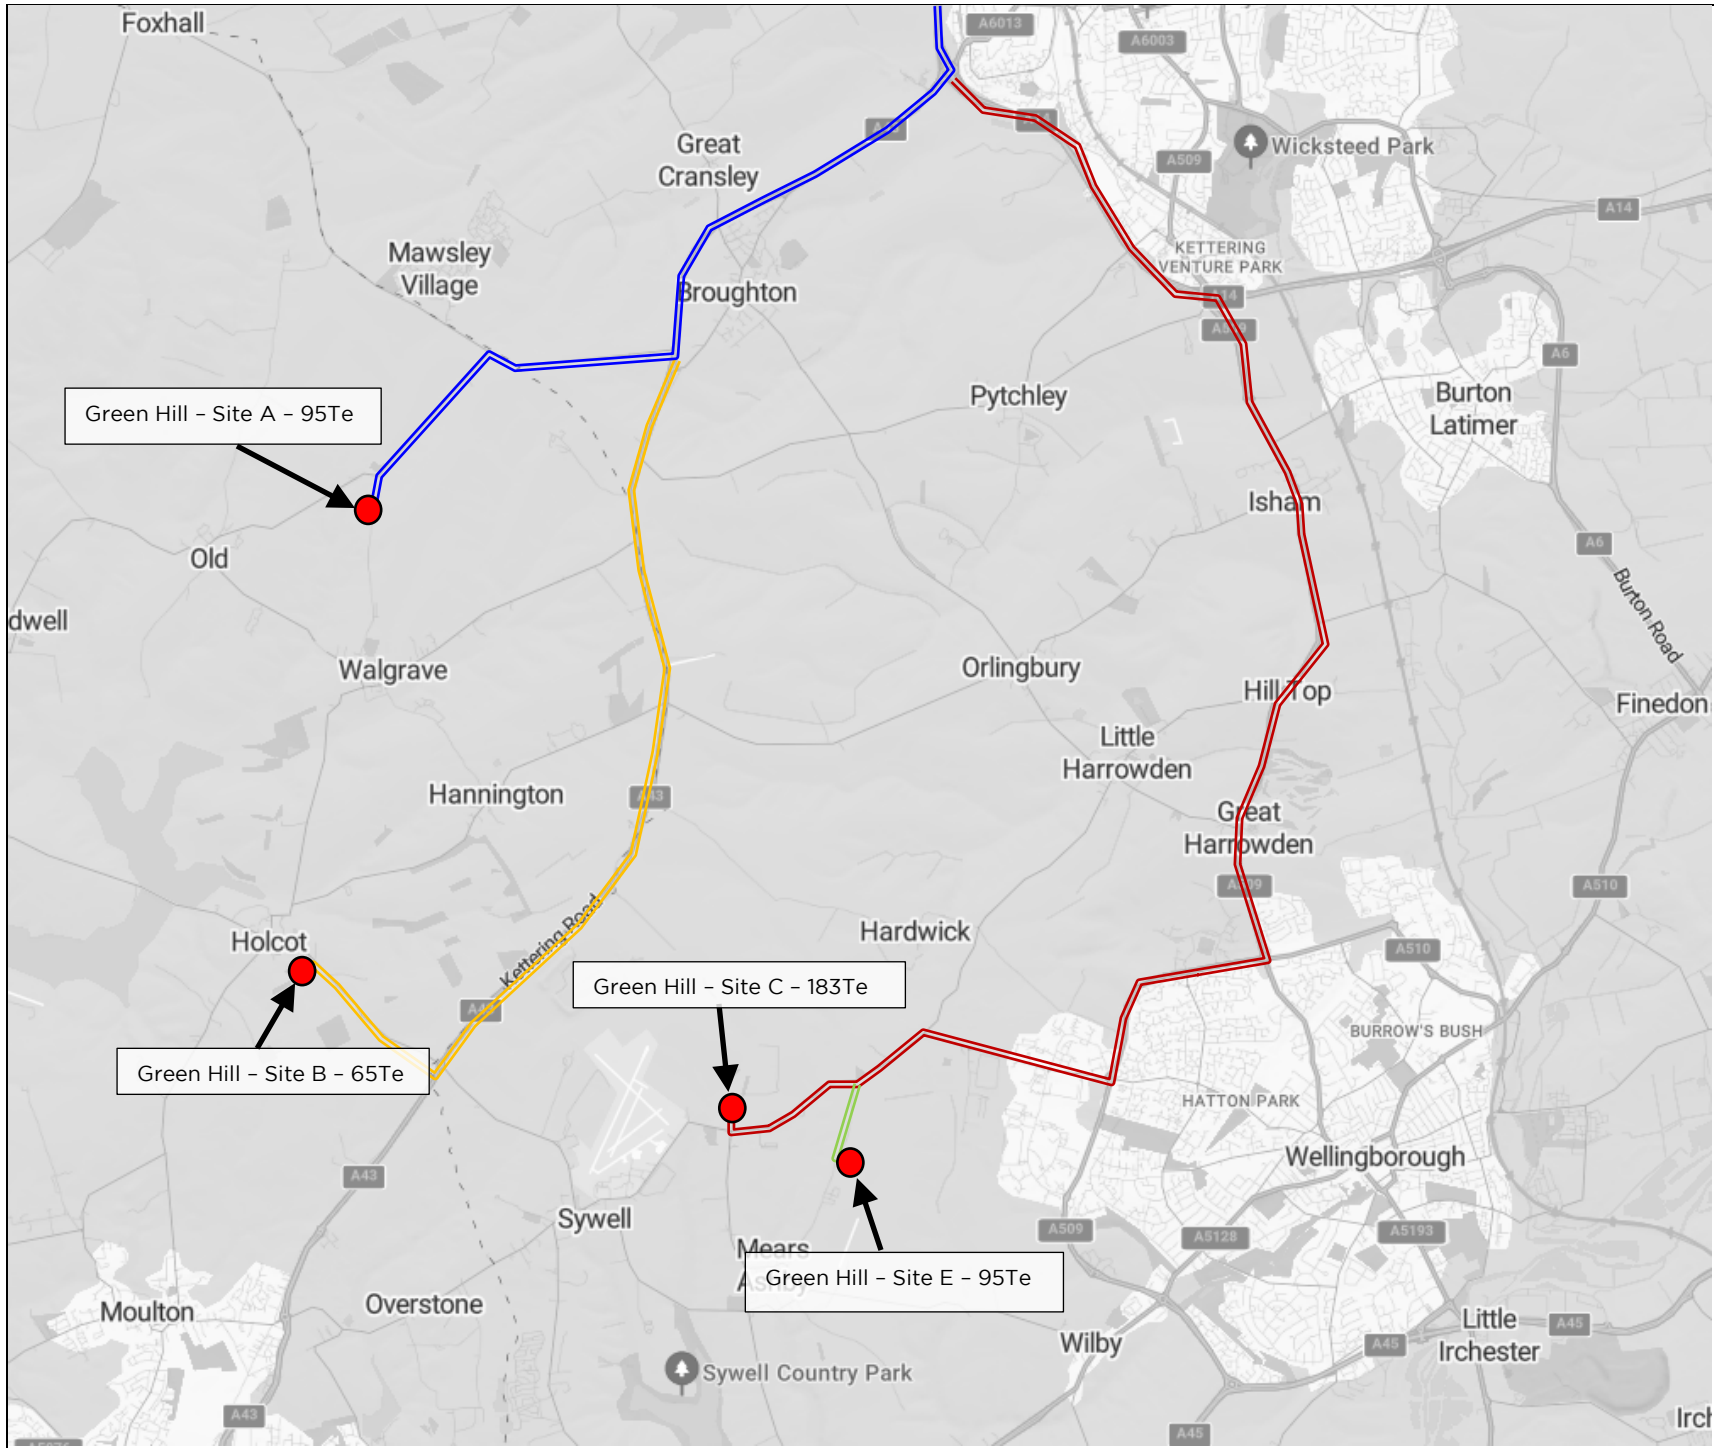








Attachment 2

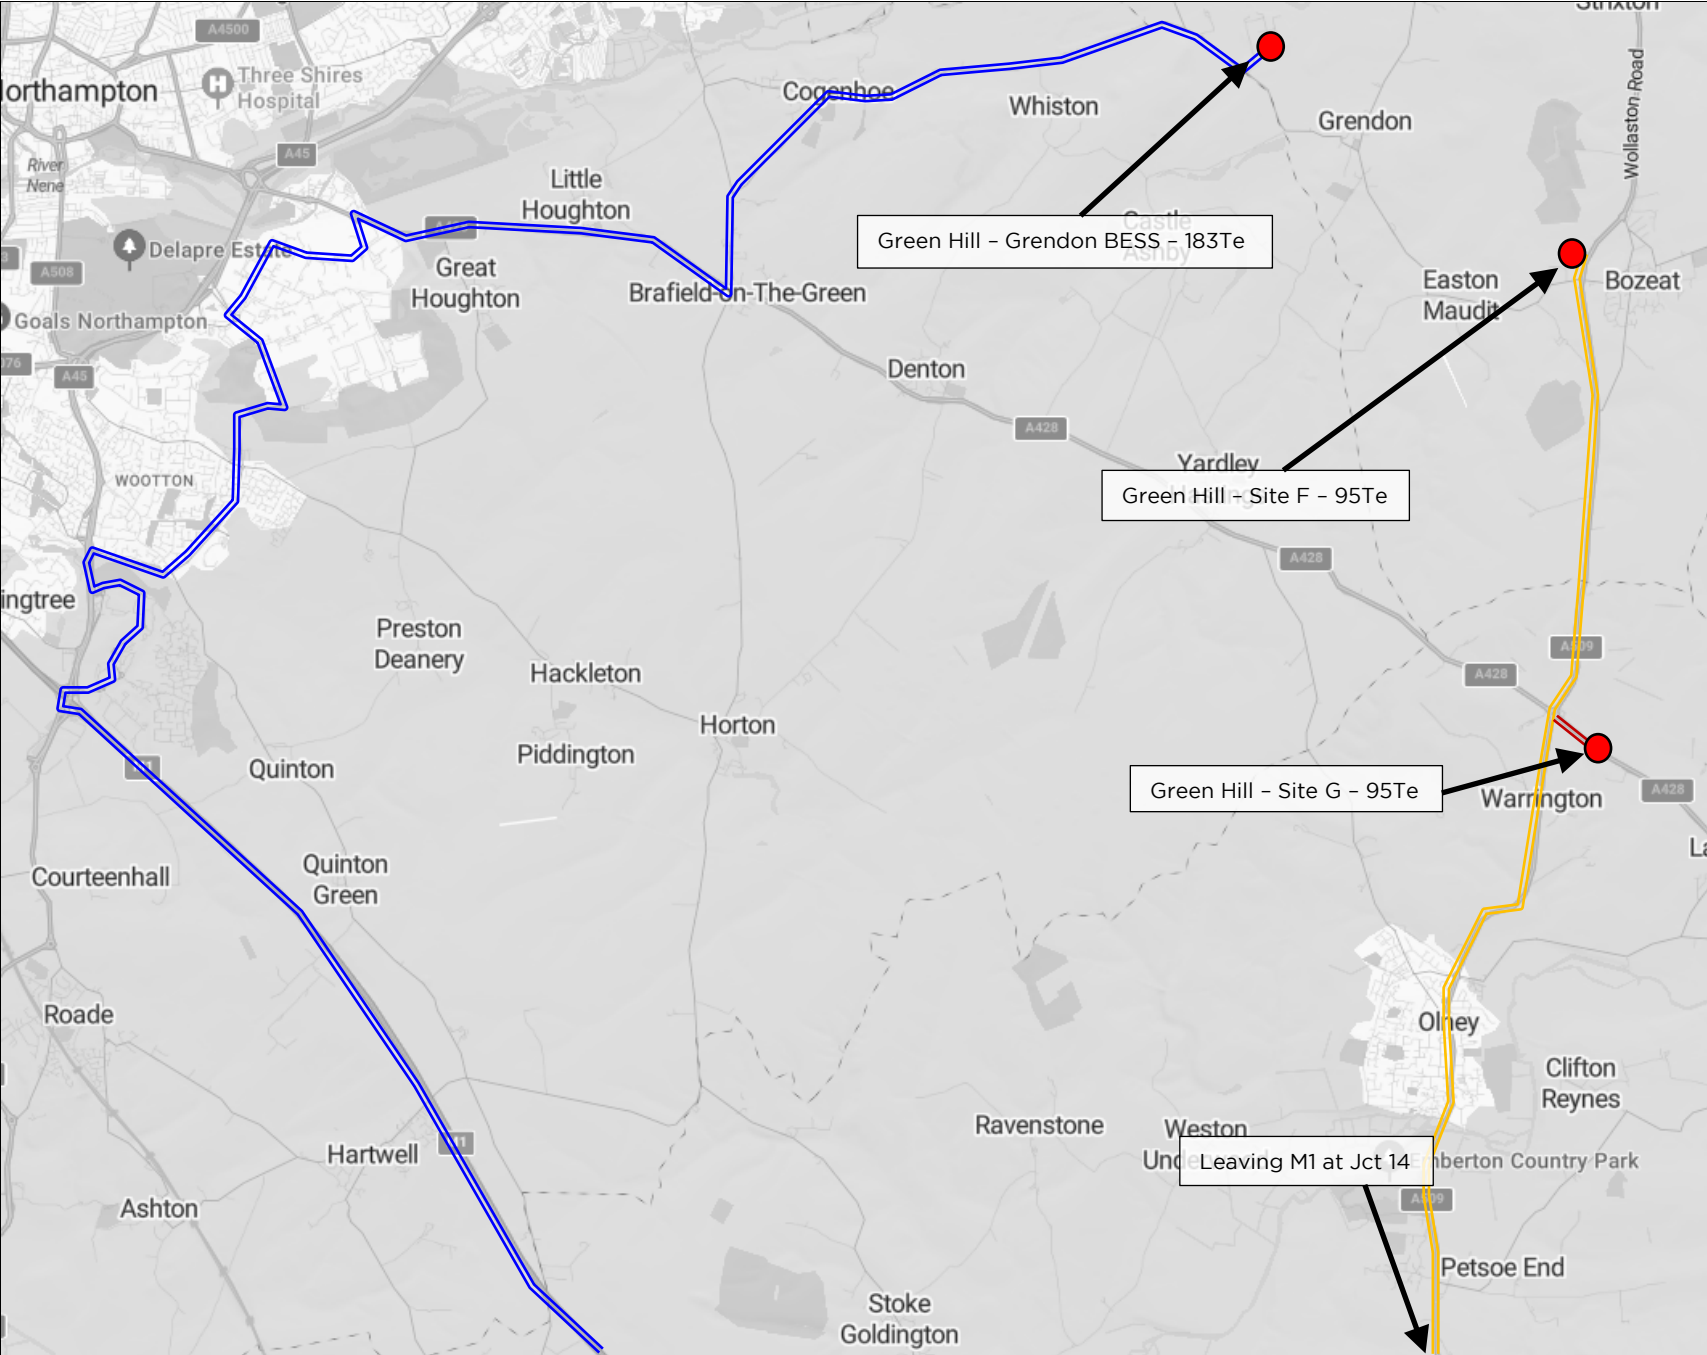Overview Map



Key		
	Route 1 to Green Hill - Site A	
	Route 2 to Green Hill - Site B	
	Route 3 to Green Hill - Site C	
	Route 4 to Green Hill - Site E	
	Sites for delivery of Transformers	
B		
A		
O	17.04.2025	First Issue
Rev	Date	Amendments:
Revisions		
<div><div>Wynns Ltd. Independent Transportation Engineers</div><div>Shaftesbury House, 2 High Street, Eccleshall, Stafford, ST21 6BZ. Tel: (01785) 850411</div></div>		
Client:		
<div></div>		
Project:		
Green Hill Solar		
Title:		
Map 1 - Routes to site locations - North of Wellingborough		
Drawing Status:		
Final Report		
Scale (A4): NTS	Drawn by: SMB	Checked by: ARP
Ref No.: 23-1218-Map1	Sheet: 1 of 2	Rev.: 0
© Wynns Ltd. This drawing is not to be reproduced in whole or in part in any form or by any means, without prior written consent.		
© Crown Copyright. All rights reserved. Licence No AL100035894		



Key		
	Route 5 to Green Hill - BESS site	
	Route 6 to Green Hill - Site F	
	Route 7 to Green Hill - Site G	
	Sites for delivery of Transformers	
B		
A		
O	17.04.2025	First Issue
Rev	Date	Amendments:
Revisions		
<div><div>Wynns Ltd. Independent Transportation Engineers</div><p>Shaftesbury House, 2 High Street, Eccleshall, Stafford, ST21 6BZ. Tel: (01785) 850411</p></div>		
Client: <div></div>		
Project: <div>Green Hill Solar</div>		
Title: <div>Map 1 - Routes to site locations - South of Wellingborough</div>		
Drawing Status: <div>Final Report</div>		
Scale (A4): NTS	Drawn by: SMB	Checked by: ARP
Ref No.: 23-1218-Map1	Sheet: 2 of 2	Rev.: 0
© Wynns Ltd. This drawing is not to be reproduced in whole or in part, in any form or by any means, without prior written consent.		
© Crown Copyright. All rights reserved. Licence No AL100035894		

3. Green Hill Solar Project Individual Summary Reports

3.1. Green Hill A (Old)

Site	Green Hill Solar - Green Hill A (Old)
Route Inspection and AIL Access Report Recently undertaken by Wynns?	Yes
Has Agreement in Principle (AIP) been provided by National Highways in line with the Water Preferred Policy	Not applicable as 100te nett transformer will be moved within STGO Category 3 and as such will not require Special Order permissions from National Highways.
National Highways AIP Reference Number	N/A
Proposed port Delivery	Port of Immingham The port of Immingham is well established for heavy project cargo and no issues are expected in respect to marine access. It should be noted that as the load is STGO it will not be specifically limited to Immingham as the closest port but Immingham does provide suitable facilities.
Maximum Transport Weight considered during the most recent report in line with future project requirements	Weight - 95te nett transformer Length - 7.60m Width - 2.70m Height - 4.5m
Typical trailer used in route clearance works	A 5 bed 5 trailer at 141te gross weight as shown in drawing number 23-1218.TC03.
Expected delivery date of next planned transformer if known	To be confirmed
Last Recorded Special Order Movement (according to available records)	No movements to this site as is a new development.

Site	Green Hill Solar - Green Hill A (Old)
Suggested route based on historical information	Exit A1 at junction of A47 and head west. (OS Grid Ref: TL 07537 99743) Turn left A43 towards Corby Turn left A14 Turn right A43 Turn right Mawsley Road Turn left Broughton Road to site (OS Grid Ref: SP 80419 74222)
Is a map available of the proposed route(s)?	Yes – See Attachment 3
Any Known Problems for AIL Access in terms of structures?	<p>No – As the gross vehicle weight of the drawbar trailer is less than 150Te the vehicle will be considered as a STGO CAT3 movement. This requires that the movement is notified through the National Highways ESDAL platform with 5 working days notice. If no rejections are received within this window, the movement has permission to travel.</p> <p>Notification WYNL/188 was transmitted on 10/12/24 via the ESDAL platform to which no rejections were received. Had a haulier made this same application, they would have therefore received the required permission to travel.</p>
Authorities consulted in respect to AIL Access	<ul style="list-style-type: none"> • A1(M) Alconbury to Peterborough DBFO • Cambridgeshire County Council Abnormal Load Service • Lincolnshire County Council • National Highways Area 7 • National Highways East Region • National Highways Yorkshire & North East Region • Network Rail LC & Rail over Road • North & West Northants Abnormal Load Service • North Lincolnshire Council Unitary Authority
Any Known Problems for AIL Access in terms of Onsite issues?	N/A – Proposal Stage
Any Known Problems for AIL Access in terms of negotiability and	<p>No</p> <p>The roundabout at A43 with Mawsley Road (OS Grid Ref:</p>




Site	Green Hill Solar - Green Hill A (Old)
other route comments?	<p>SP 82830 75106) is to be negotiated in contraflow.</p> <p>Left turn onto Broughton Road from Mawsley Road (OS Grid Ref: SP 81147 75055). Swept path analysis deemed this negotiable without any requirement for land take.</p>
Do routing issues currently present a serious risk that access to the site may be restricted?	No
Any other Relevant Information and Notes: N/A	



Attachment 3

Site A - Map

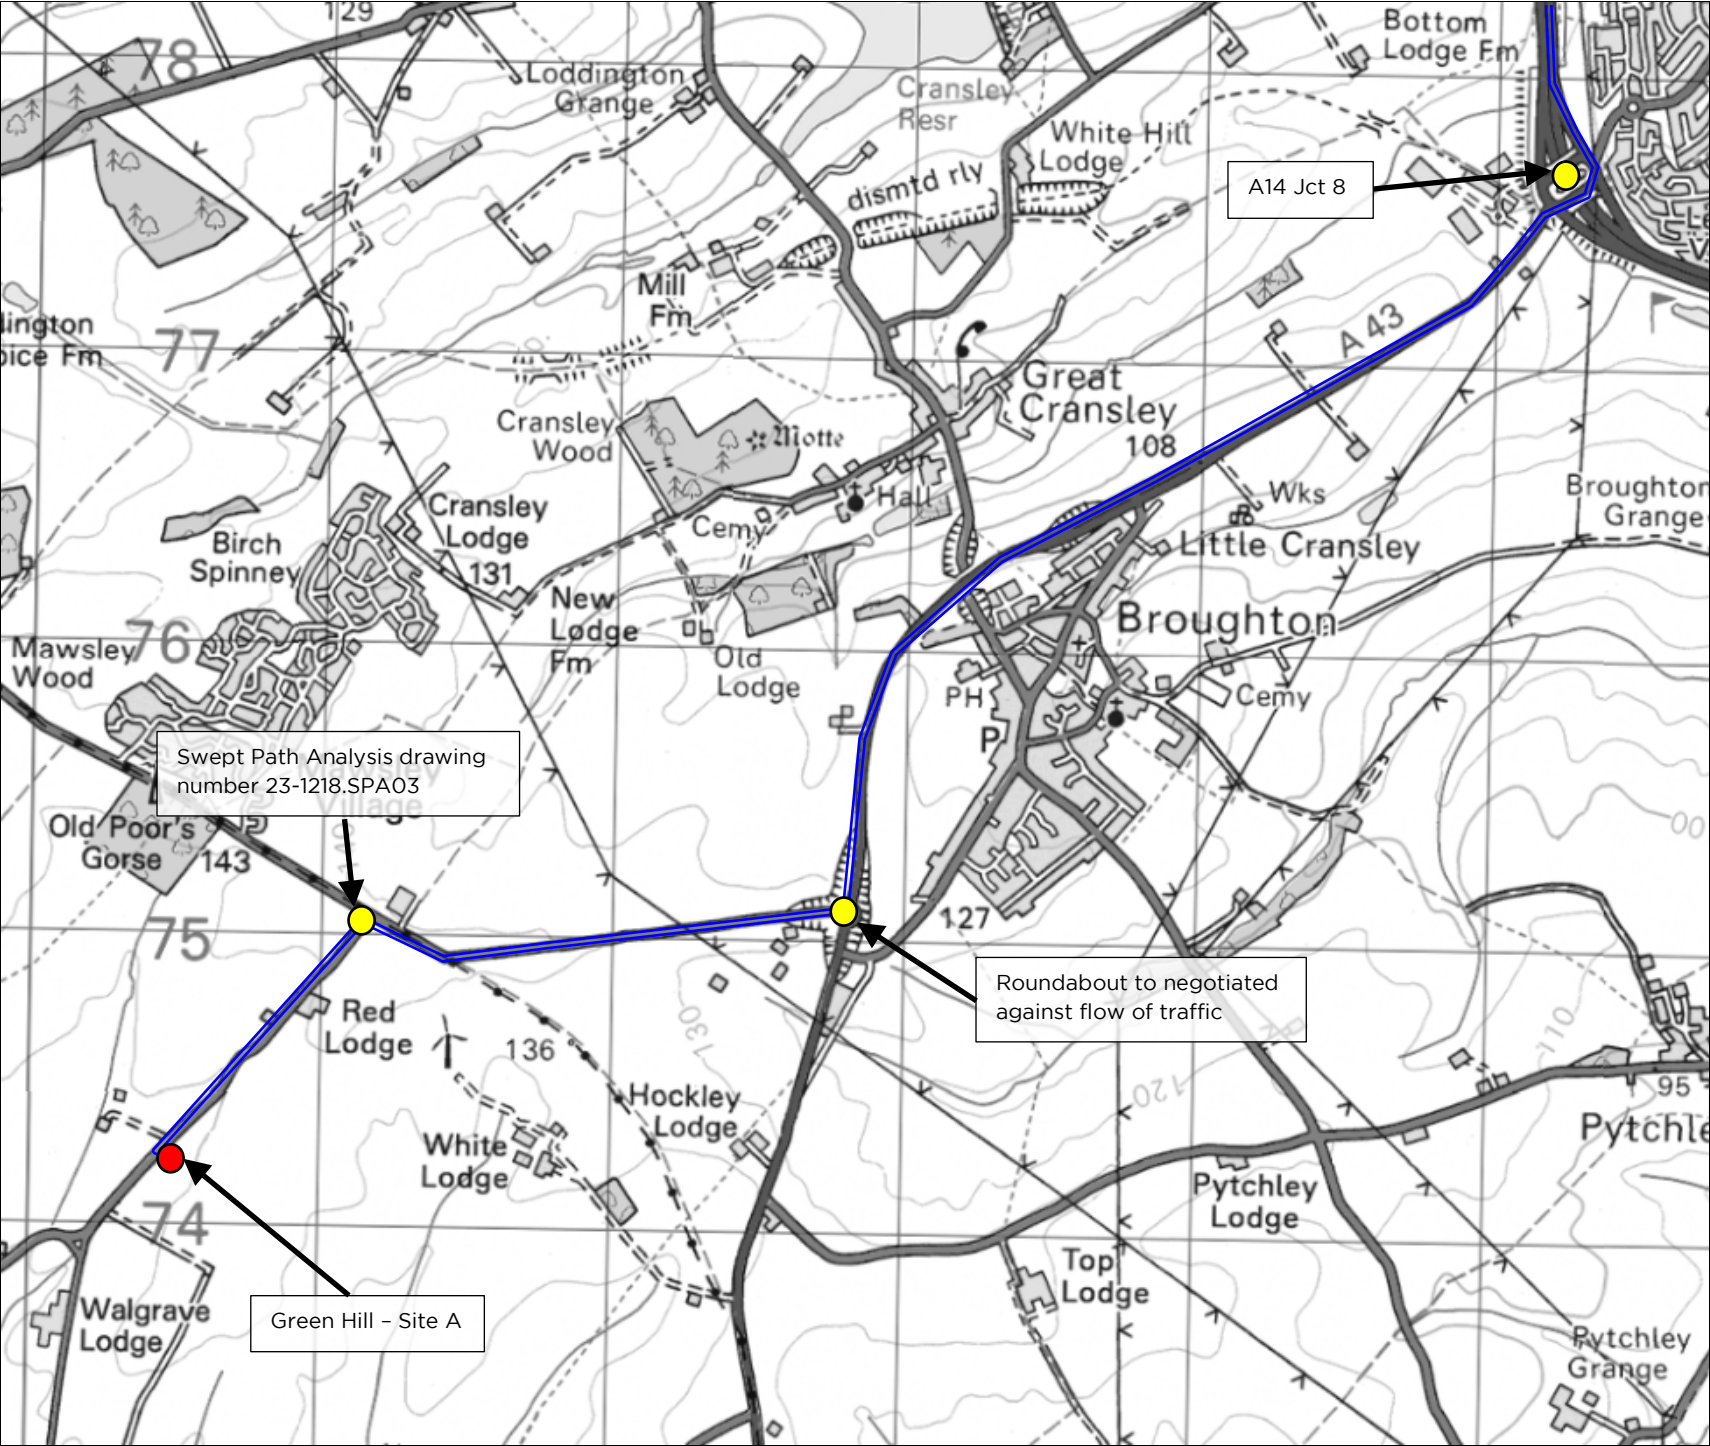

Key

Route 1 to Green Hill - Site A

Points of Interest

Green Hill - Site A

B		
A		
O	17.04.2025	First Issue
Rev	Date	Amendments:

Revisions

WYNNs

ENGINEERS

Wynns Ltd.

Independent

Transportation

Engineers

Shaftesbury House, 2 High Street, Eccleshall,

Stafford, ST21 6BZ. Tel: (01785) 850411

Client:

Island

GREEN

POWER

Project:

Green Hill Solar

Title:

Map 1 - Route to Green Hill - Site A

Drawing Status:

Final Report

Scale (A4):

Drawn by:

Checked by:

NTS

SMB

ARP

Ref No.:

Sheet:

Rev.:

23-1218-Map1

1 of 1

0

© Wynns Ltd. This drawing is not to be reproduced in whole or in part in any form or by any means, without prior written consent.

© Crown Copyright. All rights reserved. Licence No AL100035894



Attachment 4

Site A – Swept Path Analysis



Swept Path Assessment
Indicative of 5 Axle Bed 5 Axle Trailer
Constructed from OS Mastermap Data
Scale 1:1000

(Leader 1) Oversail and Overrun
on Inside/Outside of Turn
Anticipated, Recommended to
Take Wider to Avoid Third-Party
Land and Remain Within Highway
Boundary.

(Leader 2) Plating and Packing to
Overrun Area to Facilitate
Manoeuvre.

(Leader 3) Removal of Traffic Sign
on Inside of Turn, Trimming to
Foliage Depending on Growth at
Time of Movement.

140.8m

Guide Post

The delivery vehicle can be seen turning left onto Broughton Road from Unclassified Road at approximate OS grid reference: SP 81145 75059.


The configuration is recommended to occupy the full available carriageway to aid in reducing and mitigating oversail and overrun where possible. The configuration anticipates oversail and overrun on the inside and outside of the turn, this is recommended to remain within the highway boundary and mitigate possible conflict into third-party land, this anticipates an approximate clearance of 0.66m from the property boundary (Leader 1). Where overrun occurs, plating and packing to the present verges/kerbs should be implemented to facilitate delivery (Leader 2). It should be noted that traffic signs are positioned on the inside of the turn which would require removal (position is approximate), additionally, depending on growth at the time of movement, trimming to foliage may be required to facilitate; all remedial works are expected to remain within the highway boundary (Leader 3). This section is considered to be negotiable based on the aforementioned considerations.

Swept Path Assessment
Indicative of 5 Axle Bed 5 Axle Trailer
Constructed from OS Mastermap Data
Scale 1:500

Location Plan



Legend:

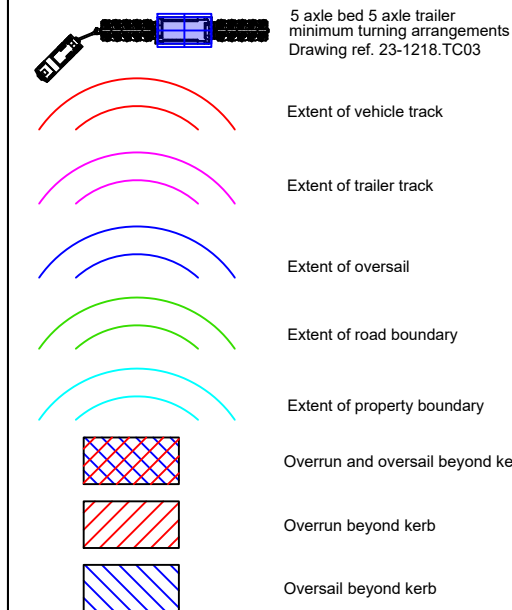

1		
0	14.03.25	Issued for comment
Rev.	Date	Amendments

Revisions

Prepared by:



Shaftesbury House, 2 High Street,
Eccleshall, Stafford, ST21 6BZ
Tel: (01785) 850411

Independent Transportation Engineers

Client:



Project:

Green Hill Solar Farm

Title: Swept Path Assessment
Negotiability of left turn onto Broughton Road from
Unclassified Road, at approximate OS grid
reference: SP 81145 75059, considerate of
indicative 100te transformer transported on 5 axle
bed 5 axle trailer.

Drawing status:

Final Report

Scale (A3):	Drawn by:	Checked by:
As shown	MTO	ARP
Dwg. no:	Sheet:	Rev:
23-1218.SPA03	1 of 2	0

© Wynns Limited. This drawing is not to be reproduced in whole or
in part, in any form or by any means, without prior written consent.

P:\Clients\Existing Clients\Island Green Power\23-1218 Solar Farm in
Northamptonshire (Grendon)\Swept Path Assessments




Swept Path Assessment
Indicative of 5 Axle Bed 5 Axle Trailer
Constructed from OS Mastermap Data
Scale 1:500

NOTE: Overlay onto aerial image is not
representative of the configuration relative to
the environment. This is for illustrative purposes
only, and should only be taken as such.


Location Plan




Legend:




5 axle bed 5 axle trailer
minimum turning arrangements
Drawing ref. 23-1218.TC03




Extent of vehicle track




Extent of trailer track




Extent of oversail




Extent of road boundary




Extent of property boundary



Overrun and oversail beyond kerb



Overrun beyond kerb



Oversail beyond kerb

1		
0	14.03.25	Issued for comment
Rev.	Date	Amendments

Revisions

Prepared by:



Shaftesbury House, 2 High Street,
Eccleshall, Stafford, ST21 6BZ
Tel: (01785) 850411

Independent Transportation Engineers

Client:



Project:

Green Hill Solar Farm

Title: Swept Path Assessment
Negotiability of left turn onto Broughton Road from
Unclassified Road, at approximate OS grid
reference: SP 81145 75059, considerate of
indicative 100te transformer transported on 5 axle
bed 5 axle trailer.


Drawing status:

Final Report

Scale (A3):	Drawn by:	Checked by:
As shown	MTO	ARP
Dwg. no:	Sheet:	Rev:
23-1218.SPA03	2 of 2	0

© Wynns Limited. This drawing is not to be reproduced in whole or
in part, in any form or by any means, without prior written consent.

P:\Clients\Existing Clients\Island Green Power\23-1218 Solar Farm in
Northamptonshire (Grendon)\Swept Path Assessments

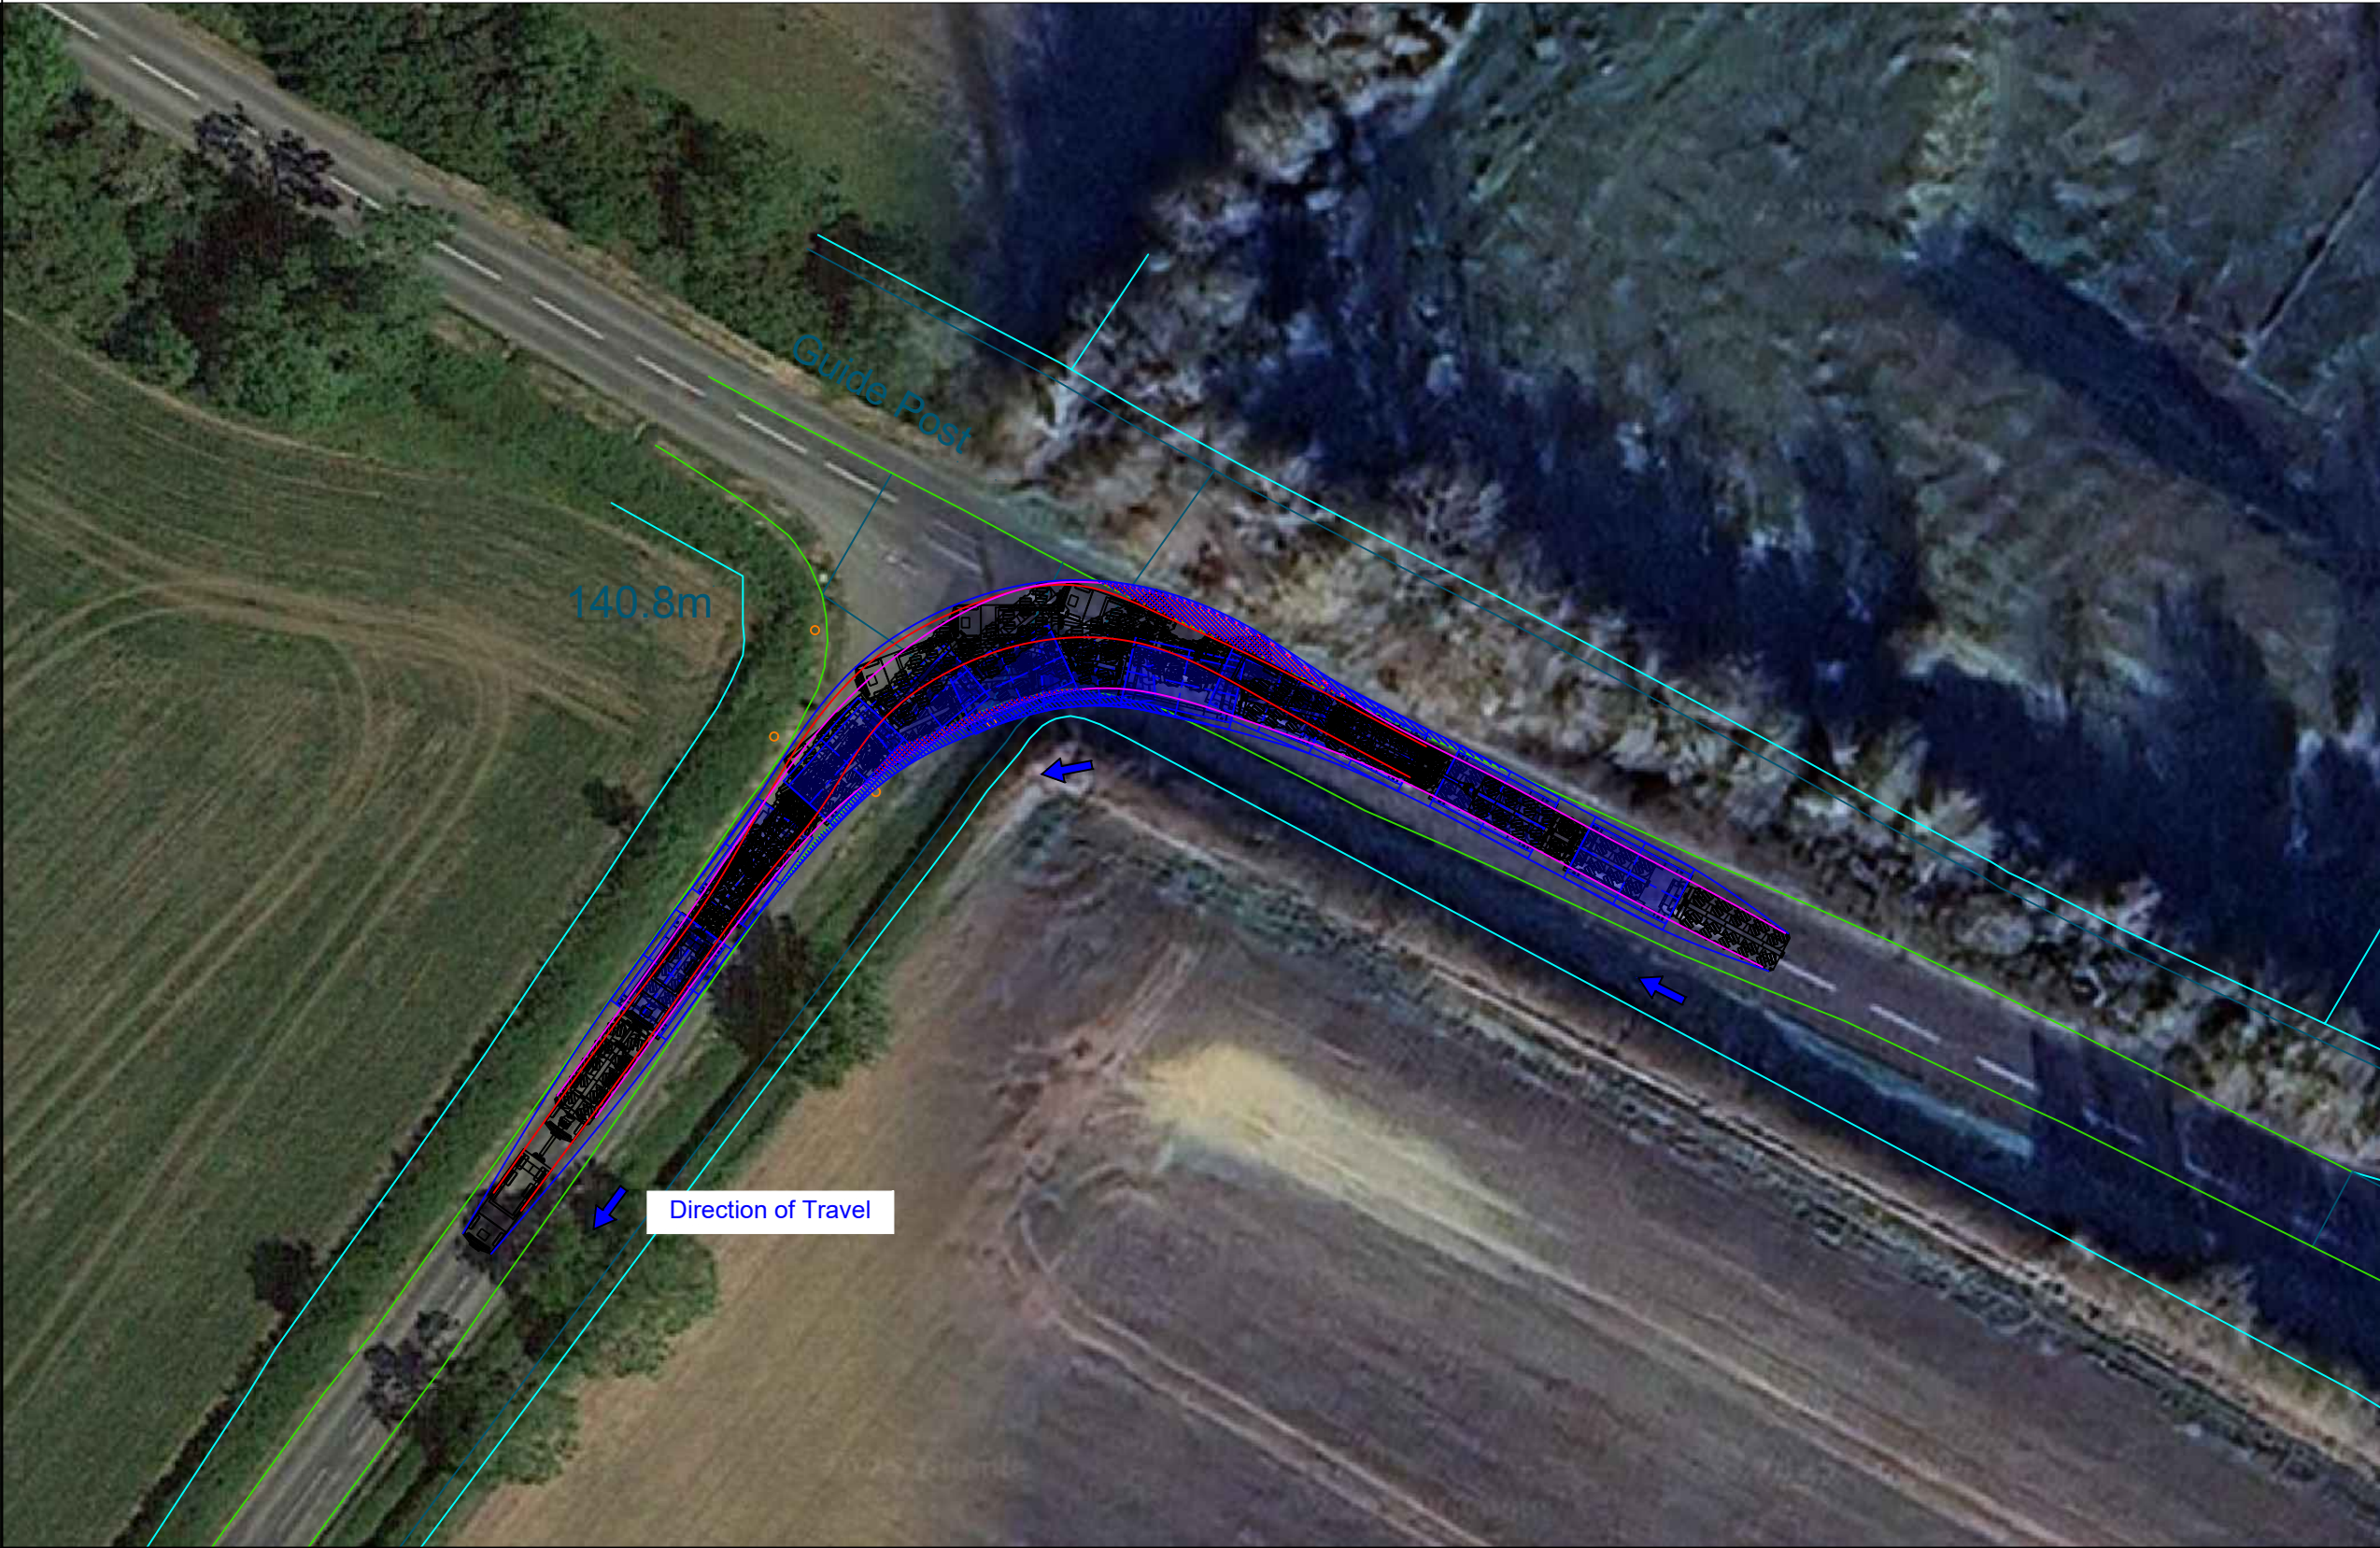

3.2. Green Hill B (Holcot)

Site	Green Hill Solar - Green Hill B (Holcot)
Route Inspection and AIL Access Report Recently undertaken by Wynns?	Yes
Has Agreement in Principle (AIP) been provided by National Highways in line with the Water Preferred Policy	Not applicable as 100te nett transformer will be moved within STGO Category 3 and as such will not require Special Order permissions from National Highways.
National Highways AIP Reference Number	N/A
Proposed port Delivery	Port of Immingham The port of Immingham is well established for heavy project cargo and no issues are expected in respect to marine access. It should be noted that as the load is STGO it will not be specifically limited to Immingham as the closest port but Immingham does provide suitable facilities.
Maximum Transport Weight considered during the most recent report in line with future project requirements	Weight - 95Te nett transformer Length - 7.60m Width - 2.70m Height - 4.5m This payload was originally investigated and received structural clearance before the size of the transformer required was reduced to 65Te nett. As the vehicle is within the agreed envelope, updated notifications are not required until made by the haulier once appointed.
Typical trailer used in route clearance works	A 5 bed 5 trailer at 141te gross weight as shown in drawing number 23-1218.TC03.
Expected delivery date of next planned transformer if known	To be confirmed

Site	Green Hill Solar - Green Hill B (Holcot)
Last Recorded Special Order Movement (according to available records)	<p>No movements to this site as is a new development.</p>
Suggested route based on historical information	<p>Exit A1 at junction of A47 and head west. (OS Grid Ref: TL 07537 99743) Turn left A43 towards Corby Turn left A14 At A14 Jct 8, turn right A43 Turn right Sywell Road to site (OS Grid Ref: SP 80024 69164)</p>
Is a map available of the proposed route(s)?	<p>Yes - See Attachment 5</p>
Any Known Problems for AIL Access in terms of structures?	<p>No - As the gross vehicle weight of the drawbar trailer is less than 150Te the vehicle will be considered as a STGO CAT3 movement. This requires that the movement is notified through the National Highways ESDAL platform with 5 working days notice. If no rejections are received within this window, the movement has permission to travel.</p> <p>Notification WYNL/189 was transmitted on 10/12/24 via the ESDAL platform to which no rejections were received. Had a haulier made this same application, they would have therefore received the required permission to travel.</p>
Authorities consulted in respect to AIL Access	<ul style="list-style-type: none"> • A1(M) Alconbury to Peterborough DBFO • Cambridgeshire County Council Abnormal Load Service • Lincolnshire County Council • National Highways Area 7 • National Highways East Region • National Highways Yorkshire & North East Region • Network Rail LC & Rail over Road • North & West Northants Abnormal Load Service • North Lincolnshire Council Unitary Authority
Any Known Problems for AIL Access in terms	<p>N/A - Proposal Stage</p>










Site	Green Hill Solar - Green Hill B (Holcot)
of Onsite issues?	
Any Known Problems for AIL Access in terms of negotiability and other route comments?	<p>No</p> <p>The roundabout at A43 with Sywell Road (OS Grid Ref: SP 80807 68634) is to be negotiated in contraflow.</p>
Do routing issues currently present a serious risk that access to the site may be restricted?	No
Any other Relevant Information and Notes: N/A	

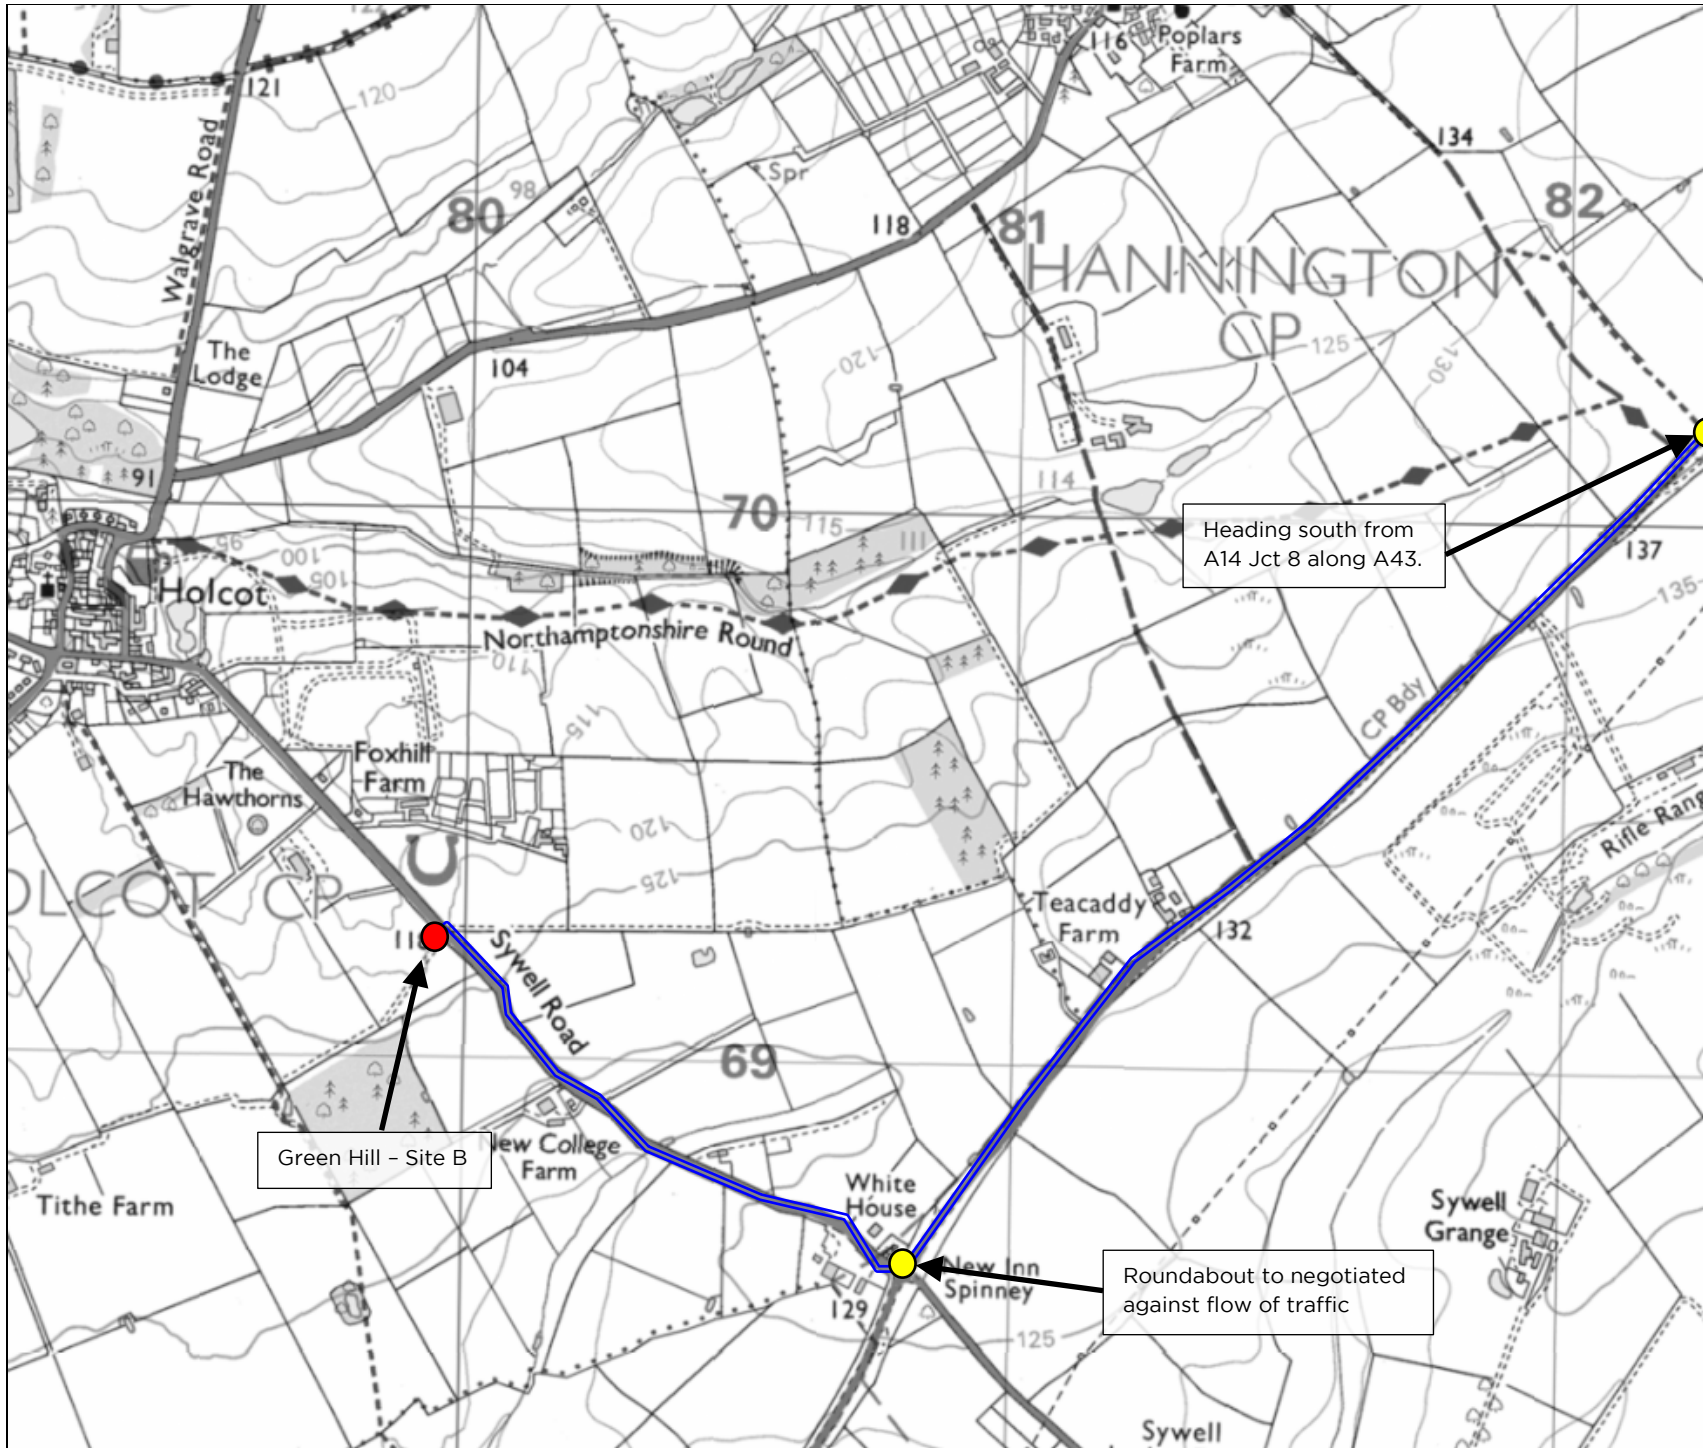

Attachment 5

Site B – Map



Key		
	Route 1 to Green Hill – Site B	
	Points of Interest	
	Green Hill – Site B	
B		
A		
O	17.04.2025	First Issue
Rev	Date	Amendments:
Revisions		
<div><div></div><div><p>Wynns Ltd. Independent Transportation Engineers</p><p>Shaftesbury House, 2 High Street, Eccleshall, Stafford, ST21 6BZ. Tel: (01785) 850411</p></div></div>		
Client:		
<div><div></div><div></div></div>		
Project:		
Green Hill Solar		
Title:		
Map 1 – Route to Green Hill - Site B		
Drawing Status:		
Final Report		
Scale (A4): NTS	Drawn by: SMB	Checked by: ARP
Ref No.: 23-1218-Map1	Sheet: 1 of 1	Rev.: 0
© Wynns Ltd. This drawing is not to be reproduced in whole or in part in any form or by any means, without prior written consent.		
© Crown Copyright. All rights reserved. Licence No AL100035894		
