



WHITESTONE
solar farm

WHITESTONE SOLAR FARM

Volume 5 - Reports and Statements

5.12.1 Outline Construction Traffic Management Plan (Tracked)

Application Document ref. EN 0110020/APP/5.12.1

Revision 024

~~August~~ June 2026

Planning Act 2008
Infrastructure Planning (Applications: Prescribed
Forms and Procedure)
Regulations 2009
Regulation 5(2)(a)

Document status					
Version	Purpose of document	Authored by	Reviewed by	Approved by	Review date
Rev01	DCO Submission	AS	MR	JS	June 2026
<u>Rev02</u>	<u>Section 51/55 Updates</u>	<u>AS</u>	<u>MR</u>	<u>JP</u>	<u>Aug 2026</u>

Approval for issue		
Whitestone Net Zero Ltd		1 June 2026 3 August 2026

The following report and supporting infographics have been produced by human authors. Artificial Intelligence (AI) has not been used to create or alter the technical meaning of these materials. AECOM is technology-enabled and may use technology including AI in service delivery, in compliance with all laws applicable to it. Where AI has been used as an administrative support function, this has been appropriately validated by human authors.

AECOM take full ownership and responsibility for the report, notwithstanding that ancillary technology (including AI tools) may have been used in service provision.

Prepared by:

AECOM

Prepared for:

Whitestone Net Zero Ltd

Contents

1	INTRODUCTION	44
1.1	Introduction	44
1.2	Background	44
1.3	Purpose of Document	44
1.4	Site Location	55
1.5	Objectives	55
2	EXISTING CONDITIONS	77
2.1	Strategic Road Network	77
2.2	Local Road Network	77
3	CONSTRUCTION MOVEMENTS	1111
3.2	Construction Programme	1111
3.3	The Site	1111
3.4	Grid Connection Corridor	1515
3.5	Cumulative Trip Generation	1717
3.6	Construction Worker Trip Distribution	1818
3.7	Construction HGV Trip Distribution	1818
3.8	Vehicle Types, Plan Requirements and Abnormal Loads	1818
3.9	Vehicle Access Arrangements and Routing	1919
3.10	Vehicle Swept Paths	1919
3.11	Access Tracks	1919
4	MANAGEMENT MEASURES AND MITIGATION	2121
4.2	Access Works	2121
4.3	Temporary Traffic Management	2121
4.4	Crossing Points	2222
4.5	HGV Management Measures and Controls	2222
4.6	Worker Vehicle Measures and Controls	2424
4.7	Management Structure	2727
4.8	Monitoring and Review	2727
5	COMPLIANCE AND ENFORCEMENT	2929
5.2	Good Practice	2929
5.3	Contractual Conditions	2929
5.4	Information Packs and Communications	2929
5.5	Enforcement	3030
1	INTRODUCTION	3
1.1	Introduction	3
1.2	Background	3
1.3	Purpose of Document	3
1.4	Site Location	4
1.5	Objectives	4
2	EXISTING CONDITIONS	6
2.1	Strategic Road Network	6
2.2	Local Road Network	6
3	CONSTRUCTION MOVEMENTS	10
3.2	Construction Programme	10
3.3	The Site	10

3.4	Grid Connection Corridor	14
3.5	Cumulative Trip Generation	16
3.6	Construction Worker Trip Distribution	17
3.7	Construction HGV Trip Distribution	17
3.8	Vehicle Types, Plan Requirements and Abnormal Loads	17
3.9	Vehicle Access Arrangements and Routing	18
3.10	Vehicle Swept Paths	18
3.11	Access Tracks	18
4	MANAGEMENT MEASURES AND MITIGATION	20
4.2	Access Works	20
4.3	Temporary Traffic Management	20
4.4	Crossing Points	21
4.5	HGV Management Measures and Controls	21
4.6	Worker Vehicle Measures and Controls	23
4.7	Management Structure	26
4.8	Monitoring and Review	26
5	COMPLIANCE AND ENFORCEMENT	28
5.2	Good Practice	28
5.3	Contractual Conditions	28
5.4	Information Packs and Communications	28
5.5	Enforcement	29

Tables

Table 3-1	Construction Worker Daily Trip Generation	<u>13</u> <u>12</u>
Table 3-2	Construction Phase Total HGV Trip Generation (Site)	<u>14</u> <u>13</u>
Table 3-3	Construction Phase Daily Peak HGV Trip Generation	<u>14</u> <u>13</u>
Table 3-4	Daily Vehicle Trips by Access Point	<u>14</u> <u>13</u>
Table 3-5	Daily Vehicle Trips by Access Point	<u>16</u> <u>15</u>
Table 3-6	Construction Phase Daily Peak HGV Trip Generation (GCC)	<u>16</u> <u>15</u>
Table 3-7	Trip Generation by Access Point	<u>16</u> <u>15</u>
Table 3-8	Total Solar PV and GCC Daily Peak Construction Worker Vehicle and HGVs - Two-Way Movements	<u>18</u> <u>17</u>

Plates

Plate Number	Plate Title
1-1	Whitestone 1 (Northern Site) Location
1-2	Whitestone 2 (Central Site) Location
1-3	Whitestone 3 (Southern Site) Location

Appendices

Appendix Number	Appendix Title
A-1	Access Point Locations
A-2	Site and Grid Connection Corridor Access Points

A-3	Proposed Access Layouts, Visibility Splays and Swept Paths

Acronyms

Acronym	Meaning
<i>AADT</i>	Average Annual Daily Traffic
<i>TS</i>	Transport Statement
<i>DCO</i>	Development Consent Order
<i>SRN</i>	Strategic Road Network
<i>PV</i>	Photo Voltaic
<i>NPPF</i>	National Planning Policy Framework
<i>ES</i>	Environmental Statement
<i>AIL</i>	Abnormal Indivisible Load
<i>HGV</i>	Heavy Goods Vehicle
<i>GCC</i>	Grid Connection Corridor
<i>PRoW</i>	Public Rights of Way
<i>HDD</i>	Horizontal Directional Drilling

1 INTRODUCTION

1.1 Introduction

- 1.1.1 This Outline Construction Traffic Management Plan (oCTMP) has been prepared for Whitestone Net Zero Ltd (the Applicant) in support of the Application for the Proposed Development and reflects inputs of consultation and discussions with relevant stakeholders. The preparation of a CTMP is secured by a DCO requirement and included within the **Draft Development Consent Order (DCO) [EN0110020/APP/3.1]**. This document should be read in conjunction with **ES Volume 2, Chapter 13: Traffic and Transport [EN0110020/6.13]**, **ES Volume 3, Appendix 13.2: Transport Statement [EN0110020/APP/6.20]**, and the **Outline Public Rights of Way Management Plan [EN0110020/APP/5.1214]**.

1.2 Background

- 1.2.1 The Proposed Development involves the construction, operation and maintenance, and decommissioning of more than 100 MW of solar photovoltaic (PV) array, Battery Energy Storage System (BESS), onsite substations and supporting infrastructure, and grid connection infrastructure. The grid connection infrastructure would connect the Proposed Development to the National Grid at the new National Grid substation Brinsworth (Long Lane 400kV Substation), located east of Long Lane, Rotherham. National Grid has applied to Rotherham Metropolitan Borough Council for the development of this new substation which is intended by National Grid to be operational in time for the Proposed Development to connect in 2029. This substation is therefore not included in the Proposed Development and will be subject to a separate planning application taken forward by National Grid.
- 1.2.2 There will be three main phases associated with the Proposed Development: Construction, Operation (and Maintenance), and Decommissioning.
- 1.2.3 During the construction phase, there will be a temporary increase in vehicle movements as equipment, materials, and workers are brought to the Site. Once construction is complete, the operational phase will generate negligible levels of traffic, limited to occasional maintenance visits by service vehicles. In the decommissioning phase, which will occur at the end of the solar farm's operational life, there will be a short-term increase in traffic similar to the construction phase, as equipment is removed and the Site is restored.

1.3 Purpose of Document

- 1.3.1 This document sets out the oCTMP, which focuses on the management of construction traffic within the vicinity of the Order limits on the Local Road Network (LRN) during the construction phase of the works associated with the Proposed Development, in order to limit any potential disruptions and implications on the wider transport network, as well as for the existing road users.
- 1.3.2 The oCTMP also provides mitigation for traffic generated during the construction phase of the Proposed Development, including Heavy Goods Vehicles (HGVs). The oCTMP covers the principal construction activities set out in **ES Volume 1, Chapter 5: The Proposed Development [EN0110020/APP/6.5]**.

- 1.3.3 The oCTMP is intended to be an emerging document, such that modifications and necessary interventions can be made following further information and advice received from consultees.
- 1.3.4 As part of the development of the oCTMP, the Applicant has undertaken proactive engagement with the relevant highway authorities. This consultation was carried out during November 2025 and included meetings with City of Doncaster Council (CDC), Rotherham Metropolitan Borough Council (RMBC), North East Derbyshire District Council (NEDDC), Derbyshire County Council (DCC) and National Highways (NH). The purpose of this engagement was to ensure that the proposed access strategy, routing arrangements and construction traffic planning fully reflect local priorities and strategic network requirements.
- 1.3.5 The feedback received has been incorporated into the refinement of the oCTMP. A CTMP substantially in accordance with this oCTMP, will be shared with the relevant planning authority following consultation with National Highways prior to commencement of construction of the Proposed Development.

1.4 Site Location

- 1.4.1 The Proposed Development is located across three areas, namely Whitestone 1 (W1) (the northern parcels of the Proposed Development), Whitestone 2 (W2) (the central parcels of the Proposed Development) and Whitestone 3 (W3) (the southern parcels of the Proposed Development). For the purposes of assessment, these areas will be used as specific study areas.
- 1.4.2 The remainder of this oCTMP is structured as follows:
- **Section 2** provides details of the Site, surrounding area and the existing highway network;
 - **Section 3** summarises the HGV, construction and worker vehicle movements which are expected to be generated by the Proposed Development across the construction phase, including during the peak of construction. Details are also provided on the proposed site accesses including details of layouts, visibility splays and swept paths, as well as routing arrangements and internal site layout considerations including access tracks and parking;
 - **Section 4** summarises the proposed measures to manage the highway network as well as pedestrian and cycle routes during the construction phase of the Proposed Development. In addition, this section summarises the measures directed at HGVs and workers, as well as for the management, monitoring and review of the CTMP; and
 - **Section 5** deals with compliance and enforcement of the CTMP.

1.5 Objectives

- 1.5.1 The objectives of this oCTMP are to set a framework for the measures that would be developed in the final CTMP, post DCO consent, to:
- Minimise the volume of construction Heavy Goods Vehicles (HGVs) and construction worker vehicles as far as reasonably practicable;
 - Maximise the safe and efficient movement of materials and workers required during the construction phase as far as reasonably practicable;

- Minimise the restrictions imposed and ensure efficient management to the local Public Rights of Way (PRoW) within the Order limits during the construction phase;
- Minimise the impacts both for the local community and visitors to the area using the LRN as far as reasonably practicable; and
- Set out the measures to be adhered to by those travelling to and from the Order limits to reduce the impact of the construction of the Proposed Development.

2 EXISTING CONDITIONS

2.1 Strategic Road Network

- 2.1.1 There are three roads forming part of Strategic Road Network (SRN) which travel close to or provide access to the Proposed Development.

A1

- 2.1.2 The A1 spans approximately 410 miles (660 km) from London to Edinburgh, passing through major towns and cities such as Peterborough, Doncaster, Newcastle-upon-Tyne, and Berwick-upon-Tweed. The A1 includes sections that are designated as A1(M), which are upgraded to motorway standards.
- 2.1.3 Junction 36 of the A1 (M) will be utilised to provide SRN routing onto the local highway network for W1.

M18

- 2.1.4 The M18 motorway is a key route in Yorkshire, stretching approximately 26 miles (42 km) from the east of Rotherham to Goole in a north-east to south-west direction. It connects several major motorways, including the M1, A1(M), M180, and M6212.
- 2.1.5 Junction 1 of the M18 motorway will be utilised to provide SRN routing onto the local highway network for W1 and W2.

M1

- 2.1.6 The M1 motorway connects London to Leeds and spans approximately 193 miles (311 km). The motorway passes through several counties, including Greater London, Hertfordshire, Bedfordshire, Buckinghamshire, Northamptonshire, Leicestershire, Nottinghamshire, Derbyshire, and Yorkshire. It also intersects with other major motorways such as the M25, M6, M69, M18, M62, and M62112.
- 2.1.7 Junction 31 of the M1 motorway will be utilised to provide SRN routing onto the local highway network for W2 and W3. Junction 33 will also provide routing to W2.

2.2 Local Road Network

- 2.2.1 Once vehicles have left the SRN, they will be routed via the local road network, following the devised routing strategy (see **Appendix A-2 Site and Grid Connection Corridor Access Points** of this oCTMP). The routes to be used are set out below for each section of the Proposed Development.
- 2.2.2 It should be noted that during the evolution of the Proposed Development since Draft ES, certain roads that were initially included within the study area (that could potentially be used as construction access routes) were removed. This includes those that were originally within the description section below.
- 2.2.3 Routing has also been considerate of the vehicle type, where possible aiming to avoid HGVs using unsuitable roads.

W1 (Northern Site)

A630

- 2.2.4 The A630 High Road is a major road providing access to residential and commercial areas. Street lighting is present, and the road supports two-way traffic. It runs west of the A1(M) Junction 36 in an east-west direction, connecting areas such as Warmsworth and Conisbrough. The speed limit varies, with sections having a limit of 40 mph through residential areas and 50 mph in all other areas.

Hellaby Lane

- 2.2.5 Hellaby Lane is a local road providing access to residential and employment areas, between Common Lane to the north and Denby Way / A631 Bawtry Road junction to the south. Street lighting is present, and the road supports two-way traffic. The speed limit is 30mph.

B6093

- 2.2.6 The B6093 is a secondary road, which connects the A630 with residential areas such as Woodlaithes and Bramley. Street lighting is present in urban sections, and the road supports two-way traffic. The speed limit varies between 40mph and down to 30mph through the residential areas.

W2 (Central Site)

A57

- 2.2.7 The A57 is a major road in northern England running from Liverpool to Lincoln, passing through cities like Manchester and Sheffield. Street lighting is present along urban sections, and the road supports two-way traffic. The speed limit is national speed limit of up to 60mph along the majority of the road sections.

A631

- 2.2.8 The A631 is a primary route and within the vicinity of the Proposed Development is a segregated dual carriageway, running between the M18 Junction 1 and Stag Roundabout (A6021 Wickersley Rd / A6123). Street lighting is present throughout, and the speed limit is 40mph along the majority of the road.

Flash Lane

- 2.2.9 Flash Lane is a secondary route between A631 Bawtry Lane to the north and the Slack Lane / Sandy Lane junction to the south. Street lighting is present, and the road supports two-way traffic. The speed limit is 30mph along the majority of the road sections.

Long Lane

- 2.2.10 Long Lane is a local road providing access to agricultural zones. It runs from the A631 to the north, under the M1 and towards Treeton. Street lighting is present in

residential areas, and the road supports two-way traffic. The road is subject to the national speed limit of up to 60mph.

A618

- 2.2.11 The A618 is a secondary road serving residential and agricultural areas. Street lighting is present in residential areas, and the road supports two-way traffic. The road varies between single and dual carriageway, and the speed limit also varies between 30mph and 50mph.

Gulthwaite Common Lane

- 2.2.12 Gulthwaite Common Lane is a local road connecting the A618 with agricultural zones. There is no street lighting present, and the road supports two-way traffic. The road is subject to the national speed limit of up to 60mph.

Reservoir Road

- 2.2.13 Reservoir Road is a local road running from the A618 and over Ulley Reservoir to Ulley Lane. No street lighting is available, and the road supports two-way traffic. The road is subject to the national speed limit of up to 60mph.

Main Street

- 2.2.14 Main Street in Ulley is a local road serving residential areas and providing access to local schools and parks. Street lighting is present, and the road supports two-way traffic. The speed limit is 30 mph.

Penny Hill Lane

- 2.2.15 Penny Hill Lane is a local road providing access to residential areas and local amenities. Street lighting is present in residential areas, and the road supports two-way traffic. The road is subject to the national speed limit of up to 60mph.

Brampton Lane

- 2.2.16 Brampton Lane is a local road connecting residential areas with agricultural zones. No street lighting is present, and the road supports two-way traffic. The road is subject to the national speed limit of up to 60mph.

Common Lane (south of Thurcroft)

- 2.2.17 Common Lane is a secondary road serving residential areas and local businesses south of Thurcroft between Wood Lane / Brampton Lane and Penny Hill Lane / Hawk Hill Lane. No street lighting is present, and the road supports two-way traffic. The road is subject to the national speed limit of up to 60mph.

Long Road

- 2.2.18 Long Road is a local road providing access to agricultural zones. No street lighting is present, and the road supports two-way traffic. The road is subject to the national speed limit of up to 60mph.

Todwick Road

- 2.2.19 Todwick Road, between Pocket Handkerchief Lane and A57, is a secondary road serving residential and commercial areas. Street lighting is present in residential areas, and the road supports two-way traffic. The speed limit varies between 40 mph and national of up to 60mph.

Pocket Handkerchief Lane

- 2.2.20 Pocket Handkerchief Lane is a local road providing access to agricultural zones. No street lighting is present, and the road supports two-way traffic. road is subject to the national speed limit of up to 60mph.

W3 (Southern Site)

A57

- 2.2.21 The A57 is described above in the W2 section at paragraph 2.2.6.

A618

- 2.2.22 The A618 is described above in the W2 section at paragraph 2.2.10.

Kiveton Lane

- 2.2.23 Kiveton Lane is a local road serving residential areas and providing access to local schools and parks. Street lighting is present in residential areas, and the road supports two-way traffic. The speed limit varies between 30 and 40 mph.

Woodall Lane

- 2.2.24 Woodall Lane is a local road serving residential areas and providing access to local amenities. Street lighting is present in residential areas, and the road supports two-way traffic. The speed limit is up to 30 mph.

Killamarsh Lane

- 2.2.25 Killamarsh Lane is a secondary road providing access to agricultural zones. No street lighting is present, and the road supports two-way traffic. The road is subject to the national speed limit of up to 60mph.

Walseker Lane

- 2.2.26 Walseker Lane is a local road serving residential areas and providing access to housing. Street lighting is present, and the road supports two-way traffic. The speed limit is up to 30 mph.

3 CONSTRUCTION MOVEMENTS

- 3.1.1 This section provides a summary of the forecast HGV and worker vehicle movements that are expected during the construction phase of the Proposed Development, based on the proposed construction phase programme, associated with the Site and Cable Corridors . Further details are provided within Section 5 of **ES Volume 3, Appendix 13.2: Transport Statement [EN0110020/APP/6.20]**.

3.2 Construction Programme

- 3.2.1 The construction phase for the whole Proposed Development is expected to span approximately 24 to 36 months. While the exact timeline will depend on various factors, construction is expected to commence in 2027 and conclude by 2029. However, construction activity, and therefore peak construction traffic, will only occur in any one location for a limited portion of this overall 24–36 month period, as works will progress sequentially across the site.
- 3.2.2 The worst-case traffic is currently expected to be during the peak construction period between mid-2028 and mid-2029. Therefore, for the purposes of this assessment, it has been assumed that 2028 is the peak construction year to allow for delays that may occur.
- 3.2.3 The earliest date of operation would be 2029, in line with the grid connection date for the Proposed Development.
- 3.2.4 Once construction is complete, the operational phase will generate negligible levels of traffic, limited to occasional maintenance visits by service vehicles. In the decommissioning phase, which will occur at the end of the solar farm's operational life of 60 years, there will be a short-term increase in traffic similar to the construction phase, as equipment is removed and the Site is restored.

3.3 The Site

Construction Worker Vehicle Movements

- 3.3.1 The trip generation for construction workers travelling to and from the Site has been calculated with modal splits applied to reflect anticipated travel behaviour. This is based on an assumption that 600 workers will be on site each day.
- 3.3.2 It was assumed that 20% of workers would travel by sustainable modes as outlined in Section 5 of **ES Volume 3, Appendix 13.2: Transport Statement [EN0110020/APP/6.20]** (including walking, cycling, and public transport – a large number of roads and bridleways on the local network are considered appropriate for cycle use especially, therefore a figure of 20% is deemed reasonable), while another 20% would be transported via shared minibuses. The number of minibuses required was estimated using an average occupancy of eight workers per vehicle. For access points well serviced by public transport, internal site shuttles will also be used to transfer workers from that location to their final destinations within the Site.
- 3.3.3 The remaining 60% of workers would be assumed to travel by car. To reflect car-sharing initiatives and reduce single-occupancy vehicle trips, a car occupancy factor of 1.2 workers per car was applied. This adjustment provided a more realistic

estimate of car-based movements and supported the development of targeted parking and access strategies.

3.3.4 Two-way vehicle trip totals were then calculated for both minibuses and cars, representing the full daily movement of vehicles to and from the Site.

3.3.5 These figures informed the overall traffic impact assessment, as described in Section 5 of **ES Volume 3, Appendix 13.2: Transport Statement [EN0110020/APP/6.20]** and are presented below in **Table 3-1**~~Table 3-1~~, which assumes that all construction worker peaks coincide and therefore represents a worst-case scenario.

3.3.6 Further details relating to worker requirements are also provided within **Volume 2, Chapter 15 Socio-Economics and Land Use [EN0110020/APP/6.15]**.

WHITESTONE SOLAR FARM

Table 3-1 Construction Worker Daily Trip Generation

Total Workers	Walking, Cycling, Public Transport (20%)	Workers Using Minibus (20%)	Minibuses (Assuming 8-Seater)	Remaining Workers (by Car)	Total After Car Share Applied (1.2 per Car)	Two-Way Car	Two-Way Minibus	Daily Two-Way Total Movements
600	120	120	15	360	300	600	30	630

Construction HGVs Trip Generation

- 3.3.7 The trip generation for construction-related HGVs was calculated using a combination of unit-based and volume-based delivery estimates. These figures were aggregated to produce total HGV movements per location over the entire construction phase.
- 3.3.8 To account for potential variability in construction activity, delivery schedules, and site logistics, a contingency factor of 25% was applied to the total HGV estimates. This ensured that the assessment captured a realistic upper-bound scenario for vehicle movements.
- 3.3.9 The resulting figures were then converted into one-way and two-way trips to reflect daily vehicle movements to and from the Site. This method provided a robust and precautionary basis for evaluating the impact of construction traffic on the surrounding highway network, and the total HGV trips are presented below in **Table 3-2**.
- 3.3.10 It should be noted that this is the worst case daily traffic numbers across the entirety of the Proposed Development area, based on all peak activities occurring at once.

Table 3-2 Construction Phase Total HGV Trip Generation (Site)

HGVs (Unit Based)	HGVs (Volume)	HGVs (Total)	HGVs (Total, inc. 25% Contingency)
5,072	15,501	20,573	25,716

- 3.3.11 **Table 3-3** presents the worst case daily peak HGV trips during the construction phase.

Table 3-3 Construction Phase Daily Peak HGV Trip Generation

Daily One-Way Movements	Daily Two-Way Movements
102	204

The Site Total Trip Generation by Access Point

- 3.3.12 Details of the total daily number of worker vehicle and HGV trips generated by each proposed Site access point are presented in **Table 3-4**. The access point locations are shown visually in **Appendix A-1 Access Point Locations**.

Table 3-4 Daily Vehicle Trips by Access Point

Access Point	Worker Vehicles (Two-Way)	HGVs (Two-Way)
SR-01	189	69
SL-01	22	7
SL-02	22	7
PEHL-02	22	7
PEHL-03	22	7

LL-02	19	6
GCL-02	22	7
LL-01	22	7
WL-02	19	6
CL-01	21	6
HHL-01	21	6
HHL-02	21	6
HHL-03	21	6
CL-03	21	6
LR-05	21	6
SR-03	21	6
POHL-02	21	6
HL-02	35	11
RR-01	35	11
RR-02	30	10
Total	627¹	203¹

3.4 Grid Connection Corridor

- 3.4.1 Traffic generated by the GCC will primarily consist of Worker (Cars / LGVs) and a limited number of HGVs during the construction phase of the Proposed Development. These movements will be scheduled to align with existing traffic management protocols and have been distributed across the same peak periods already assessed for the main development (Site).
- 3.4.2 The corridor works are linear and will be delivered in phases, meaning that traffic demand will be spread out both spatially and temporally. This proposed approach further reduces the likelihood of any concentrated traffic impact at any one location or time. Additionally, the nature of the works, primarily involving cable laying and associated works, means that vehicle types and volumes will be consistent with those already considered in the Transport Statement and ES chapter.

Construction Worker Trip Generation

- 3.4.3 The vehicle trip generation for workers will follow the same assumptions as those for the Site (e.g., 20% sustainable travel). When these assumptions are applied,

¹ These numbers have a small difference compared with the total worker vehicle (shown in Table 3-1) and HGV (shown in Table 3-3) trip generation due to rounding.

the following forecast peak daily worker vehicle trips are produced, as shown in **Table 3-5**.

Table 3-5 Daily Vehicle Trips by Access Point

Daily One-Way Vehicle Movements	Daily Two-Way Vehicle Movements
282	564

Construction HGV Trip Generation

3.4.4 The trip generation for HGVs will follow the same assumptions as those for the Site. **Table 3-6** shows the forecast peak daily HGV trip generation.

3.4.5 It should be noted that this is the worst case daily traffic numbers across the entirety of the Proposed Development area, based on all peak activities occurring at once.

Table 3-6 Construction Phase Daily Peak HGV Trip Generation (GCC)

Daily One-Way HGV Movements	Daily Two-Way HGV Movements
188	376

GCC Total Trip Generation by Access Point

3.4.6 In terms of access to the GCC, the vehicles will use either:

- Site access points; or
- GCC only access points.

3.4.7 The total number of GCC related worker vehicle and HGV trips travelling to and from each proposed access point is presented in **Table 3-7**. The access point locations are shown visually in **Appendix A-1 Access Point Locations**.

Table 3-7 Trip Generation by Access Point

Access Point	Worker Vehicles (Two-Way)	HGVs (Two-Way)
Existing Site access points		
SL-01	10	6
SL-02	10	6
LL-01	6	4
GCL-02	12	8
PEHL-03	4	2
CL-03	12	8
LR-05	14	10
POHL-02	8	6

SR-03	26	18
HL-02	24	16
RR-01	4	2
RR-02	6	4
GCC only access points		
CC-01	42	28
CC-02	6	4
CC-03	8	6
CC-04	12	8
CC-05B	36	24
CC-06	22	14
CC-07	8	6
CC-08	12	8
CC-09	20	14
CC-10	70	46
CC-11	10	6
CC-13	26	18
CC-14	36	24
CC-17	54	36
CC-25	66	44
Total	564	376

- 3.4.8 With regard to vehicle access through CC-06, it should be noted that a secondary access (CC-06c) would be provided in place of CC-06 for a smaller volume of traffic, if required as a result of detailed design. This is to help enable key equipment to move in if required, such as drilling equipment, or cable deliveries. The volumes accessed here would be deducted from the volume of movements to CC-06. The cap on HGV one way movements would be two per day, and non-HGV 6 per day. Where possible, construction compounds in the Solar PV area would be used, and workers shuttled via minibus to avoid parking on residential streets.

3.5 Cumulative Trip Generation

- 3.5.1 To assess a worst-case scenario, it has been assumed that the Site and GCC peak daily trip generation will occur during the same period. As the design develops, the

Applicant will (where possible) work to minimise concurrent works, except where required to meet the programme in a safe and efficient manner.

- 3.5.2 The total peak daily construction vehicle movements (two-way) are presented below in **Table 3-8**.

Table 3-8 Total Solar PV and GCC Daily Peak Construction Worker Vehicle and HGVs - Two-Way Movements

Construction Worker Vehicle Movements (Car/LGV/Minibus)	HGV Movements	Total Movements
1,194	579	1,773

3.6 Construction Worker Trip Distribution

- 3.6.1 Trip distribution for construction workers was established using a gravity-based approach that considered both the population size of origin areas and their proximity to the Proposed Development. Population data for each origin zone was combined with straight-line (crow-fly) distances to the centre of the entire Proposed Development extents within W2, between the Sites East and West of the M1. Further details are contained within **ES Volume 3, Appendix 13.2: Transport Statement [EN0110020/APP/6.20]**.

3.7 Construction HGV Trip Distribution

- 3.7.1 A strategic approach was adopted to estimate their distribution based on access from the SRN. It was assumed that HGVs would enter the local road network from key SRN corridors, reflecting typical freight movement patterns and regional connectivity. This method prioritised major trunk roads and motorways that provide logical and efficient access to the Site and GCC, ensuring that HGVs would approach from routes designed to accommodate heavy goods traffic.
- 3.7.2 HGV movements have been proportionally distributed across all access points for the Site, ensuring that the total accounts for 100% of the movements associated with W1, W2 and W3.
- 3.7.3 For the GCC, the HGV movements to each access point are known, based on:
- Uniform construction duration (15 weeks per access point, with any extension further reducing the peak, and spreading equivalent deliveries over longer period);
 - 5-day working week; and
 - The HGVs needed per km of cable corridor are known.

3.8 Vehicle Types, Plan Requirements and Abnormal Loads

- 3.8.1 It is expected that construction vehicles accessing the Proposed Development will consist of the following:
- Cars;
 - Small vans;

- 10 m rigid vehicles;
- Max articulated lorries (HGVs);
- Tractor-trailer vehicle (up to 12 m in length) (for internal or ad-hoc movements of materials on the road network);
- Mobile cranes; and
- AILs.

3.8.2 All large vehicles and other AILs will be required to follow the routing strategy agreed with the Local Highways Authority when travelling to/from the Proposed Development.

3.9 Vehicle Access Arrangements and Routing

3.9.1 It is anticipated that the main construction access points to the Proposed Development will be from the local road network. The proposed access points for the Site and Grid Connection Corridor (GCC) are presented in a figure within **Appendix A-1 Access Point Locations** of this oCTMP, as well as listed in **Table 5-4 (Site)** and **Table 5-7 (Grid Connection Corridor)**.

3.9.2 Workers will travel to the access points based on the origin of their trips, as detailed within **Appendix A-1, Proposed Access Layouts, Visibility Splays and Swept Paths** included within this oCTMP.

3.9.3 The proposed HGV routing strategy (see **Appendix A-2 Site and Grid Connection Corridor Access Points** of this oCTMP) will utilise the local road network to connect to the following SRN junctions:

- Junction 36 of the A1 (M) will be utilised to provide SRN routing onto the local highway network for W1.
- Junction 1 of the M18 motorway will be utilised to provide SRN routing onto the local highway network for W1 and W2.
- Junction 31 of the M1 motorway will be utilised to provide SRN routing onto the local highway network for W2 and W3.
- Junction 33 of the M1 also provides routing to W2.

3.10 Vehicle Swept Paths

3.10.1 All points of access to the Site and GCC have been assessed using swept path analysis using the largest assumed vehicles to enter the respective accesses.

3.10.2 All swept path drawings at the points of access are provided within **Appendix A-3, Proposed Access Layouts, Visibility Splays and Swept Paths** included within this oCTMP.

3.10.3 The vehicle-swept paths demonstrate that construction vehicles will be able to turn in/out of the proposed Site and GCC access points. An appropriate level of visibility will be achievable to/from the access, as set out above.

3.11 Access Tracks

3.11.1 It is proposed that internal routes through the Site where practicable will be utilised as the primary route for deliveries and worker movements across the Site. Where

necessary, upgrades to existing tracks through widening and resurfacing may be necessary.

- 3.11.2 It is proposed that within the Site internal access tracks will be up to 6m in width and passing places will be up to 20m in length and installed at strategic locations to ensure safe passage of construction vehicles. The internal tracks will enable free-flowing movement within the Site whilst removing construction traffic from local roads. In terms of design, there would be a preference for following the alignment of existing tracks where practicable to limit the requirement for new crossings, disturbances to soils or habitat removals.

4 MANAGEMENT MEASURES AND MITIGATION

- 4.1.1 This section outlines the construction traffic management measures that will be implemented in support of the Proposed Development, to avoid any adverse impacts on the surrounding networks during the construction phase.

4.2 Access Works

- 4.2.1 Access designs have been provided for all locations where vehicles will be required to enter the Proposed Development. The access layout drawings are provided within **Appendix A-3 Proposed Access Layouts, Visibility Splays and Swept Paths** of this oCTMP,

4.3 Temporary Traffic Management

- 4.3.1 The GCC will require temporary traffic management at several points along the road network during the construction phase, to allow construction vehicles to safely cross and access cable routes sections, as well as organising traffic to avoid impacts on the road network and traffic. These measures, described below, are secured within the DCO and within the **Rights of Way, Streets and Access Plans [EN0110020/APP/2.4]**, and **Traffic Regulations Plans [EN0110020/APP/2.5]**.
- 4.3.2 Where necessary along busier roads, temporary traffic signals are proposed to mitigate the impact of the laying of the cable across the road. Where roads are less busy, traffic management will be conducted by traffic marshals where necessary. Any works will comply with relevant guidance and legislative requirements. Traffic signs will comply with the Traffic Signs Regulations and General Directions 2016 and its subsequent amendments. At required locations, temporary speed limits would be introduced to enhance management of traffic.
- 4.3.3 The GCC cables would be buried below ground and would typically be installed using an open trench method. At this stage, the number of potential trenchless crossing (such as Horizontal Directional Drilling (HDD)) locations have not been identified, **Outline Cable Construction Method Statement [EN0110020/APP/5.19]** provides more information on potential crossing locations and methods.
- 4.3.4 Open-cut installation may alternatively be used for the roads which are crossed by the GCC. Wherever practical, these roads will use temporary traffic management measures, such as lane closures to facilitate implementation rather than full road closures.
- 4.3.5 The exact methodology for implementing temporary traffic management will be determined by the contractor once appointed and designed to minimise any potential effects as far as possible. Further detail will be provided within the final CTMP. These are to be collaborated on with the relevant LHAs, after completion of Road Safety Audits (RSA), Stopping Sight Distance (SSD) forward visibility drawings and Vertical visibility assessments, and road condition assessments as required.

4.4 Crossing Points

- 4.4.1 It should be noted that the construction access points will be gated following the implementation of fencing early on in the construction phase, and supporting measures (e.g. traffic marshals and signage) will safely facilitate construction vehicles as they enter or exit the carriageway where a need has been specified and agreed with the LHA.

4.5 HGV Management Measures and Controls

- 4.5.1 The CTMP is likely to include the following measures to manage HGV deliveries to the Site and Cable Corridor:
- Designing entry / exit points onto the road network in accordance with national road design standards and in consultation with the local highway authority to ensure safety;
 - Managing interactions with the public road network through visibility splays, signage, and traffic controls, with construction traffic yielding to other road users;
 - Distributing details of vehicle routes to workers to reduce peak-time congestion in sensitive areas;
 - Scheduling HGV movements outside of peak traffic hours to avoid additional congestion;
 - Implementing a delivery management system to regulate HGV arrival times and monitor compliance with routing and scheduling;
 - Monitoring HGV routes and delivery times to ensure adherence to agreed protocols and address any non-compliance;
 - Employing specialised haulage services for abnormal loads, including necessary permits and coordination with relevant authorities.

Delivery Management System

- 4.5.2 A Delivery Management System (DMS) would be implemented as part of the CTMP to control bookings of HGV deliveries from the start of the construction phase. This will be used to regulate the arrival times of HGVs via timed delivery slots, as well to monitor compliance of proposed HGV routing. In addition, adequate space will be made available within the site at access junctions to ensure no queuing back onto the surrounding road network occurs.

Traffic Management and Monitoring

- 4.5.3 A Traffic Management and Monitoring System (TMMS) will be considered for implementation as part of the CTMP to provide details of the technologies and other means employed to monitor HGVs to/from the Compounds (e.g. Global Positioning System (GPS) and Automatic Number Plate Recognition (ANPR)). This will enable the Applicant to monitor the following:
- Compliance with the HGV routes;
 - Compliance with the number of HGV limits in terms of the number of deliveries arriving and departing at any one time and over the course of the day; and

- Compliance with the timing restrictions.

- 4.5.4 In addition, the TMMS will also record all LGVs which enter and exit the Site, to allow all vehicles to be monitored accordingly. In the instance that a complaint has been made in relation to inappropriate routes being used, then this will be cross-referenced with the TMMS to allow appropriate actions to then be taken.
- 4.5.5 The precise form of TMMS will be determined following the appointment of a contractor and will be set out in the CTMP. This would include a summary of the contractual requirements that those visiting the Site will have to adhere to, along with the measures to be taken for non-compliance.

HGV Routing

- 4.5.6 HGVs will be required to comply with the HGV and AIL routing strategy, apart from in the case of exceptional circumstances where the proposed routing to the Site is compromised due to an incident or road closure for example. In this circumstance, it is considered acceptable for HGVs to be redirected via an alternative route or to deliver outside of the established scheduling if required. Backloading of vehicles is also likely to be implemented.

HGV and AIL Timing Restrictions

- 4.5.7 To reduce the potential impact of HGV and AIL deliveries, the arrival and departure times will be managed to minimise the number of HGVs travelling to the Site during the network peak hours for the local highway network. For example, HGVs could be delayed in the afternoon to avoid being released from the Site during the PM network peak hour.
- 4.5.8 The timing restrictions, considered likely to be implemented within the CTMP at this stage are:
- Avoiding arrivals or departures on a weekday during the network peak hours (08:00–09:00 and 17:00–18:00);
 - Limiting deliveries to between the hours of 09:00 and 16:00;
 - No arrivals or departures on Saturday before 08:00 or after 13:00;
 - No arrivals or departures on Sundays or public holidays.

Traffic Marshalling and Site Management

- 4.5.9 Suitably qualified traffic marshals will be positioned at the proposed Site accesses, and at any crossing points between the road network and the Site during the construction phase to ensure vehicle movements are controlled safely.
- 4.5.10 Visibility will be maximised between construction vehicles and other users at the crossing points (e.g. through hedgerow clearance if required), and advanced signage will be provided to warn users of the potential presence of construction vehicles. Staffed controls will be provided at each crossing point (including traffic marshals and gates), with a default priority that construction traffic will give way to other users.

Communications Strategy

- 4.5.11 A communications strategy will be developed, set out in the CTMP and will be communicated with those working on the Site. This would include an information pack setting out the contractual requirements which will be provided to the contractors. Furthermore, regular meetings will be held with contractors to discuss HGV management and to address any issues associated with travel to/from the Site, as well as to relay information including any restrictions and requirements which should be followed.

Site Access Arrangements

- 4.5.12 The Site access layouts have been designed to accommodate HGVs and other construction vehicles as shown by the vehicle swept path analysis, as provided in **Appendix A-3 Proposed Access Layouts, Visibility Splays and Swept Paths**. A hardstanding surface will be provided at the proposed accesses to ensure the weight of the HGVs can be accommodated. In addition, wheel washing facilities will be provided within each temporary construction compound to prevent mud from being trafficked onto the highway.
- 4.5.13 Vegetation clearance will be carried out at the proposed Site accesses where required in order to achieve appropriate levels of visibility as agreed with the local authorities as shown in **Appendix A-3 Proposed Access Layouts, Visibility Splays and Swept Paths**.

Abnormal Indivisible Loads (AILs)

- 4.5.14 AILs will be required to deliver transformer units. A specialised haulage service will be employed to allow these components to be transported with the necessary escort, permits and traffic management, with the contractor consulting the relevant highways authorities to ensure the correct permits are obtained. The police will also be given advanced notification under the Road Vehicle Authorisation of Special Types Order 2003.
- 4.5.15 All AILs will be expected to follow the agreed HGV routing strategy when travelling to/from the Site. Further details related to the AILs will be included within the final CTMP for the Proposed Development.

4.6 Worker Vehicle Measures and Controls

- 4.6.1 Worker movements will be managed through the implementation of the following measures:
- Implementation of a Worker Travel Plan;
 - Worker arrival and departure times;
 - Limited and allocated car parking;
 - Car sharing;
 - Minibus service.

Worker Travel Plan

- 4.6.2 A Worker Travel Plan will be developed, to manage the arrival and departure profile of workers and to encourage sustainable modes of transport, especially car-sharing. A package of measures would include:
- Provision of public transport information to access where workers will be resident or collected from by buses provided under the Worker Travel Plan, so there is no need for non-local workers to bring cars to the wider area;
 - Minibus service for transport of non-local construction workers;
 - Promotion of a car sharing scheme; and
 - Car parking management.
- 4.6.3 The Worker Travel Plan will be developed to reduce the number of single occupancy car journeys to and from the Proposed Development during construction and will minimise traffic on the local road network.
- 4.6.4 The Worker Travel Plan will be administered by the CTMP Co-ordinator and would be a contractual requirement as part of the Principal Contractor's contract with the Applicant.
- 4.6.5 The Worker Travel Plan will include targets to reduce car use during construction and will apply to Site visitors, where it is practical to do so.
- 4.6.6 The Worker Travel Plan will be monitored by the Applicant's agents to ensure that it remains effective and that all contractors are abiding by it.

Worker Arrival and Departure Times

- 4.6.7 The proposed summer working hours will be between the hours of 07:00 and 19:00 on weekdays and between 07:00 and 13:00 on Saturdays and as such few or no worker vehicle movements are anticipated during the weekday network peak hours.
- 4.6.8 During the winter months, worker numbers may be reduced, with the workers possibly arriving at the Site later and departing the Site earlier and working shorter hours. These traffic movements would still occur outside the network peak hours, so these key periods would not be impacted. In addition, the percentage increase in traffic would likely be lower in this situation due to higher traffic baseline in later hours in the AM period and earlier hours in the PM period. The assessment of worker traffic during the summer months therefore represents a robust worst-case scenario.
- 4.6.9 Any other on-site works where construction workers are moving outside of the above working hours are anticipated to be limited.

Car Parking

- 4.6.10 During the construction phase, parking will be provided at the Site, as well as at temporary construction compounds for the Cable Corridor.
- 4.6.11 Limited, but sufficient on-site car and cycle parking to accommodate the expected parking demand of workers for the Proposed Development will be provided.

Car Sharing

- 4.6.12 To reduce the potential impact of vehicles associated with workers that are locally based during the construction phase, the contractor will implement measures to encourage car sharing to reduce the number of vehicles travelling to/from the Site each day. The benefits of car sharing will be promoted to encourage multi-occupancy vehicle use, such as reduced fuel costs and ease of parking with guaranteed spaces for those workers car sharing onsite.
- 4.6.13 A car share scheme will be implemented to match potential sharers and to help workers identify any colleagues who could potentially be collected along their route to/from the Site. It should be noted that parking will be limited to encourage workers to travel together.
- 4.6.14 A minimum occupancy rate of 1.2 persons per vehicle for locally based workers (an assumption adopted within **ES Volume 3, Appendix 13.2: Transport Statement [EN0110020/APP/6.20]** is expected; however, the aspiration is to achieve a higher average occupancy level to further reduce the impact of the Proposed Development on the local highway network and the SRN.

Minibus Service

- 4.6.15 As detailed within **ES Volume 3, Appendix 13.2: Transport Statement [EN0110020/APP/6.20]** it has been assumed that 20% of workers will travel to the Site via minibus, due to living in local villages and towns or staying in hotels within these areas. The locations and routes of the shuttle services are yet to be determined, though drivers would be directed to use the most direct route across the SRN to deliver workers to the Compounds from local areas. Further details will be confirmed as part of the CTMP.
- 4.6.16 The following assumptions have been adopted for the shuttle service which will be provided for non-local workers travelling to/from the Site, with further details to be confirmed as part of the CTMP:
- The shuttle services will travel between the Site and local worker accommodation to transfer all non-local workers to/from the Site each day;
 - The shuttle services will depart from the Site to pick up construction workers from local worker accommodation and residential areas and return to the Site before the start of a shift;
 - The shuttle services will depart from the Site to drop off construction workers back at their local worker accommodation within the hour after the completion of a shift (before returning back to the Site);
 - The shuttle services will each be expected to have an average occupancy of 8 people when transferring construction workers;
- 4.6.17 The above is designed to minimise vehicle trips on the surrounding highway network as far as practicable.

Internal Movements

- 4.6.18 Minibuses will also be used to transport workers around the Site by making use of the internal routes wherever practicable to travel. This will minimise trips and will also avoid trips on the surrounding highway network.

4.7 Management Structure

- 4.7.1 The overall management and implementation of the CTMP will be the responsibility of the Applicant. A Traffic Safety Control Officer will be appointed by the Applicant to develop, implement and manage the CTMP. On behalf of the Applicant, the Traffic Safety Control Officer will:
- Implement and monitor the CTMP to identify successful measures and areas for improvement;
 - Promote the CTMP to all workers and contractors travelling to and from the Site to ensure compliance with its contents;
 - Liaise as appropriate with local transport and traffic groups, local planning authorities, local highway authorities and National Highways; Monitor data relating to HGV routes, timing of HGV arrivals and departures and compliance with the HGV routing;
 - Manage the Car Share Scheme;
 - Manage the minibuss service between local worker accommodation and the Site; and
 - Discuss any issues with relevant parties and identify any amendments to the CTMP (including measures) to ensure compliance is maintained.

4.8 Monitoring and Review

HGVs

- 4.8.1 The CTMP will be monitored and revised to ensure that contractors are complying with the document. This process will be led by the Traffic Safety Control Officer.
- 4.8.2 The Traffic Safety Control Officer will monitor data relating to HGV routes, the timing of HGV arrivals and departures and compliance with the HGV routing plans set out. The results of the data monitoring will be reported to identify any issues which need to be resolved and any additional measures which should be implemented to these from arising again. The reports will be developed by the Applicant as part of the CTMP and shared with the contractor.
- 4.8.3 All fuel will be transported by suitably qualified contractors, and all regulations for the transportation and storage of hazardous substances will be observed.

Worker Vehicles

- 4.8.4 Construction worker vehicles will be monitored when entering and exiting the Site accesses to determine routes workers may be taking to travel to the Site. This monitoring will determine whether any additional measures should be explored to minimise workers trips on the local highway network.
- 4.8.5 Construction workers will be directed to available parking bays upon arrival to assist them in parking in a timely manner. Given the working patterns identified, it is expected that the car parks at the compounds will be managed between 06:30-07:00 and between 19:00-19:30 in the summer when the majority of workers are expected to arrive/depart. During the winter months, worker parking will be managed accordingly based on varied arrival and departure times.

Additional Monitoring

- 4.8.6 The following monitoring will also be carried out during the construction phase, and secured as part of the CTMP:
- Construction vehicles will be monitored to ensure drivers are adhering to the agreed routing strategy; and
 - Vehicle safety will be monitored within the Site, including at the PRow crossing points, temporary PRow diversion points, and Grid Connection Corridor intersection points.
 - Road condition surveys to monitor adverse effects on the local road network

5 COMPLIANCE AND ENFORCEMENT

- 5.1.1 This section of the oCTMP provides a summary of the mechanisms that will be implemented to maximise compliance with the CTMP.

5.2 Good Practice

- 5.2.1 The Applicant will use internal management procedures to maximise compliance and its enforcement with the requirements of the CTMP, including:
- Contractor kick-off meetings: contractors will be reminded of the Applicant's standards and expectations as set out in contract documentation.
 - Site induction: drivers will be briefed on the aims and objectives of the CTMP, including the booking system, designated routes and expected driver behaviour. A copy of the CTMP will be provided to each contractor to provide details of how the Site will be managed as well as the rules and regulations.
 - Reporting: incidents of non-compliance will be investigated within the CTMP. Reports from each incident will be raised and shared with the relevant contractor. The CTMP will be updated where necessary to resolve any ongoing issues.

5.3 Contractual Conditions

- 5.3.1 Each contractor will be provided with a contract setting out their contractual requirements in terms of compliance with this oCTMP upon appointment. A copy of the oCTMP will be provided along with details of the agreed routing strategy for HGVs to ensure that this route is followed.


5.4 Information Packs and Communications

- 5.4.1 Information packs will be provided to all contractors once they have been confirmed. The information pack will form part of the agreement between the Applicant and the designated contractors. The information pack will include details of the following:
- Code of Good Practice;
 - Details of the Traffic Safety Control Officer;
 - Delivery routing restrictions;
 - Worker routing;
 - Emergency procedures;
 - Non-compliance guidance; and
 - Complaint procedures.



5.5 Enforcement

- 5.5.1 The Applicant and contractor will be committed to ensuring compliance with the CTMP. The following steps would be taken:
- 5.5.2 The Traffic Safety Control Officer will notify the Applicant where compliance with the CTMP is being breached.
- The Applicant will issue a warning letter to the relevant contractor outlining what action would be taken in the event of any further noncompliance (in general terms).
 - The Applicant will report the details of the response to the Traffic Safety Control Officer as part of the monitoring report. The monitoring report will be made available to the relevant local planning authorities and relevant highway authorities at their request to ensure compliance and to demonstrate that action is being taken where necessary.
- 5.5.3 Further detail on the measures which could be applied will be included within the CTMP. Engagement with the local highway authorities regarding enforcement of the CTMP would also be required at this stage.

A.1 Access Point Locations

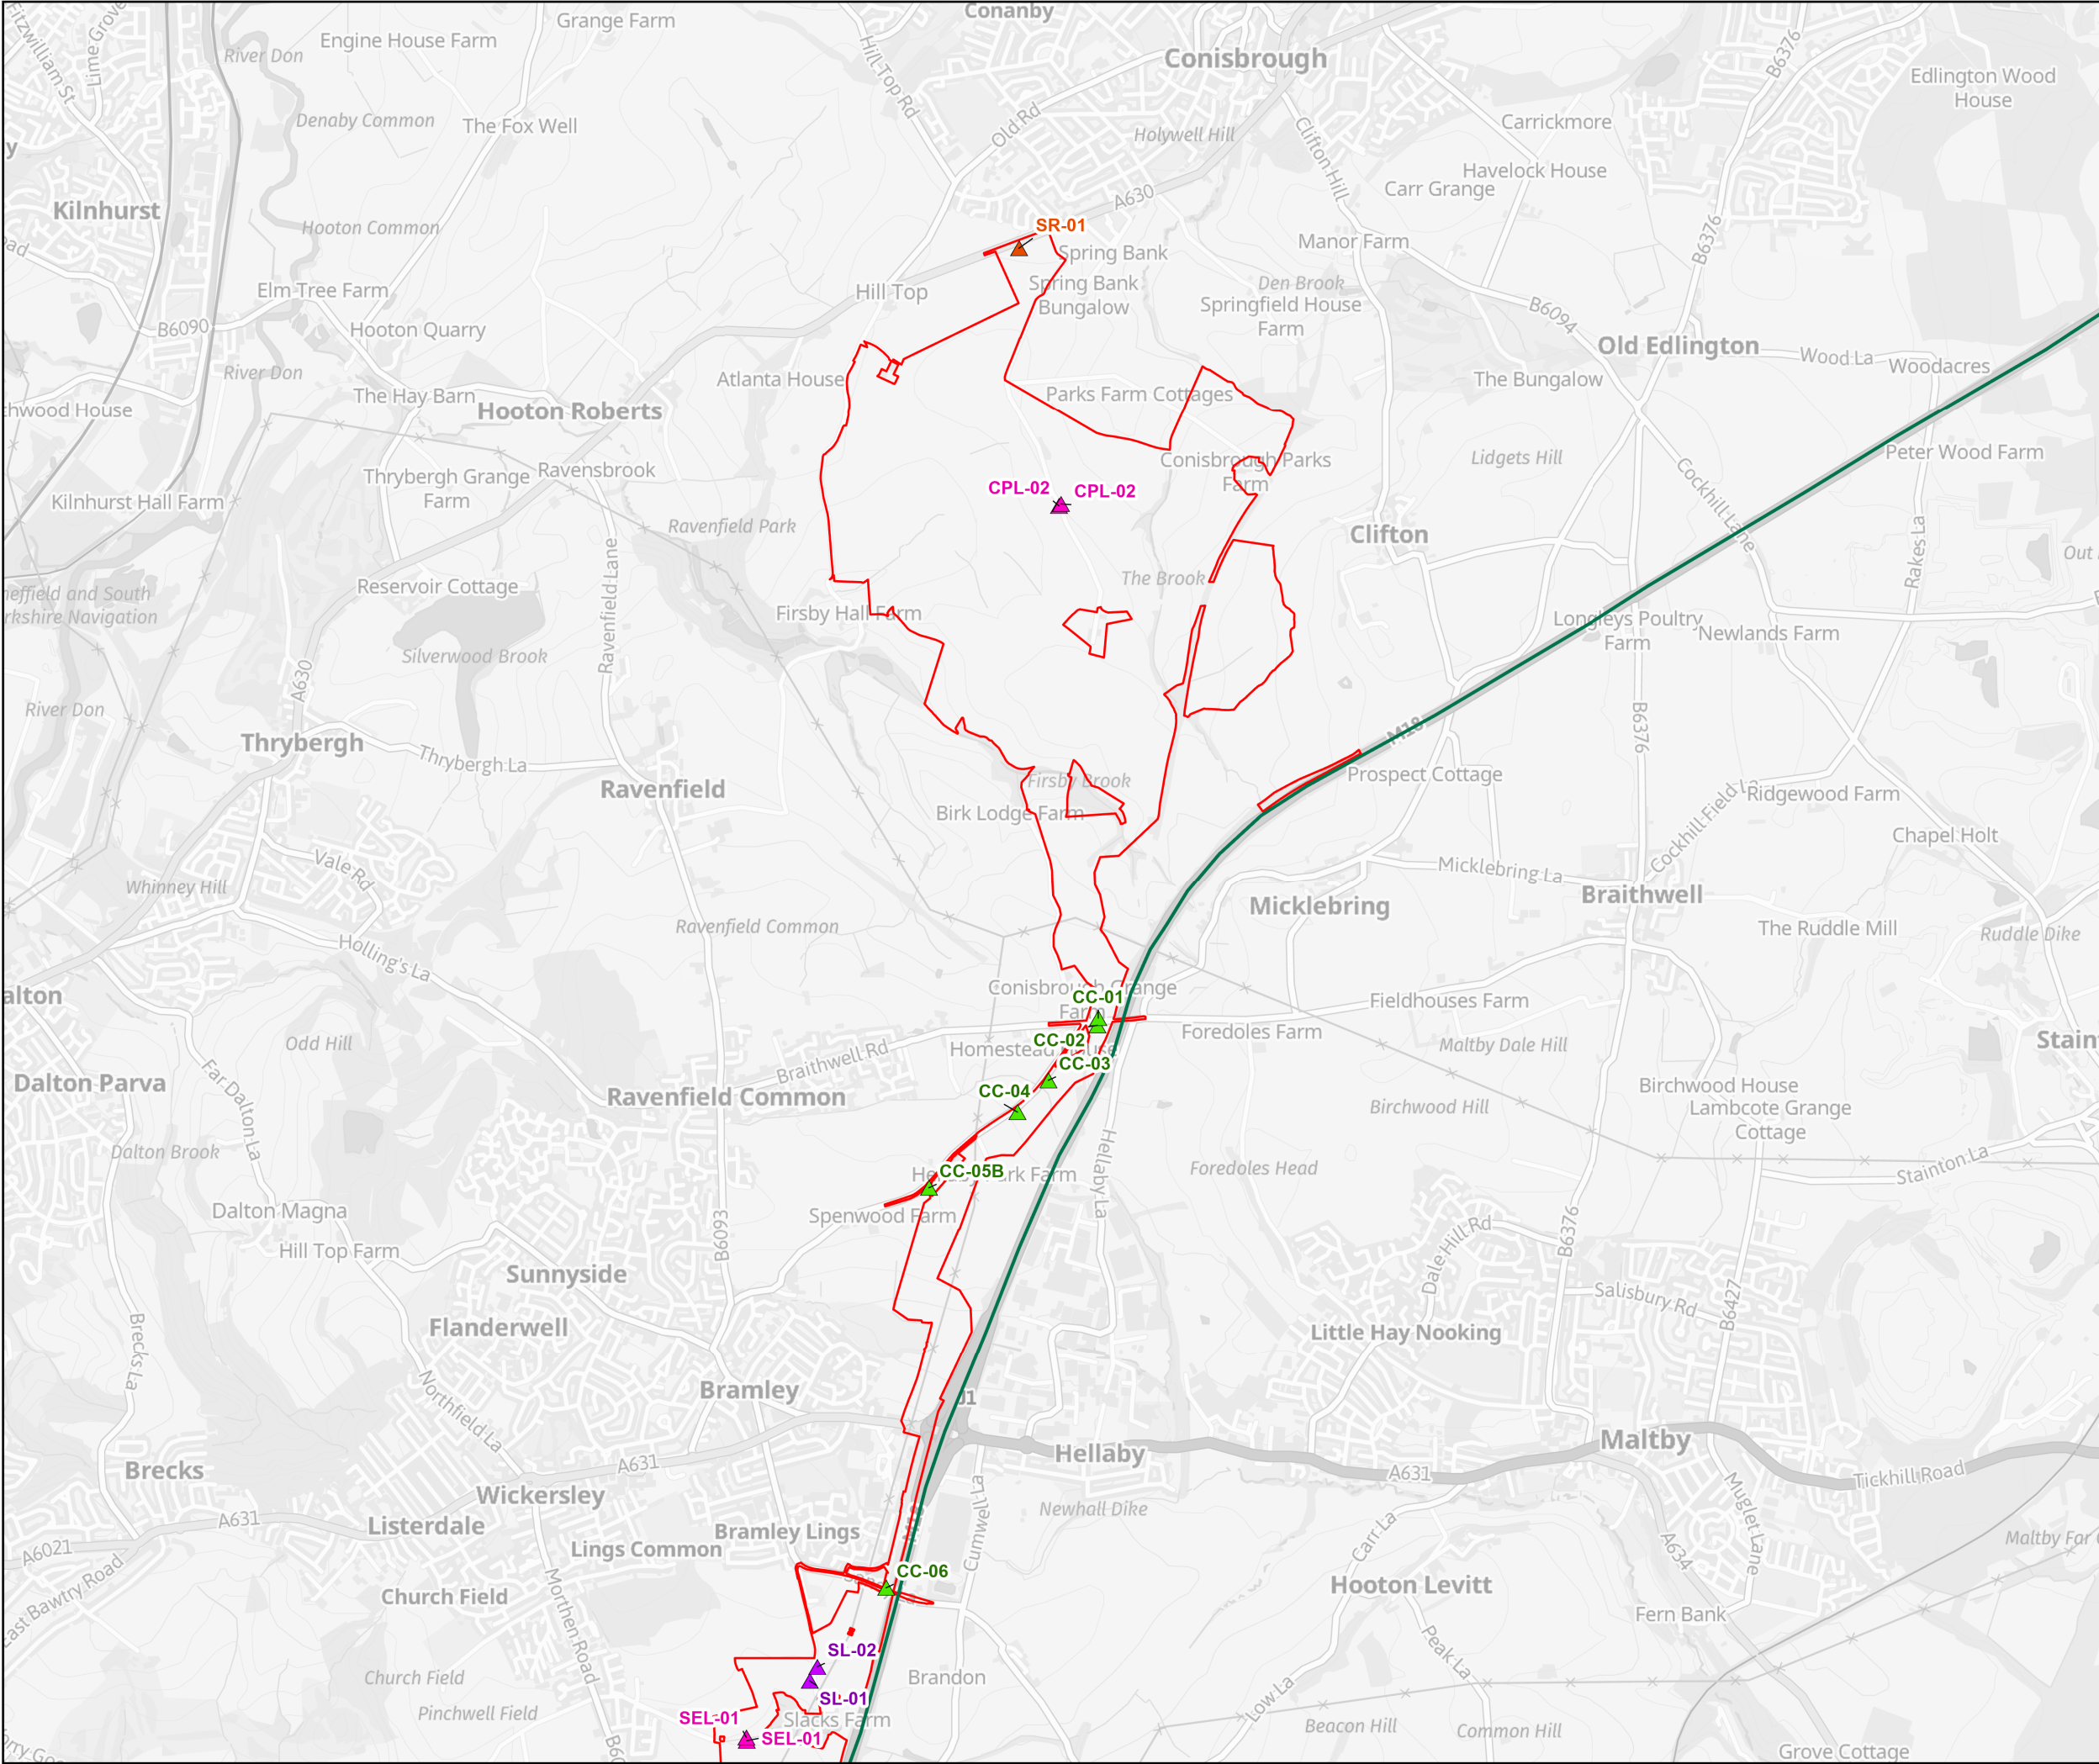

- Order Limits
- Solar PV Site Access Point
- Grid Connection Corridor Only Access Point
- Solar PV Site & Grid Connection Corridor Access Point
- Crossing Point
- M18 Motorway

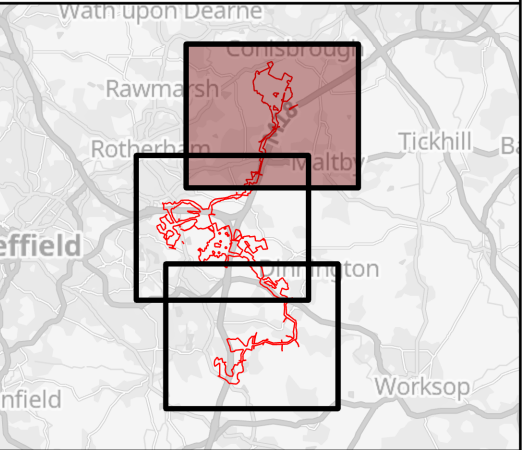


SCALE: 1:30,000	VERSION: A01
SIZE: A3	DRAWN: EB
APPLICATION: EN0110020	CHECKED: DF
DATE: 30/04/2026	APPROVED: AS



Whitestone Solar Farm
Outline Construction Traffic Management Plan
Appendix A.1
Access Point Locations
Sheet 1 of 3

Reference: EN0110020/APP/6.19
Infrastructure Planning (Applications: Prescribed
Forms and Procedure) Regulations 2009 -
Regulations 5(2)(a)



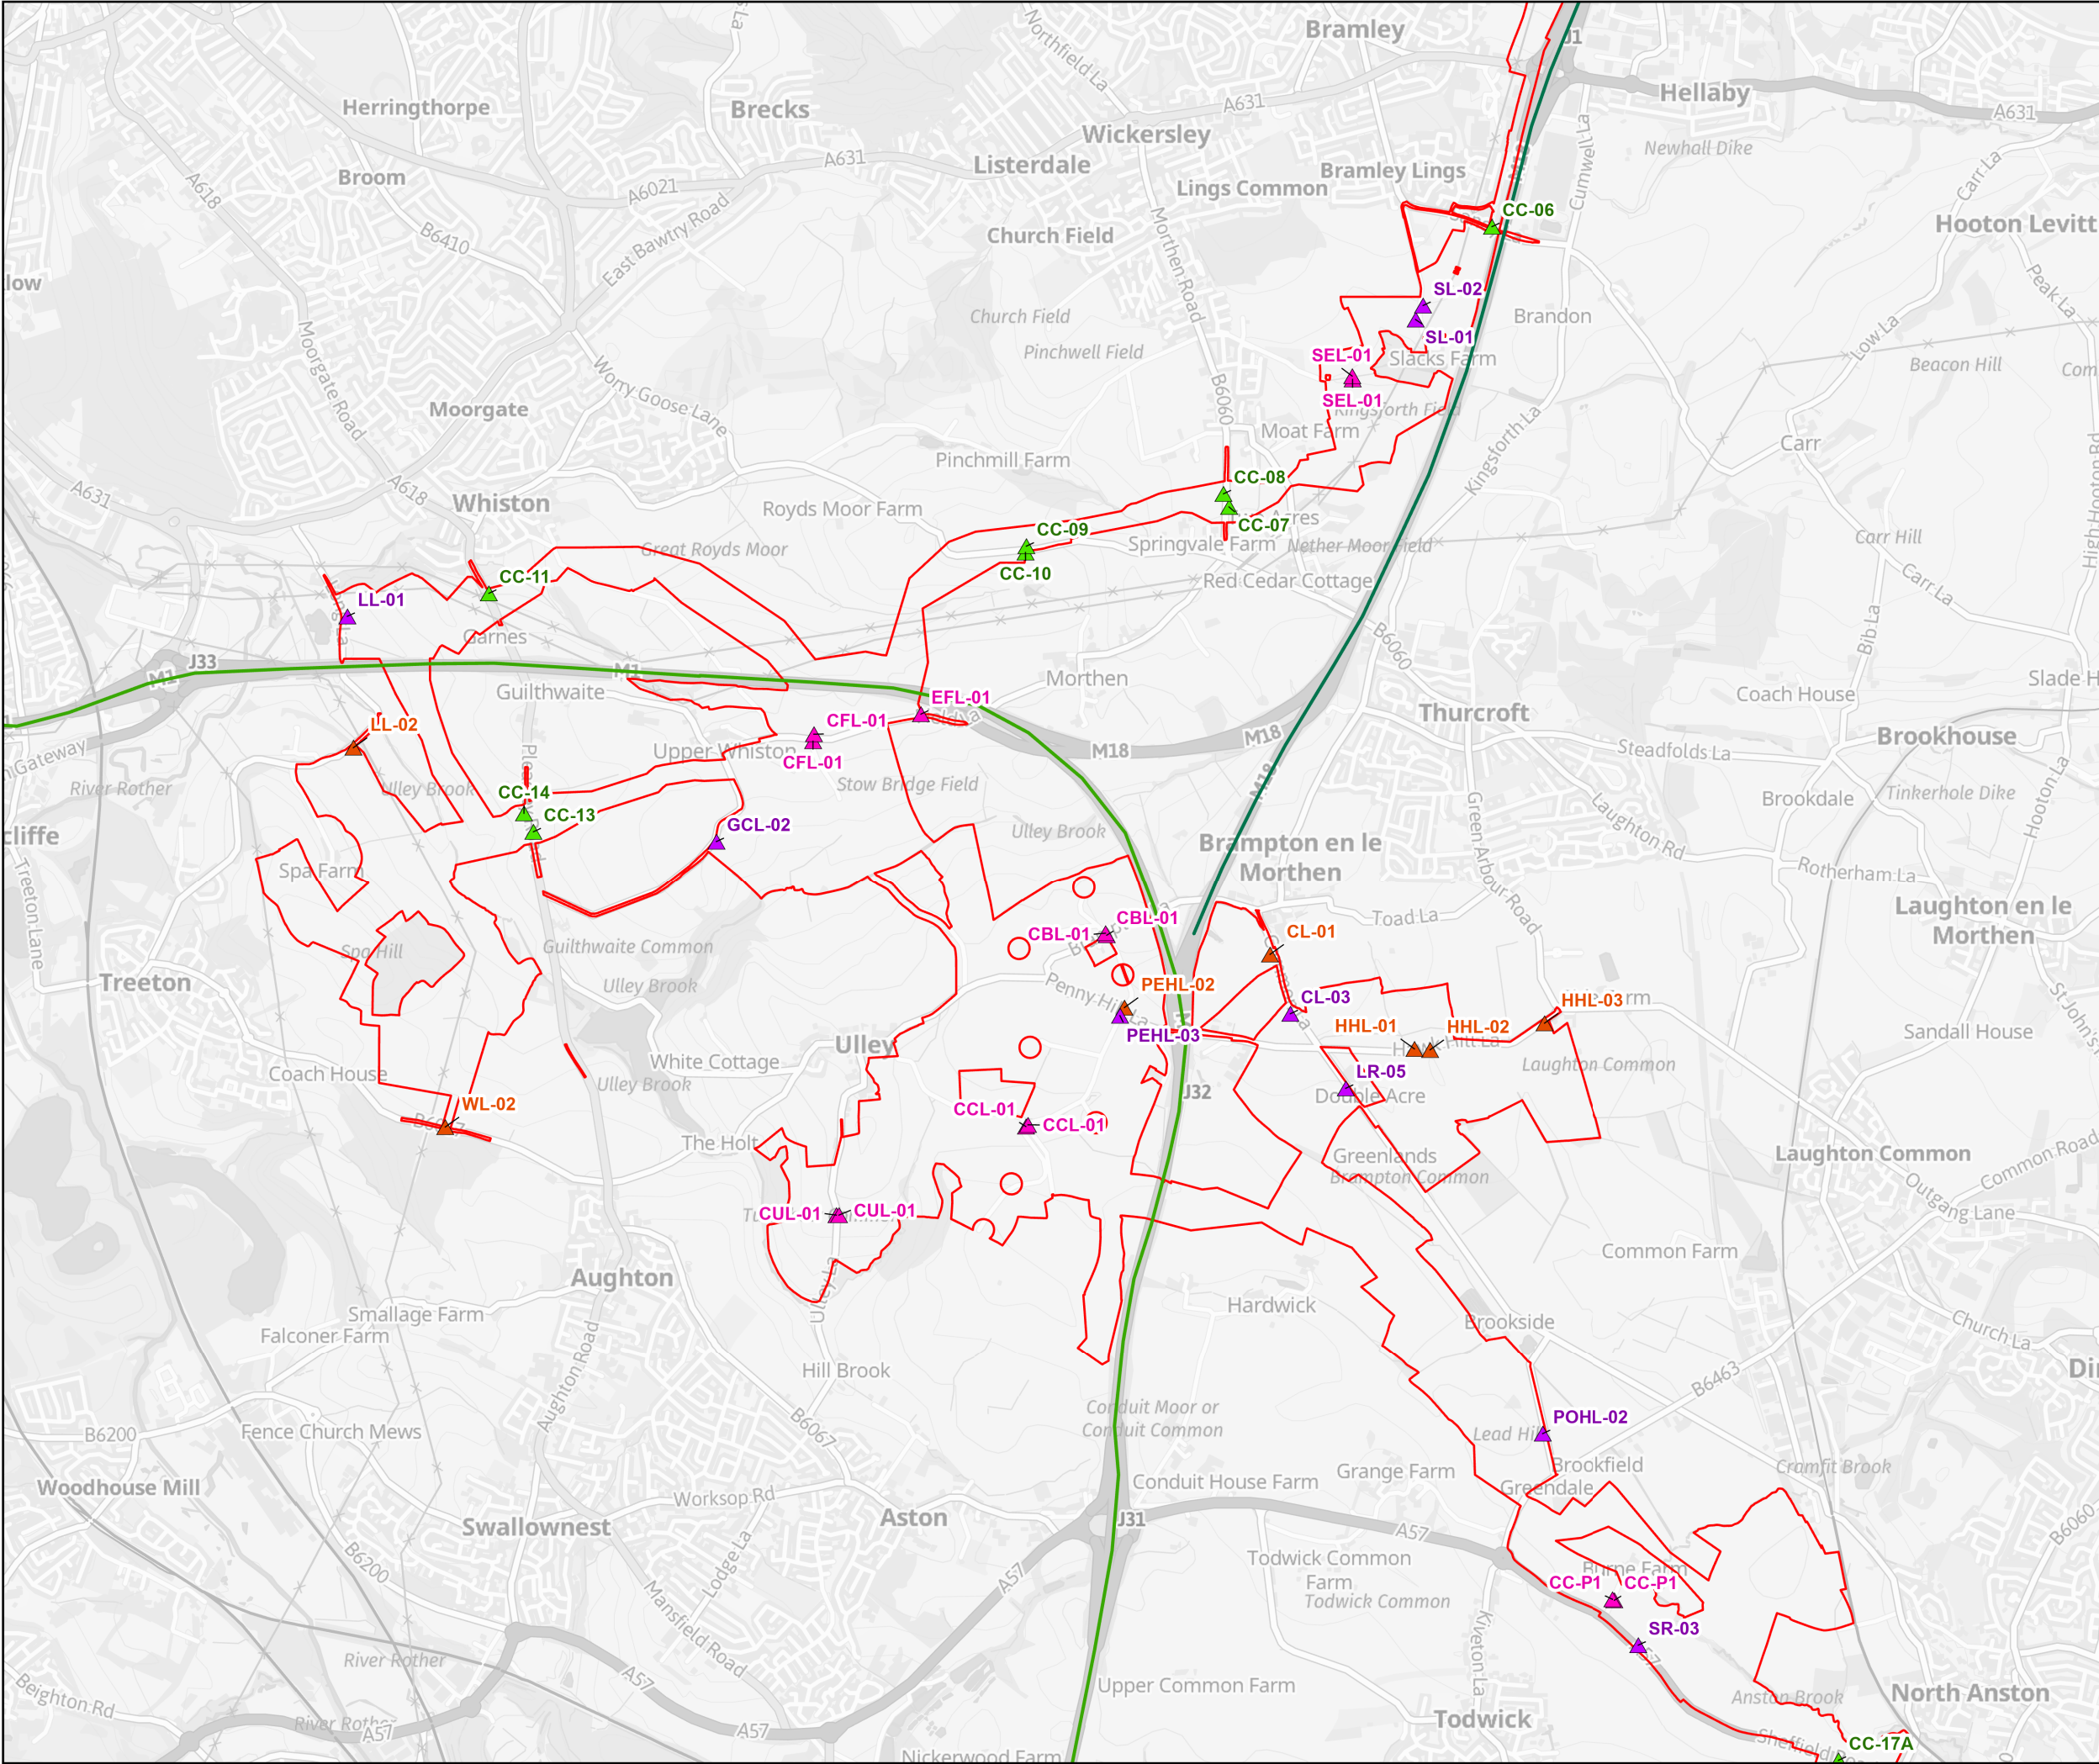

- Order Limits
- Solar PV Site Access Point
- Grid Connection Corridor Only Access Point
- Solar PV Site & Grid Connection Corridor Access Point
- Crossing Point
- M1 Motorway
- M18 Motorway

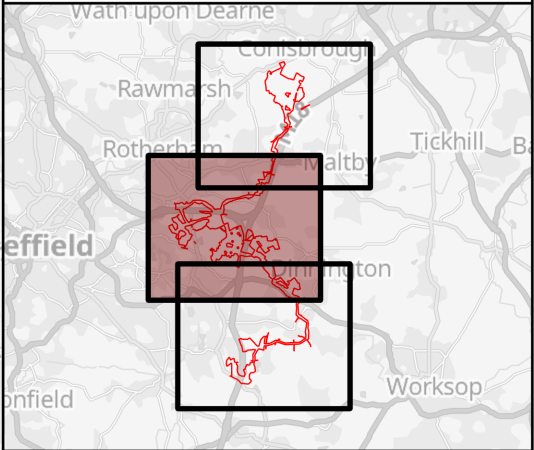


SCALE: 1:30,000	VERSION: A01
SIZE: A3	DRAWN: EB
APPLICATION: EN0110020	CHECKED: DF
DATE: 30/04/2026	APPROVED: AS



Whitestone Solar Farm
Outline Construction Traffic Management Plan
Appendix A.1
Access Point Locations
Sheet 2 of 3

Reference: EN0110020/APP/6.19
Infrastructure Planning (Applications: Prescribed
Forms and Procedure) Regulations 2009 -
Regulations 5(2)(a)



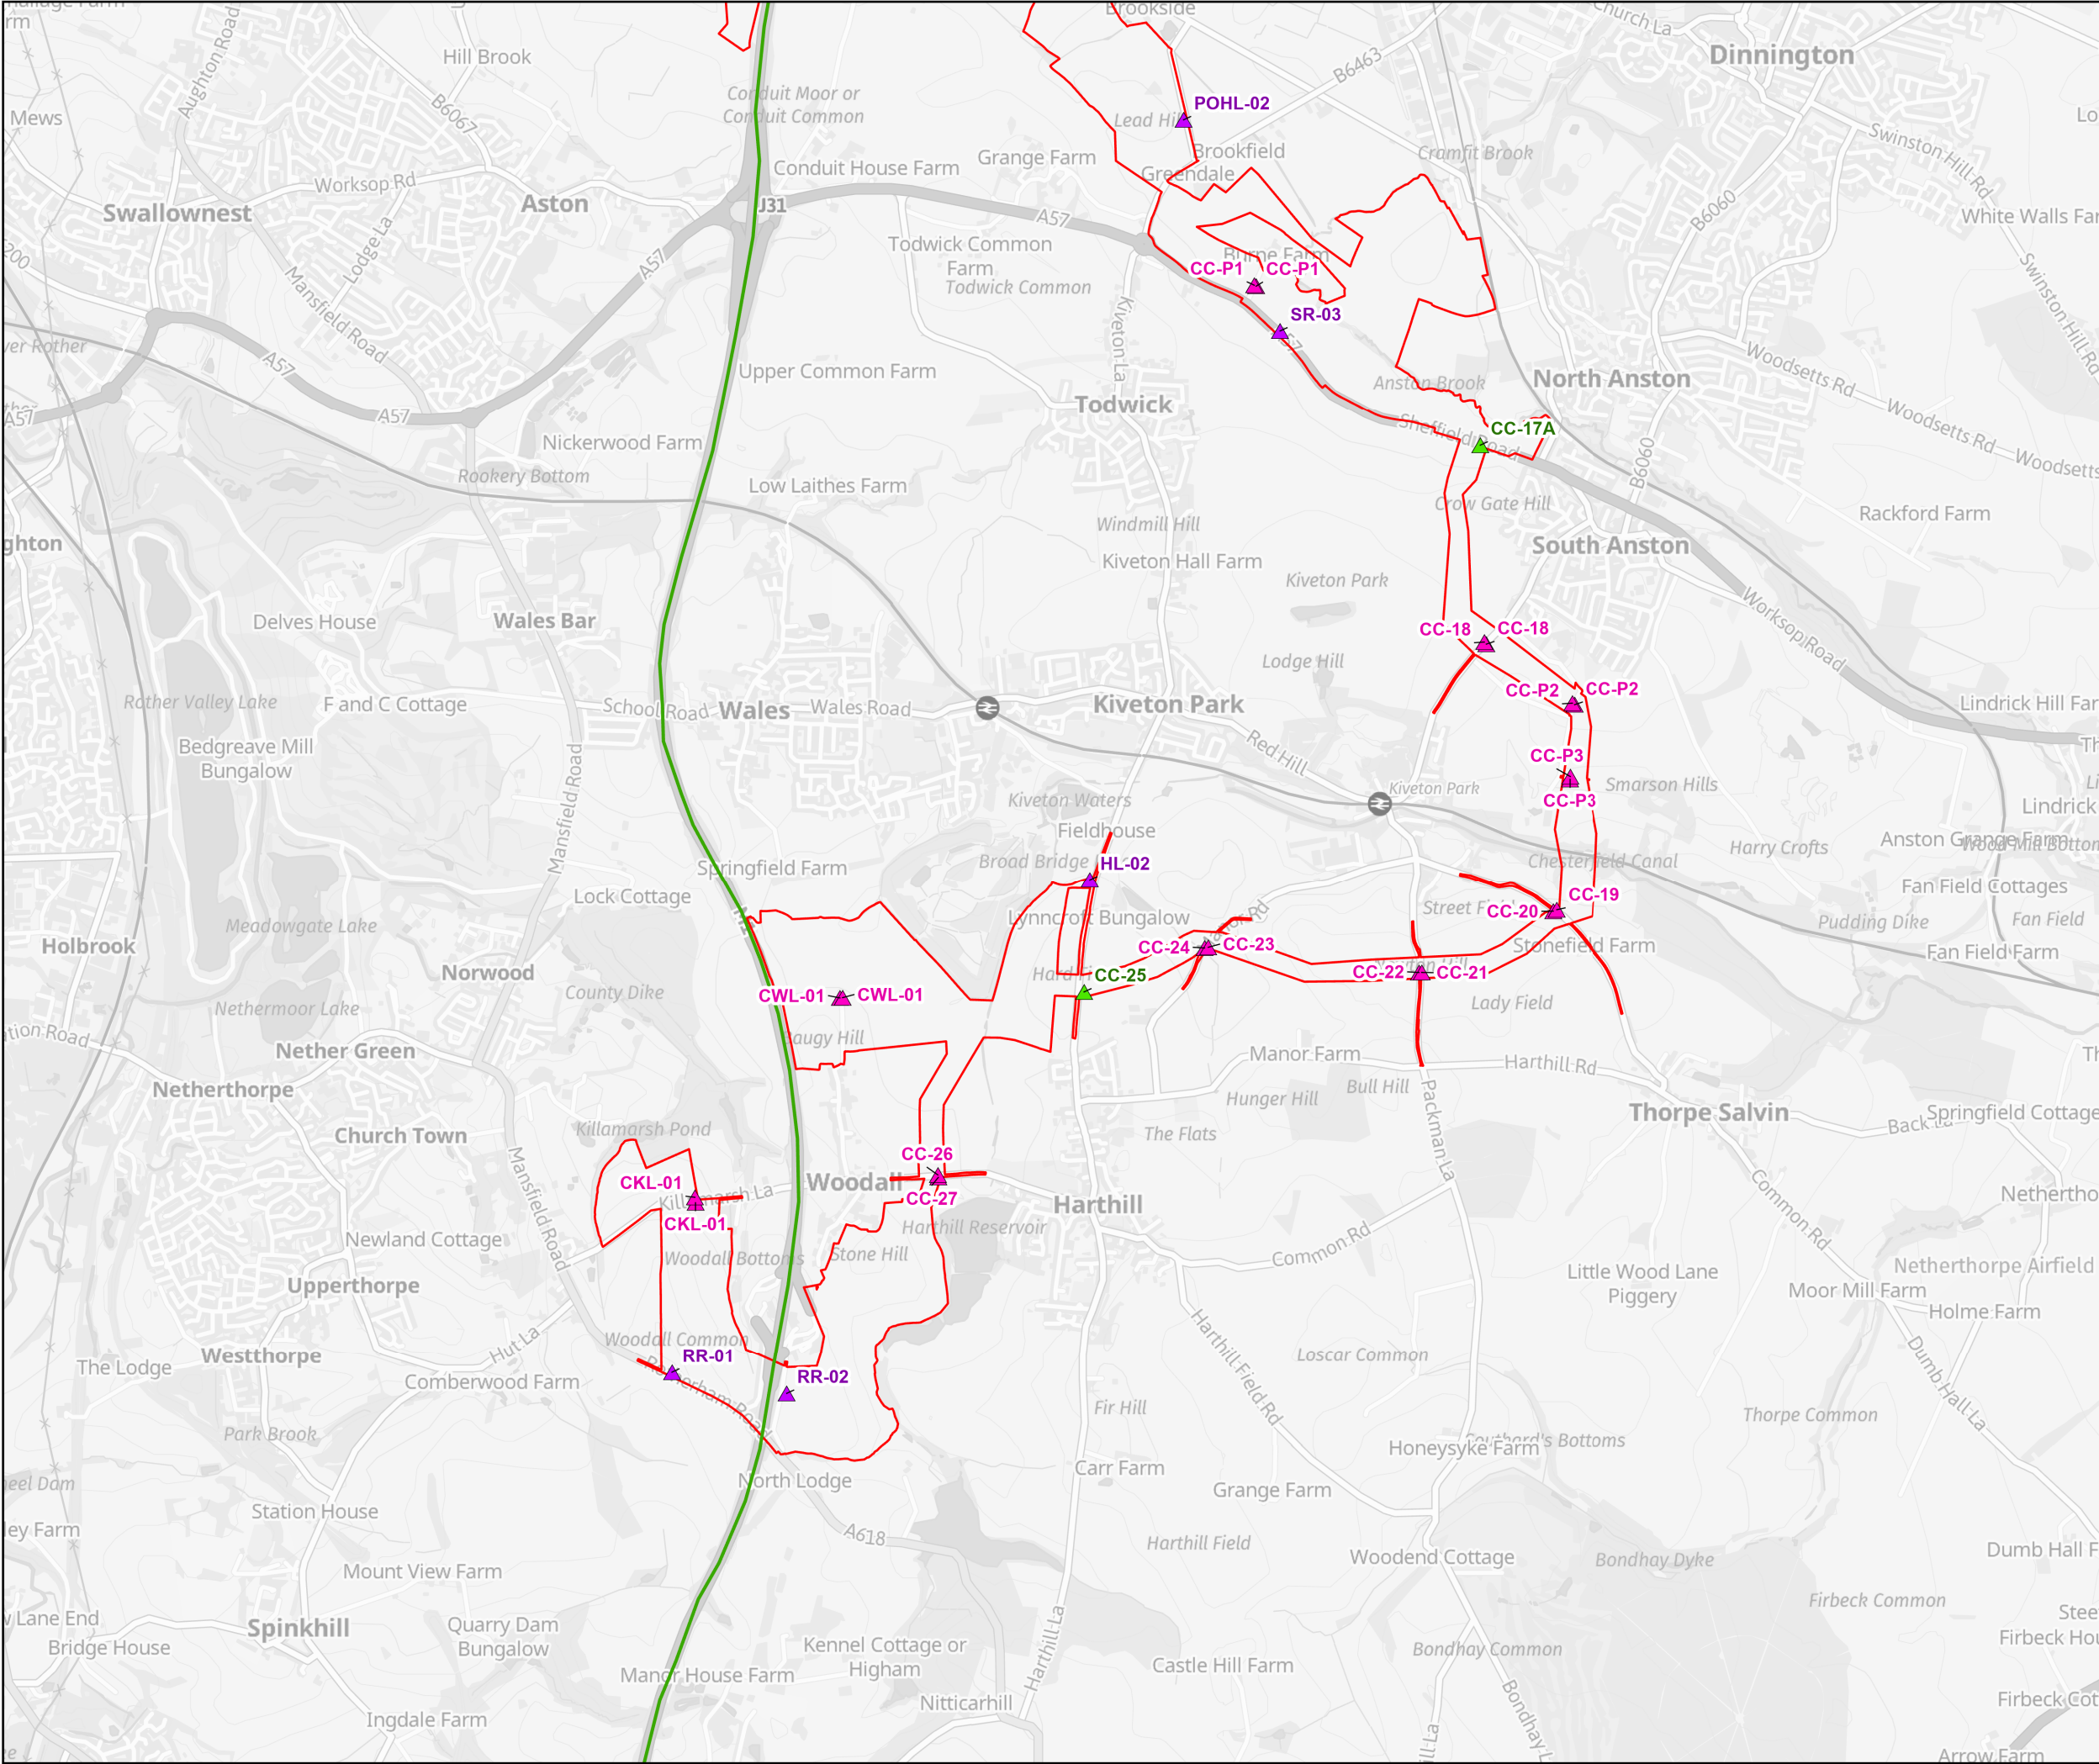

- Order Limits
- Grid Connection Corridor Only Access Point
- Solar PV Site & Grid Connection Corridor Access Point
- Crossing Point
- M1 Motorway

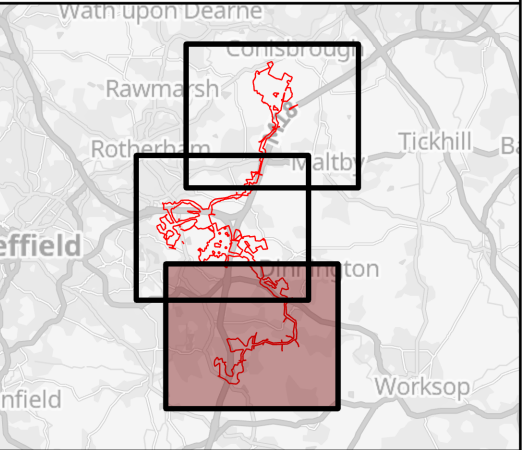


SCALE: 1:30,000	VERSION: A01
SIZE: A3	DRAWN: EB
APPLICATION: EN0110020	CHECKED: DF
DATE: 30/04/2026	APPROVED: AS

Whitestone Solar Farm
Outline Construction Traffic Management Plan
Appendix A.1
Access Point Locations
Sheet 3 of 3



Reference: EN0110020/APP/6.19
Infrastructure Planning (Applications: Prescribed
Forms and Procedure) Regulations 2009 -
Regulations 5(2)(a)



A.2 Site and Grid Connection Corridor Access Points

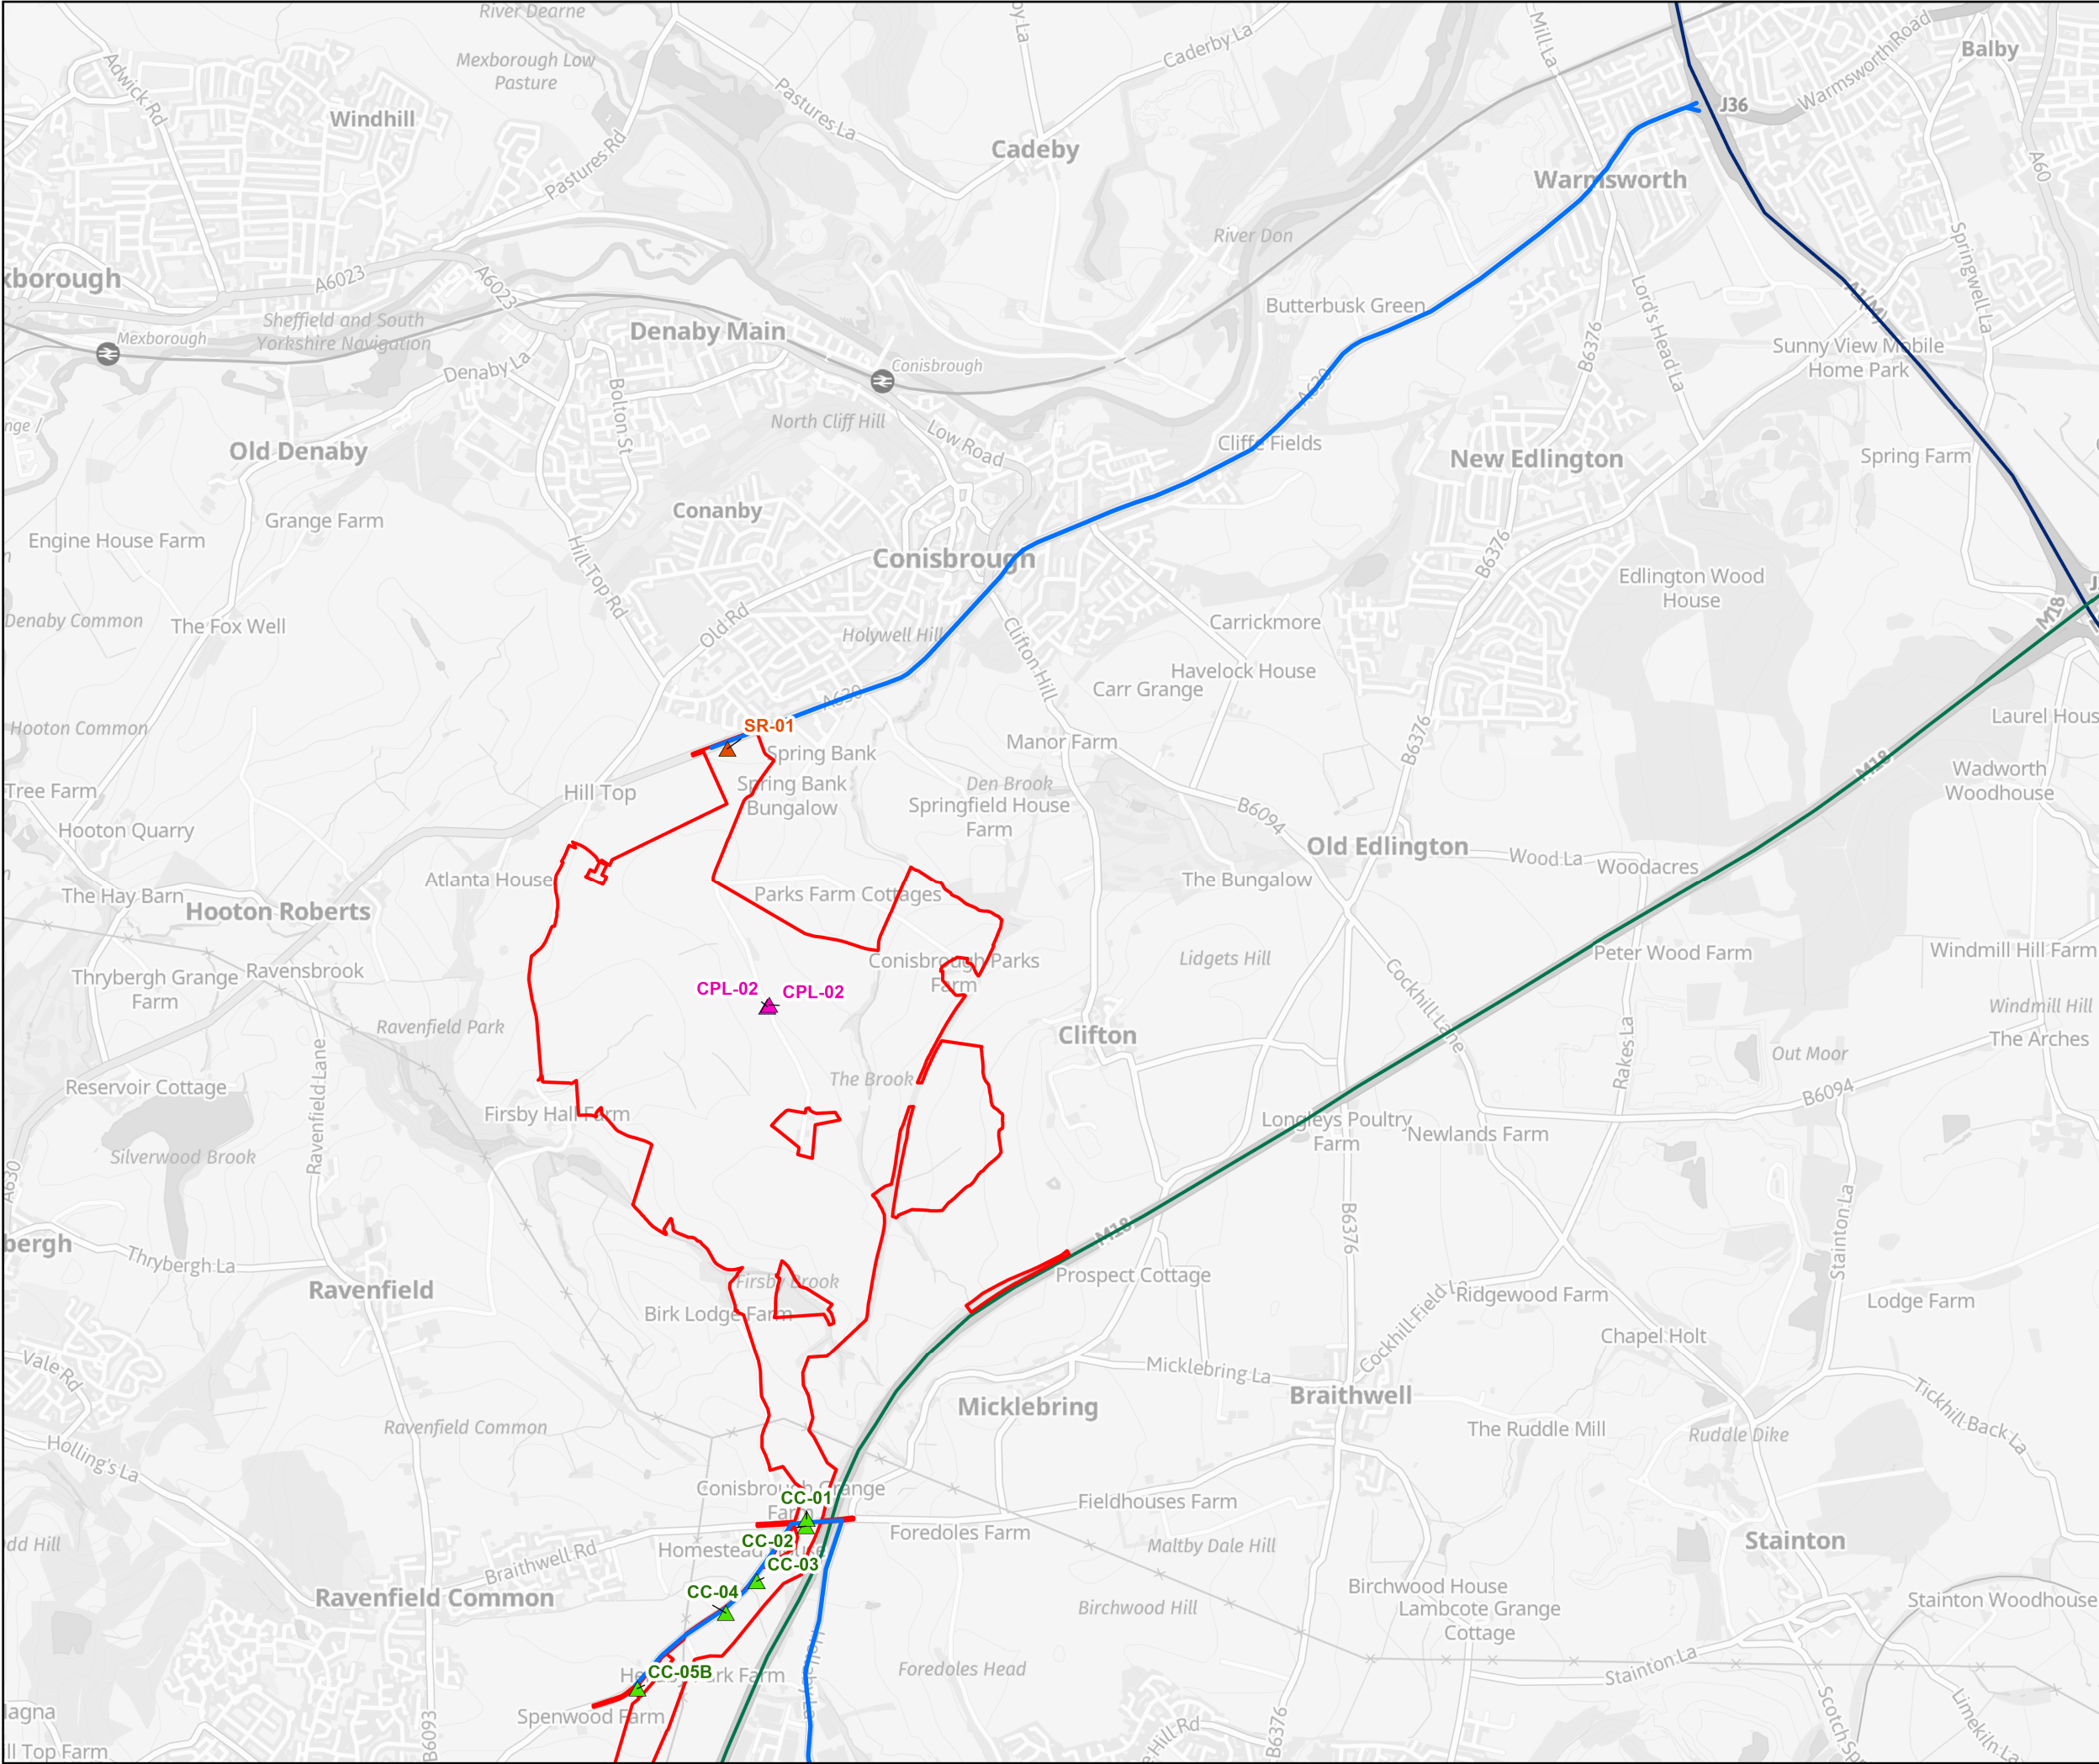


- Order Limits
- Solar PV Site Access Point
- Grid Connection Corridor Only Access Point
- Crossing Point
- Solar PV Site & Grid Connection Corridor Access Routes
- A1(M) Motorway
- M18 Motorway

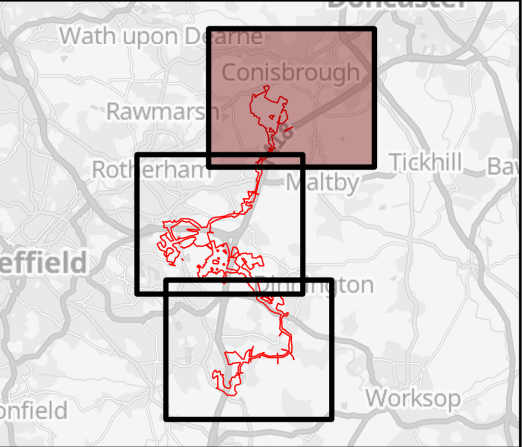


SCALE: 1:30,000	VERSION: A01
SIZE: A3	DRAWN: EB
APPLICATION: EN0110020	CHECKED: DF
DATE: 30/04/2026	APPROVED: AS



Whitestone Solar Farm
Outline Construction Traffic Management Plan
Appendix A.2
Site and Grid Connection Corridor Access Points
Sheet 1 of 3

Reference: EN0110020/APP/6.19
Infrastructure Planning (Applications: Prescribed Forms and Procedure) Regulations 2009 - Regulations 5(2)(a)



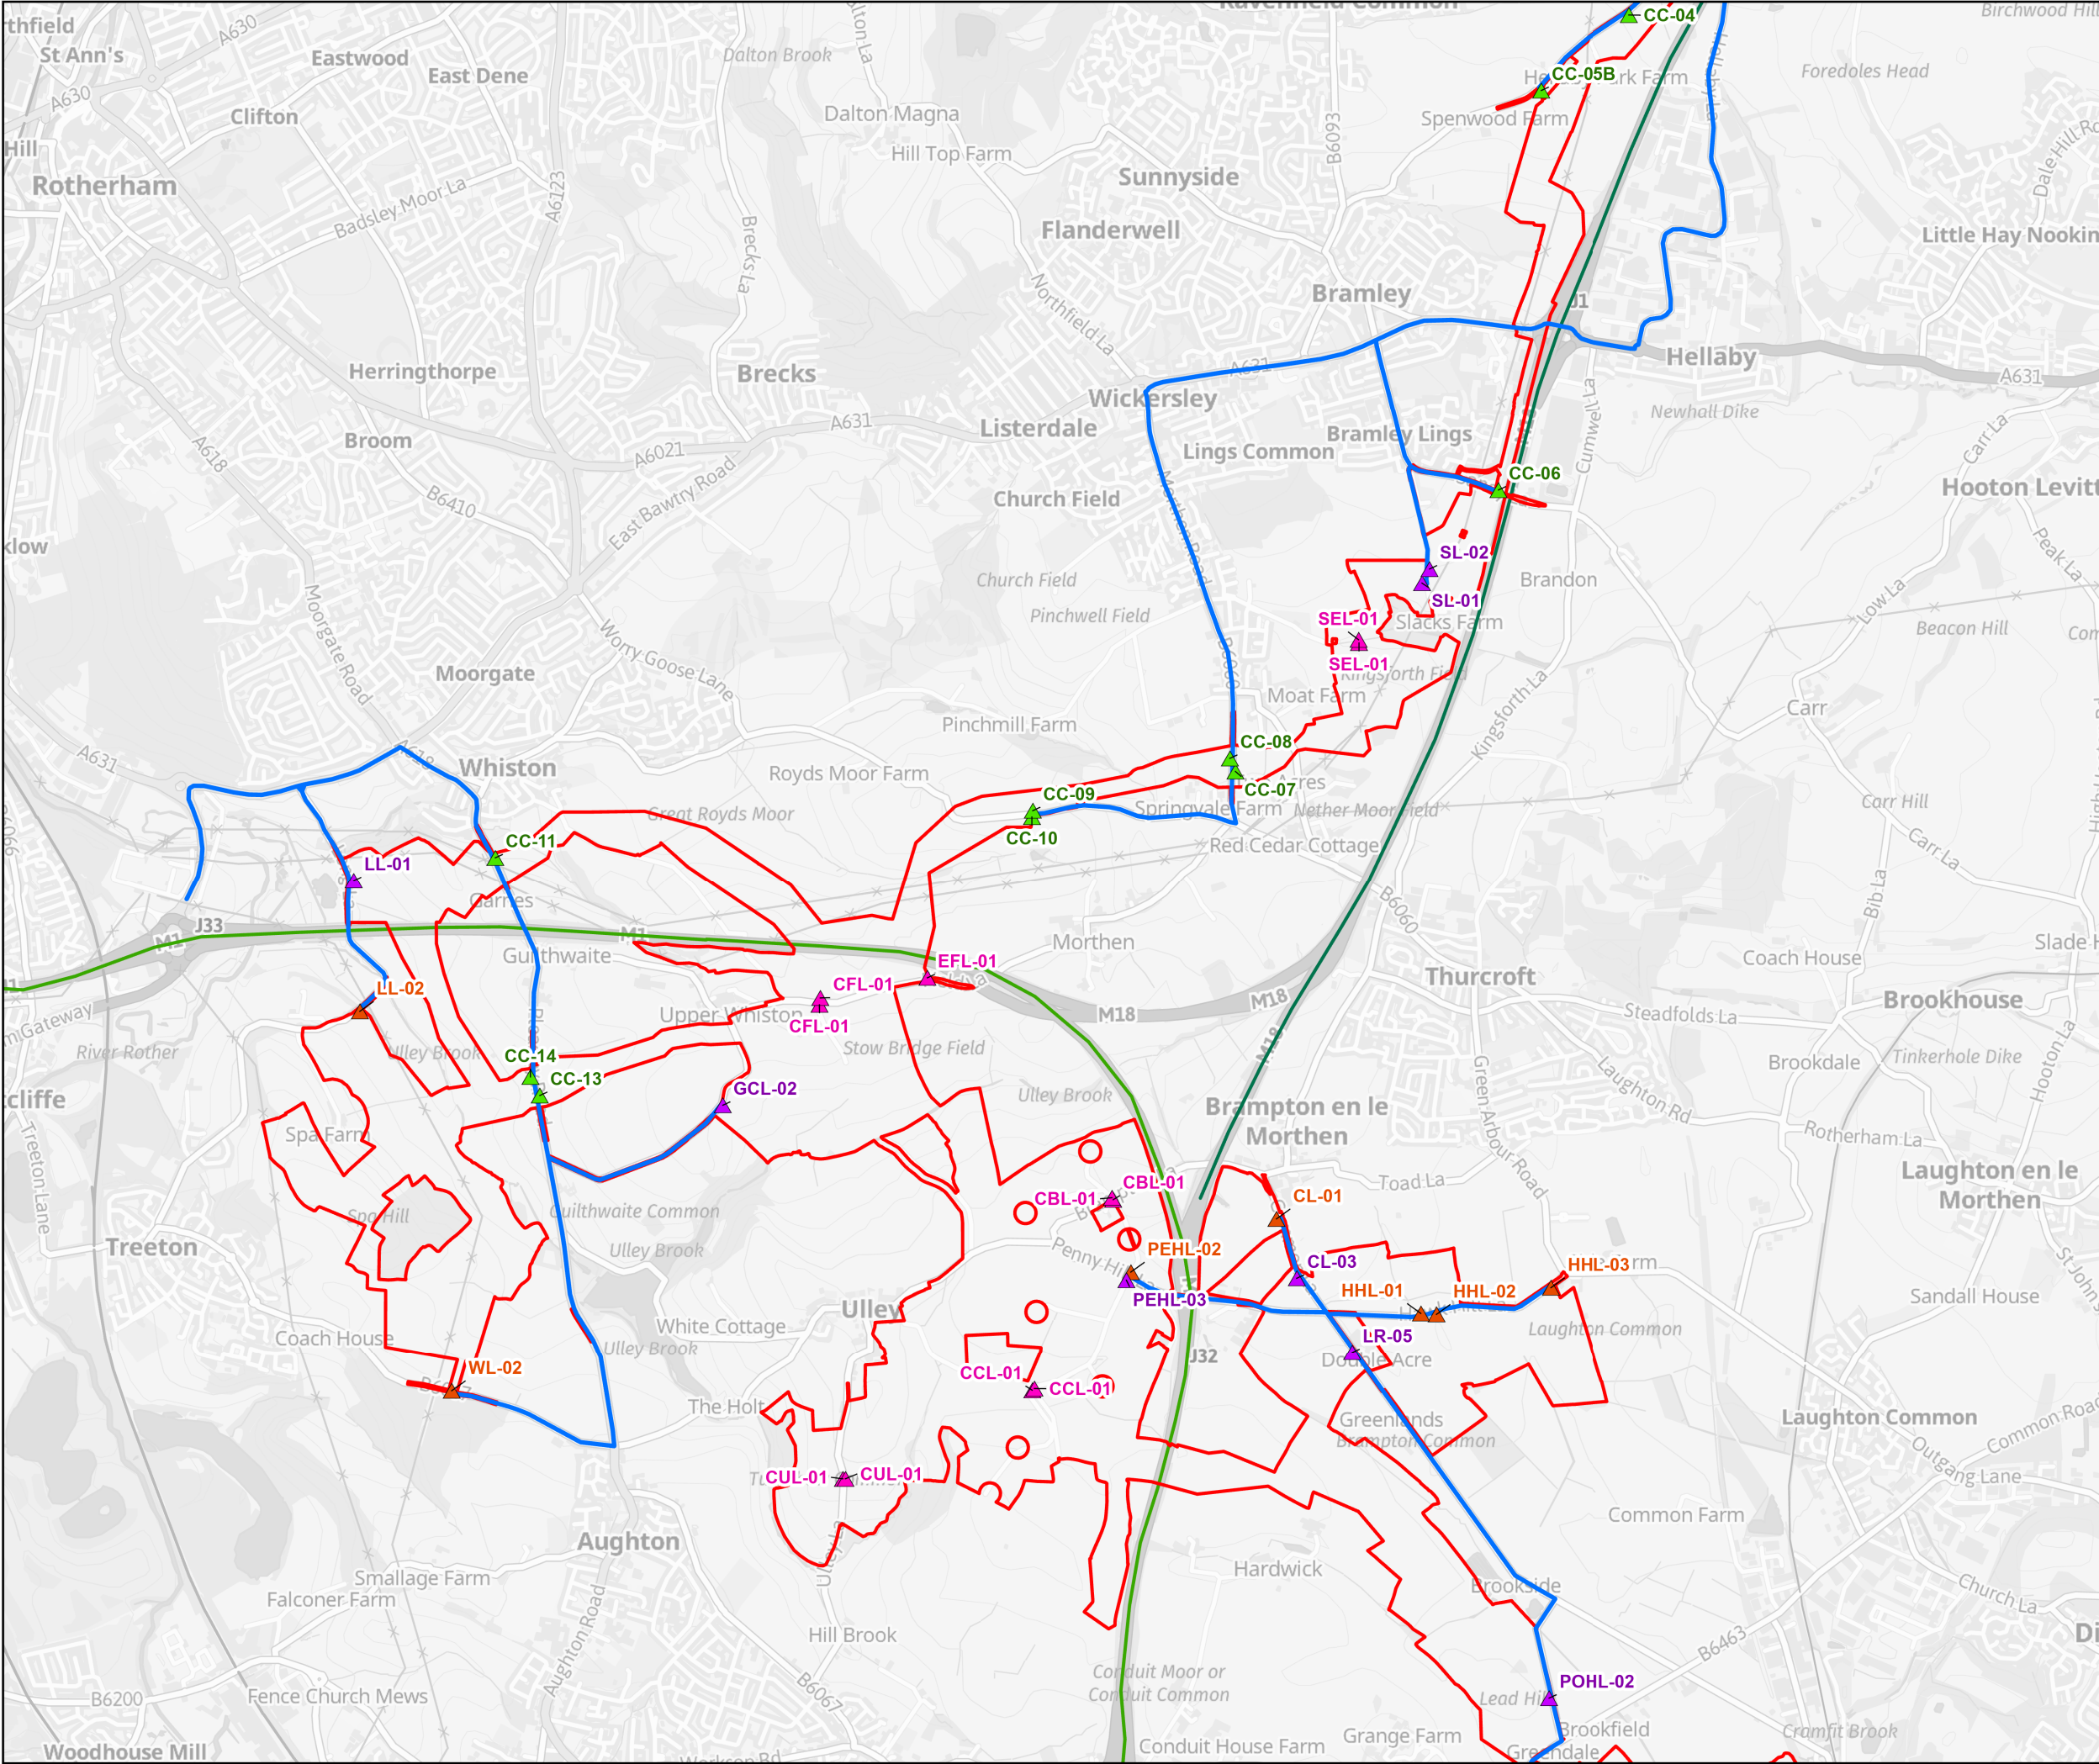


- Order Limits
- Solar PV Site Access Point
- Grid Connection Corridor Only Access Point
- Solar PV Site & Grid Connection Corridor Access Point
- Crossing Point
- Solar PV Site & Grid Connection Corridor Access Routes
- M1 Motorway
- M18 Motorway

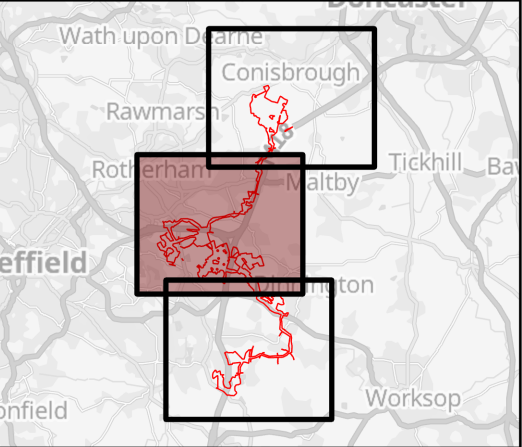



SCALE: 1:30,000	VERSION: A01
SIZE: A3	DRAWN: EB
APPLICATION: EN0110020	CHECKED: DF
DATE: 30/04/2026	APPROVED: AS

Whitestone Solar Farm
Outline Construction Traffic Management Plan
Appendix A.2
Site and Grid Connection Corridor Access Points
Sheet 2 of 3

Reference: EN0110020/APP/6.19
Infrastructure Planning (Applications: Prescribed
Forms and Procedure) Regulations 2009 -
Regulations 5(2)(a)



A.3 Proposed Access Layouts, Visibility Splays and Swept Paths

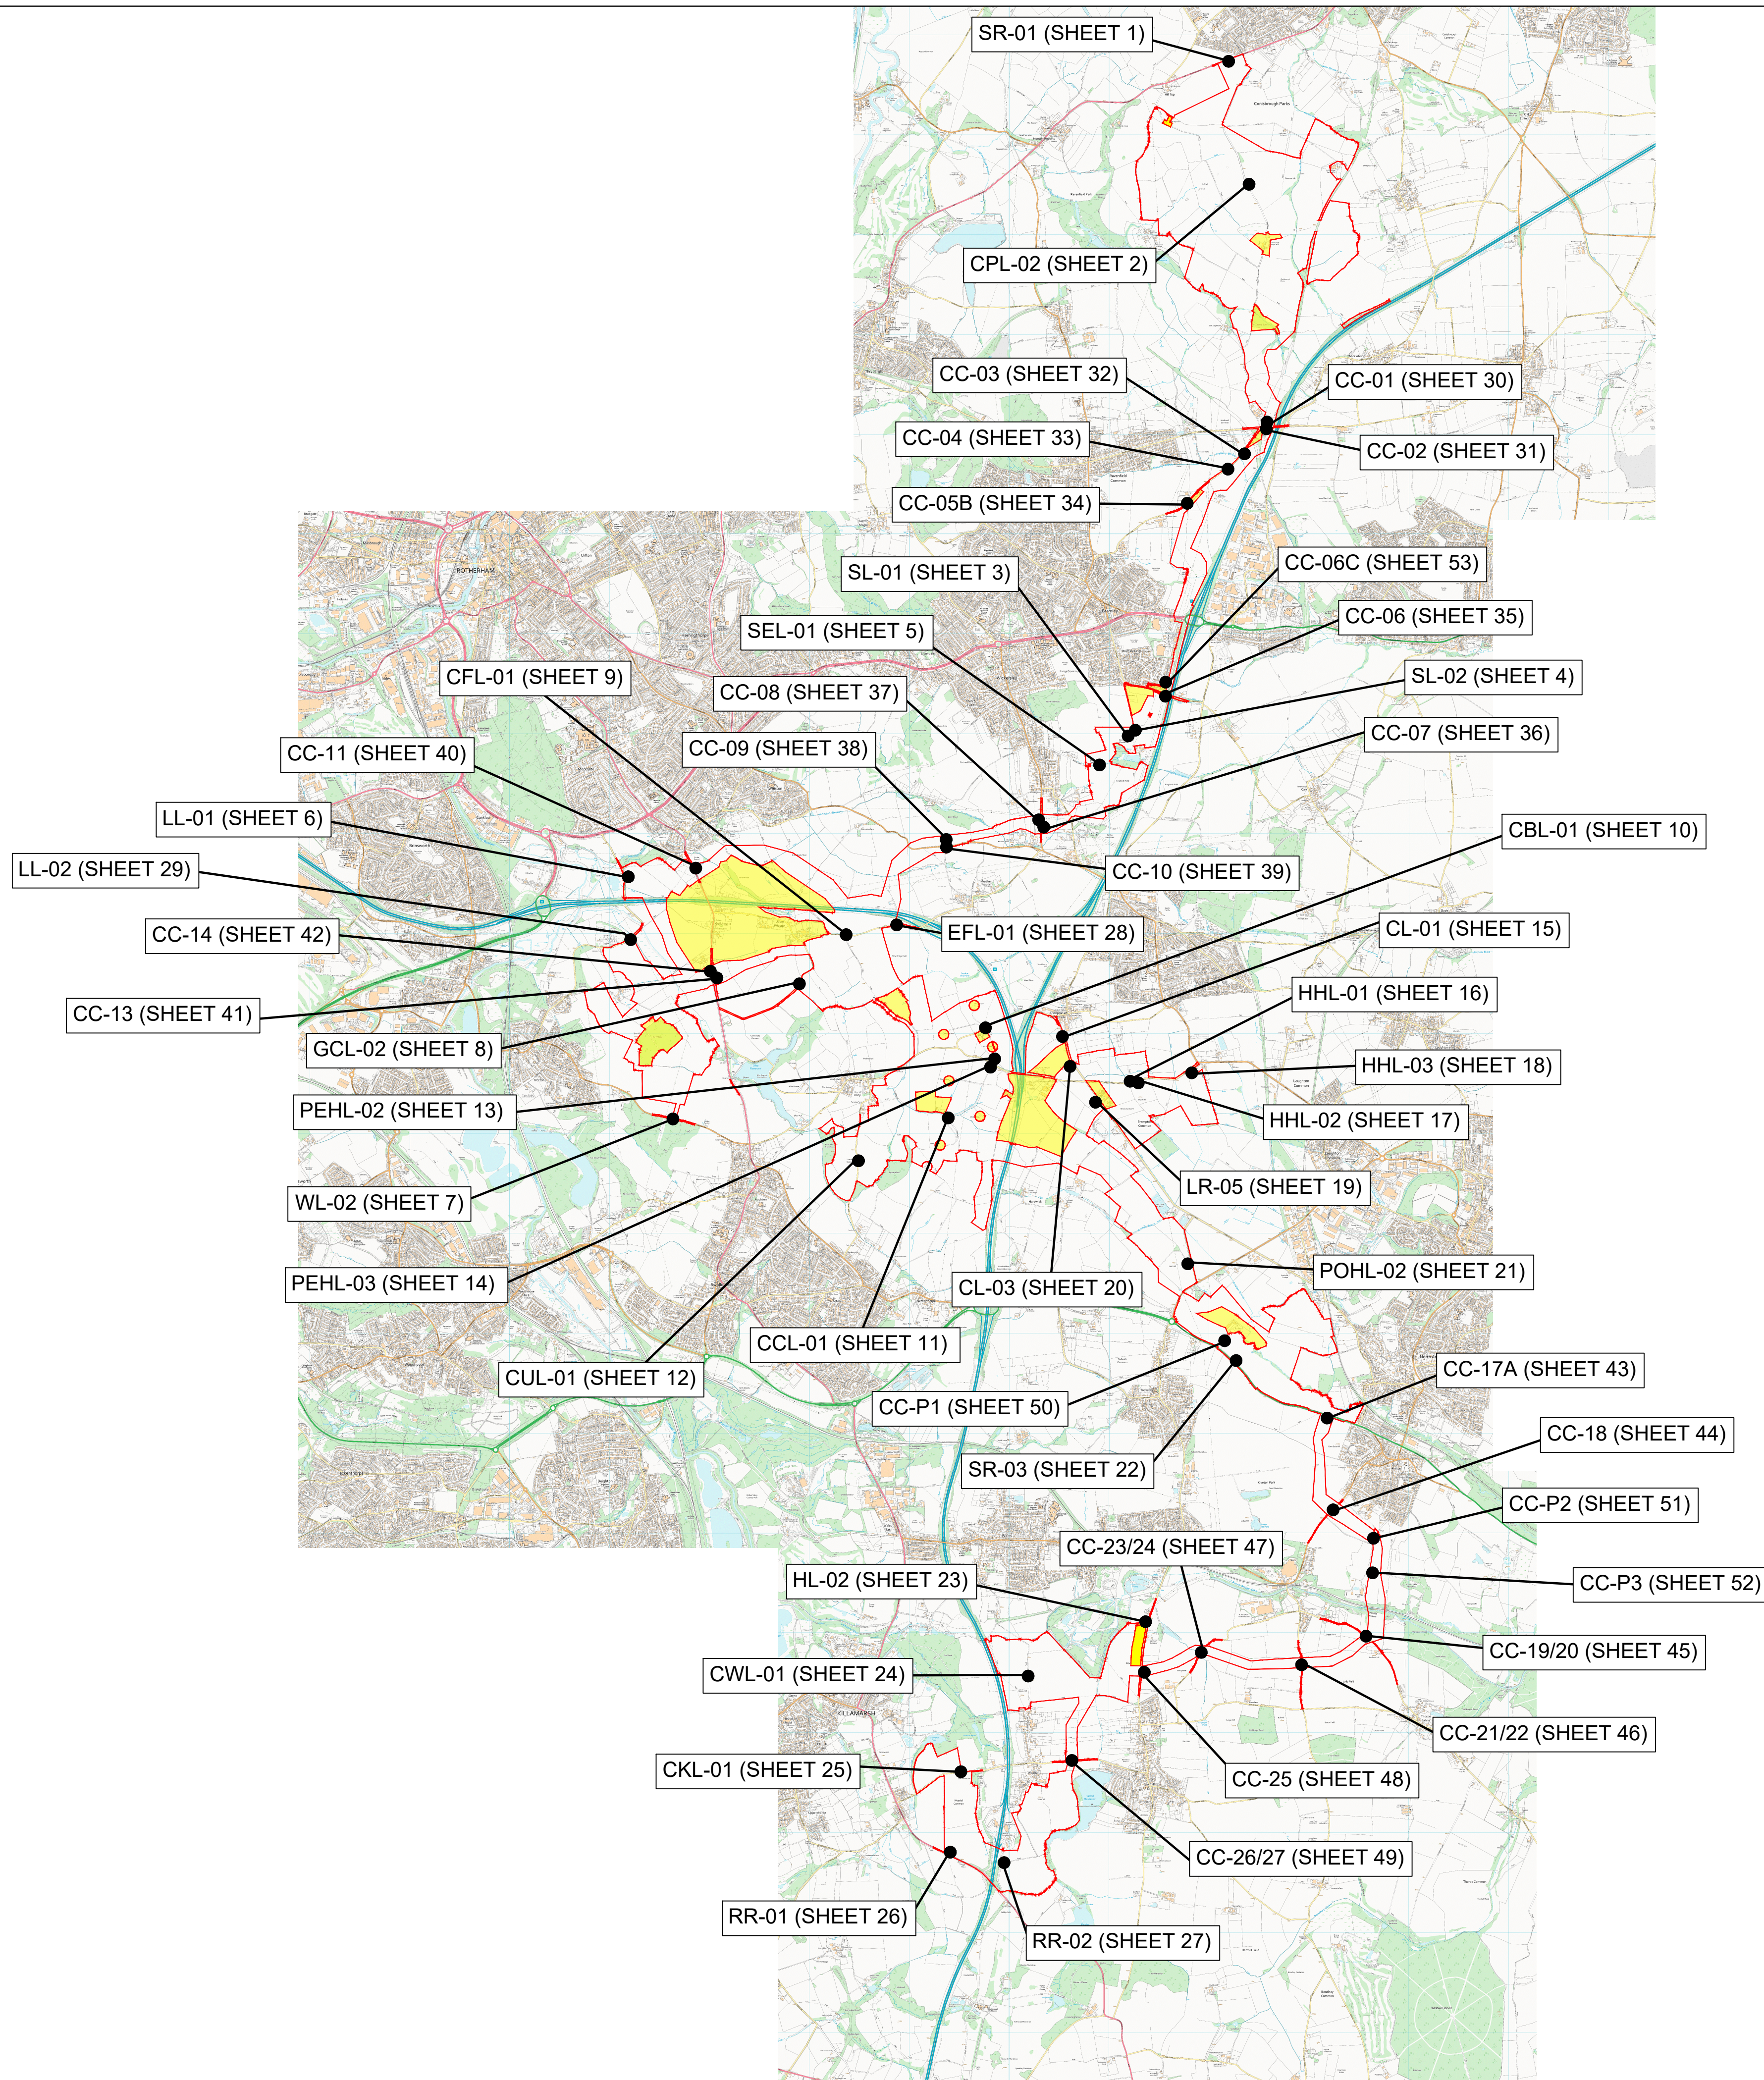

- NOTES**
1. All dimensions in meters unless stated otherwise.
 2. Do not scale from this drawing use only printed dimensions.
 3. This drawing is to be read in conjunction with all other relevant documentation.
 4. Refer to the drawing for the location, naming and corresponding drawing number for each access point.

- LEGEND**
- Order Limits
 - Access marker
 - AB-00 (SHEET XX)
 - Access identifier

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED


TITLE:
Access Location Plan
Appendix 3 - Key Plan - Sheet 0 of 53
Whitestone Solar Farm
Regulation 5 (2)(o)




DRAWING DATE: 03/06/2026

SCALE: 1:37,500	SHEET: Sheet 0 of 53
SIZE: A1	REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020



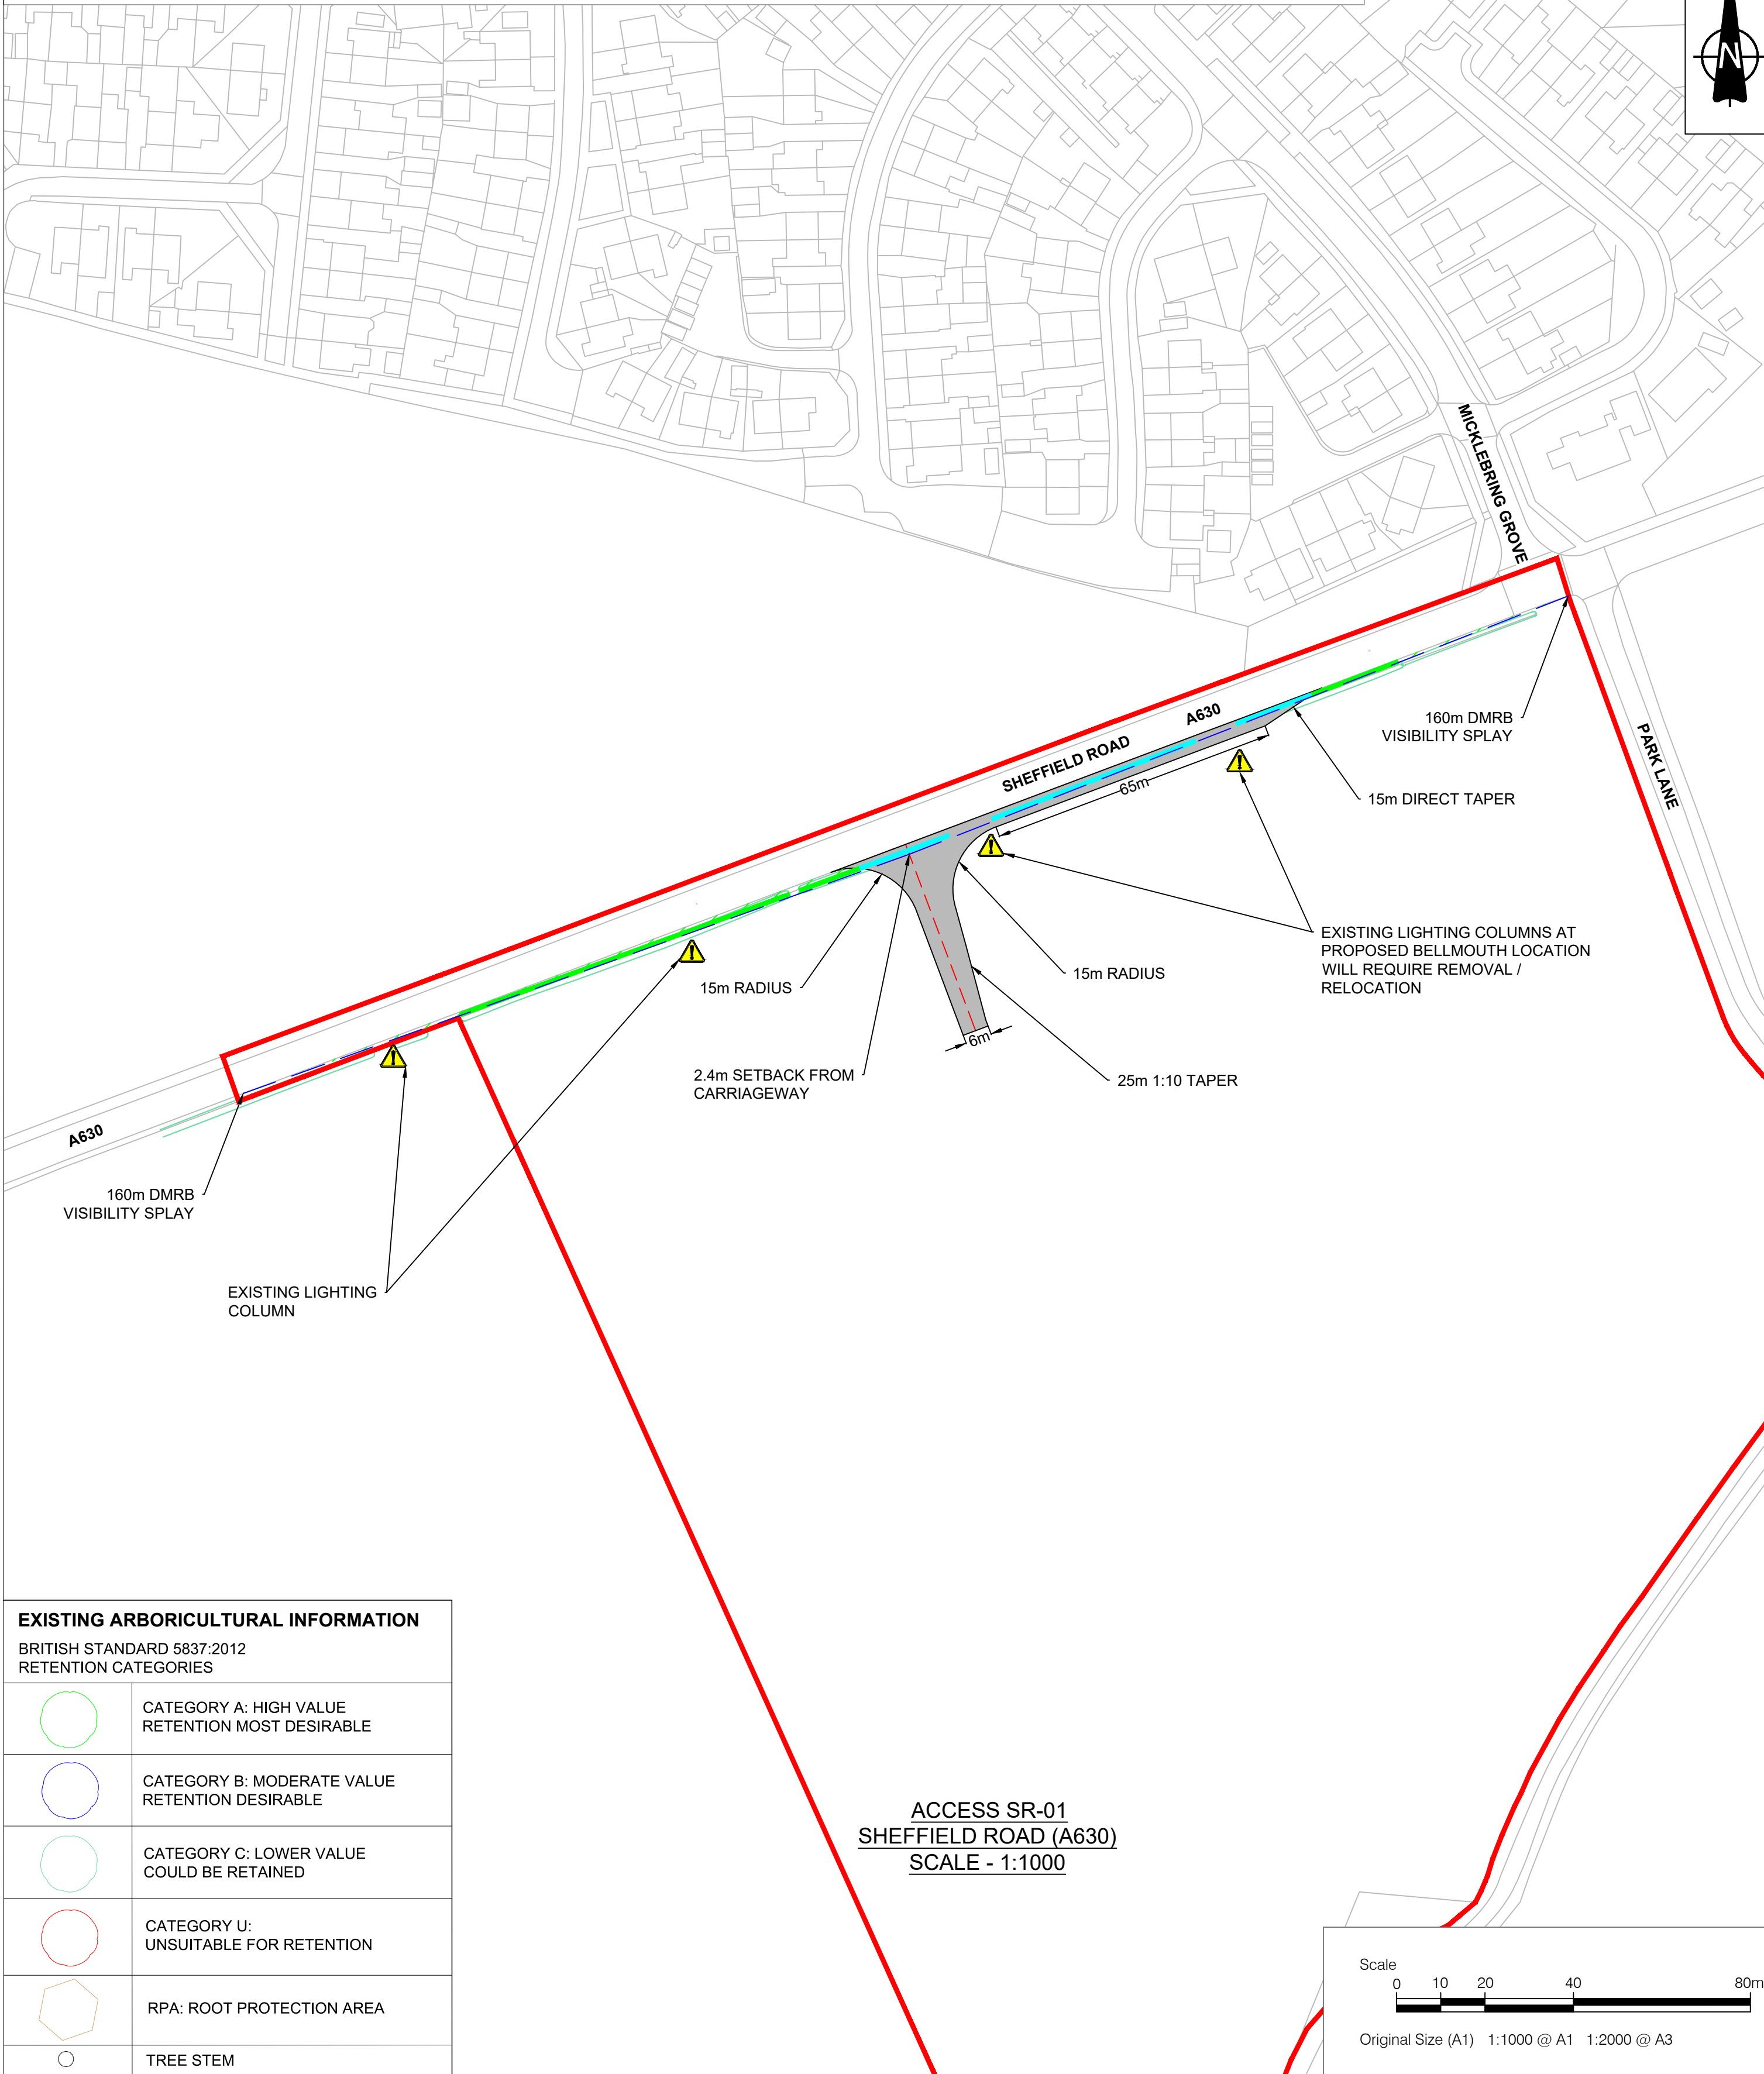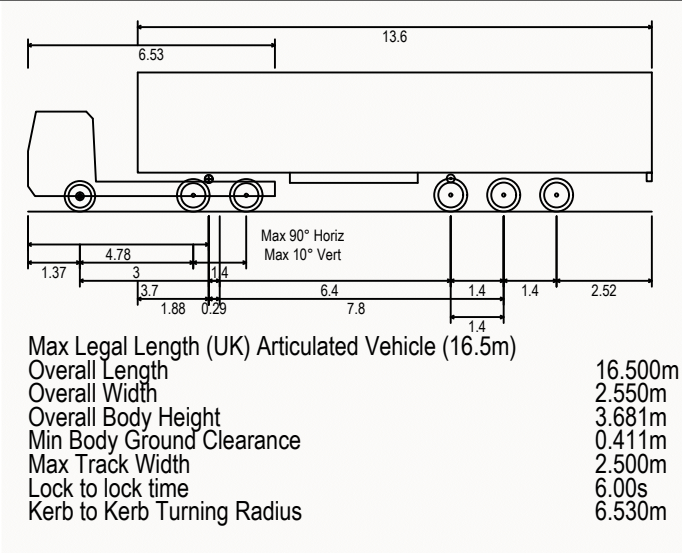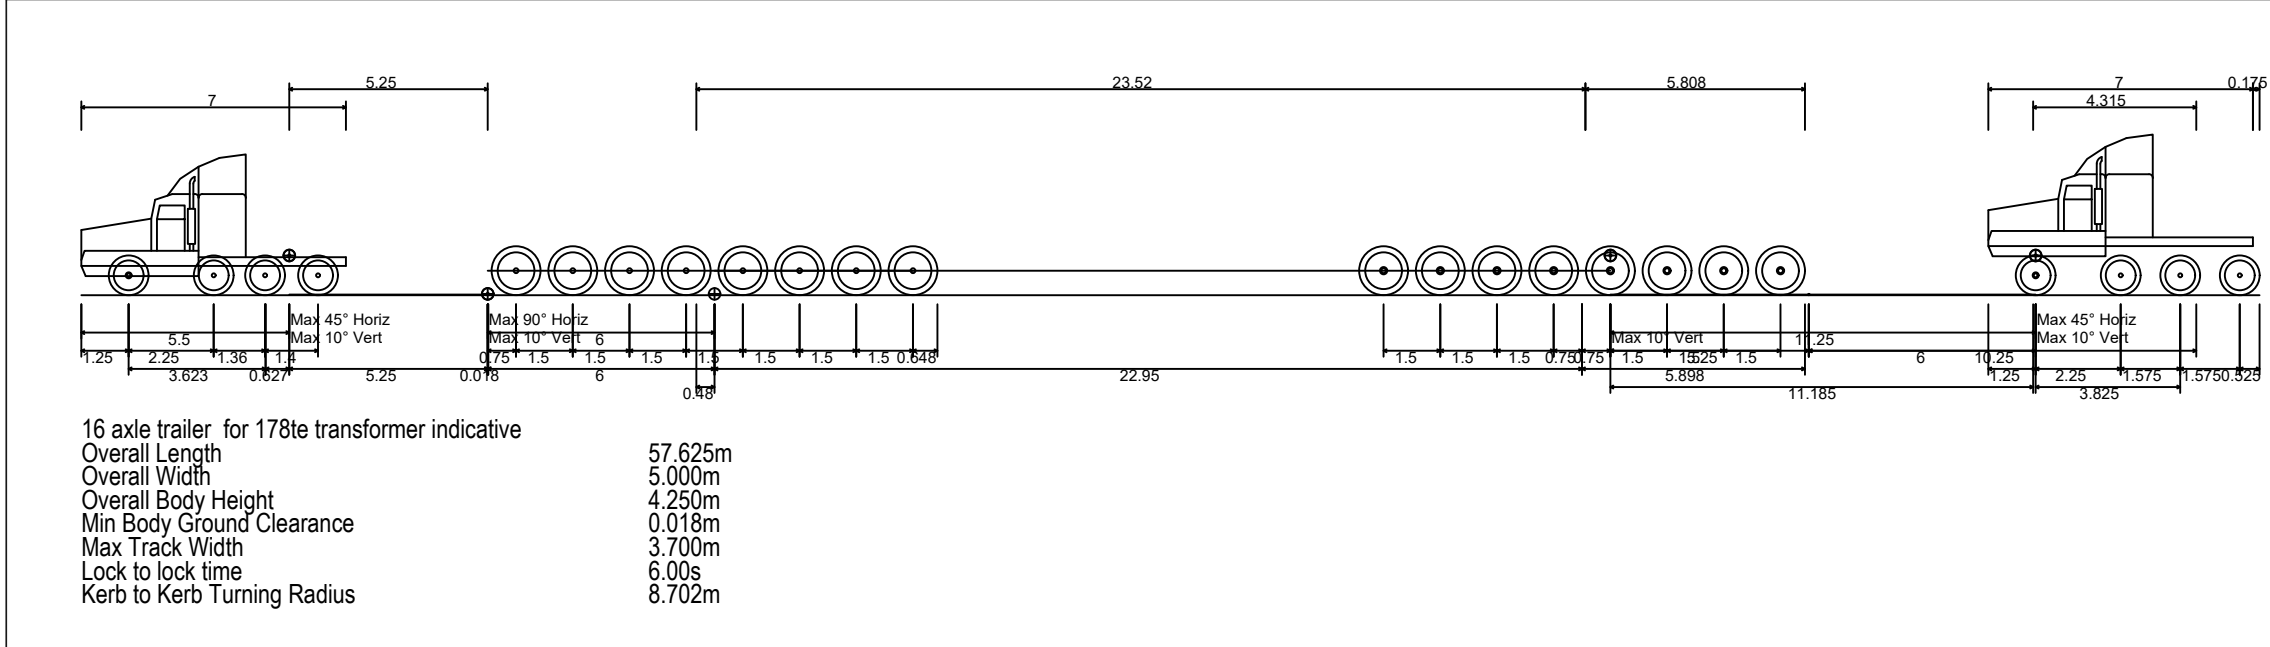

EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012 RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

- #### NOTES
- This drawing is to be read in conjunction with all other relevant documentation.
 - Do not scale from this drawing, use only printed dimensions.
 - All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
 - This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
 - Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
 - The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
 - Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
 - Junction visibility for the access is based upon DMRB CD109 Table 2.10.

- #### LEGEND
- Extent of Access Footprint
 - Order Limits
 - Land Excluded from Order Limits
 - Vehicle Body
 - Vehicle Body Path
 - Vehicle Load
 - Vehicle Load Path
 - Vehicle Wheels Path
 - Edge of Road
 - Access Centreline
 - Junction Visibility
 - Vegetation to be Removed for Vis Splay
 - Indicative Hedgerow Removal Vis Splay
 - Indicative Hedgerow Removal for Bellmouth Access
 - Health and Safety Risk Identifier
 - Existing Public Right of Way

SHEET PLAN

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED




TITLE:
PV Area Access SR-01
Appendix 3 - Sheet 1 of 53
Whitestone Solar Farm
Regulation 5(2)(o)

DRAWING DATE: 03/06/2026

SCALE: 1:1000	SHEET: Sheet 1 of 53
SIZE: A1	REVISION: 01


DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020

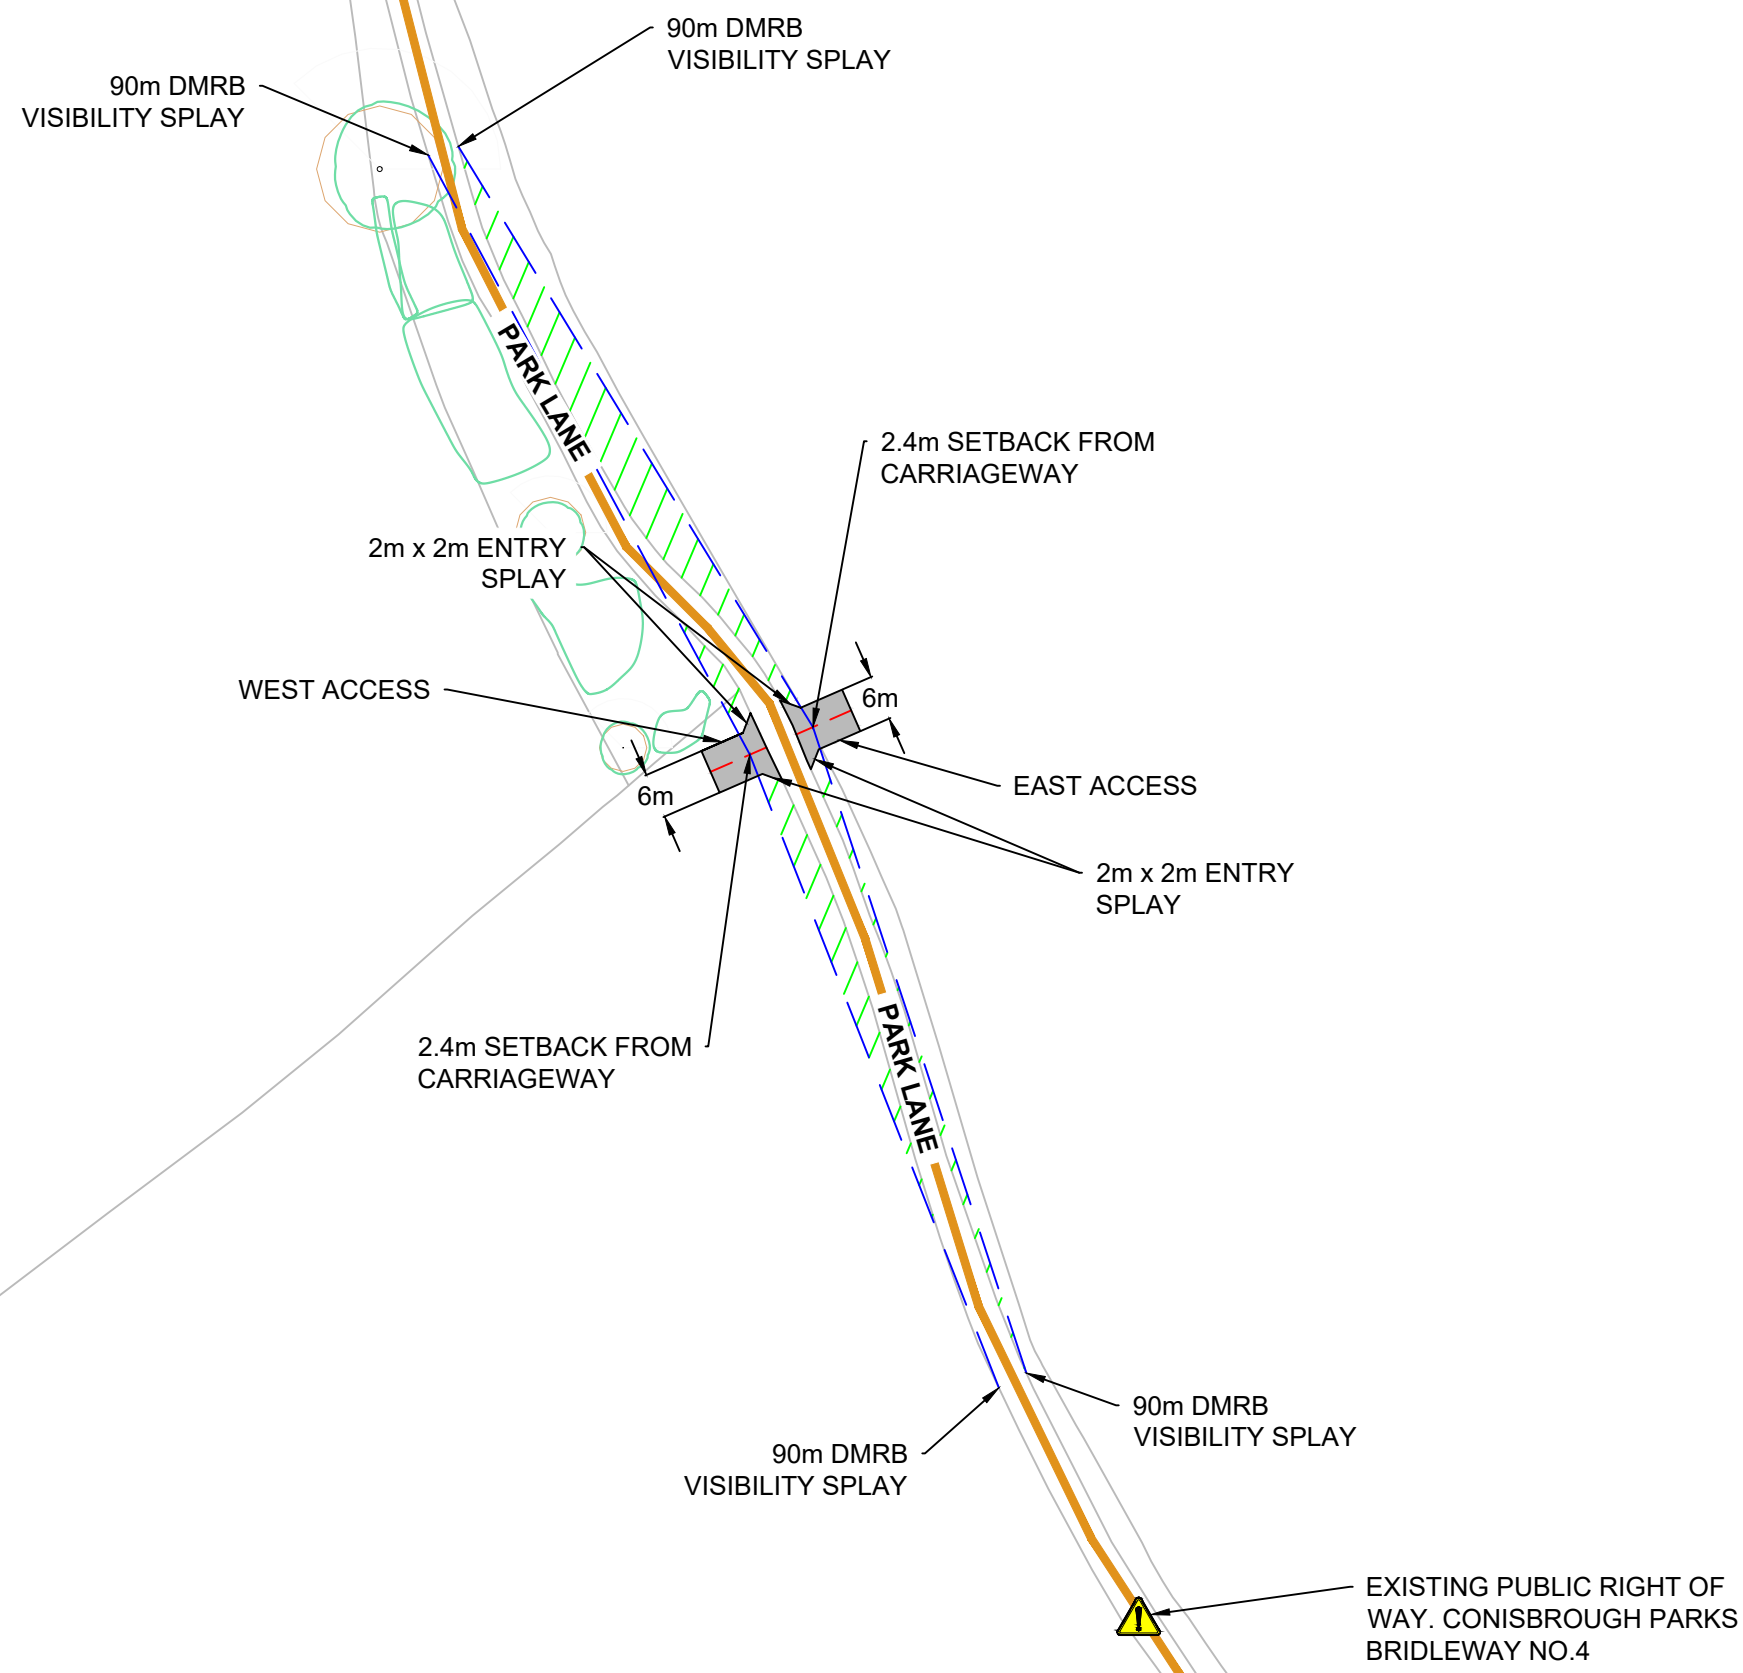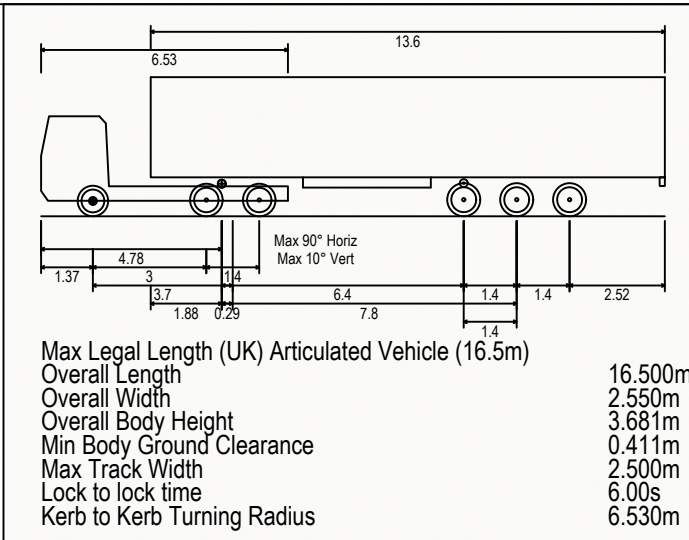
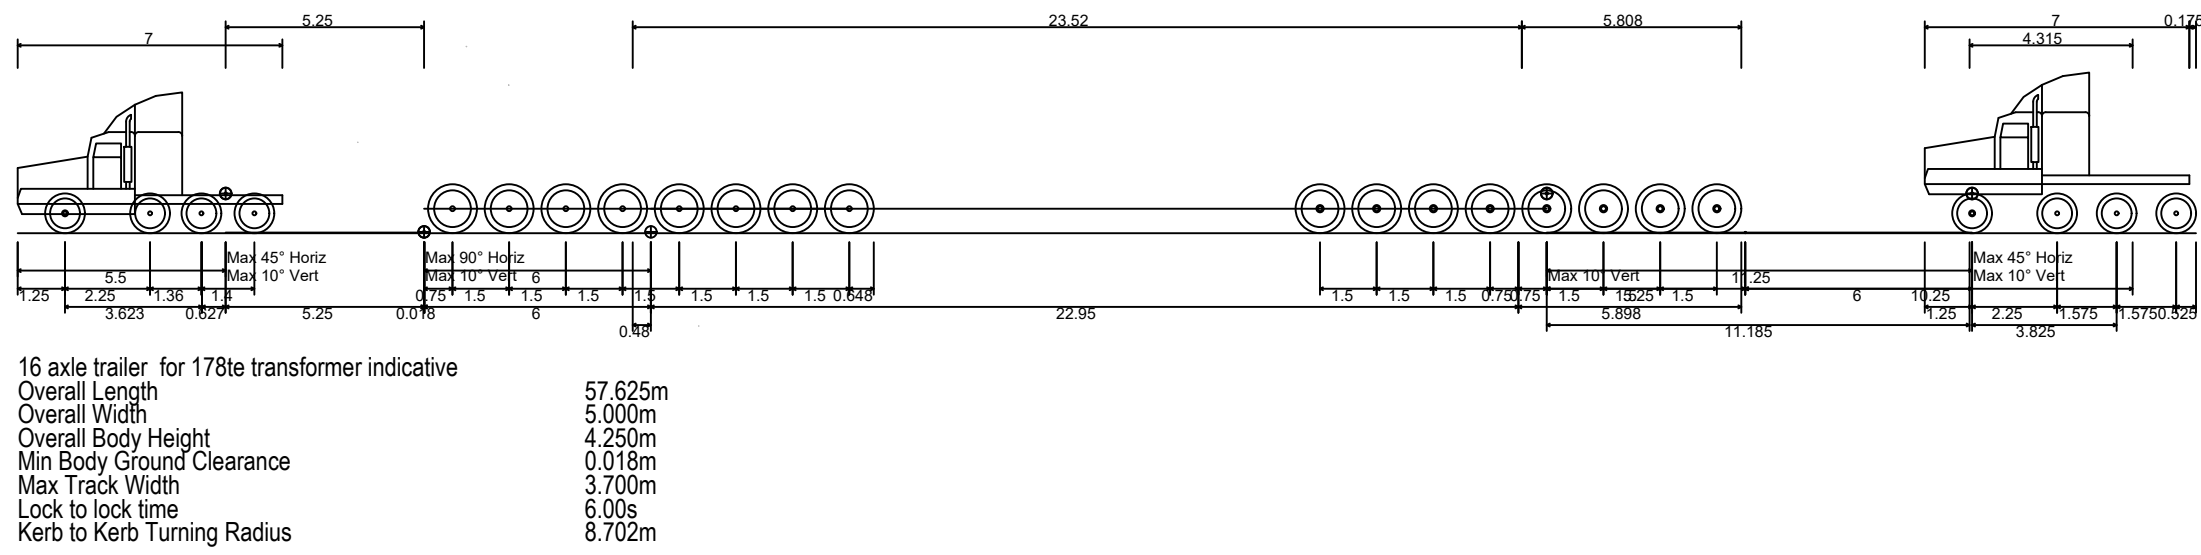


EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012 RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

ACCESS CPL-02
PARK LANE
SCALE - 1:1000




INSET A: 16.5m ARTICULATED VEHICLE HEADING NORTH-EAST ACROSS PARK LANE - SCALE 1:500

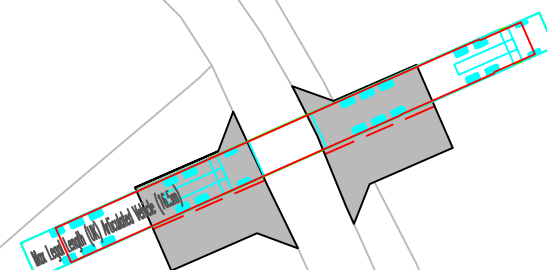


INSET B: 16.5m ARTICULATED VEHICLE HEADING SOUTH-WEST ACROSS PARK LANE - SCALE 1:500

ABNORMAL LOAD CROSSING MOVEMENTS TO BE CONTROLLED TO ENSURE MOVEMENTS ARE COMPLETED SAFELY. ANY OTHER CONSTRUCTION VEHICLES WISHING TO EGRESS DURING ABNORMAL LOAD DELIVERIES ARE TO BE HELD WITHIN THE SITE TO AVOID VEHICULAR CONFLICTS





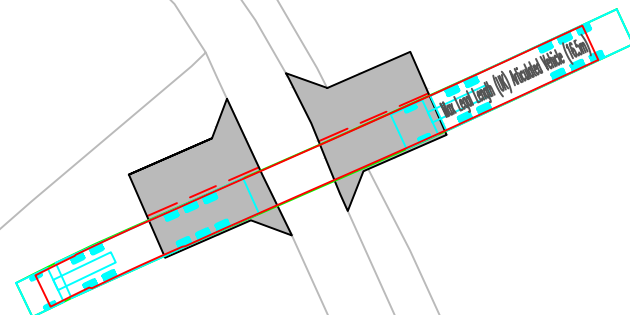


INSET C: 58m 16 AXLE TRAILER VEHICLE HEADING NORTH-EAST ACROSS PARK LANE - SCALE 1:1000

ABNORMAL LOAD CROSSING MOVEMENTS TO BE CONTROLLED TO ENSURE MOVEMENTS ARE COMPLETED SAFELY. ANY OTHER CONSTRUCTION VEHICLES WISHING TO EGRESS DURING ABNORMAL LOAD DELIVERIES ARE TO BE HELD WITHIN THE SITE TO AVOID VEHICULAR CONFLICTS

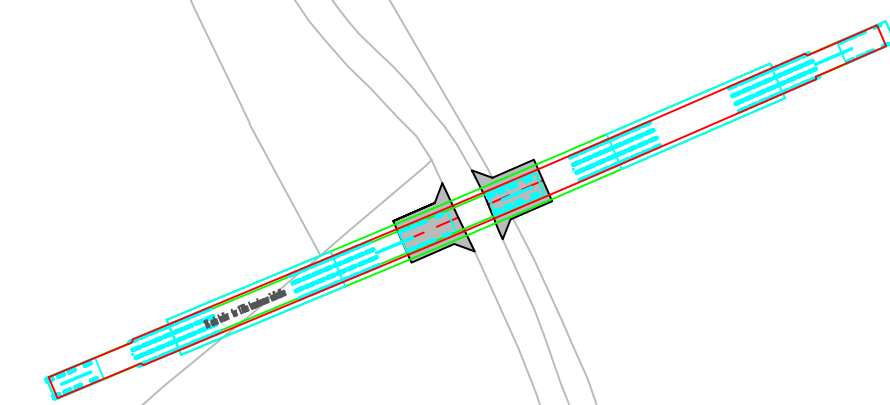

INSET D: 58m 16 AXLE TRAILER VEHICLE HEADING SOUTH-WEST ACROSS PARK LANE - SCALE 1:1000

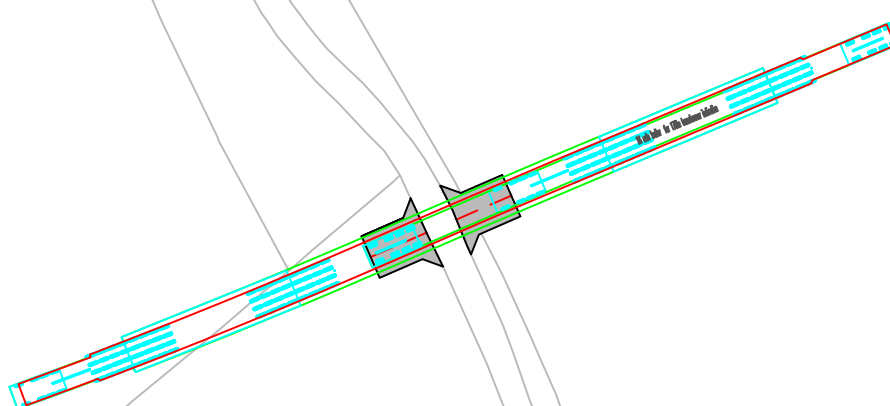


NOTES

- This drawing is to be read in conjunction with all other relevant documentation.
- Do not scale from this drawing, use only printed dimensions.
- All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
- This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
- Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
- The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
- Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
- Junction visibility for the access is based upon DMRB CD109 Table 2.10.

LEGEND

- Extent of Access Footprint
- Order Limits
- Land Excluded from Order Limits
- Vehicle Body
- Vehicle Body Path
- Vehicle Load
- Vehicle Load Path
- Vehicle Wheels Path
- Edge of Road
- Access Centreline
- Junction Visibility
- Vegetation to be Removed for Vis Splay
- Indicative Hedgerow Removal Vis Splay
- Indicative Hedgerow Removal for Bellmouth Access
- Health and Safety Risk Identifier
- Existing Public Right of Way

SHEET PLAN

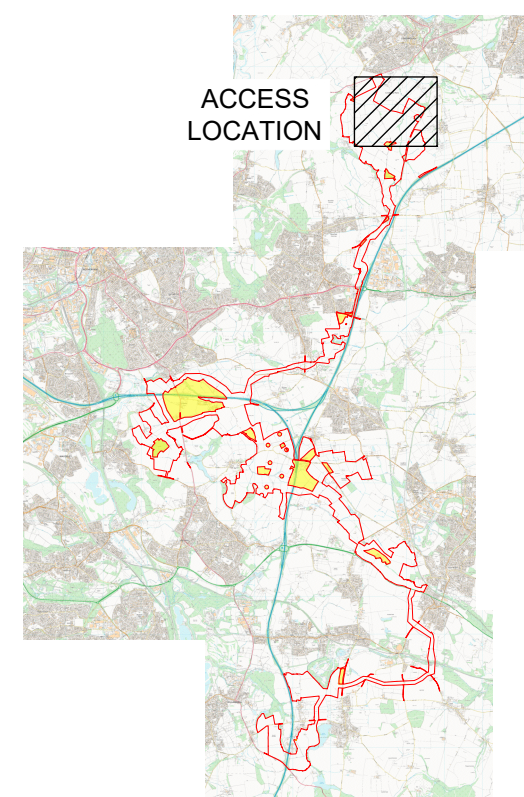

01	03/06/2026	DCO SUBMISSION	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:

PV Area Access CPL-02
Appendix 3 - Sheet 2 of 53
Whitestone Solar Farm
Regulation 5(2)(o)

DRAWING DATE: 03/06/2026

SCALE: AS SHOWN

SHEET: Sheet 2 of 53

SIZE: A1



REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020



EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012 RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

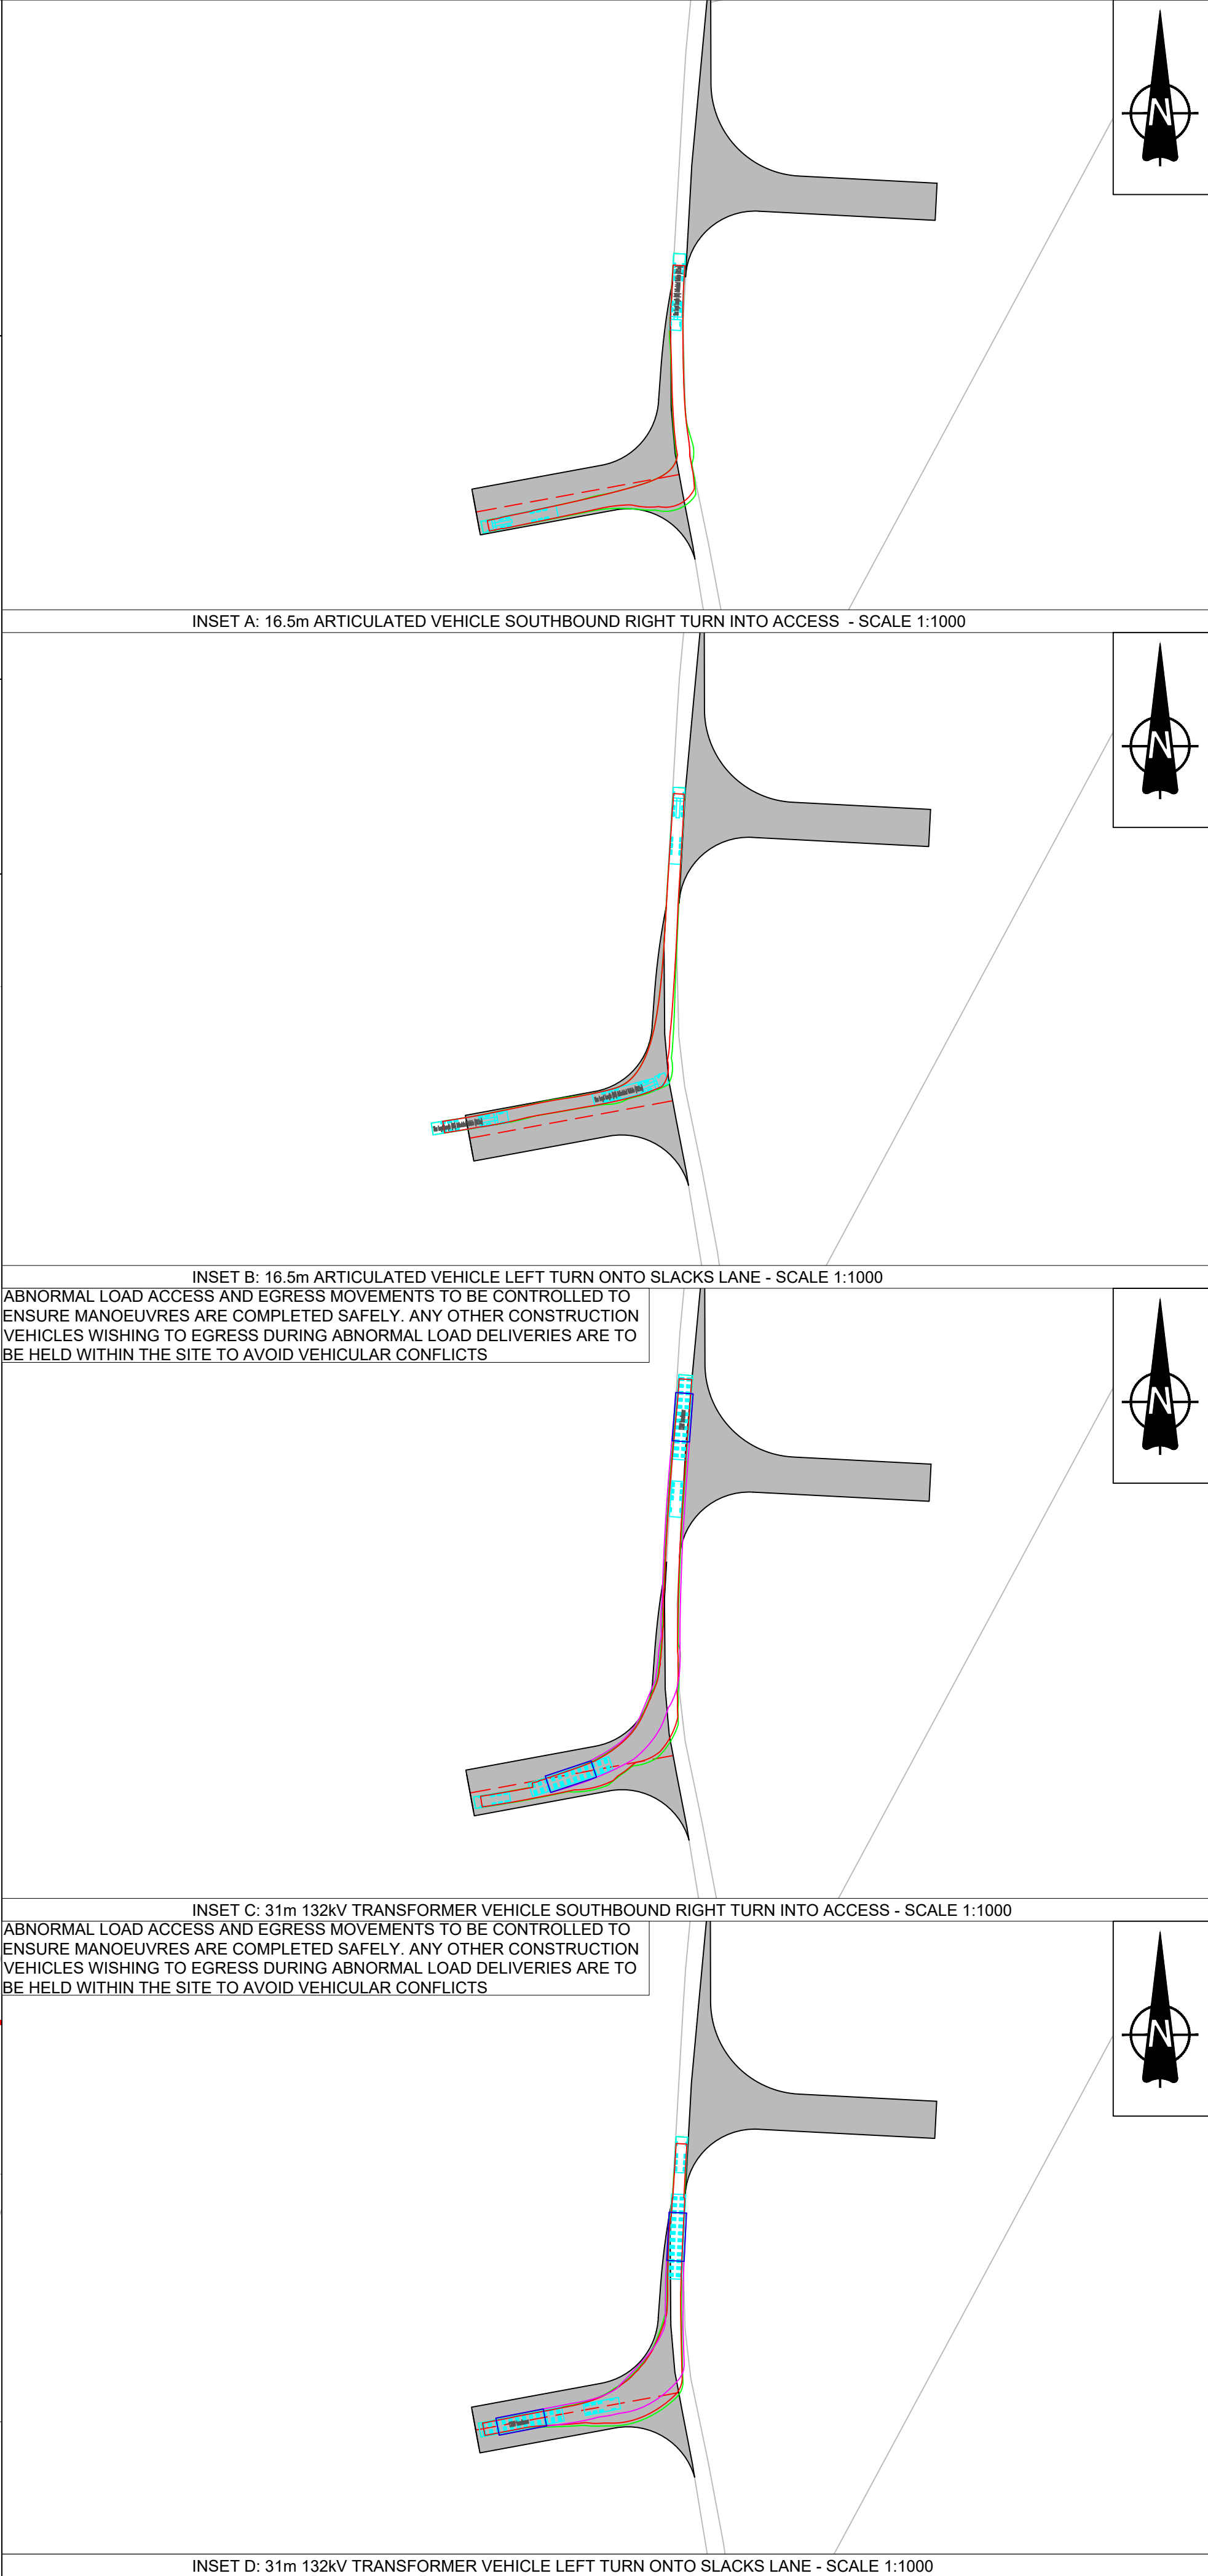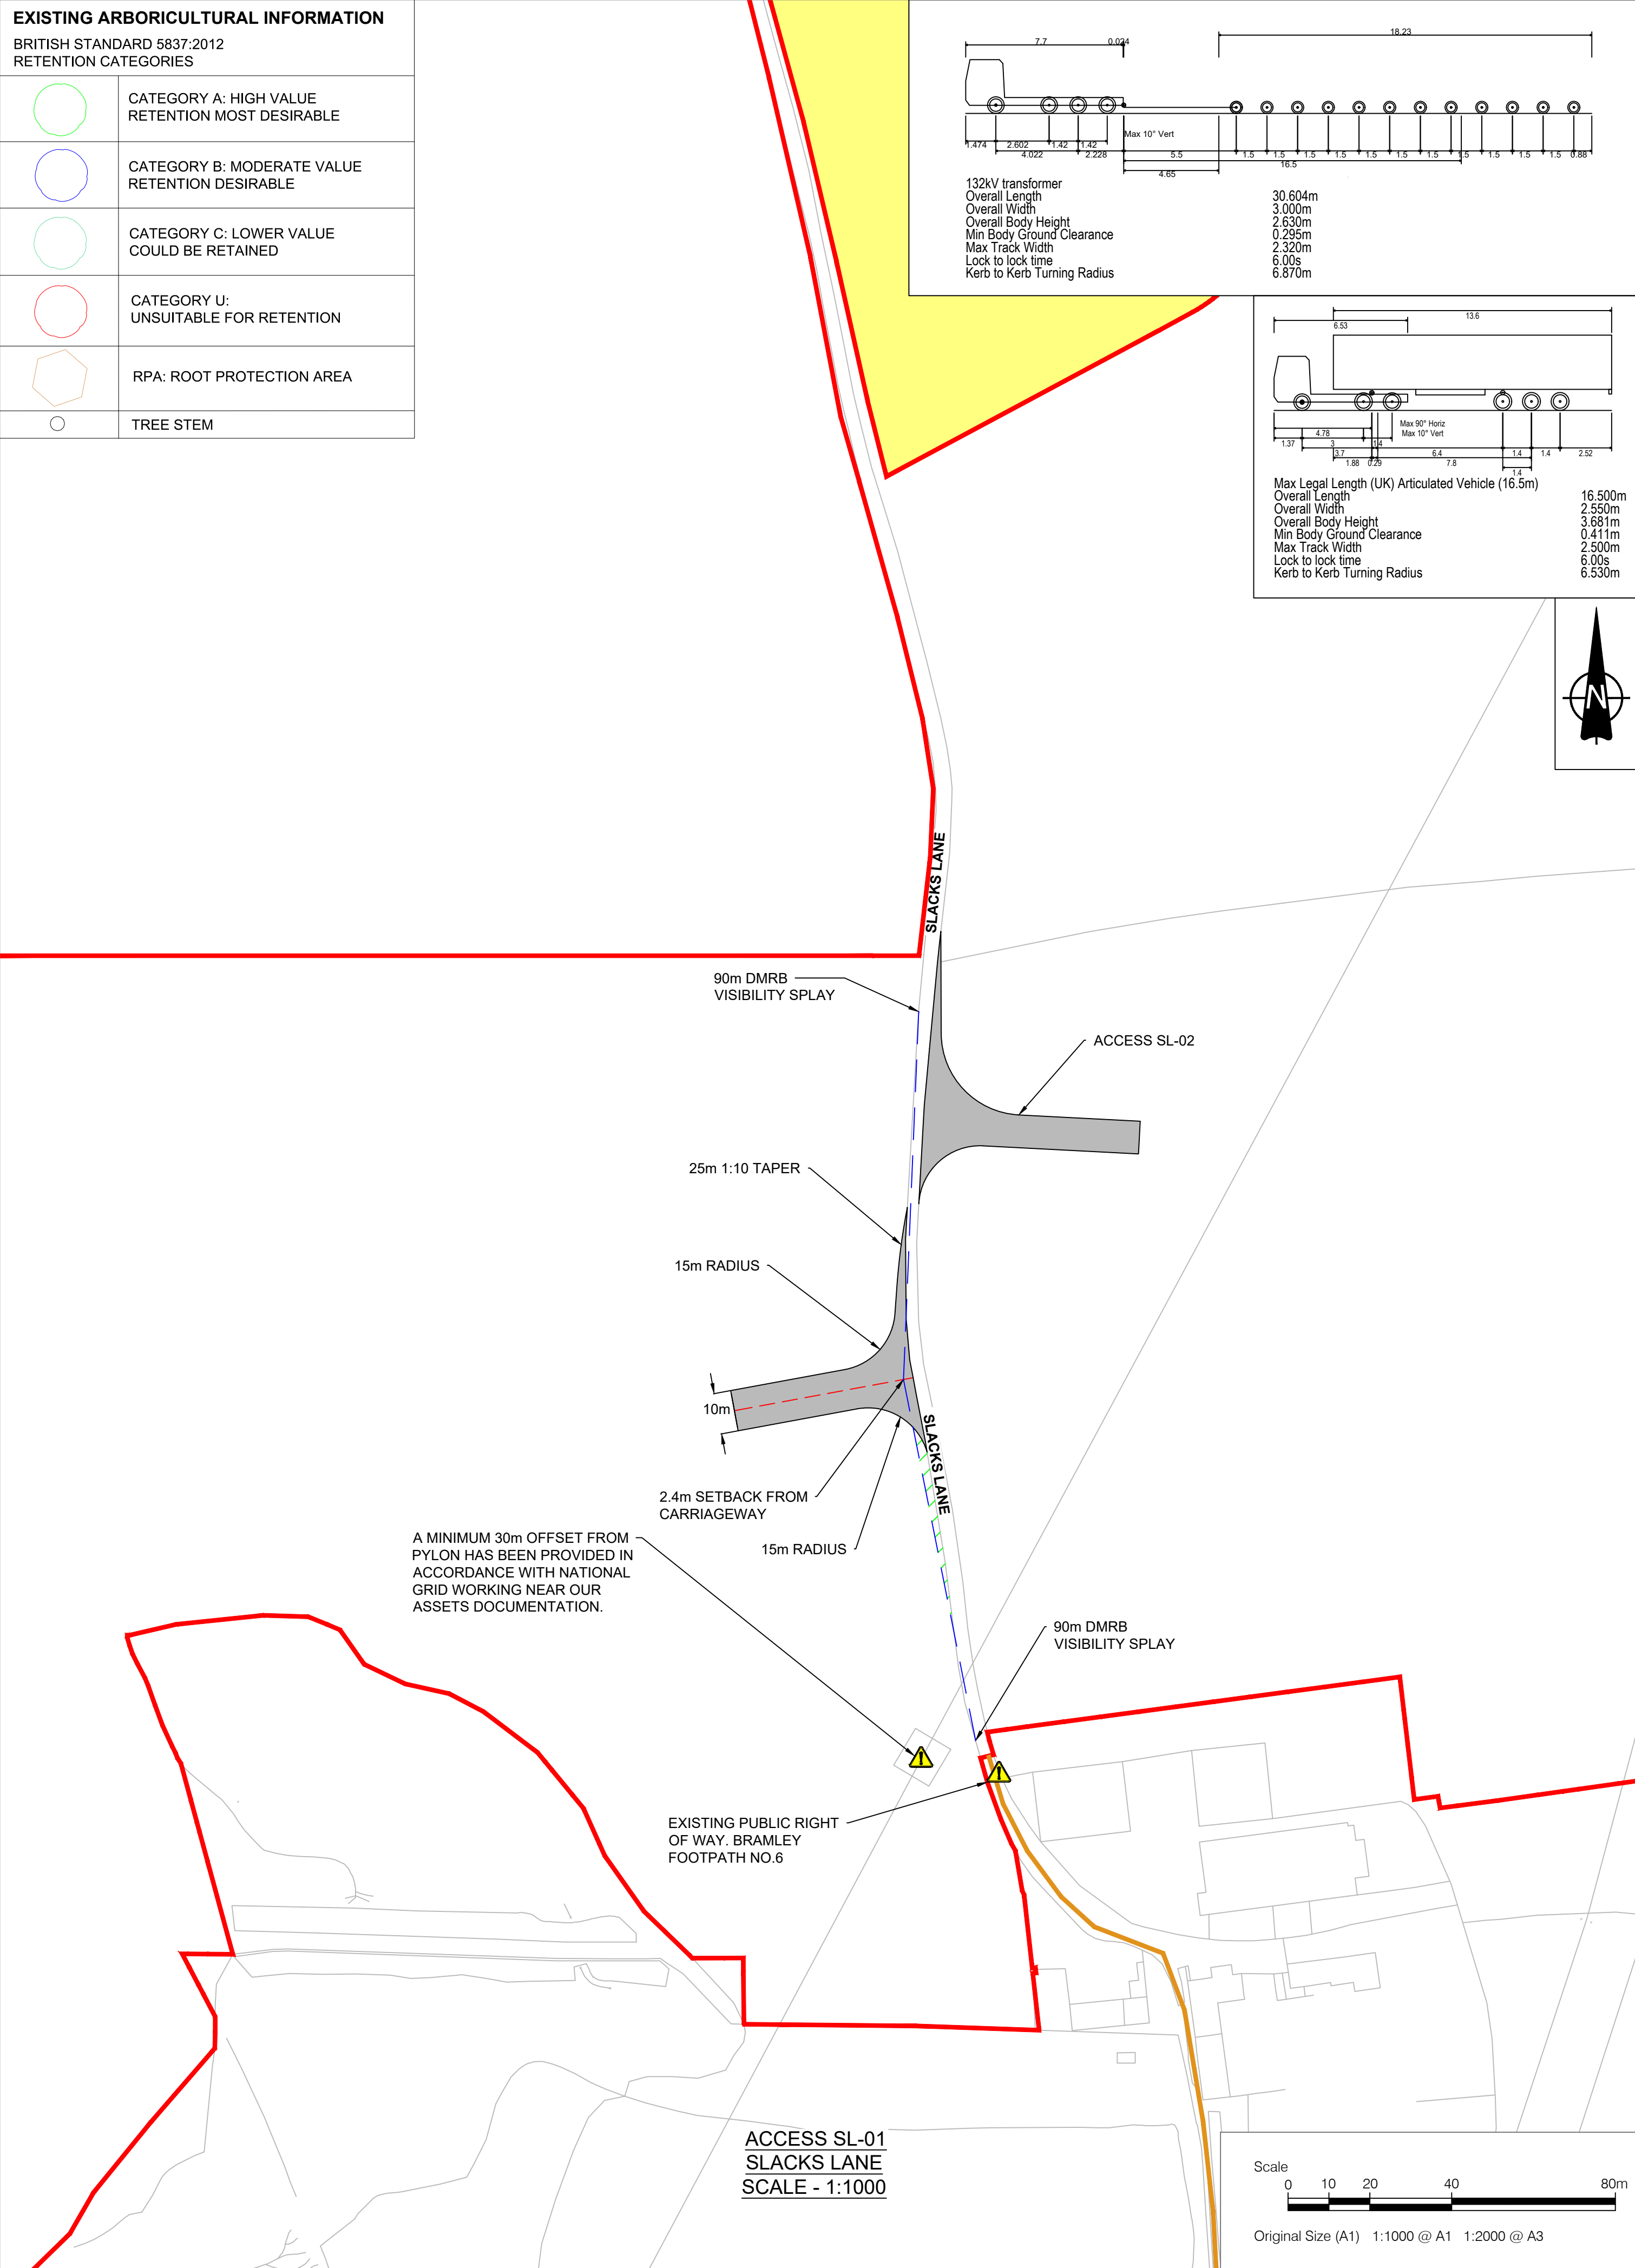

NOTES

- This drawing is to be read in conjunction with all other relevant documentation.
- Do not scale from this drawing, use only printed dimensions.
- All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
- This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
- Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
- The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
- Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
- Junction visibility for the access is based upon DMRB CD109 Table 2.10.

LEGEND

- Extent of Access Footprint
- Order Limits
- Land Excluded from Order Limits
- Vehicle Body
- Vehicle Body Path
- Vehicle Load
- Vehicle Load Path
- Vehicle Wheels Path
- Edge of Road
- Access Centreline
- Junction Visibility
- Vegetation to be Removed for Vis Splay
- Indicative Hedgerow Removal Vis Splay
- Indicative Hedgerow Removal for Bellmouth Access
- Health and Safety Risk Identifier
- Existing Public Right of Way

SHEET PLAN

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:

PV Area Access SL-01

Appendix 3 - Sheet 3 of 53

Whitestone Solar Farm

Regulation 5(2)(o)


DRAWING DATE: 03/06/2026

SCALE: 1:1000	SHEET: Sheet 3 of 53
SIZE: A1	REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020

EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012 RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

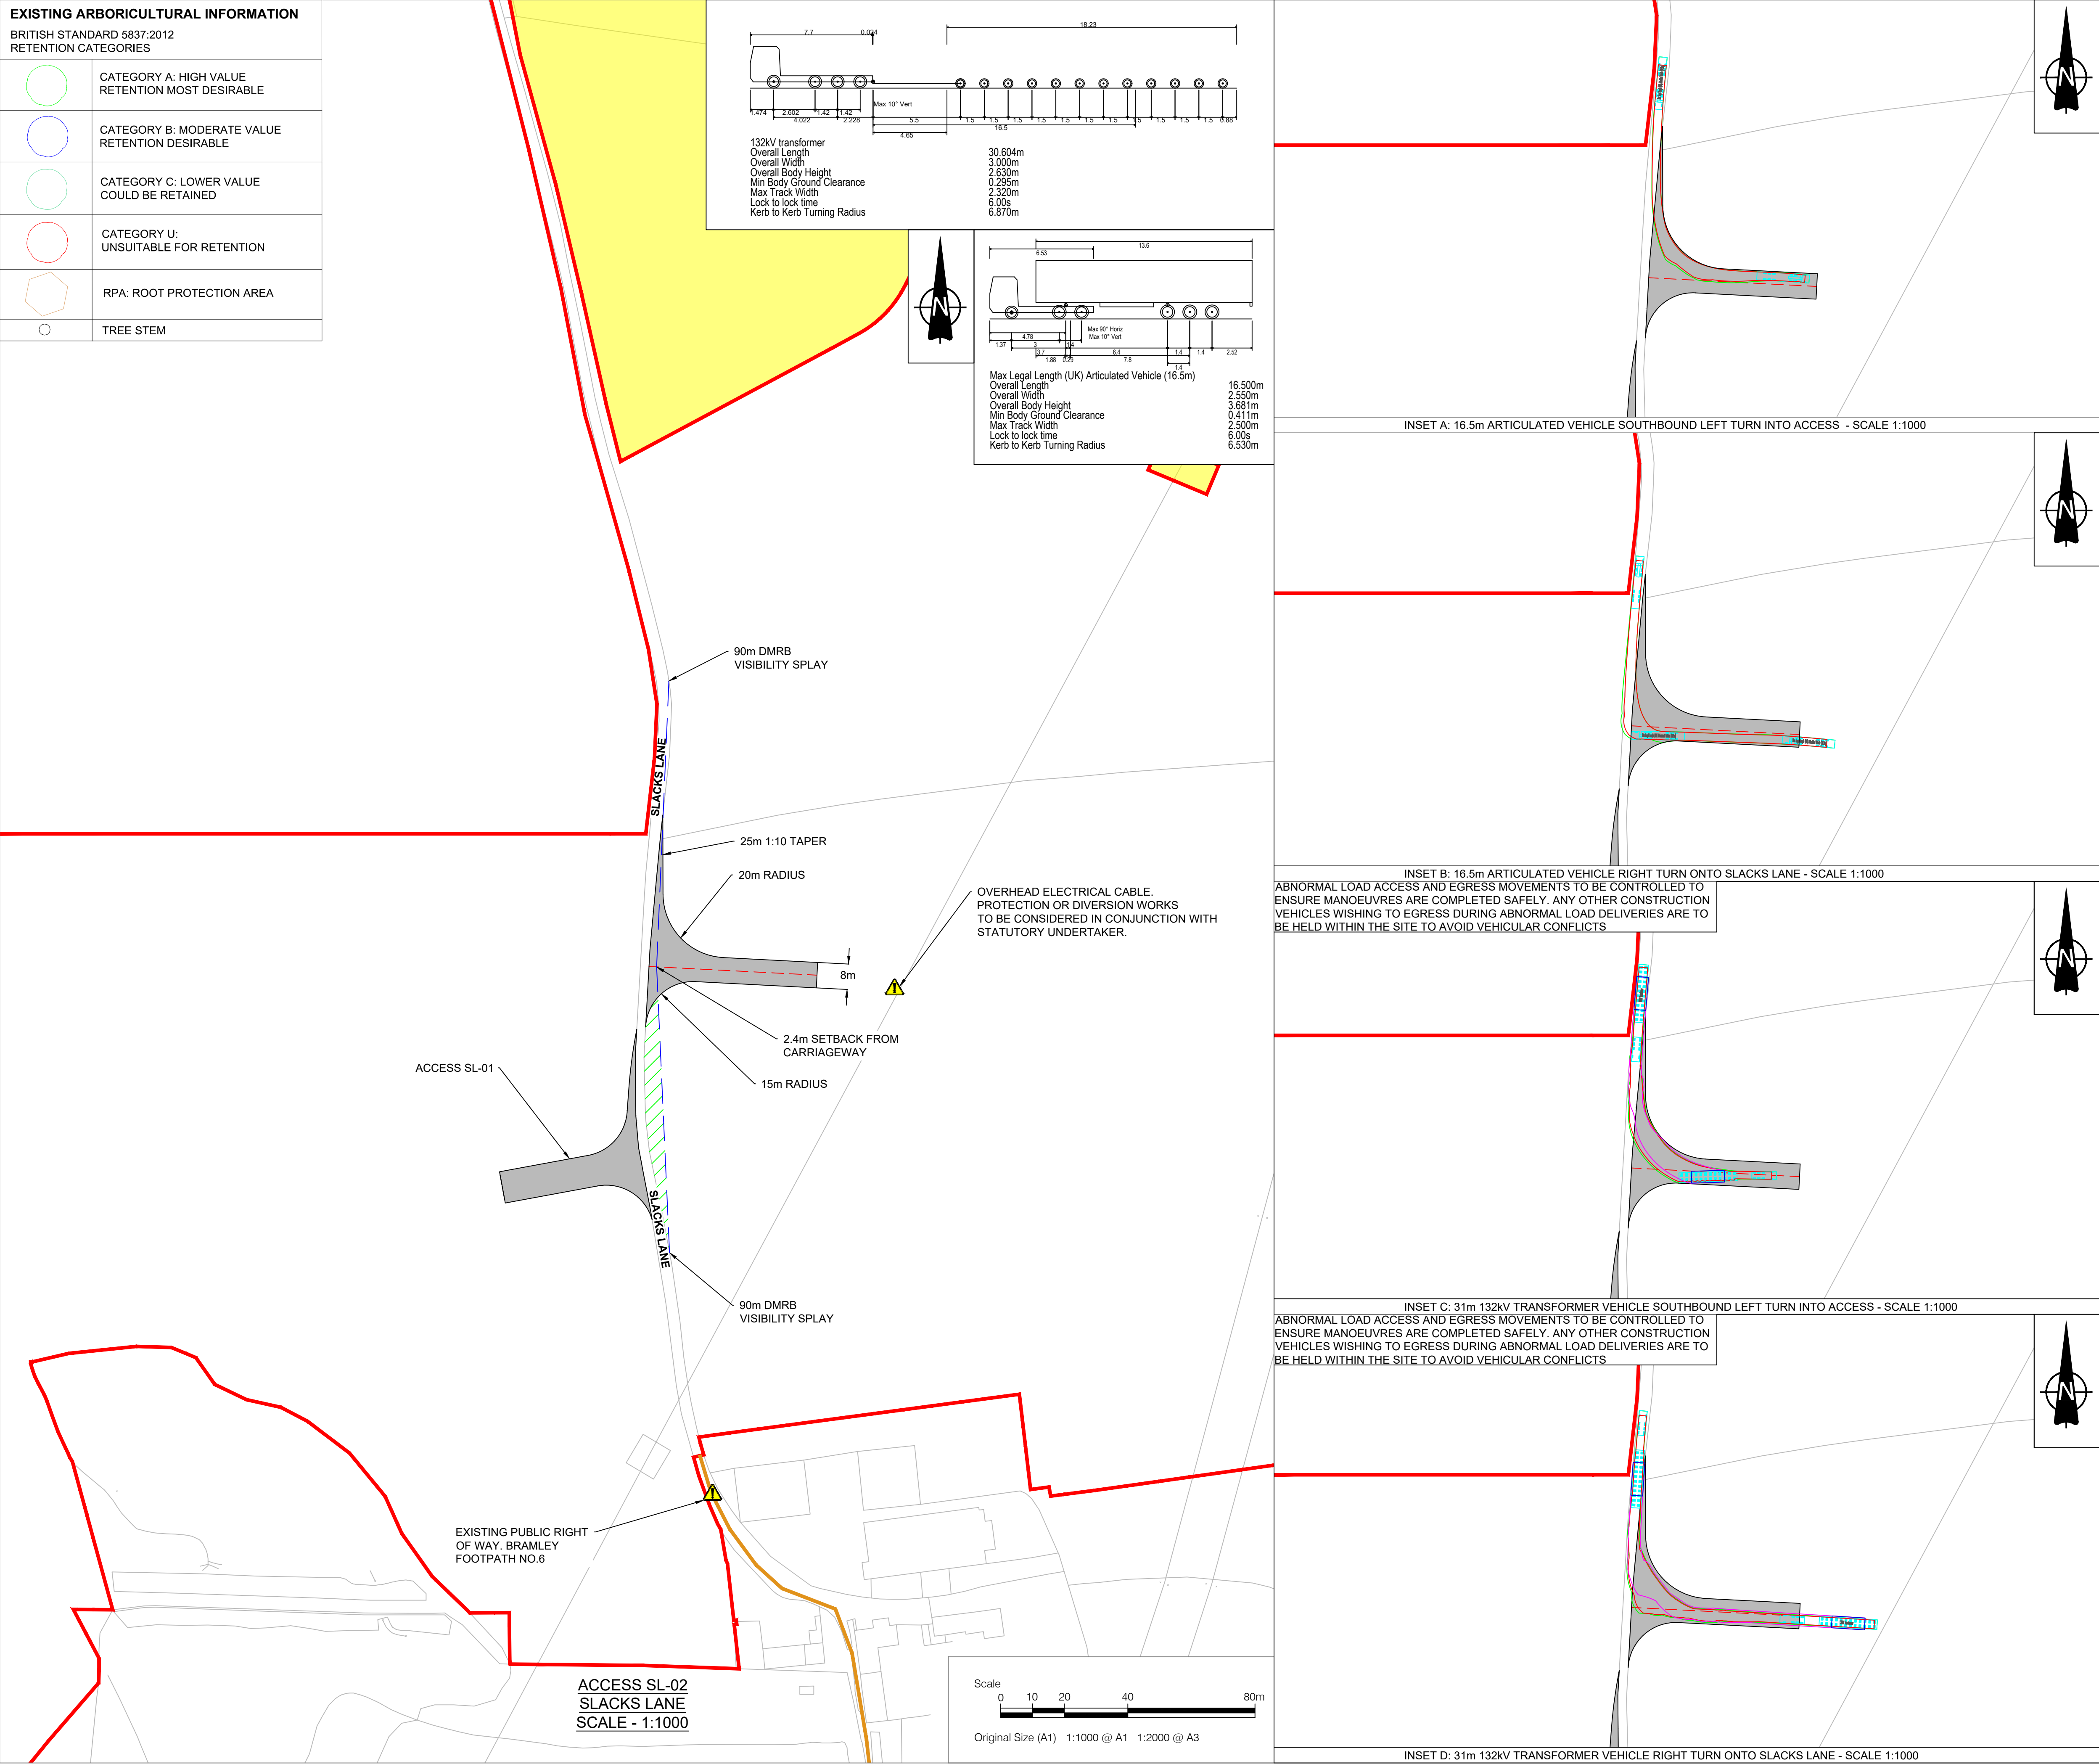

- NOTES**
- This drawing is to be read in conjunction with all other relevant documentation.
 - Do not scale from this drawing, use only printed dimensions.
 - All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
 - This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
 - Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
 - The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
 - Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
 - Junction visibility for the access is based upon DMRB CD109 Table 2.10.

- LEGEND**
- Extent of Access Footprint
 - Order Limits
 - Land Excluded from Order Limits
 - Vehicle Body
 - Vehicle Body Path
 - Vehicle Load
 - Vehicle Load Path
 - Vehicle Wheels Path
 - Edge of Road
 - Access Centreline
 - Junction Visibility
 - Vegetation to be Removed for Vis Splay
 - Indicative Hedgerow Removal Vis Splay
 - Indicative Hedgerow Removal for Bellmouth Access
 - Health and Safety Risk Identifier
 - Existing Public Right of Way

SHEET PLAN

ACCESS LOCATION

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:
PV Area Access SL-02
Appendix 3 - Sheet 4 of 53
Whitestone Solar Farm
Regulation 5(2)(o)


DRAWING DATE: 03/06/2026

SCALE: 1:1000	SHEET: Sheet 4 of 53
SIZE: A1	REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020


EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012 RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

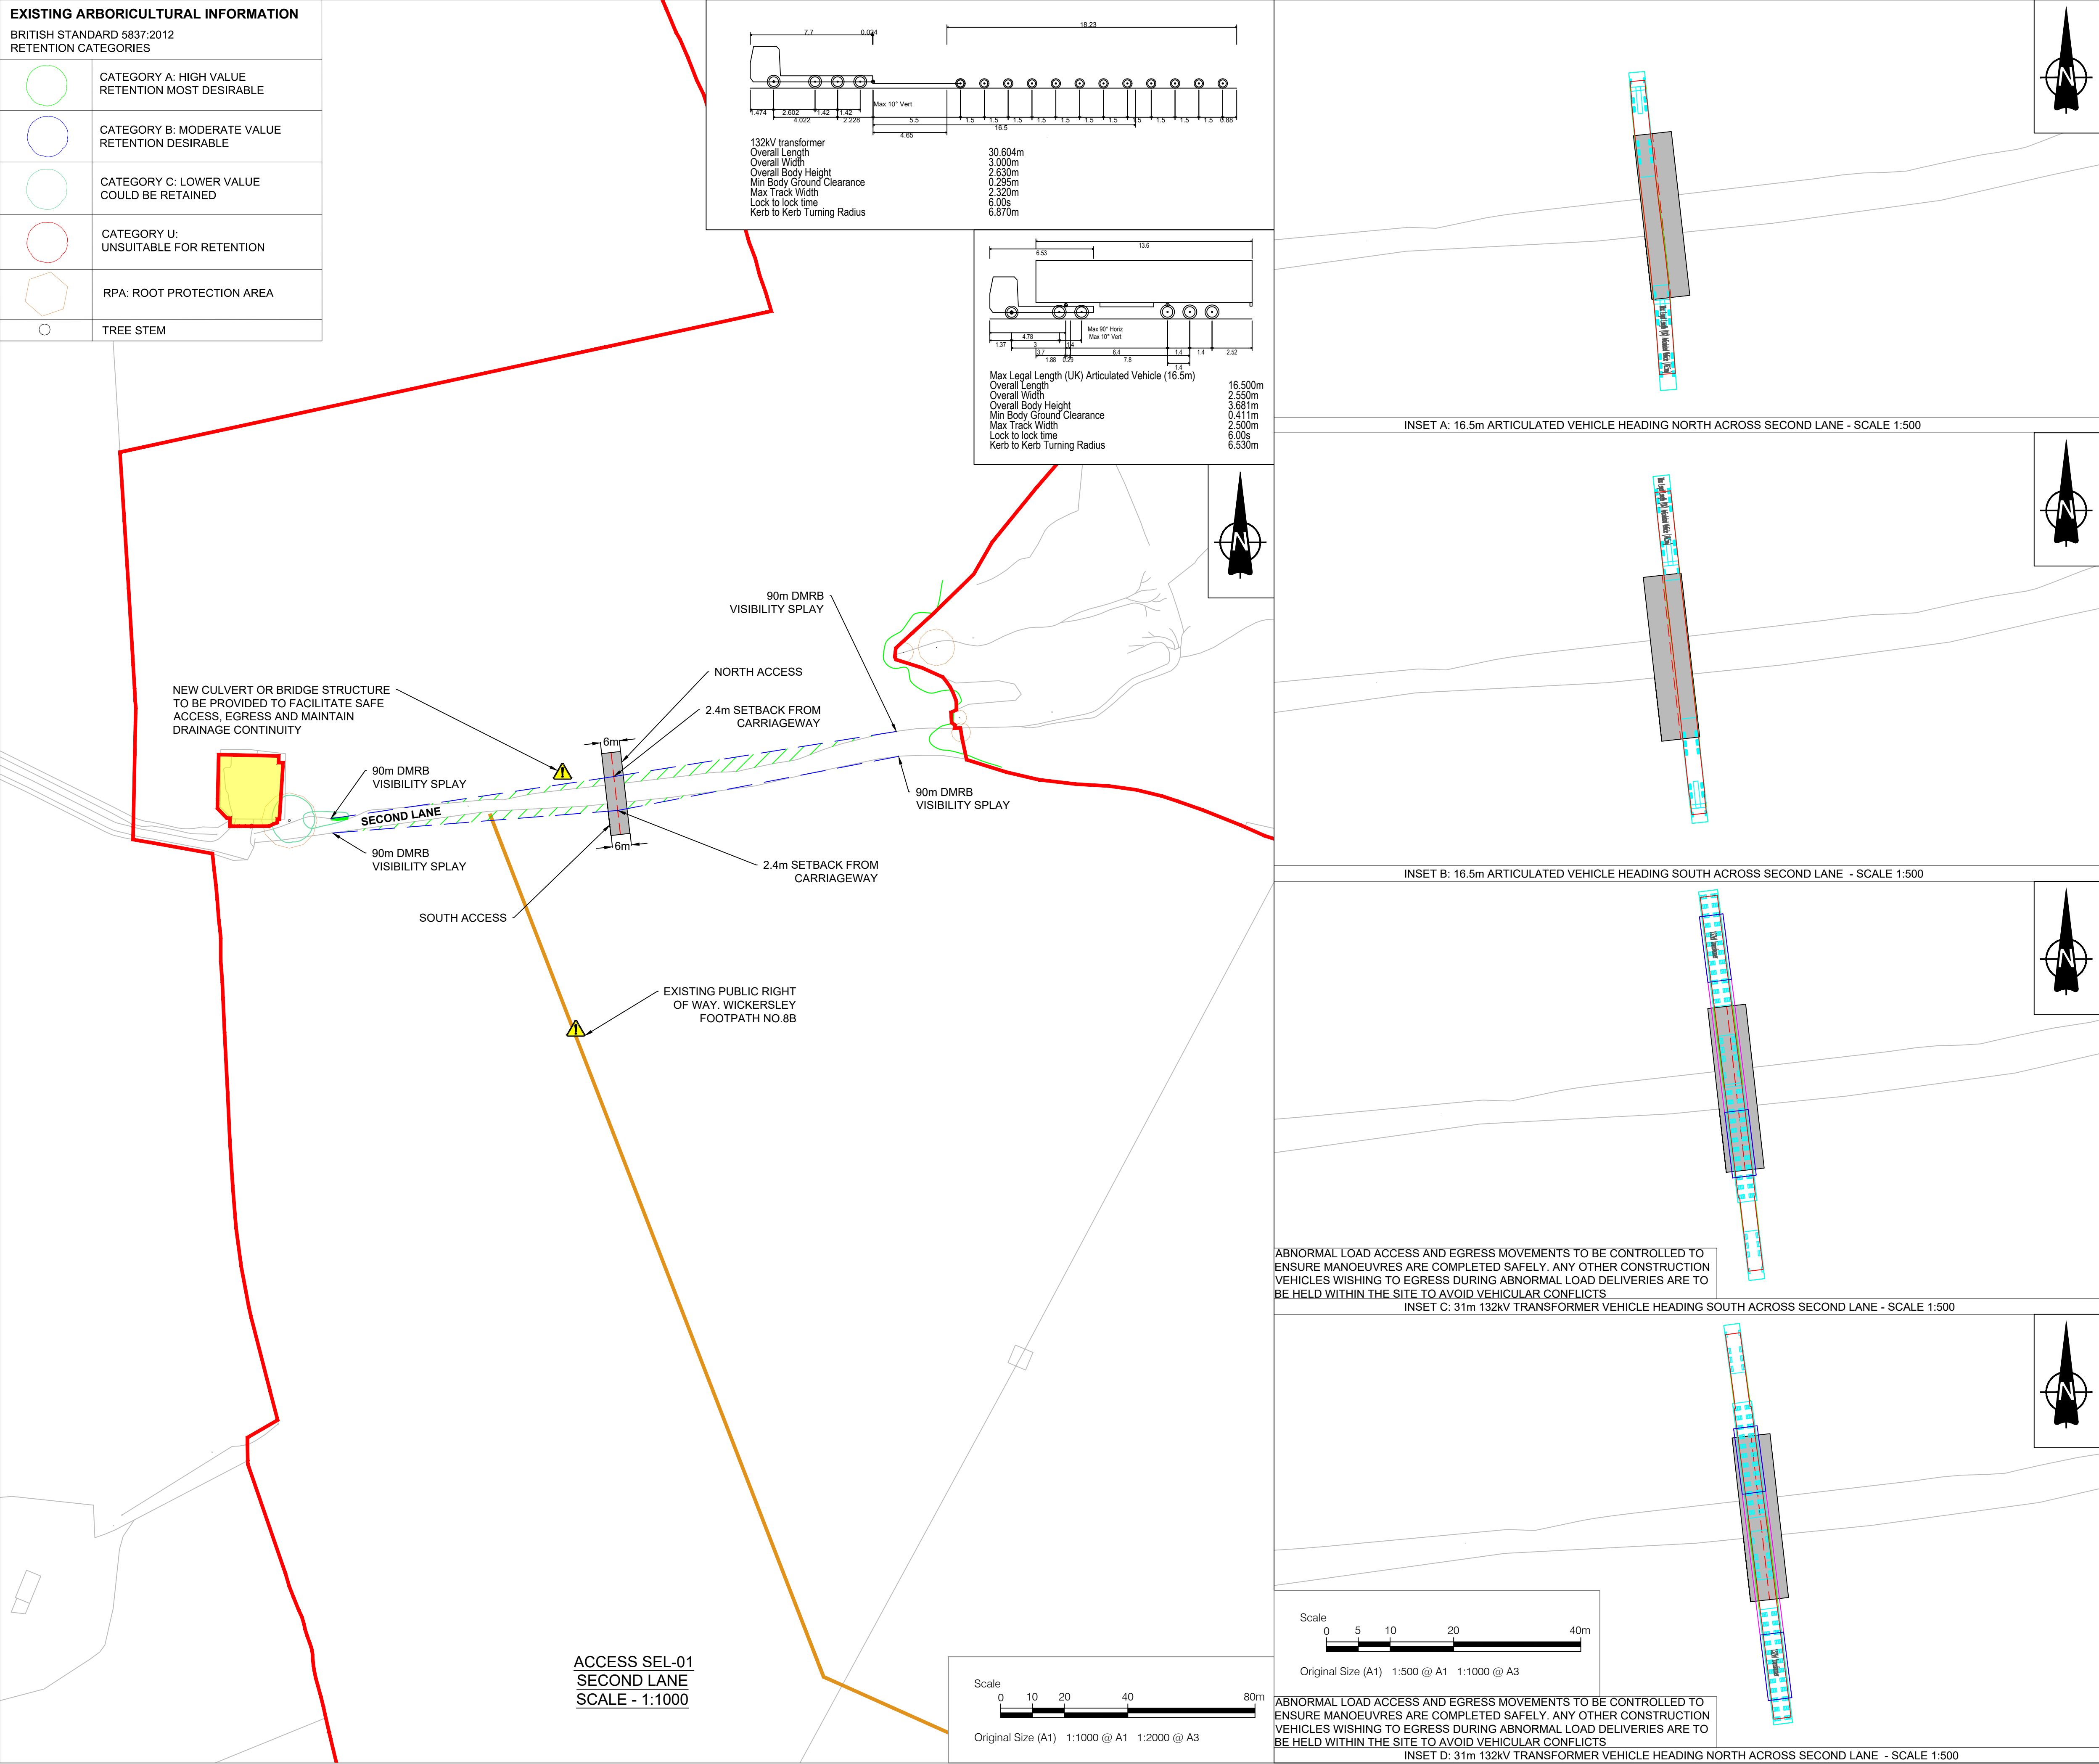

Sources: Esri, TomTom, Garmin, FAO, NOAA, USGS, © OpenStreetMap contributors, and the GIS User Community. Reproduced from Ordnance Survey digital map data © Crown copyright 2026. All rights reserved. License number 0000848182

- NOTES**
- This drawing is to be read in conjunction with all other relevant documentation.
 - Do not scale from this drawing, use only printed dimensions.
 - All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
 - This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
 - Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
 - The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
 - Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
 - Junction visibility for the access is based upon DMRB CD109 Table 2.10.

- LEGEND**
- Extent of Access Footprint
 - Order Limits
 - Land Excluded from Order Limits
 - Vehicle Body
 - Vehicle Body Path
 - Vehicle Load
 - Vehicle Load Path
 - Vehicle Wheels Path
 - Edge of Road
 - Access Centreline
 - Junction Visibility
 - Vegetation to be Removed for Vis Splay
 - Indicative Hedgerow Removal Vis Splay
 - Indicative Hedgerow Removal for Bellmouth Access
 - Health and Safety Risk Identifier
 - Existing Public Right of Way

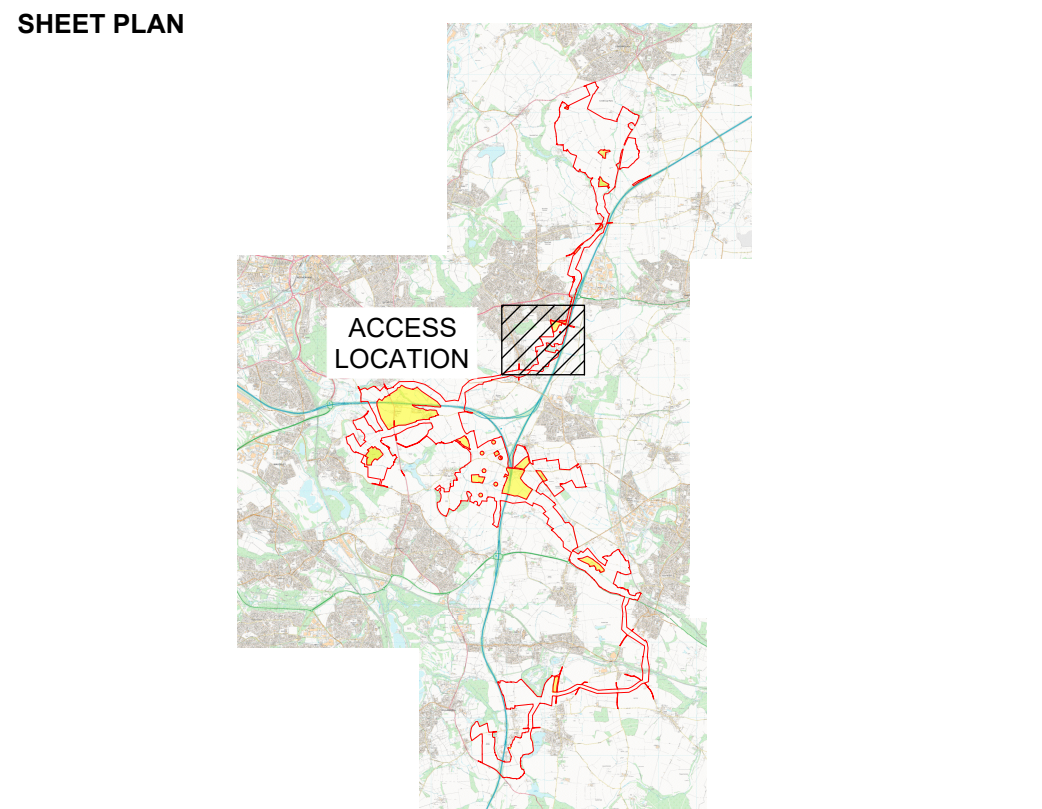

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:
PV Area Access SEL-01
Sheet 5 of 53
Whitestone Solar Farm
Regulation 5(2)(o)

DRAWING DATE: 03/06/2026


SCALE: AS SHOWN	SHEET: Sheet 5 of 53
SIZE: A1	REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12



APPLICATION NUMBER: EN0110020



EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012 RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

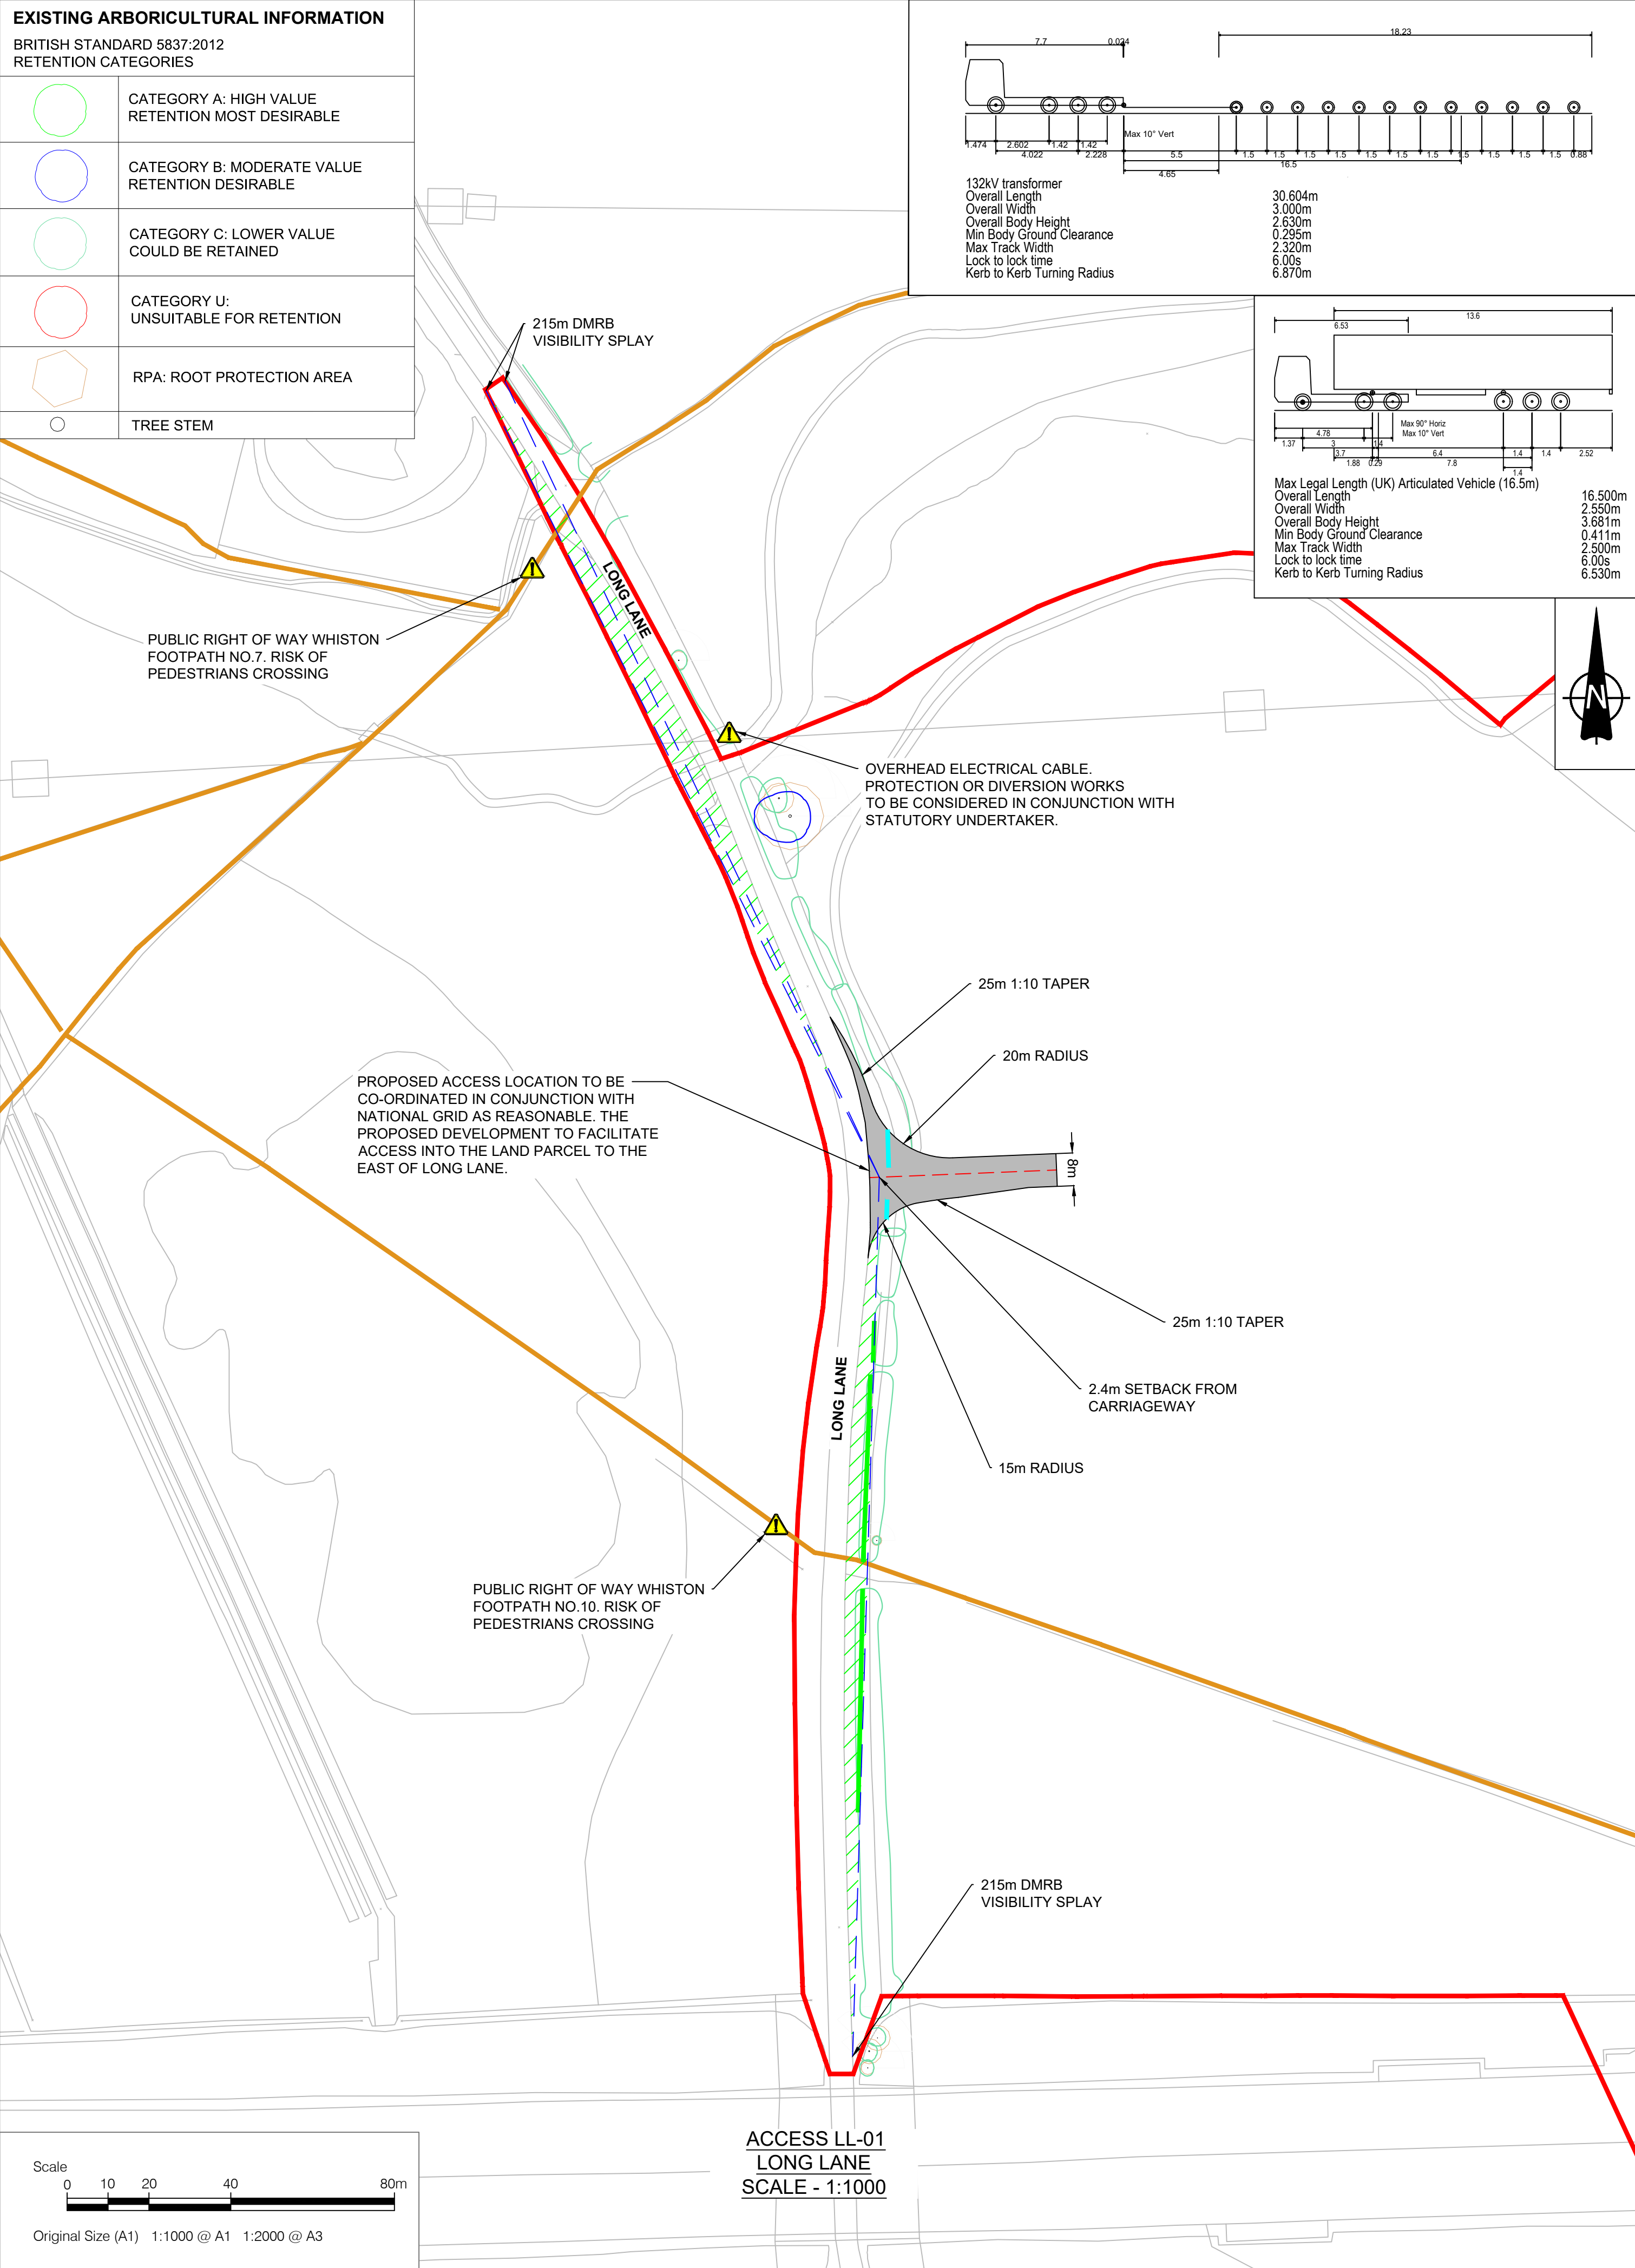

ACCESS LL-01
LONG LANE
SCALE - 1:1000

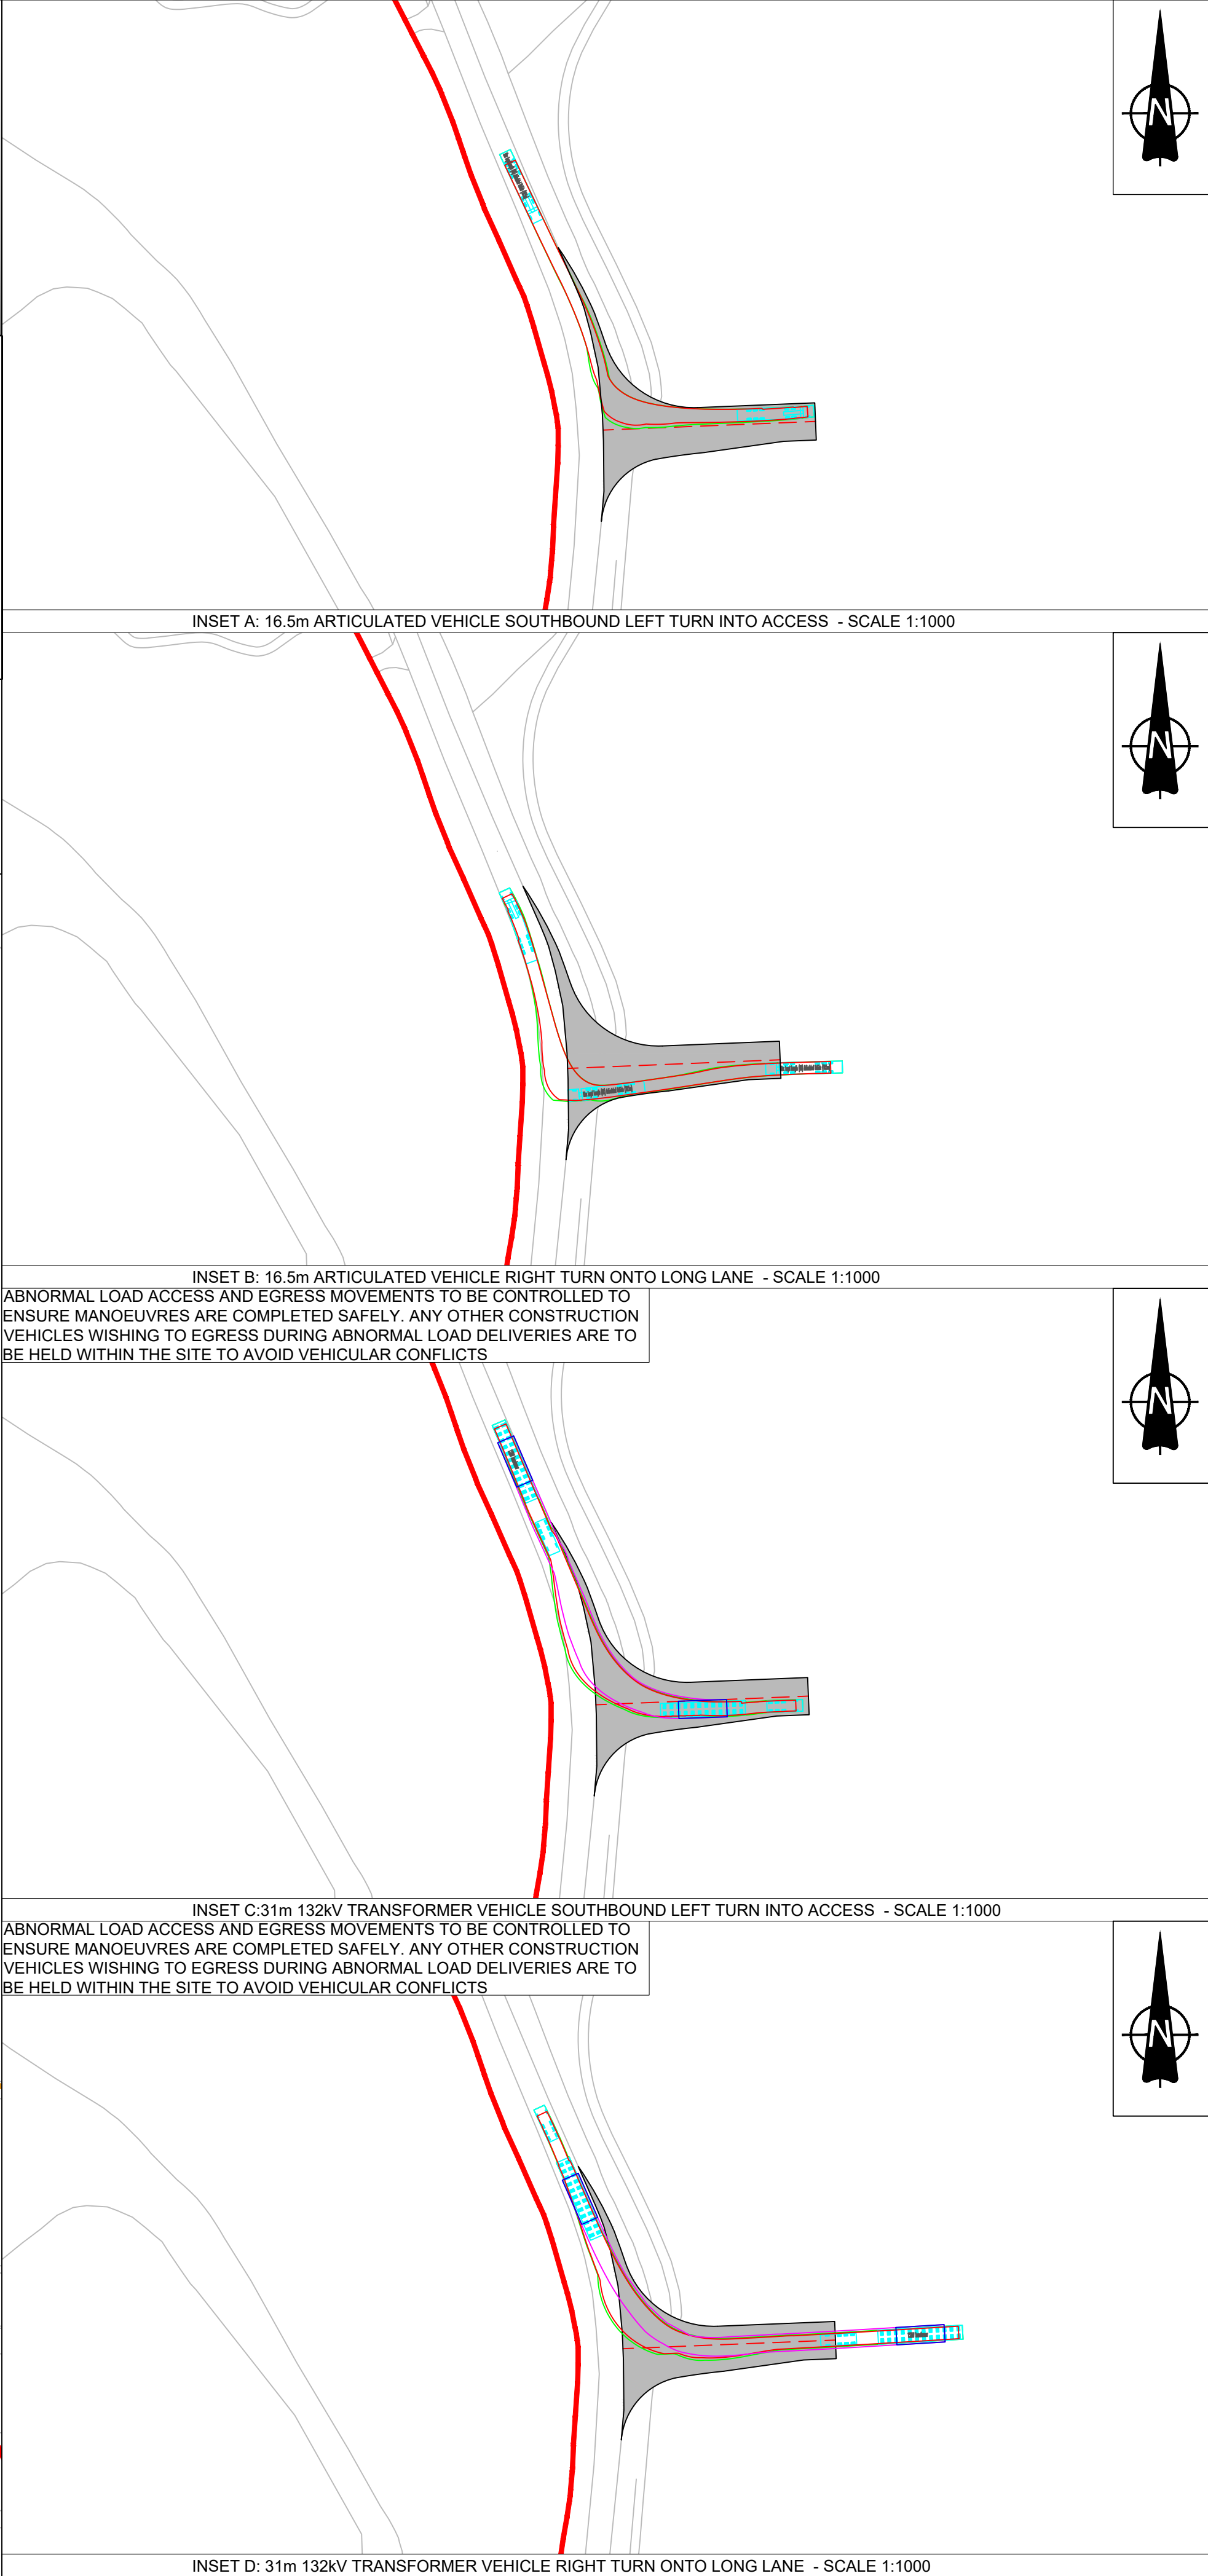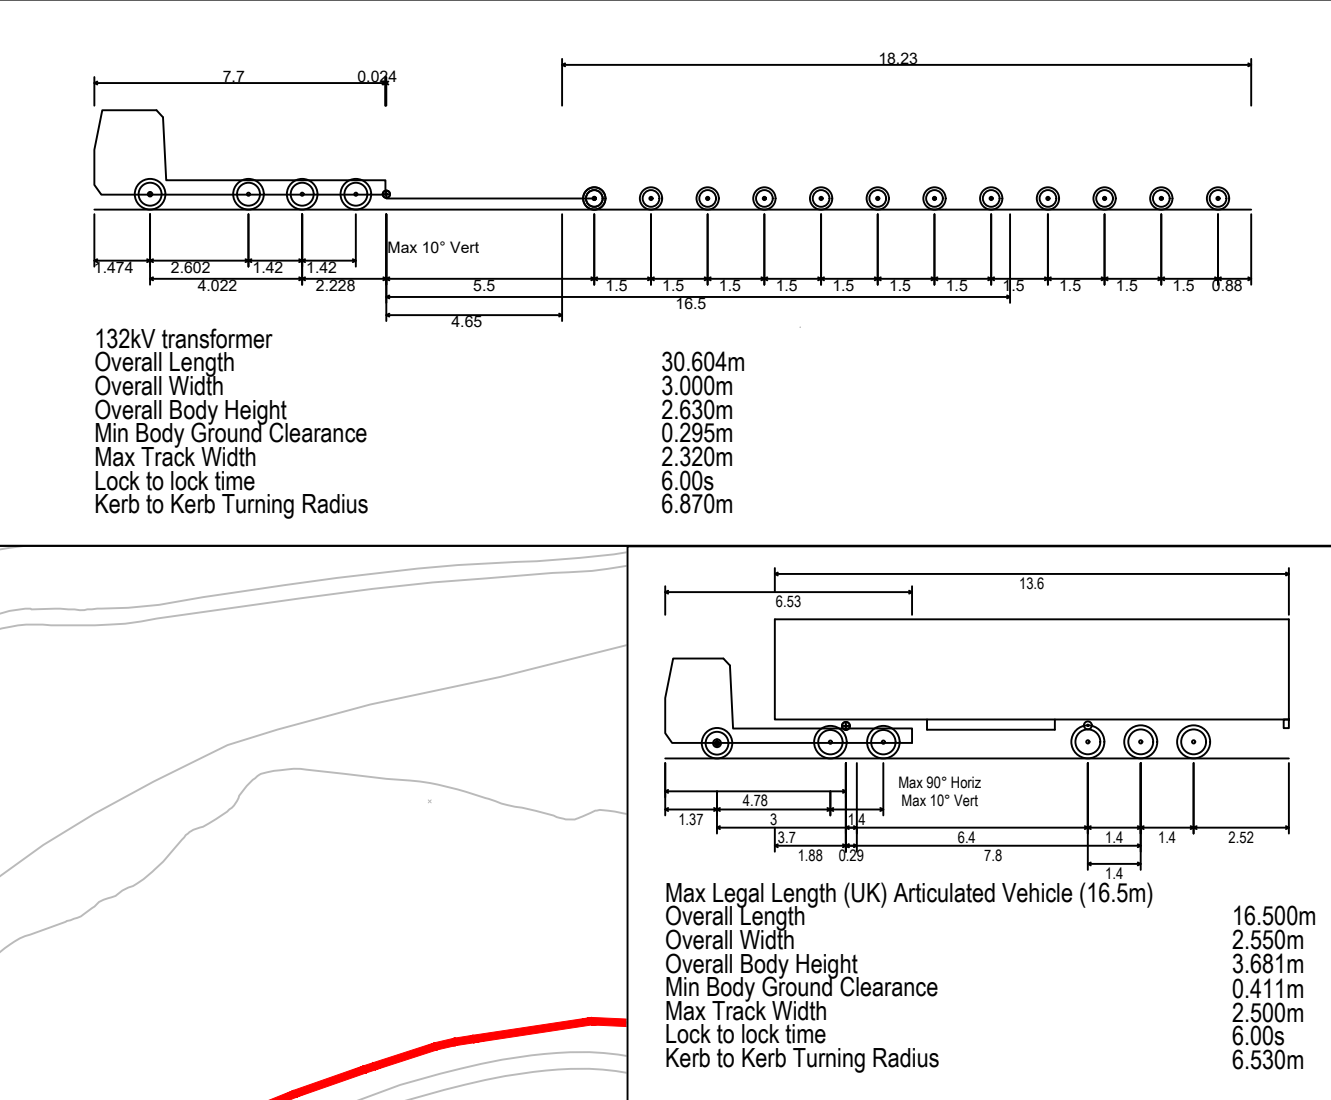

NOTES

- This drawing is to be read in conjunction with all other relevant documentation.
- Do not scale from this drawing, use only printed dimensions.
- All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
- This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
- Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
- The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
- Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
- Junction visibility for the access is based upon DMRB CD109 Table 2.10.

LEGEND

- Extent of Access Footprint
- Order Limits
- Land Excluded from Order Limits
- Vehicle Body
- Vehicle Body Path
- Vehicle Load
- Vehicle Load Path
- Vehicle Wheels Path
- Edge of Road
- Access Centreline
- Junction Visibility
- Vegetation to be Removed for Vis Splay
- Indicative Hedgerow Removal Vis Splay
- Indicative Hedgerow Removal for Bellmouth Access
- Health and Safety Risk Identifier
- Existing Public Right of Way

SHEET PLAN

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:

PV Area Access LL-01

Appendix 3 - Sheet 6 of 53

Whitestone Solar Farm

Regulation 5(2)(o)

DRAWING DATE: 03/06/2026

SCALE: 1:1000

SHEET: Sheet 6 of 53


SIZE: A1

REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020

EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012	
RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

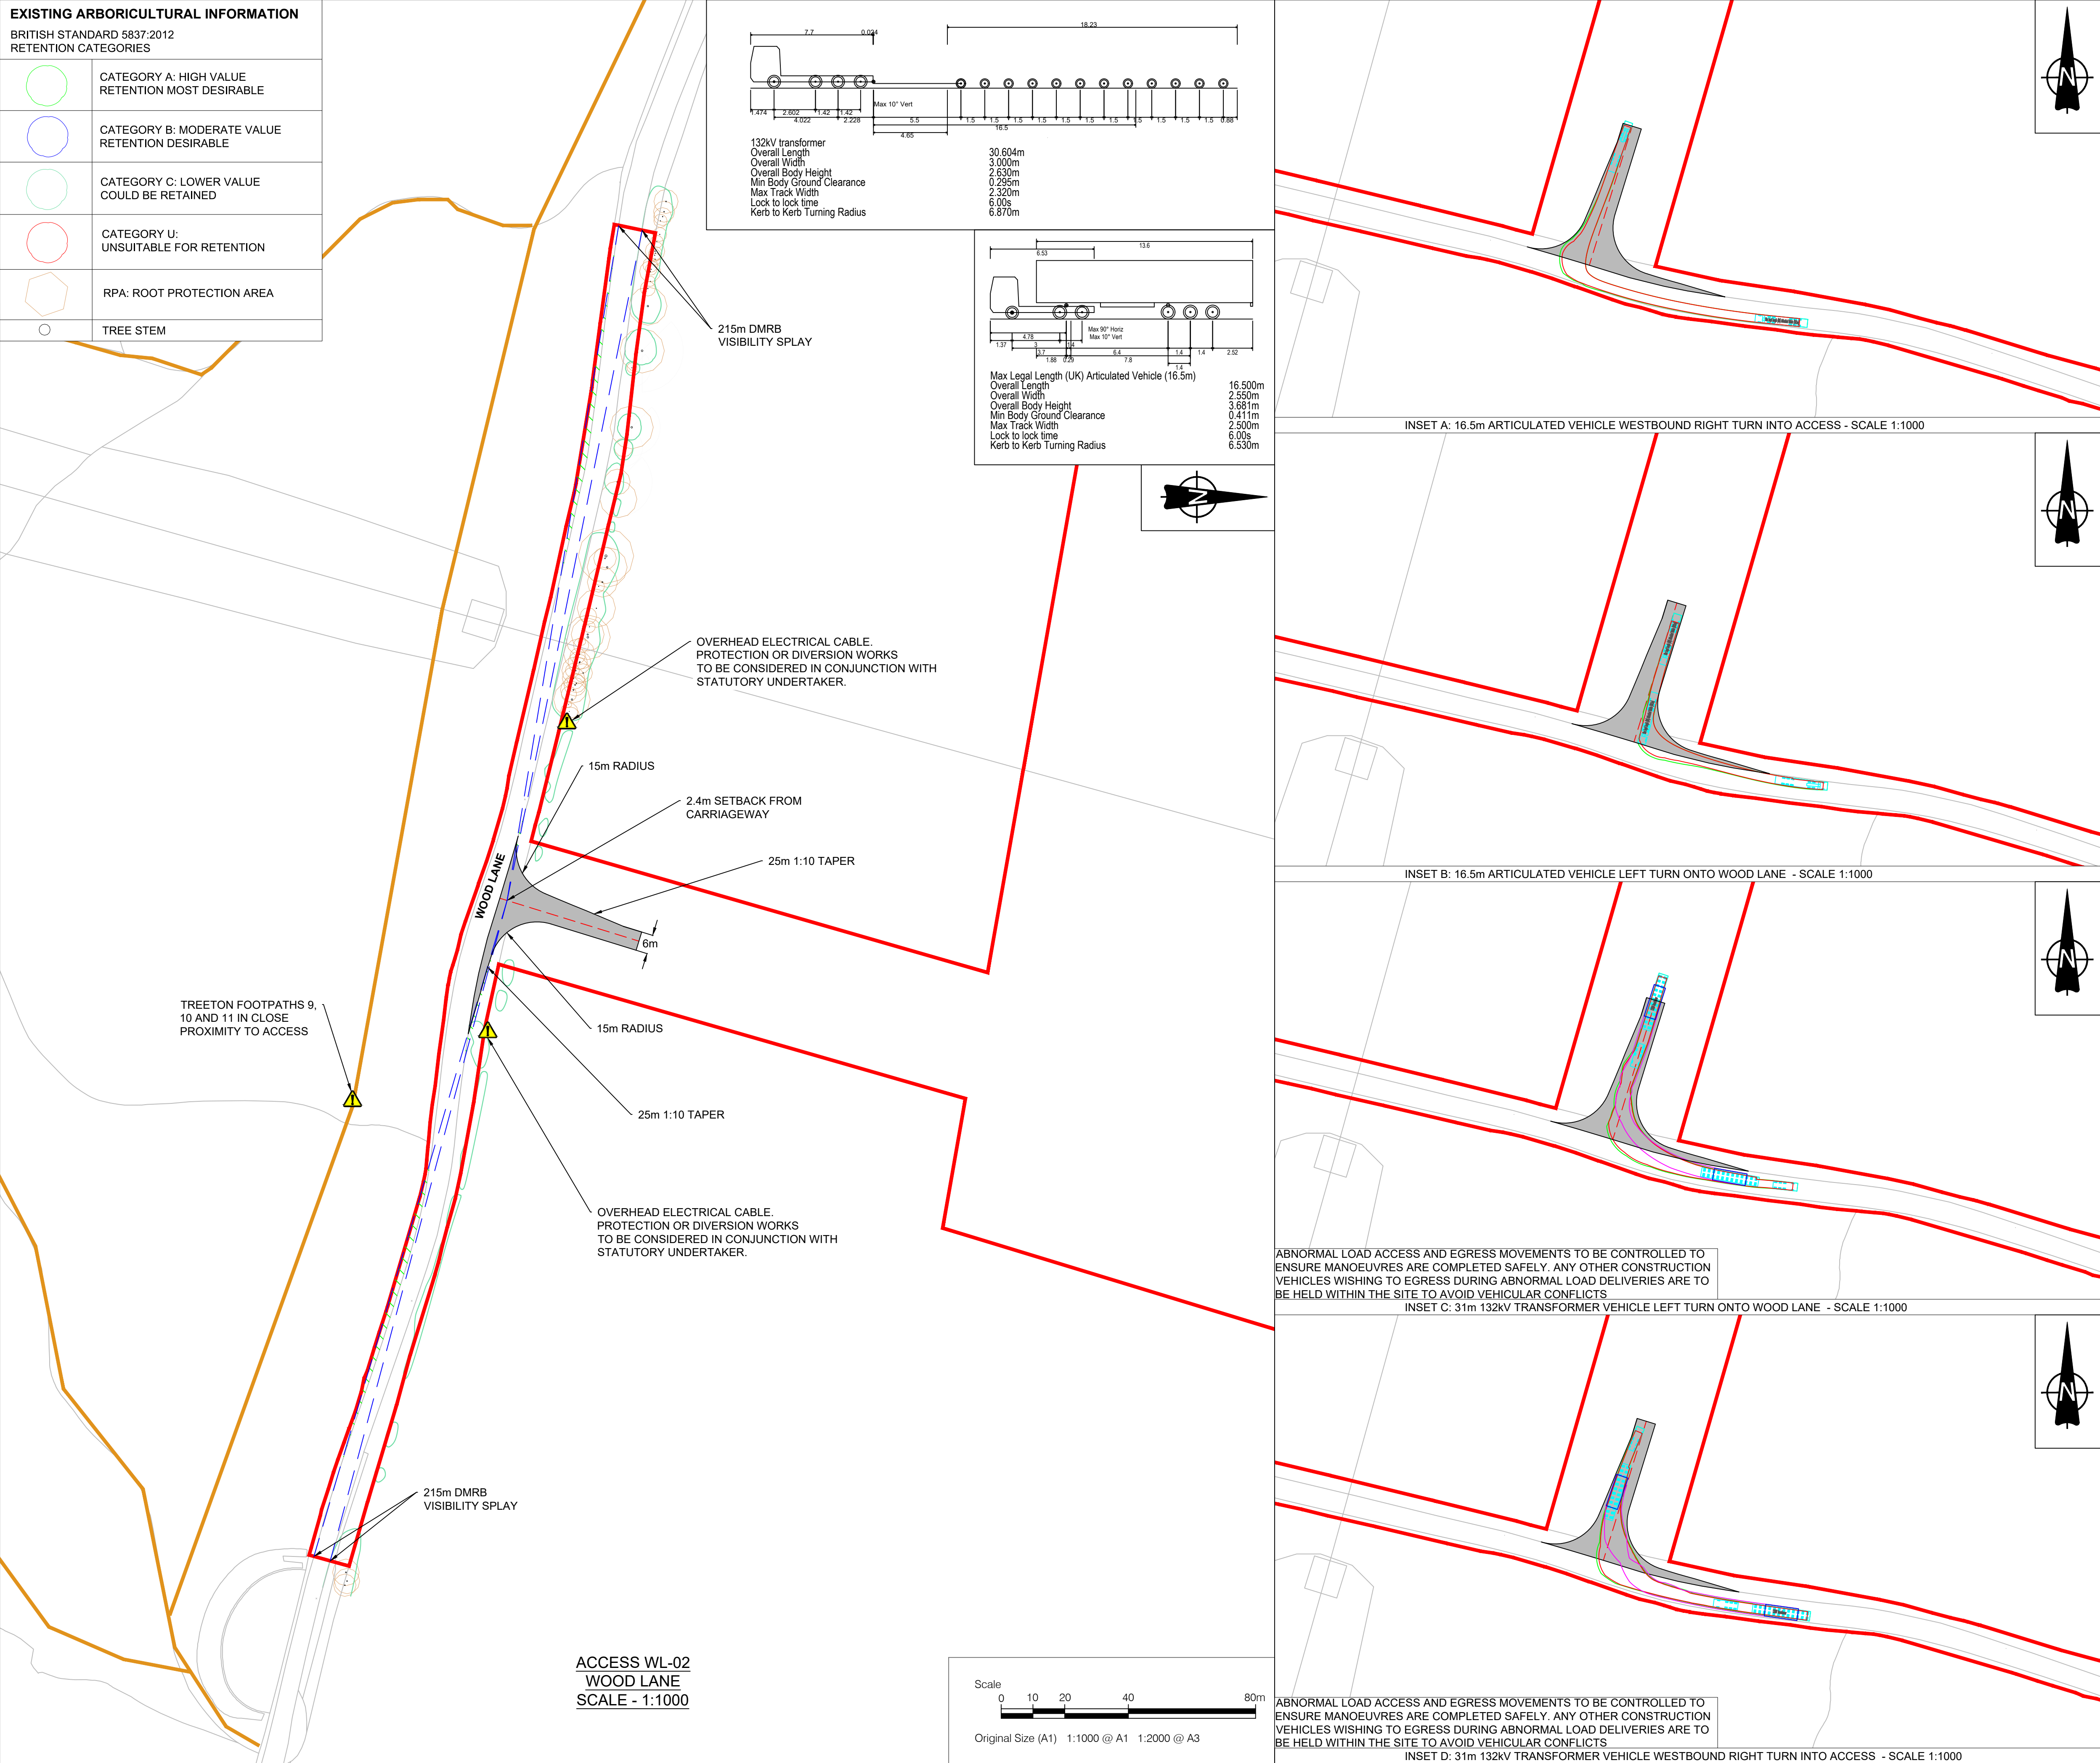

- NOTES**
- This drawing is to be read in conjunction with all other relevant documentation.
 - Do not scale from this drawing, use only printed dimensions.
 - All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
 - This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
 - Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
 - The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
 - Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
 - Junction visibility for the access is based upon DMRB CD109 Table 2.10.

- LEGEND**
- Extent of Access Footprint
 - Order Limits
 - Land Excluded from Order Limits
 - Vehicle Body
 - Vehicle Body Path
 - Vehicle Load
 - Vehicle Load Path
 - Vehicle Wheels Path
 - Edge of Road
 - Access Centreline
 - Junction Visibility
 - Vegetation to be Removed for Vis Splay
 - Indicative Hedgerow Removal Vis Splay
 - Indicative Hedgerow Removal for Bellmouth Access
 - Health and Safety Risk Identifier
 - Existing Public Right of Way

SHEET PLAN

ACCESS LOCATION

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:
PV Area Access WL-02
Appendix 3 - Sheet 7 of 53
Whitestone Solar Farm
Regulation 5(2)(o)



DRAWING DATE: 03/06/2026

SCALE: 1:1000	SHEET: Sheet 7 of 53
SIZE: A1	REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020

EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012 RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

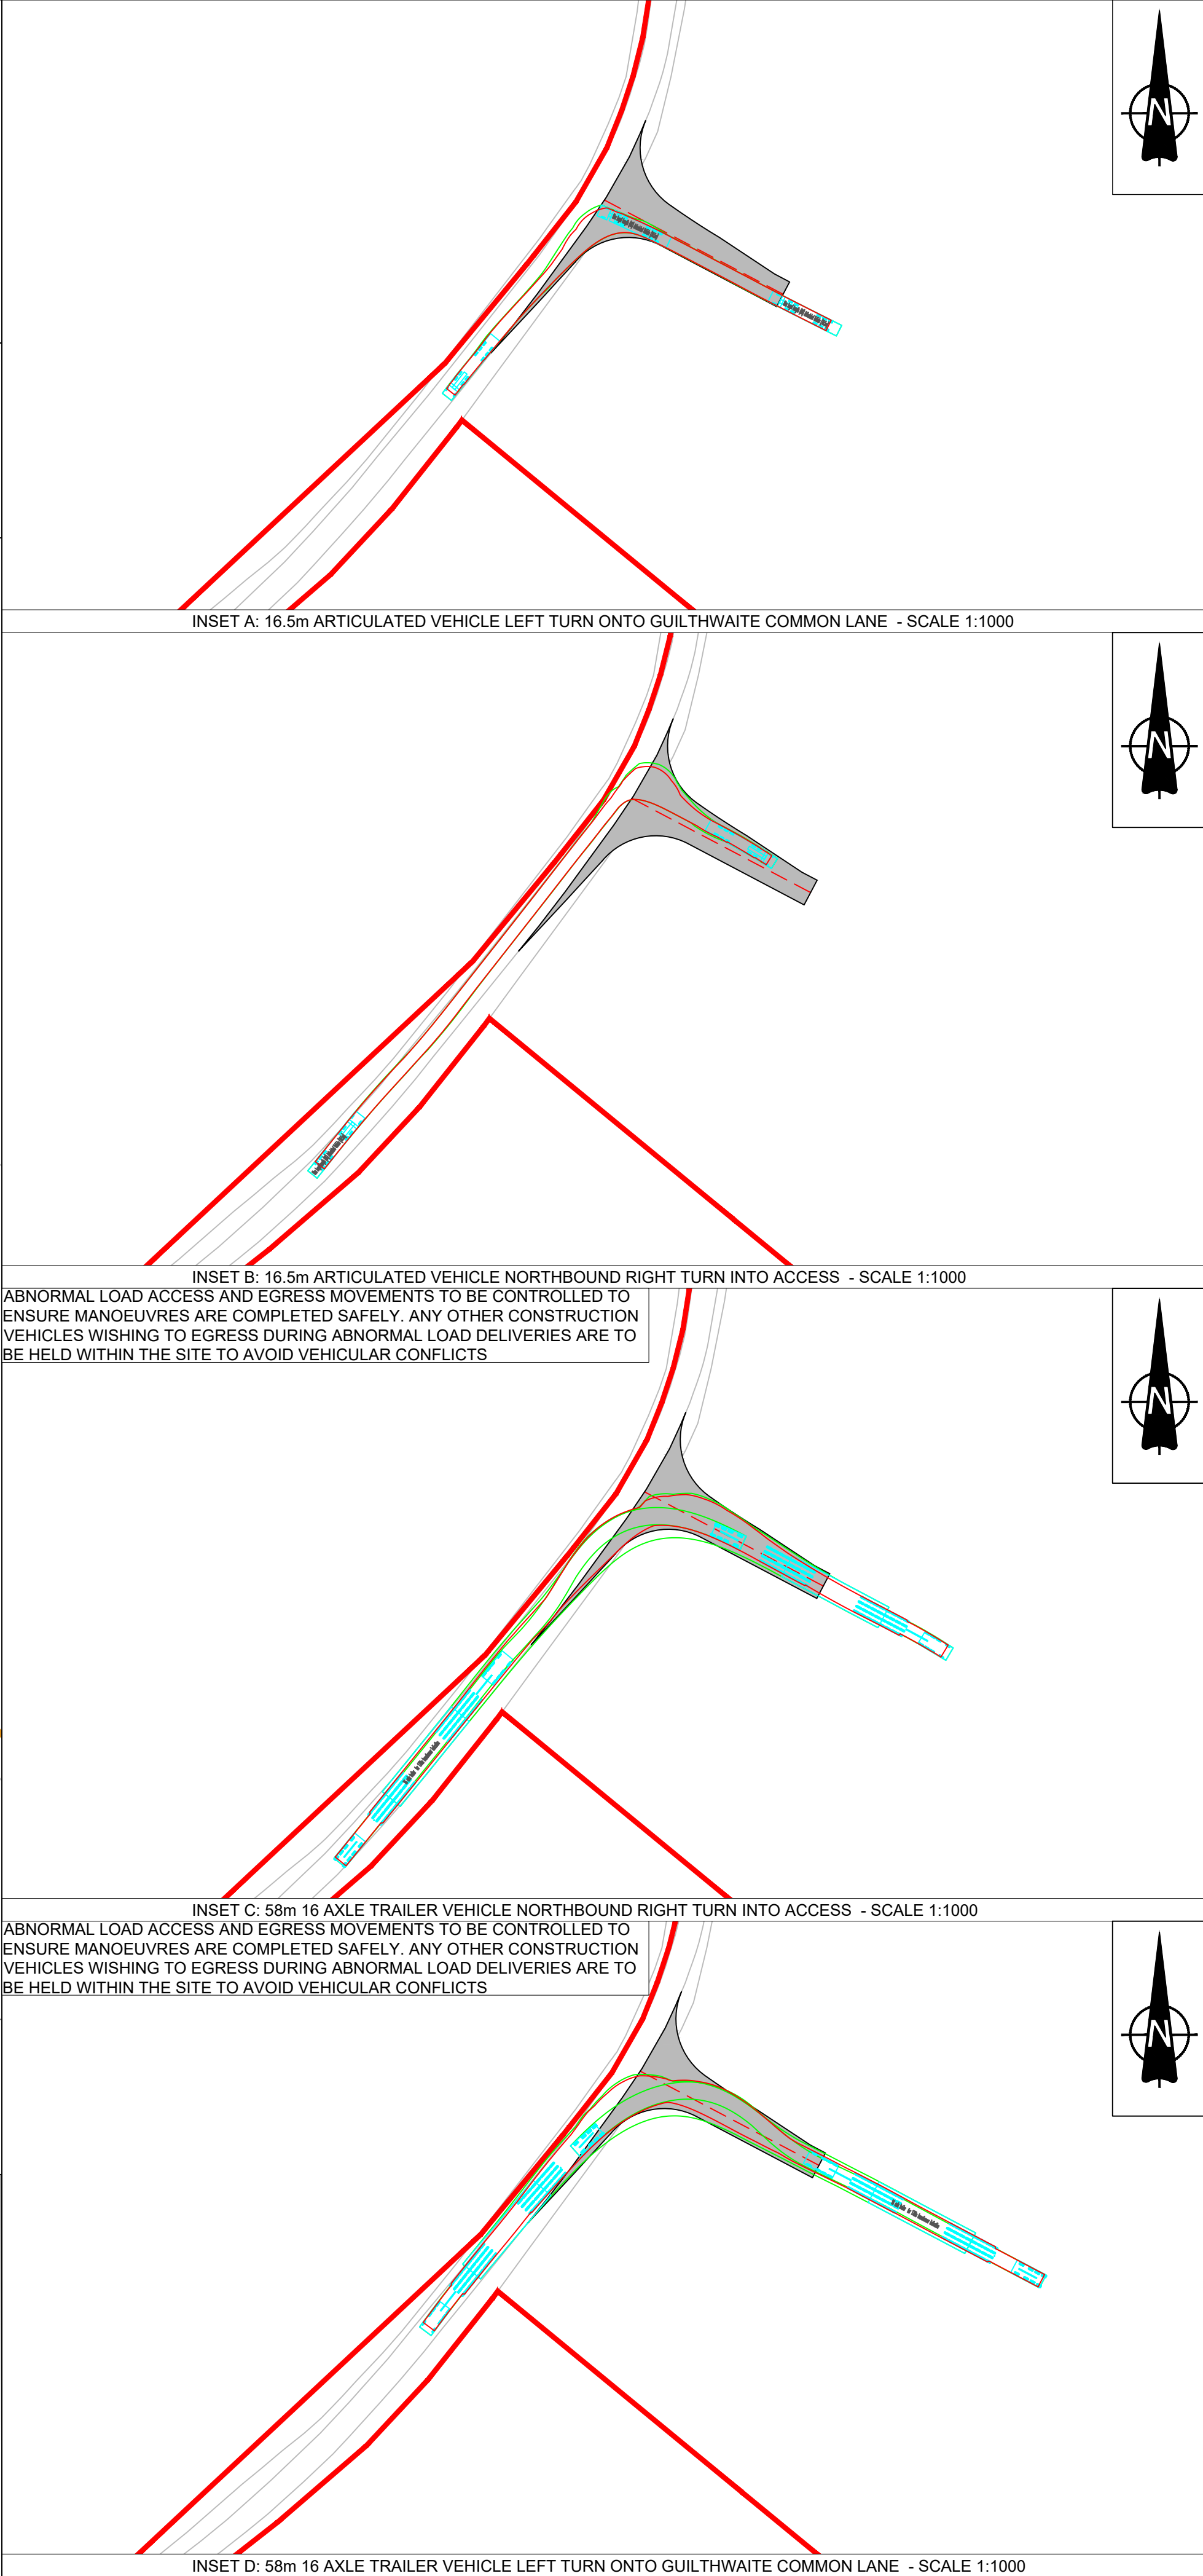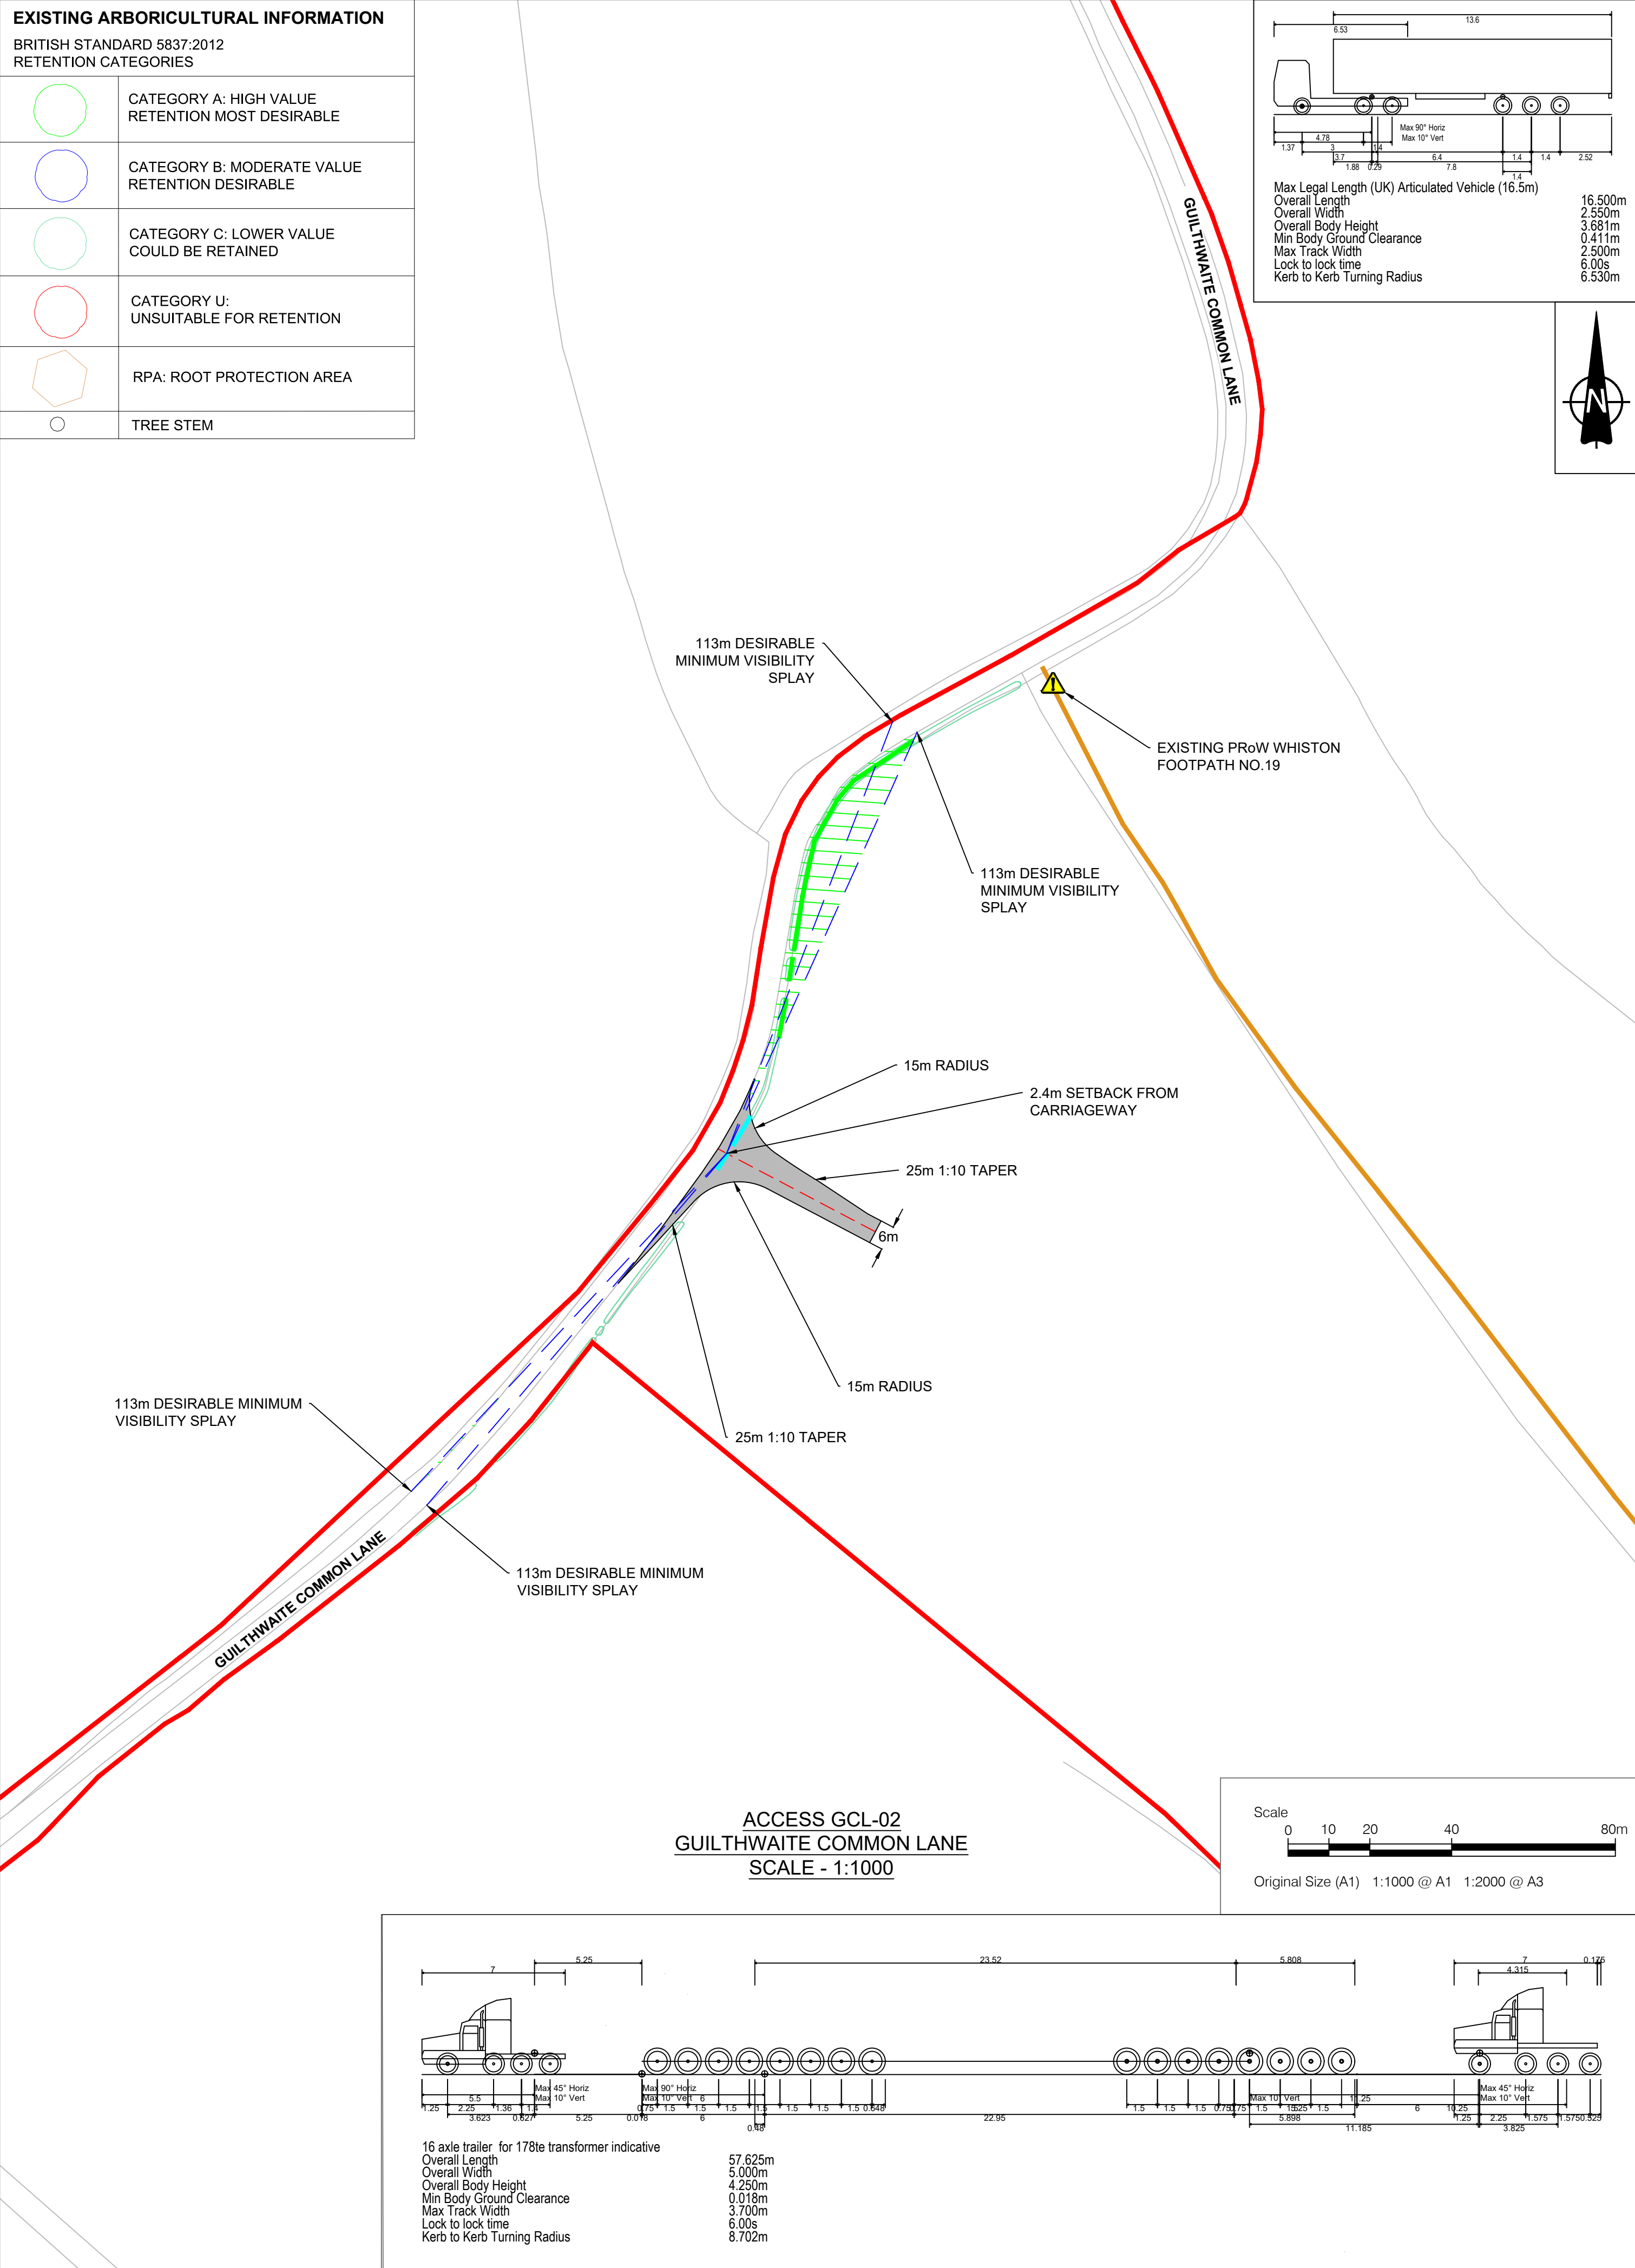

- NOTES**
- This drawing is to be read in conjunction with all other relevant documentation.
 - Do not scale from this drawing, use only printed dimensions.
 - All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
 - This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
 - Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
 - The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
 - Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
 - Junction visibility for the access is based upon visibility parameters derived using the 85th percentile speed survey conducted between the 4th June 2025 to the 10th June 2025.

- LEGEND**
- Extent of Access Footprint
 - Order Limits
 - Land Excluded from Order Limits
 - Vehicle Body
 - Vehicle Body Path
 - Vehicle Load
 - Vehicle Load Path
 - Vehicle Wheels Path
 - Edge of Road
 - Access Centreline
 - Junction Visibility
 - Vegetation to be Removed for Vis Splay
 - Indicative Hedgerow Removal Vis Splay
 - Indicative Hedgerow Removal for Bellmouth Access
 - Health and Safety Risk Identifier
 - Existing Public Right of Way

SHEET PLAN

ACCESS LOCATION

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:
PV Area Access GCL-02
Appendix 3 - Sheet 8 of 53
Whitestone Solar Farm
Regulation 5(2)(o)





DRAWING DATE: 03/06/2026

SCALE: 1:1000	SHEET: Sheet 8 of 53
SIZE: A1	REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12







APPLICATION NUMBER: EN0110020

EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012	
RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

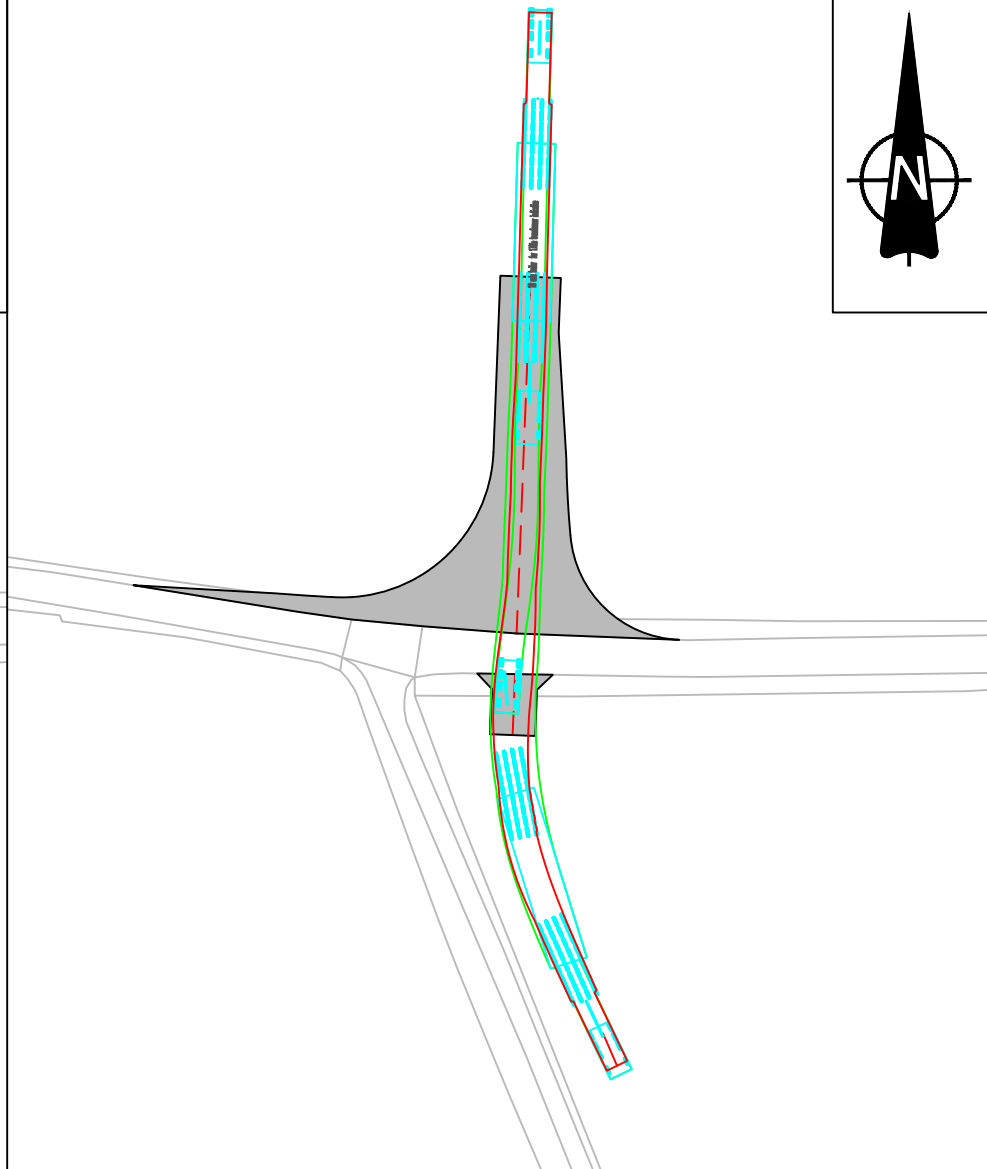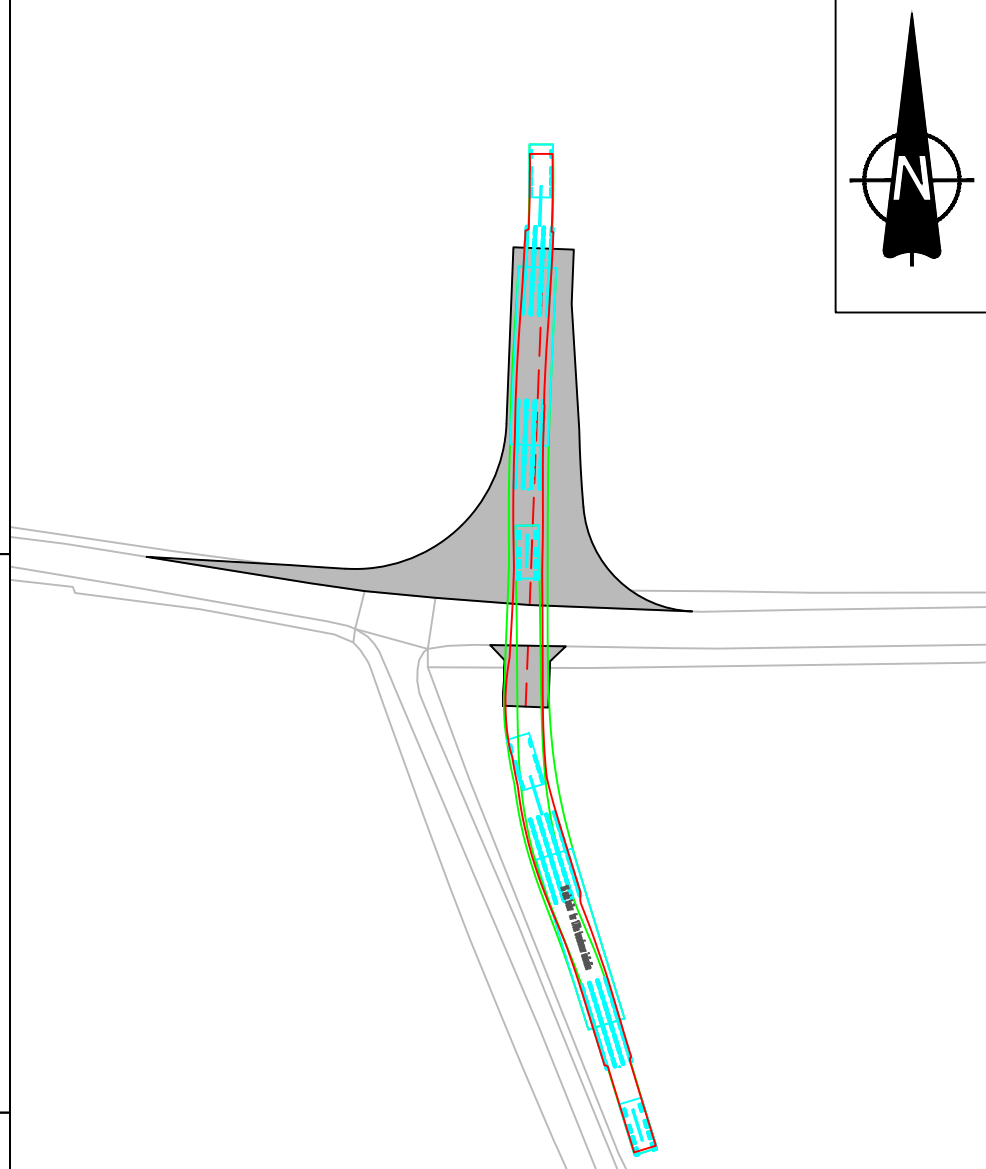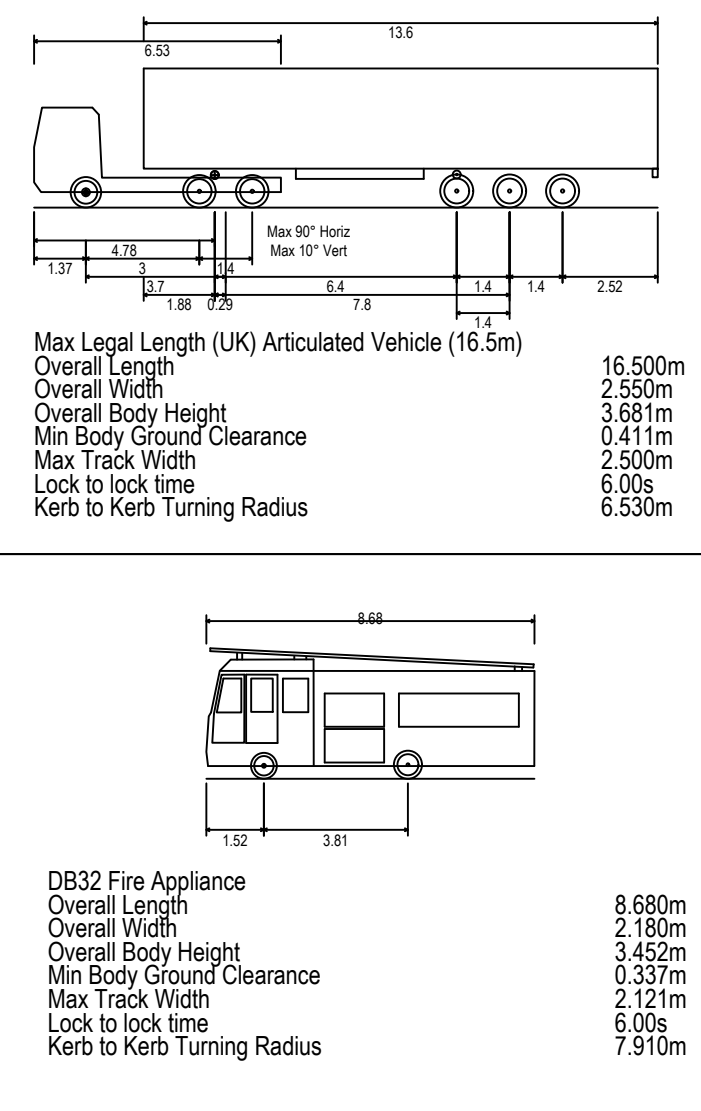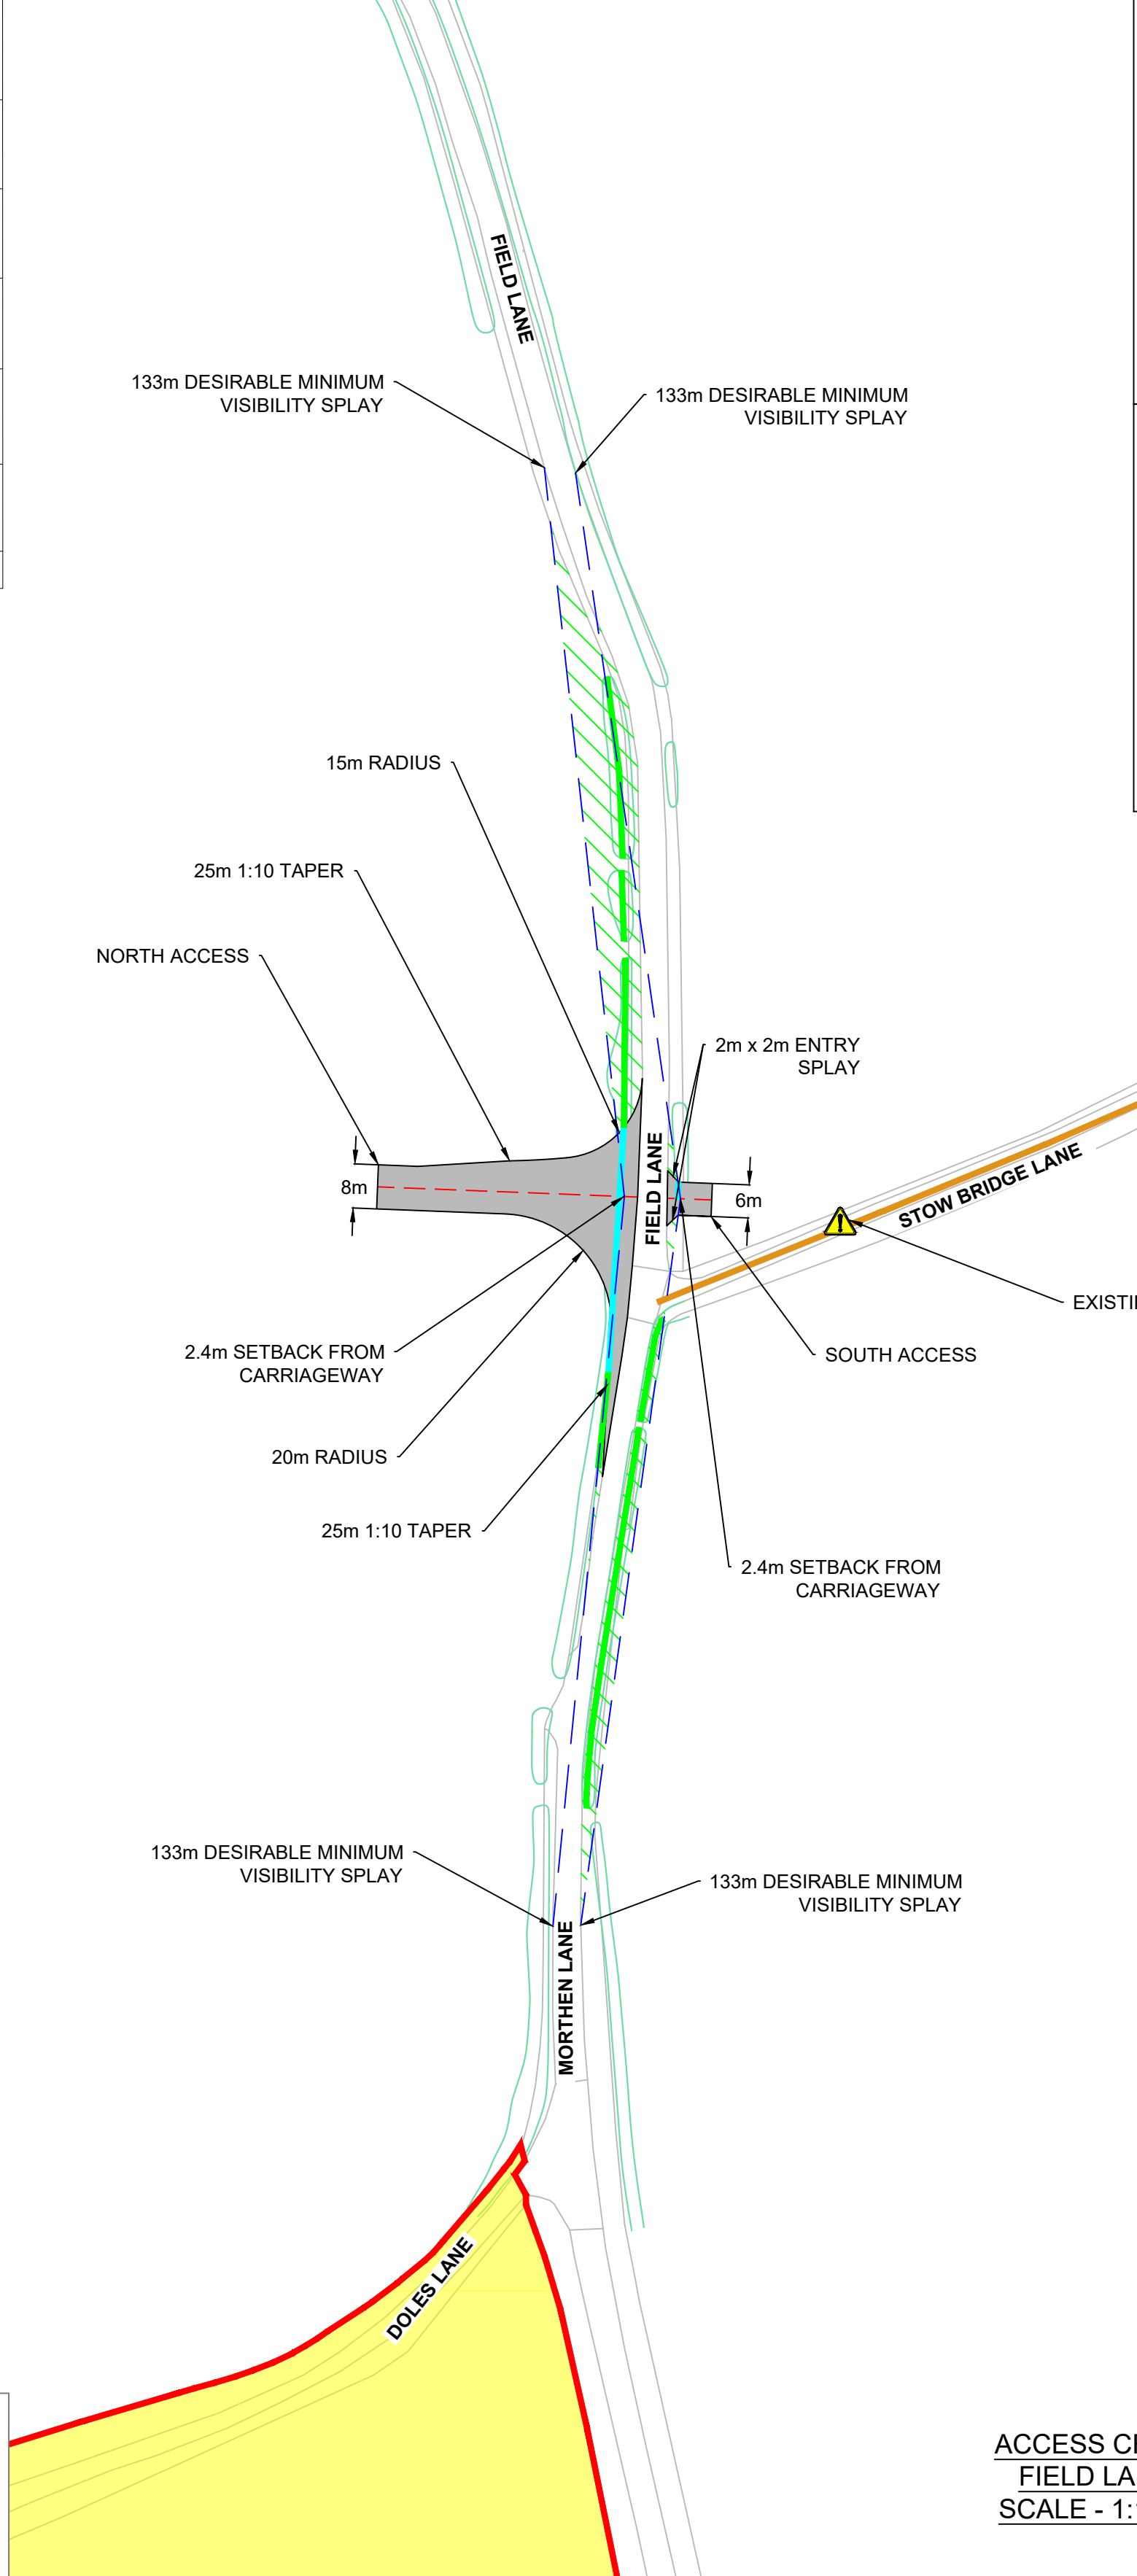


ABNORMAL LOAD ACCESS AND EGRESS MOVEMENTS TO BE CONTROLLED TO ENSURE MANOEUVRES ARE COMPLETED SAFELY. ANY OTHER CONSTRUCTION VEHICLES WISHING TO EGRESS DURING ABNORMAL LOAD DELIVERIES ARE TO BE HELD WITHIN THE SITE TO AVOID VEHICULAR CONFLICTS

ABNORMAL LOAD ACCESS AND EGRESS MOVEMENTS TO BE CONTROLLED TO ENSURE MANOEUVRES ARE COMPLETED SAFELY. ANY OTHER CONSTRUCTION VEHICLES WISHING TO EGRESS DURING ABNORMAL LOAD DELIVERIES ARE TO BE HELD WITHIN THE SITE TO AVOID VEHICULAR CONFLICTS

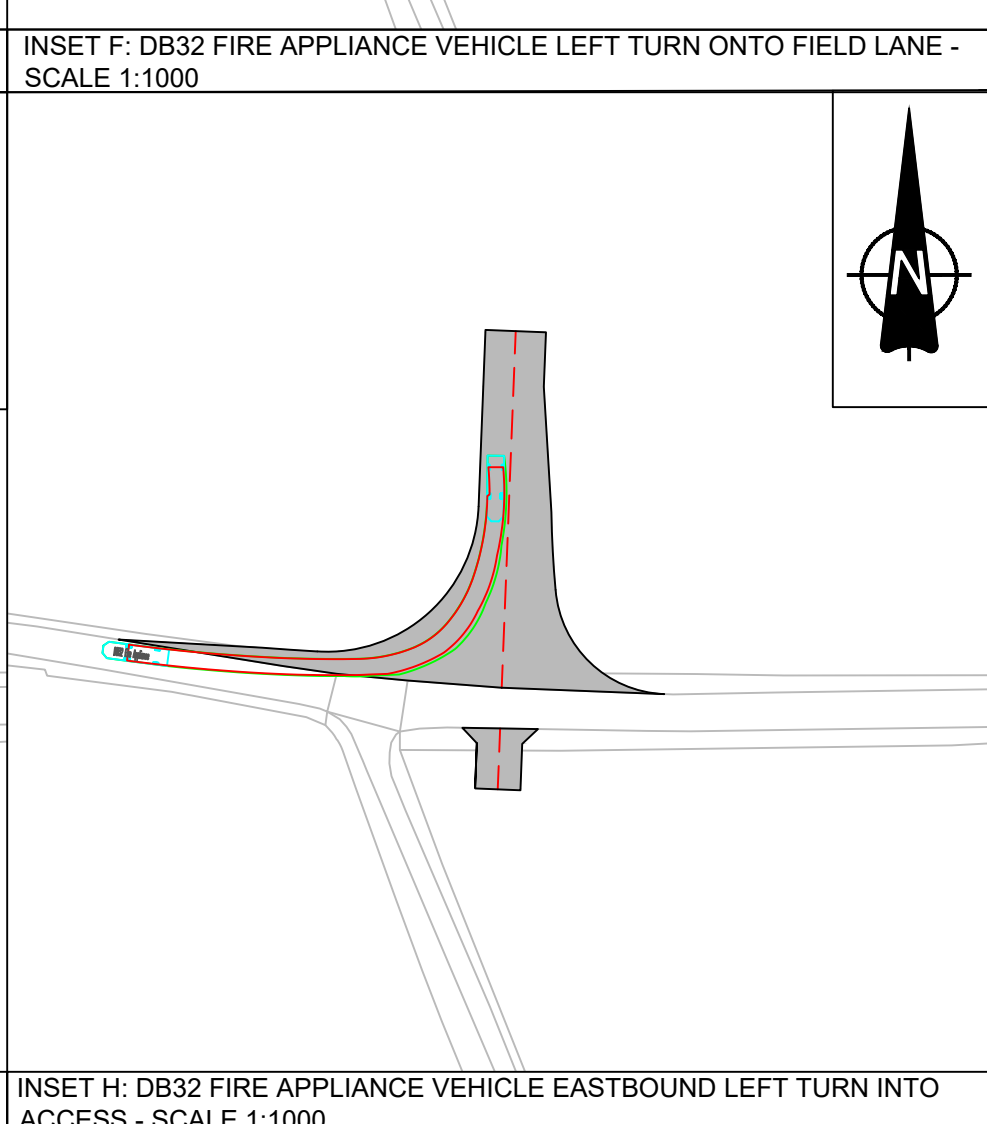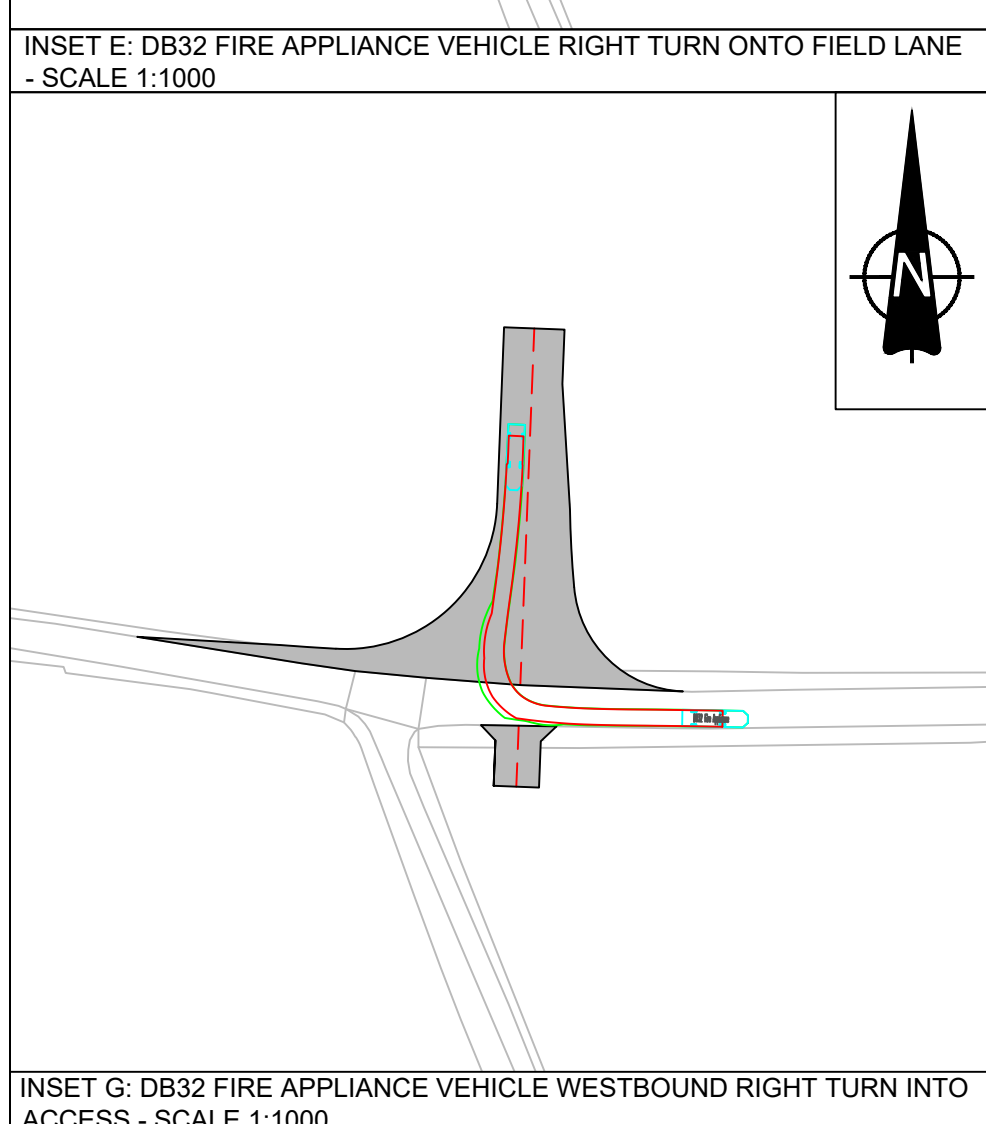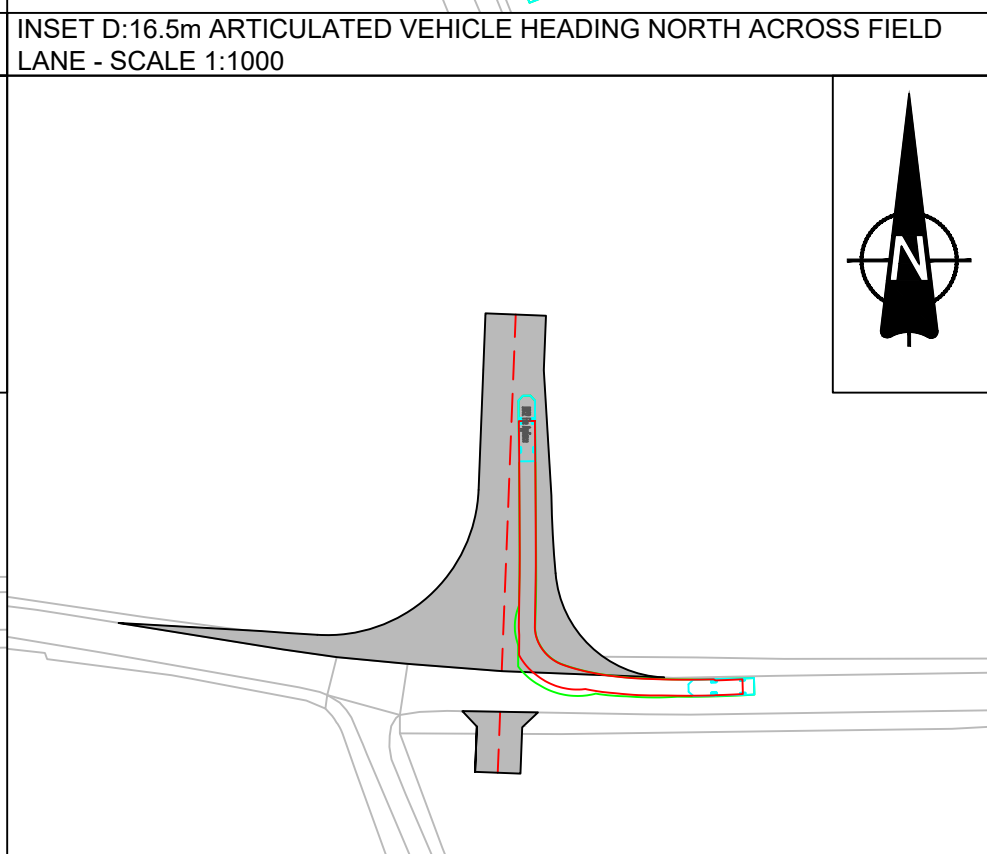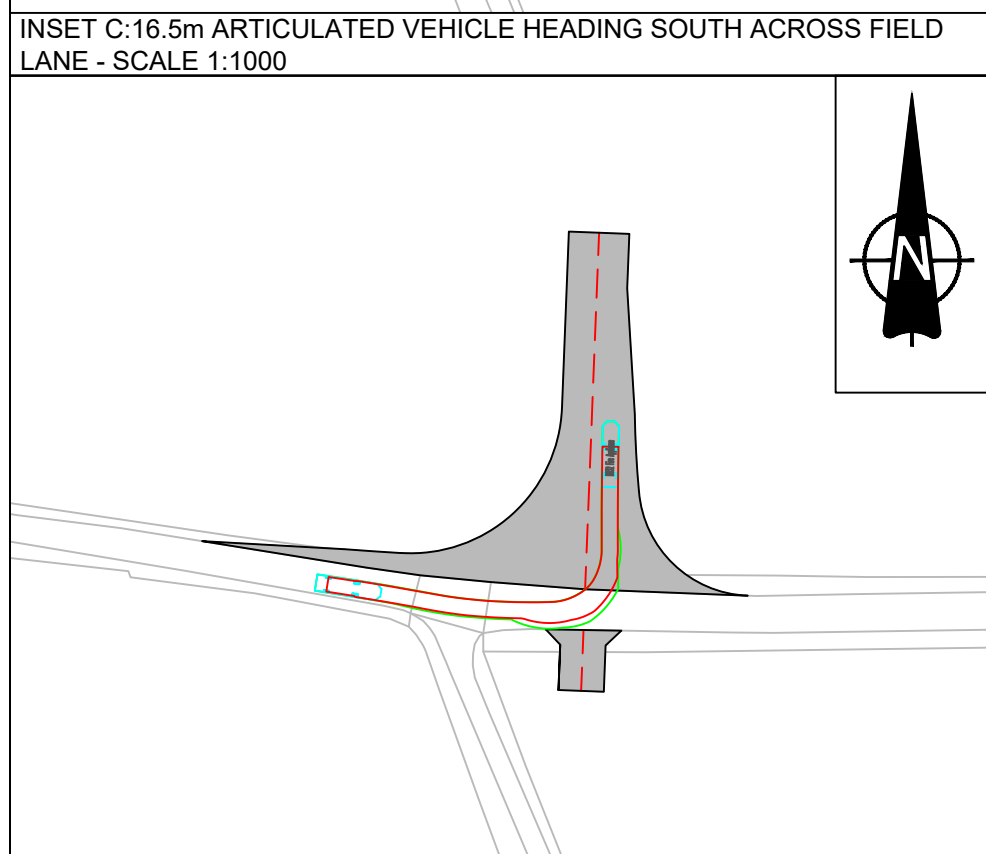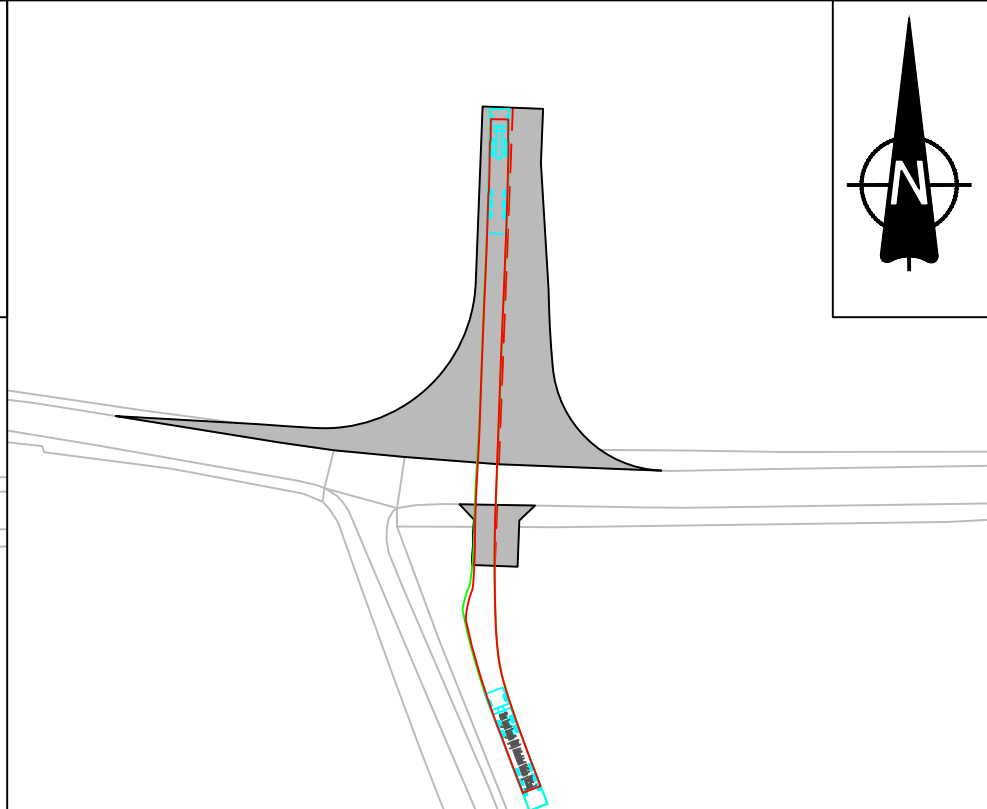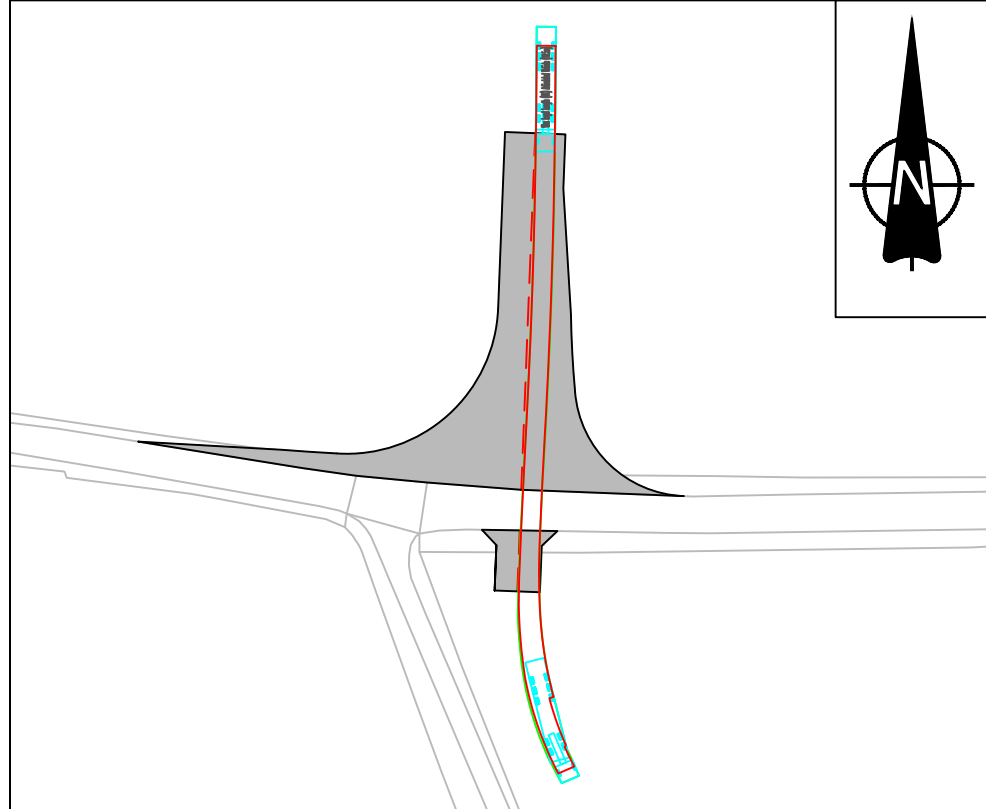

- NOTES**
- This drawing is to be read in conjunction with all other relevant documentation.
 - Do not scale from this drawing, use only printed dimensions.
 - All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
 - This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
 - Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
 - The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
 - Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
 - Junction visibility for the access is based upon visibility parameters derived using the 85th percentile speed survey conducted between the 4th June 2025 to the 10th June 2025.

- LEGEND**
- Extent of Access Footprint
 - Order Limits
 - Land Excluded from Order Limits
 - Vehicle Body
 - Vehicle Body Path
 - Vehicle Load
 - Vehicle Load Path
 - Vehicle Wheels Path
 - Edge of Road
 - Access Centreline
 - Junction Visibility
 - Vegetation to be Removed for Vis Splay
 - Indicative Hedgerow Removal Vis Splay
 - Indicative Hedgerow Removal for Bellmouth Access
 - Health and Safety Risk Identifier
 - Existing Public Right of Way

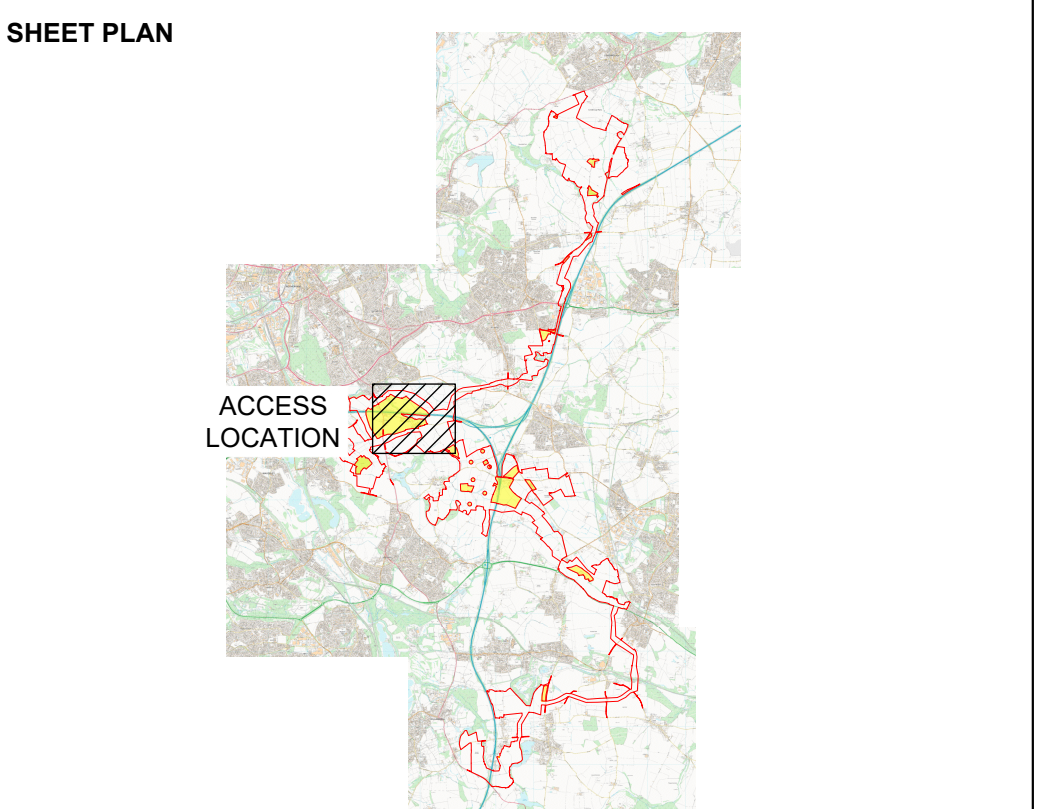

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:
PV Area Access CFL-01
Appendix 3 - Sheet 9 of 53
Whitestone Solar Farm
Regulation 5(2)(o)

DRAWING DATE: 03/06/2026



SCALE: 1:1000
SIZE: A1
SHEET: Sheet 9 of 53
REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020



EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012 RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

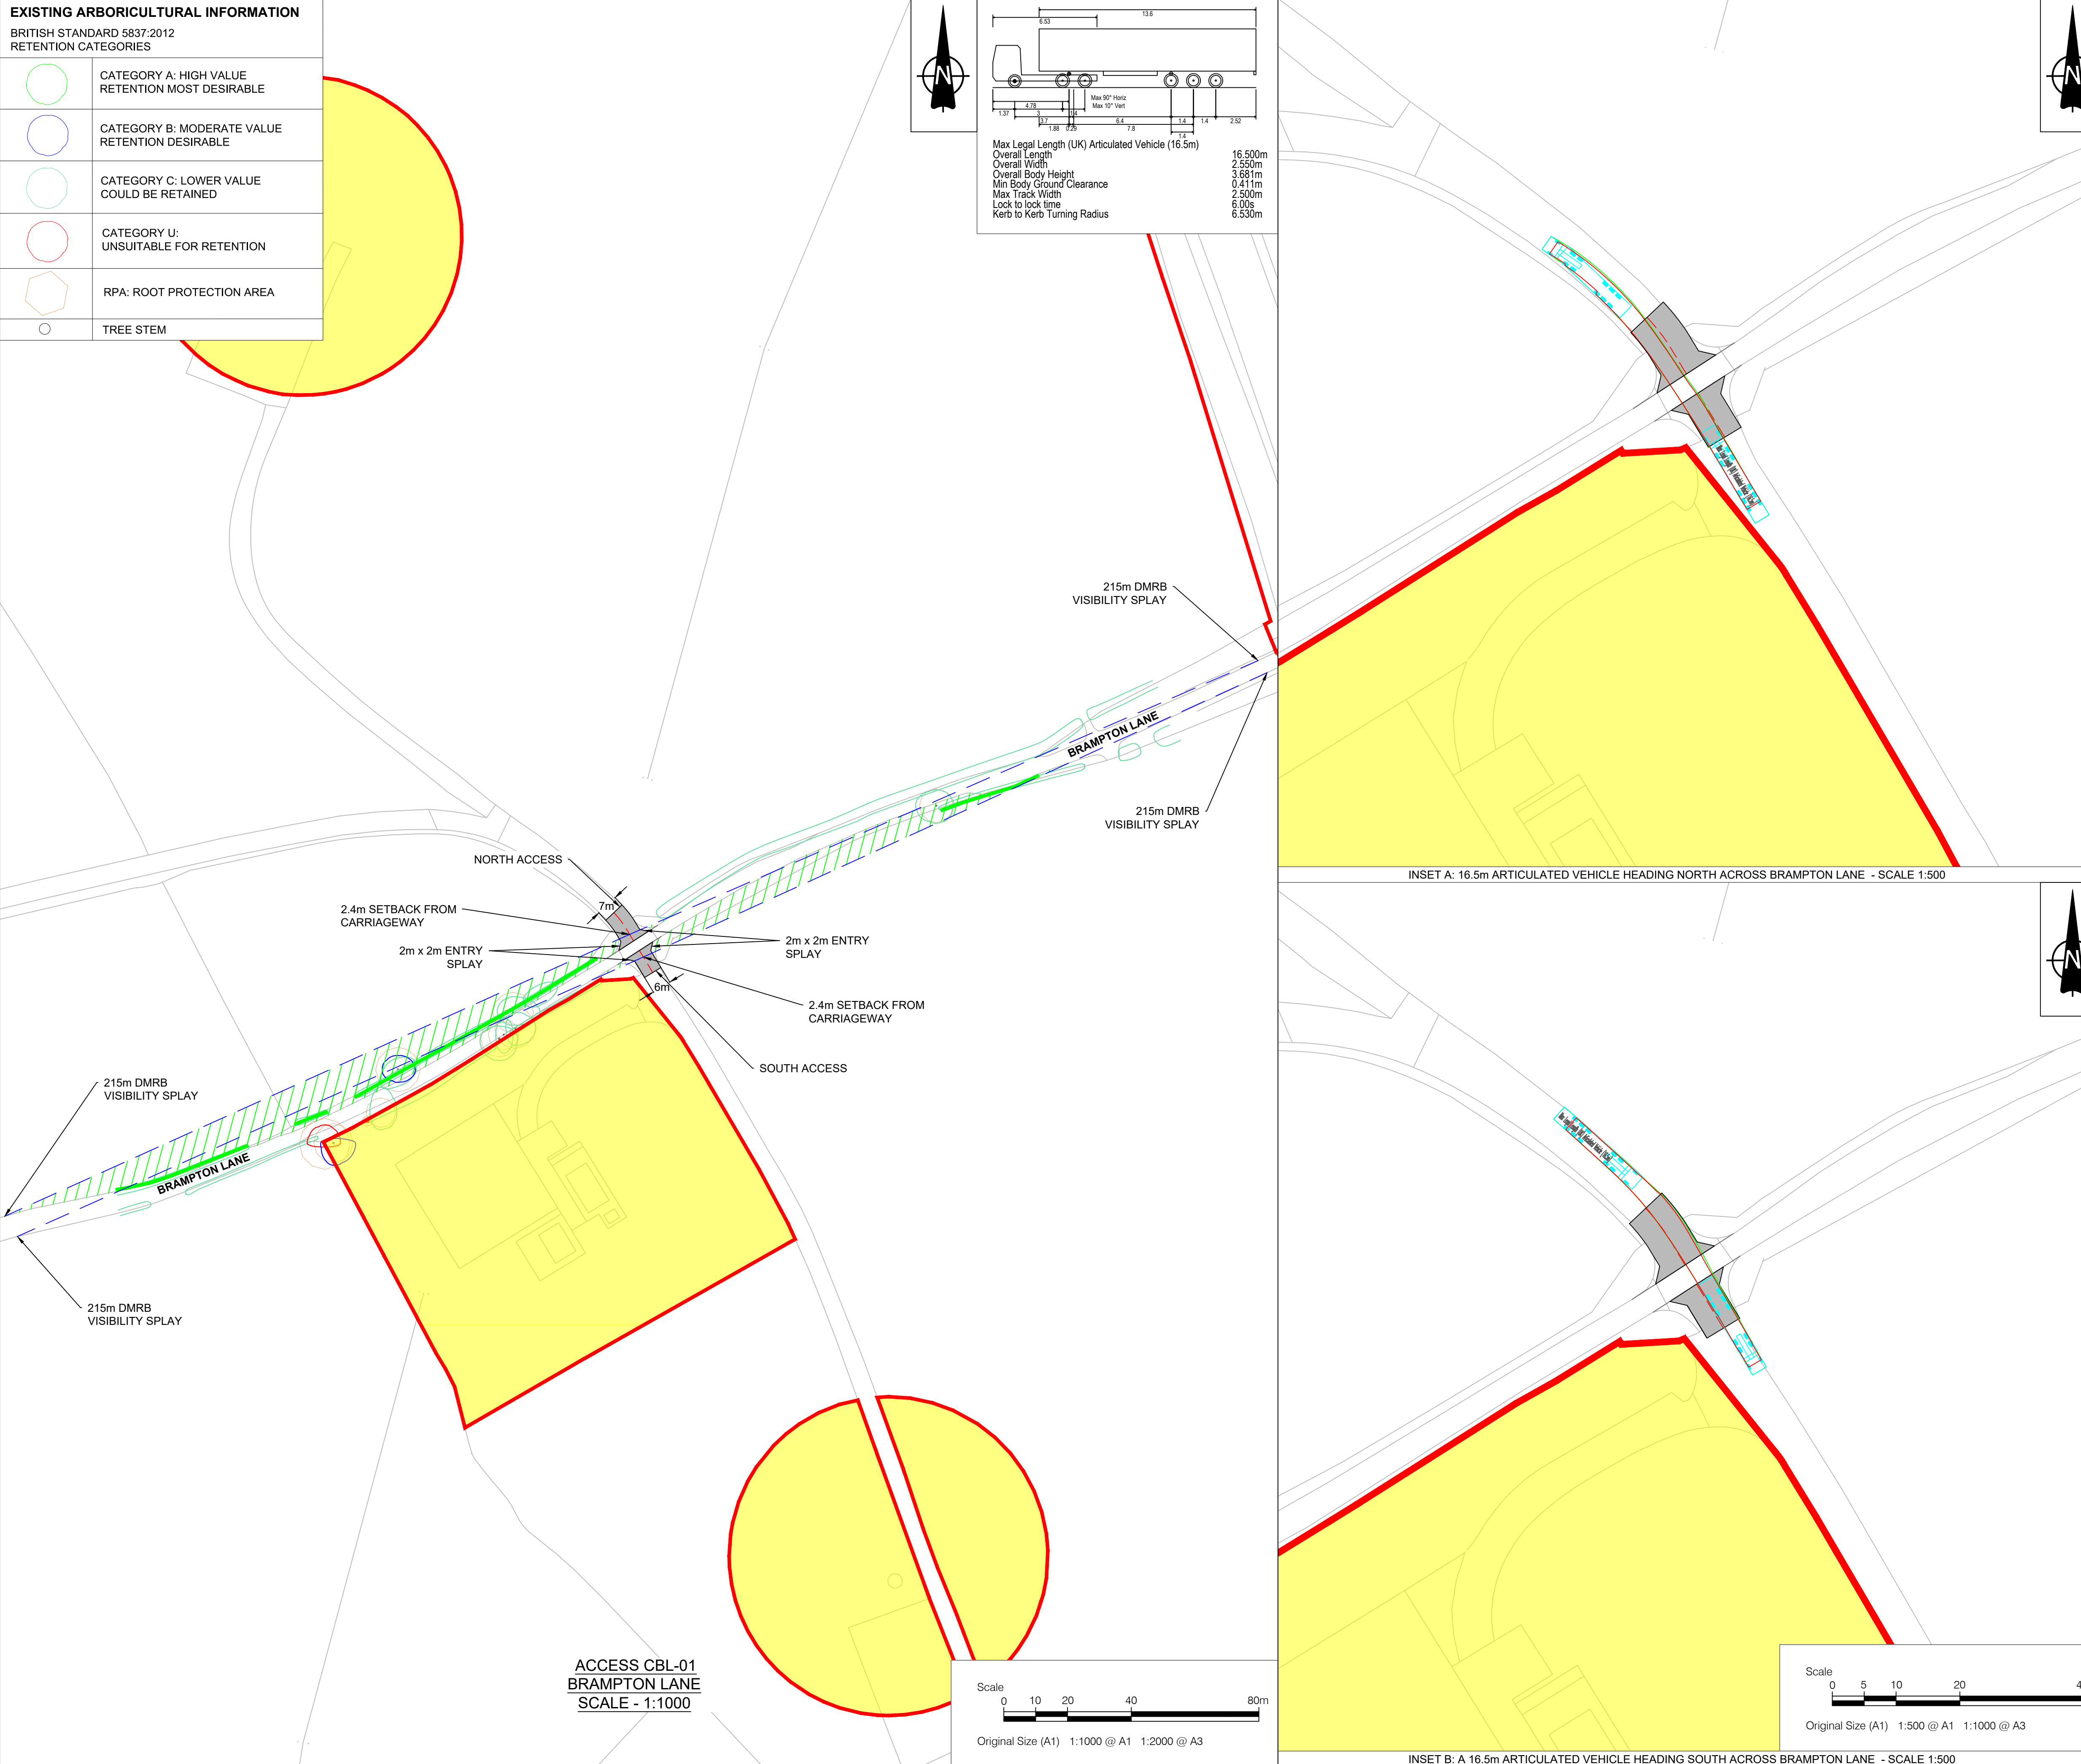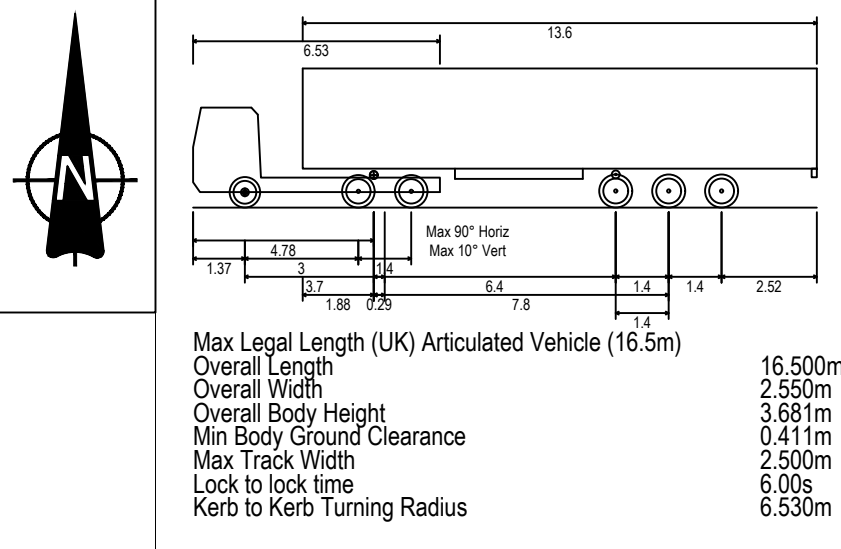


- ## NOTES
1. This drawing is to be read in conjunction with all other relevant documentation.
 2. Do not scale from this drawing, use only printed dimensions.
 3. All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
 4. This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
 5. Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
 6. The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
 7. Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
 8. Junction visibility for the access is based upon DMRB CD109 Table 2.10.

LEGEND

-  Extent of Access Footprint
-  Order Limits
-  Land Excluded from Order Limits
-  Vehicle Body
-  Vehicle Body Path
-  Vehicle Load
-  Vehicle Load Path
-  Vehicle Wheels Path
-  Edge of Road
-  Access Centreline
-  Junction Visibility
-  Vegetation to be Removed for Vis Splay
-  Indicative Hedgerow Removal Vis Splay
-  Indicative Hedgerow Removal for Bellmouth Access
-  Health and Safety Risk Identifier
-  Existing Public Right of Way

SHEET PLAN

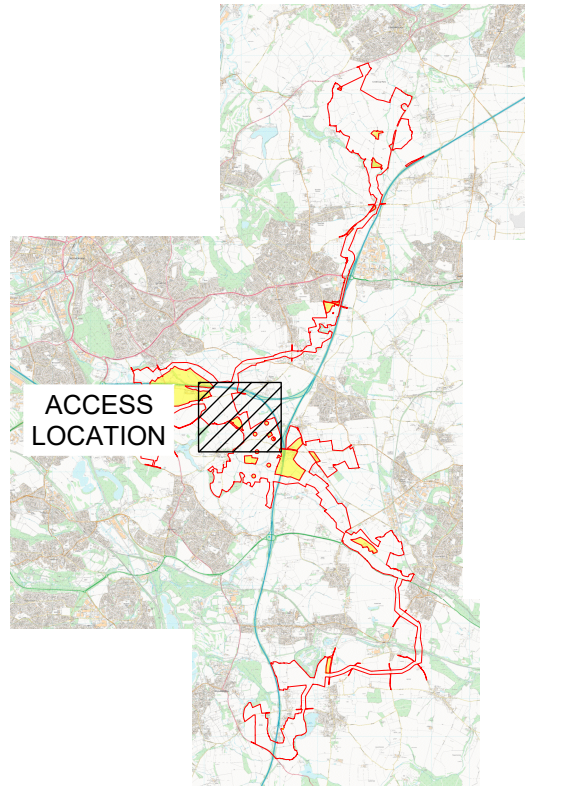

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:
PV Area Access CBL-01
Appendix 3 - Sheet 10 of 53
Whitestone Solar Farm
Regulation 5(2)(o)

DRAWING DATE: 03/06/2026

SCALE: AS SHOWN




SIZE: A1

DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020



EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012	
RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

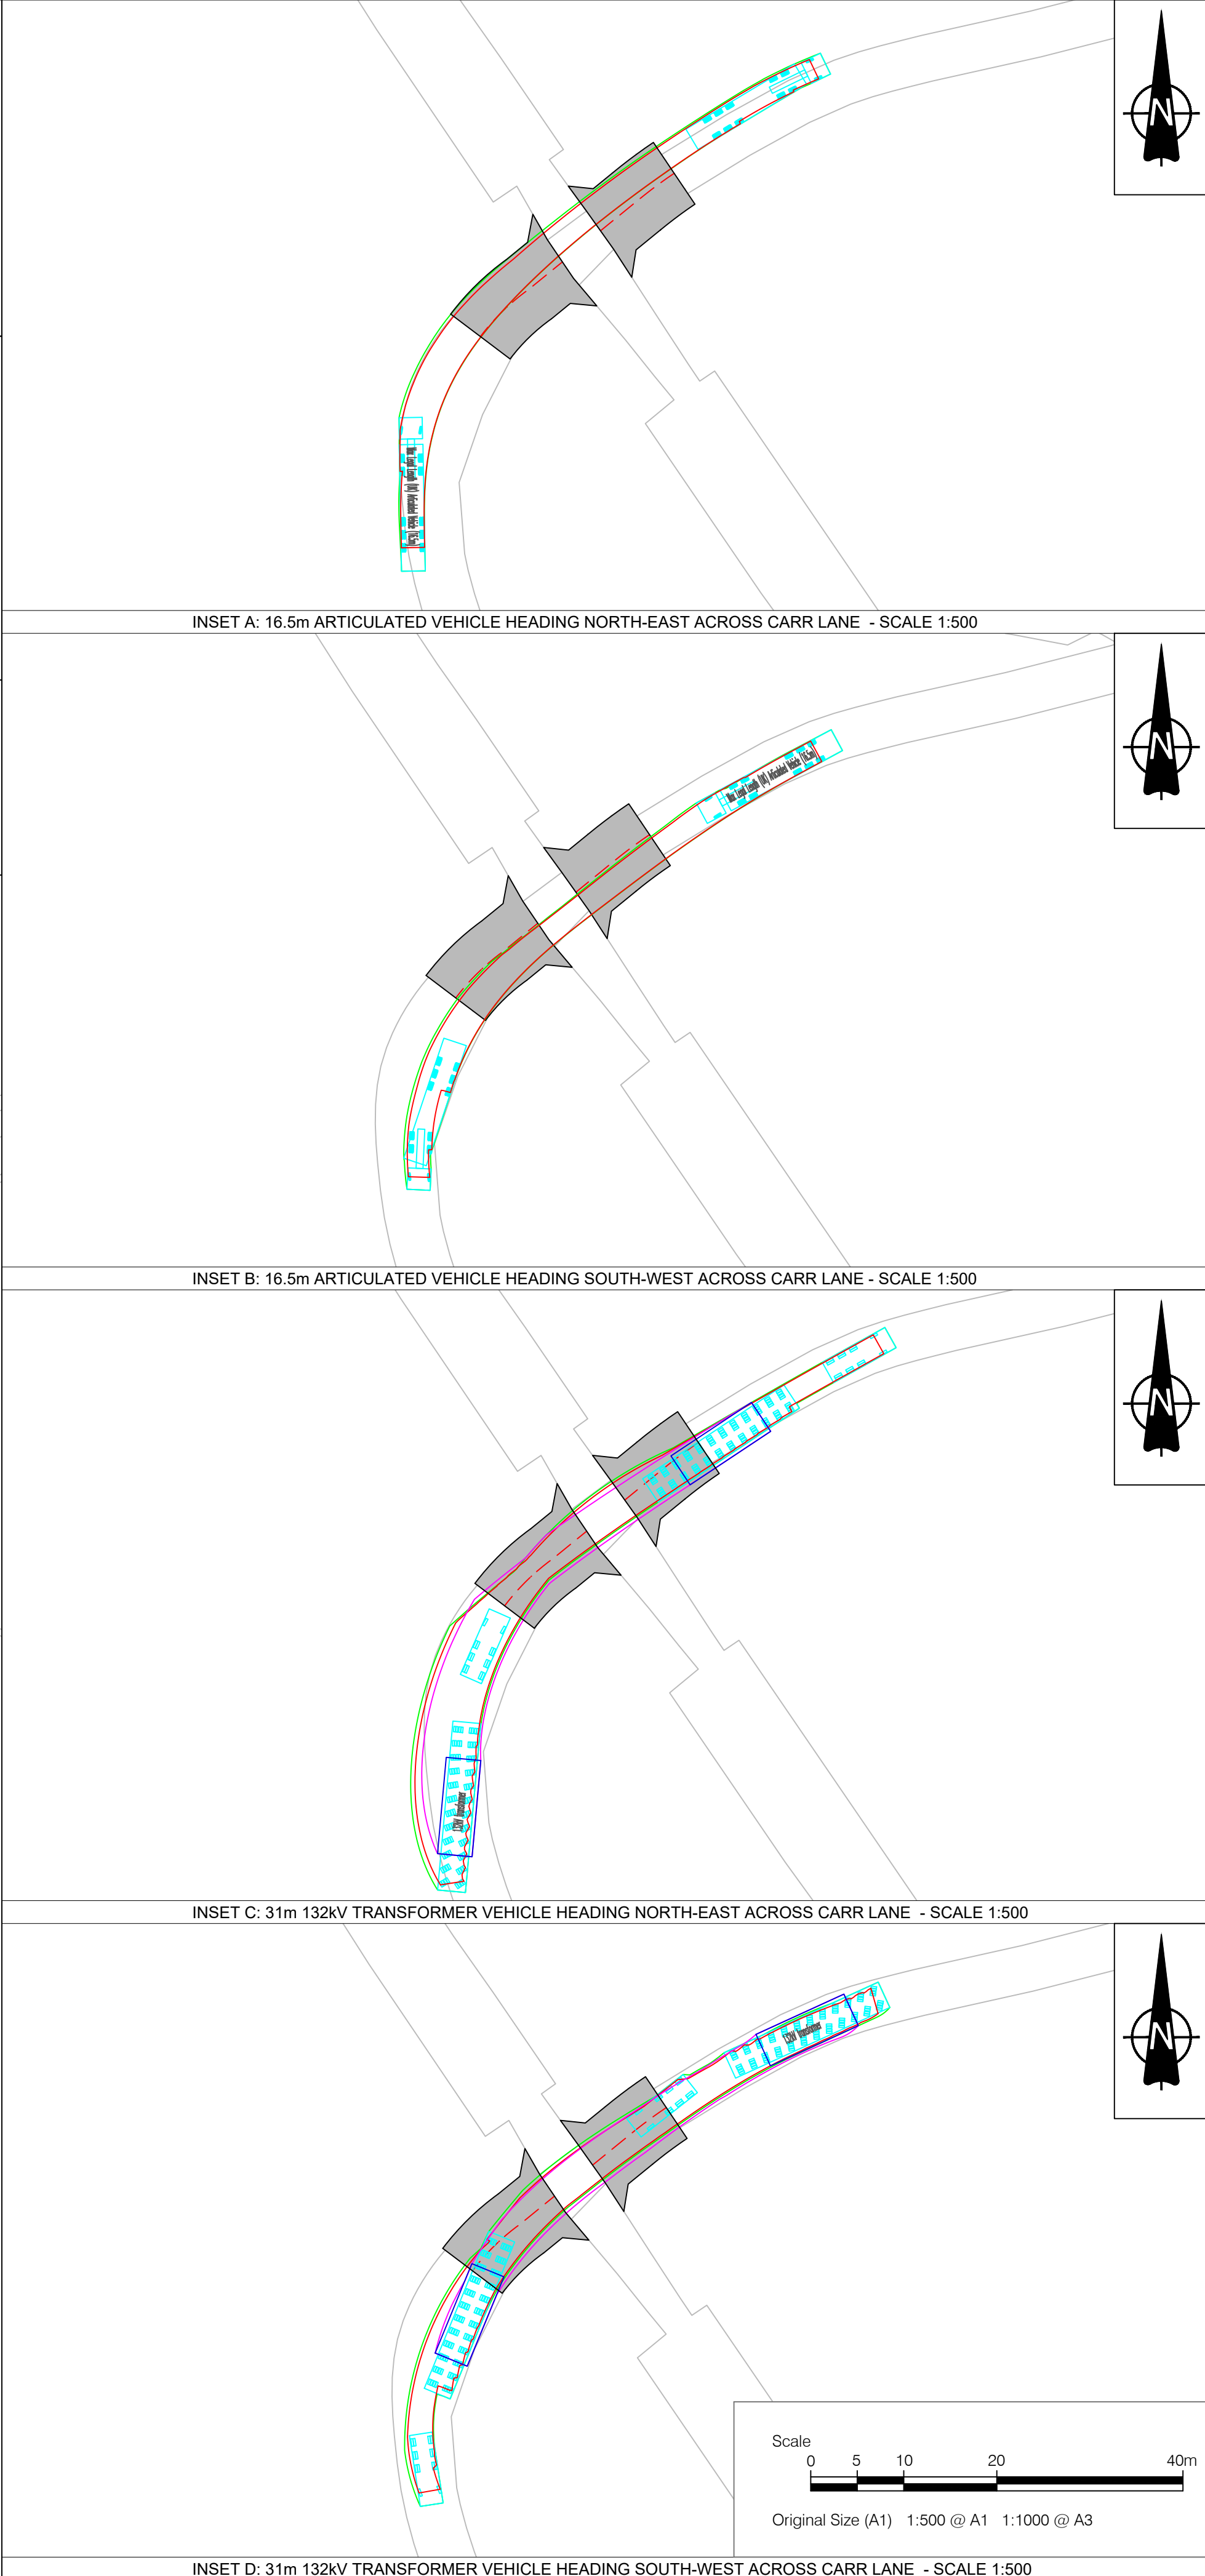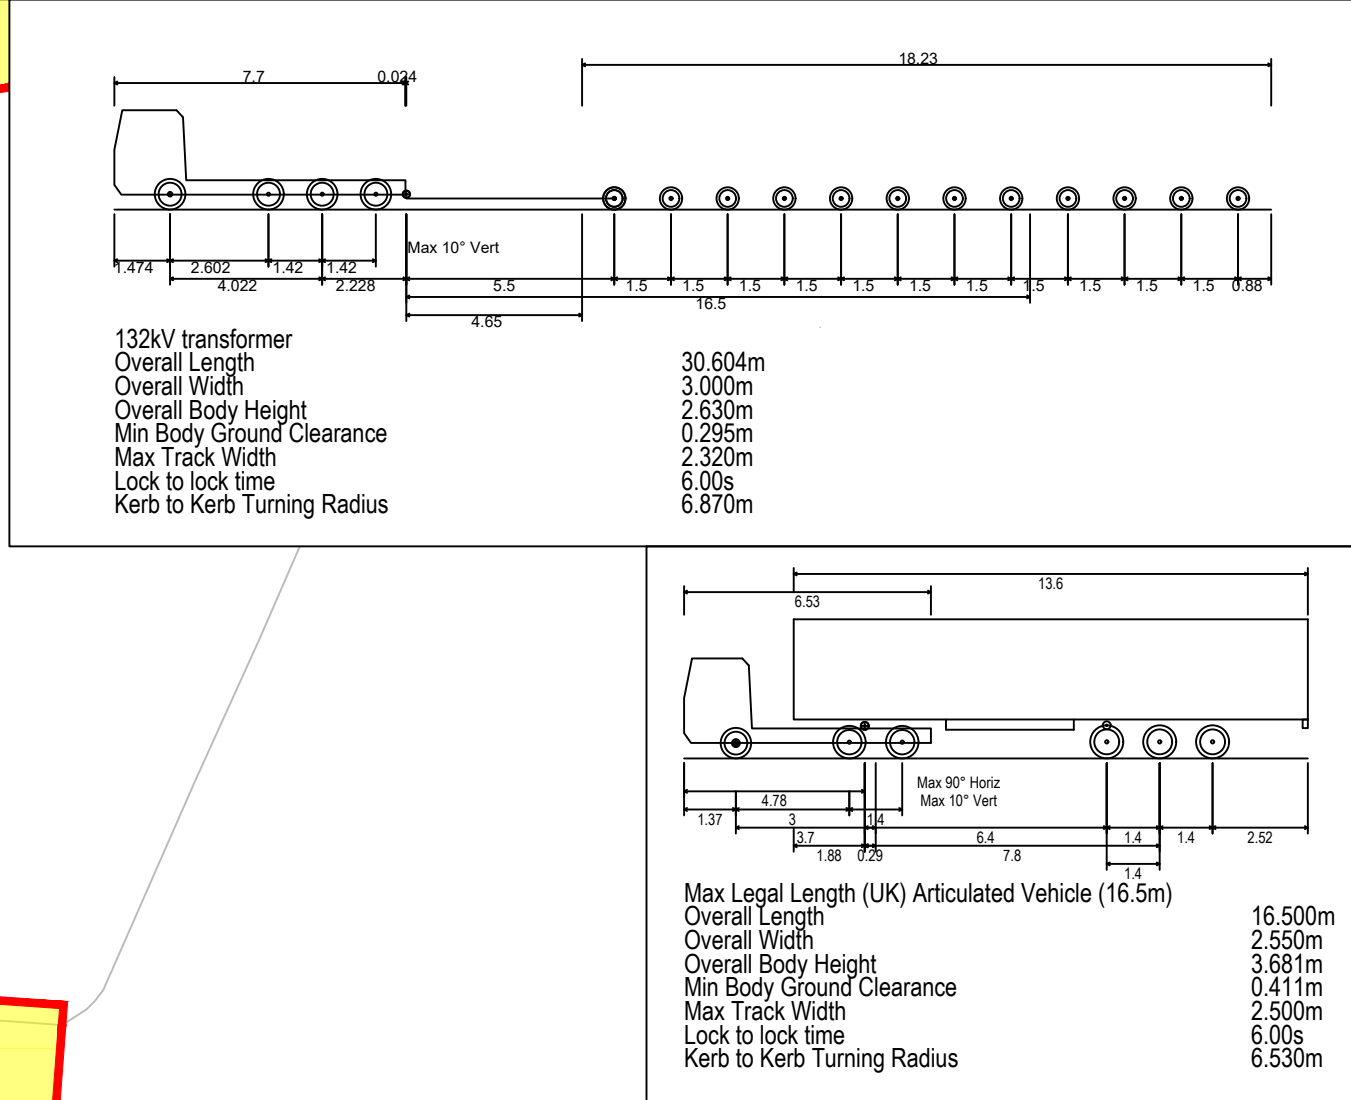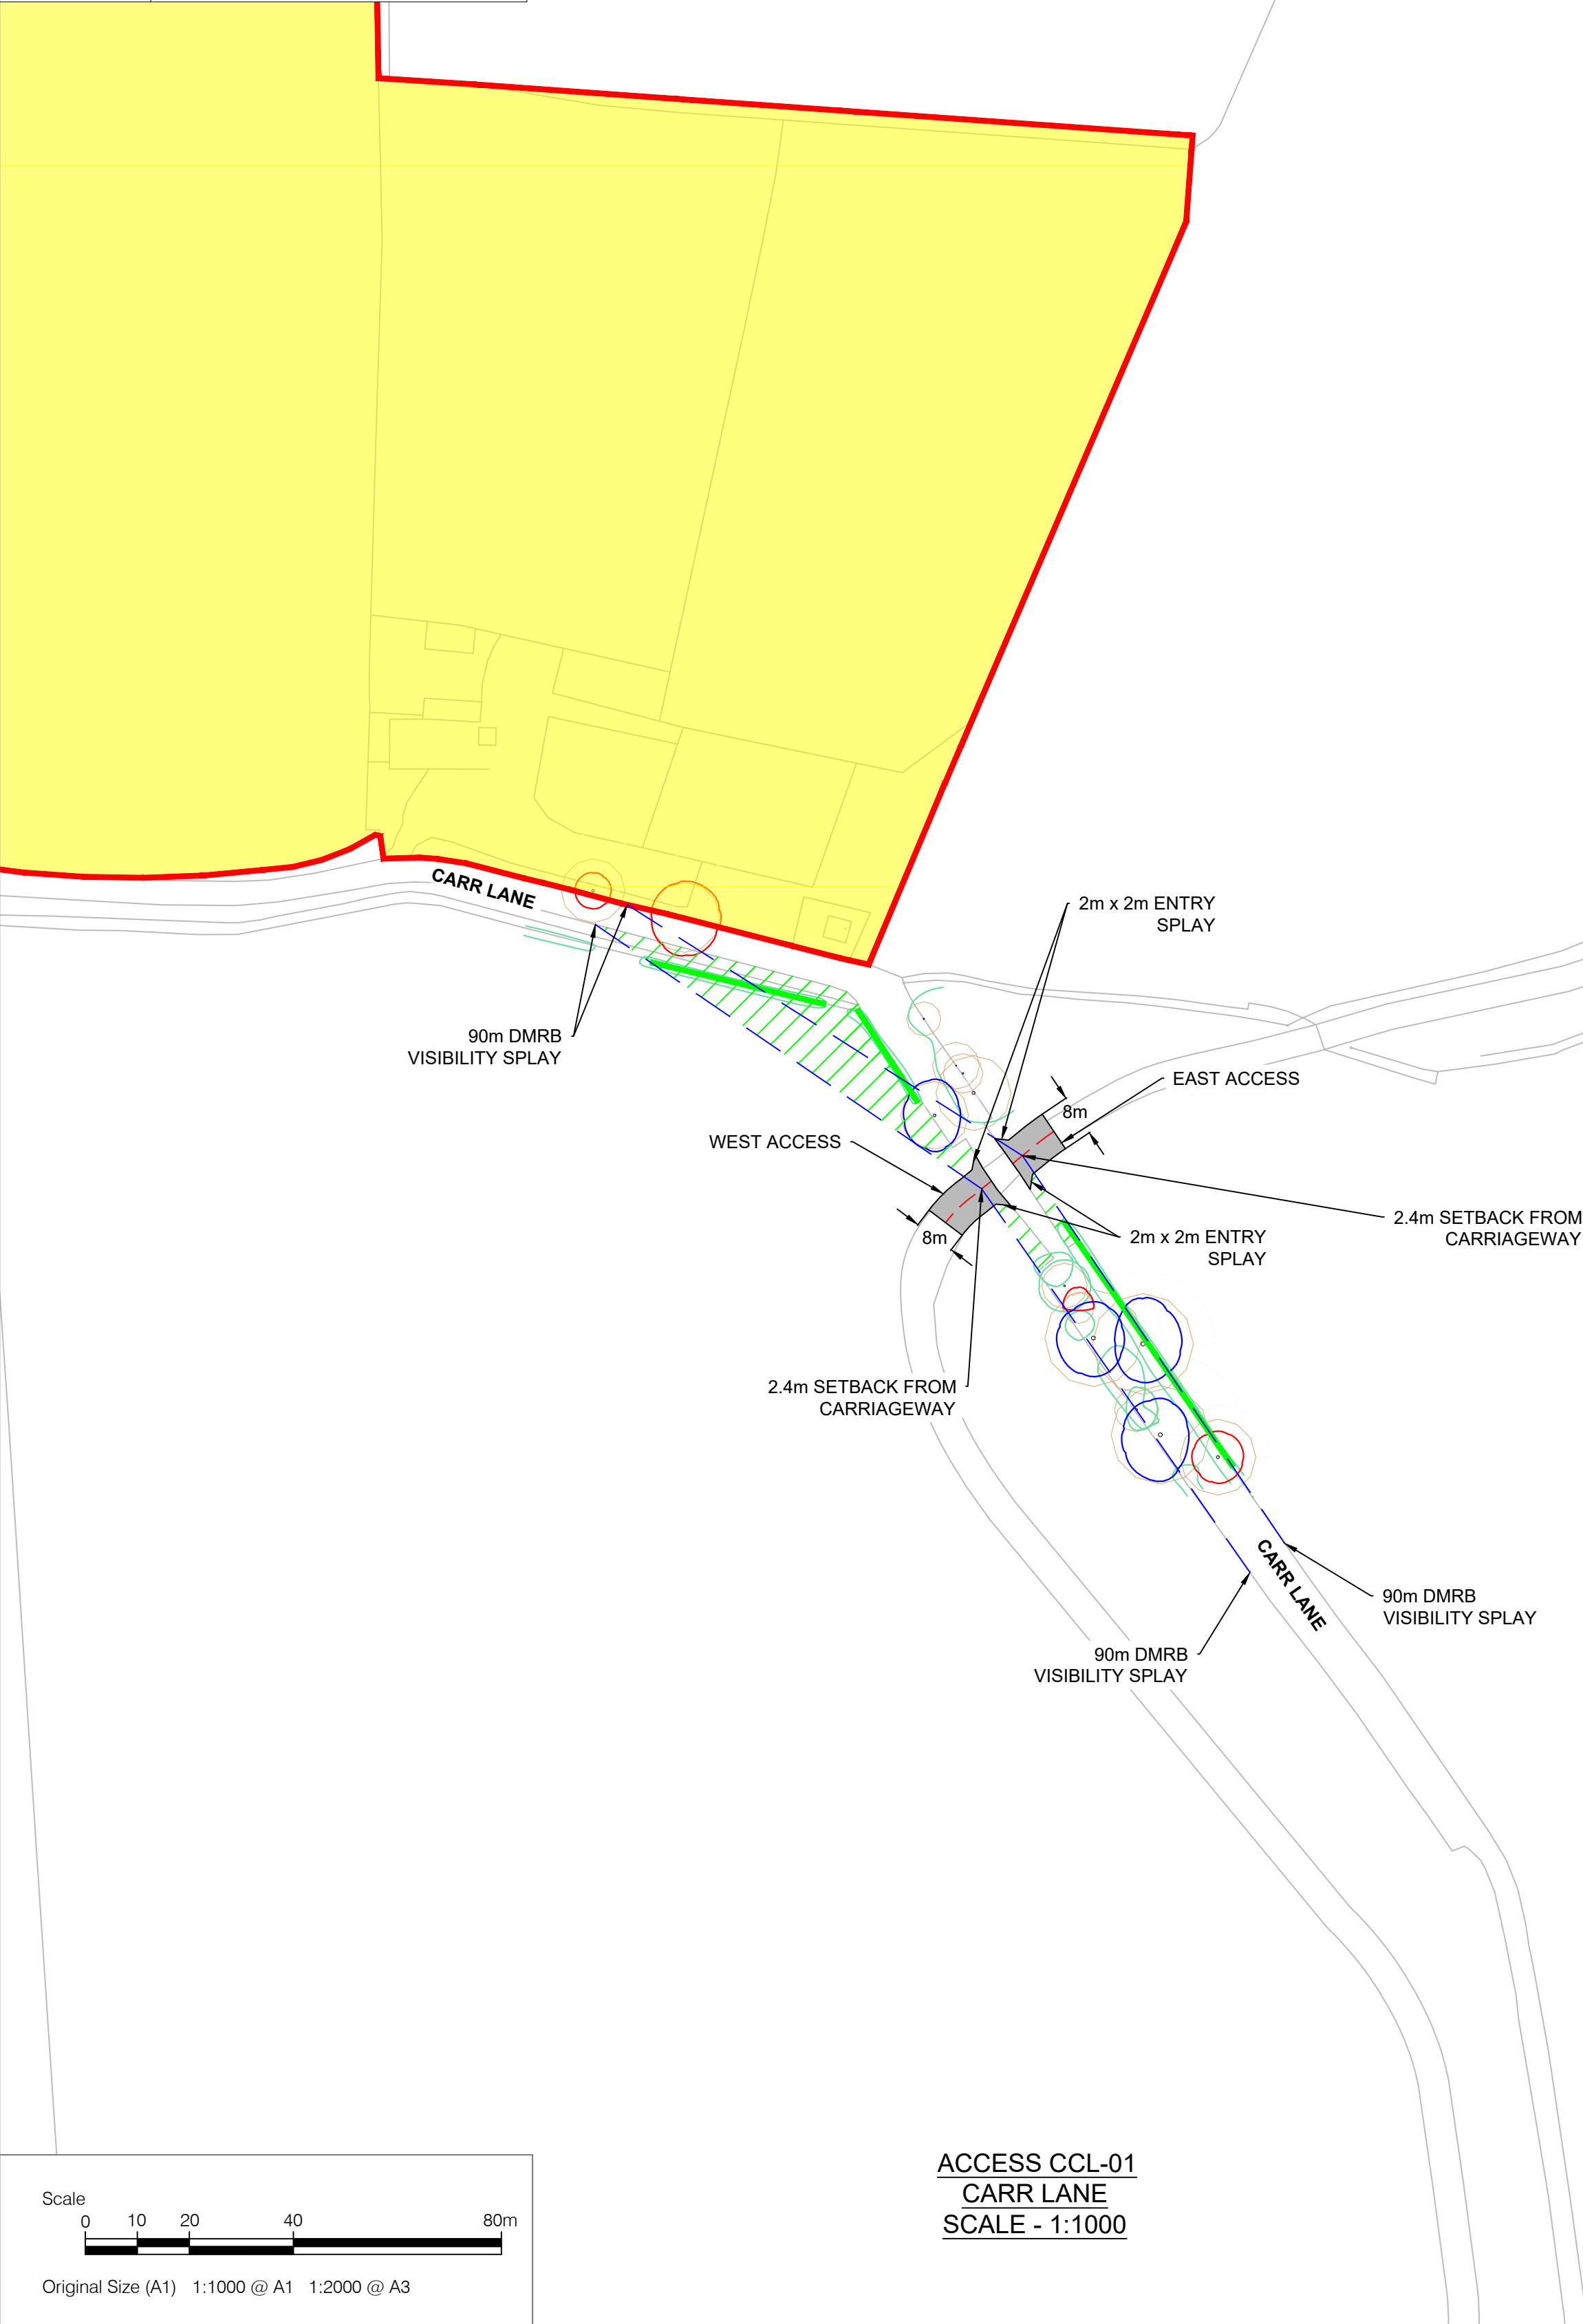

- ### NOTES
- This drawing is to be read in conjunction with all other relevant documentation.
 - Do not scale from this drawing, use only printed dimensions.
 - All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
 - This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
 - Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
 - The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
 - Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
 - Junction visibility for the access is based upon DMRB CD109 Table 2.10.

- ### LEGEND
- Extent of Access Footprint
 - Order Limits
 - Land Excluded from Order Limits
 - Vehicle Body
 - Vehicle Body Path
 - Vehicle Load
 - Vehicle Load Path
 - Vehicle Wheels Path
 - Edge of Road
 - Access Centreline
 - Junction Visibility
 - Vegetation to be Removed for Vis Splay
 - Indicative Hedgerow Removal Vis Splay
 - Indicative Hedgerow Removal for Bellmouth Access
 - Health and Safety Risk Identifier
 - Existing Public Right of Way

SHEET PLAN

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:
PV Area Access CCL-01
Appendix 3 - Sheet 11 of 53
Whitestone Solar Farm
Regulation 5(2)(o)





DRAWING DATE: 03/06/2026

SCALE: AS SHOWN	SHEET: Sheet 11 of 53
SIZE: A1	REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020

EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012 RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

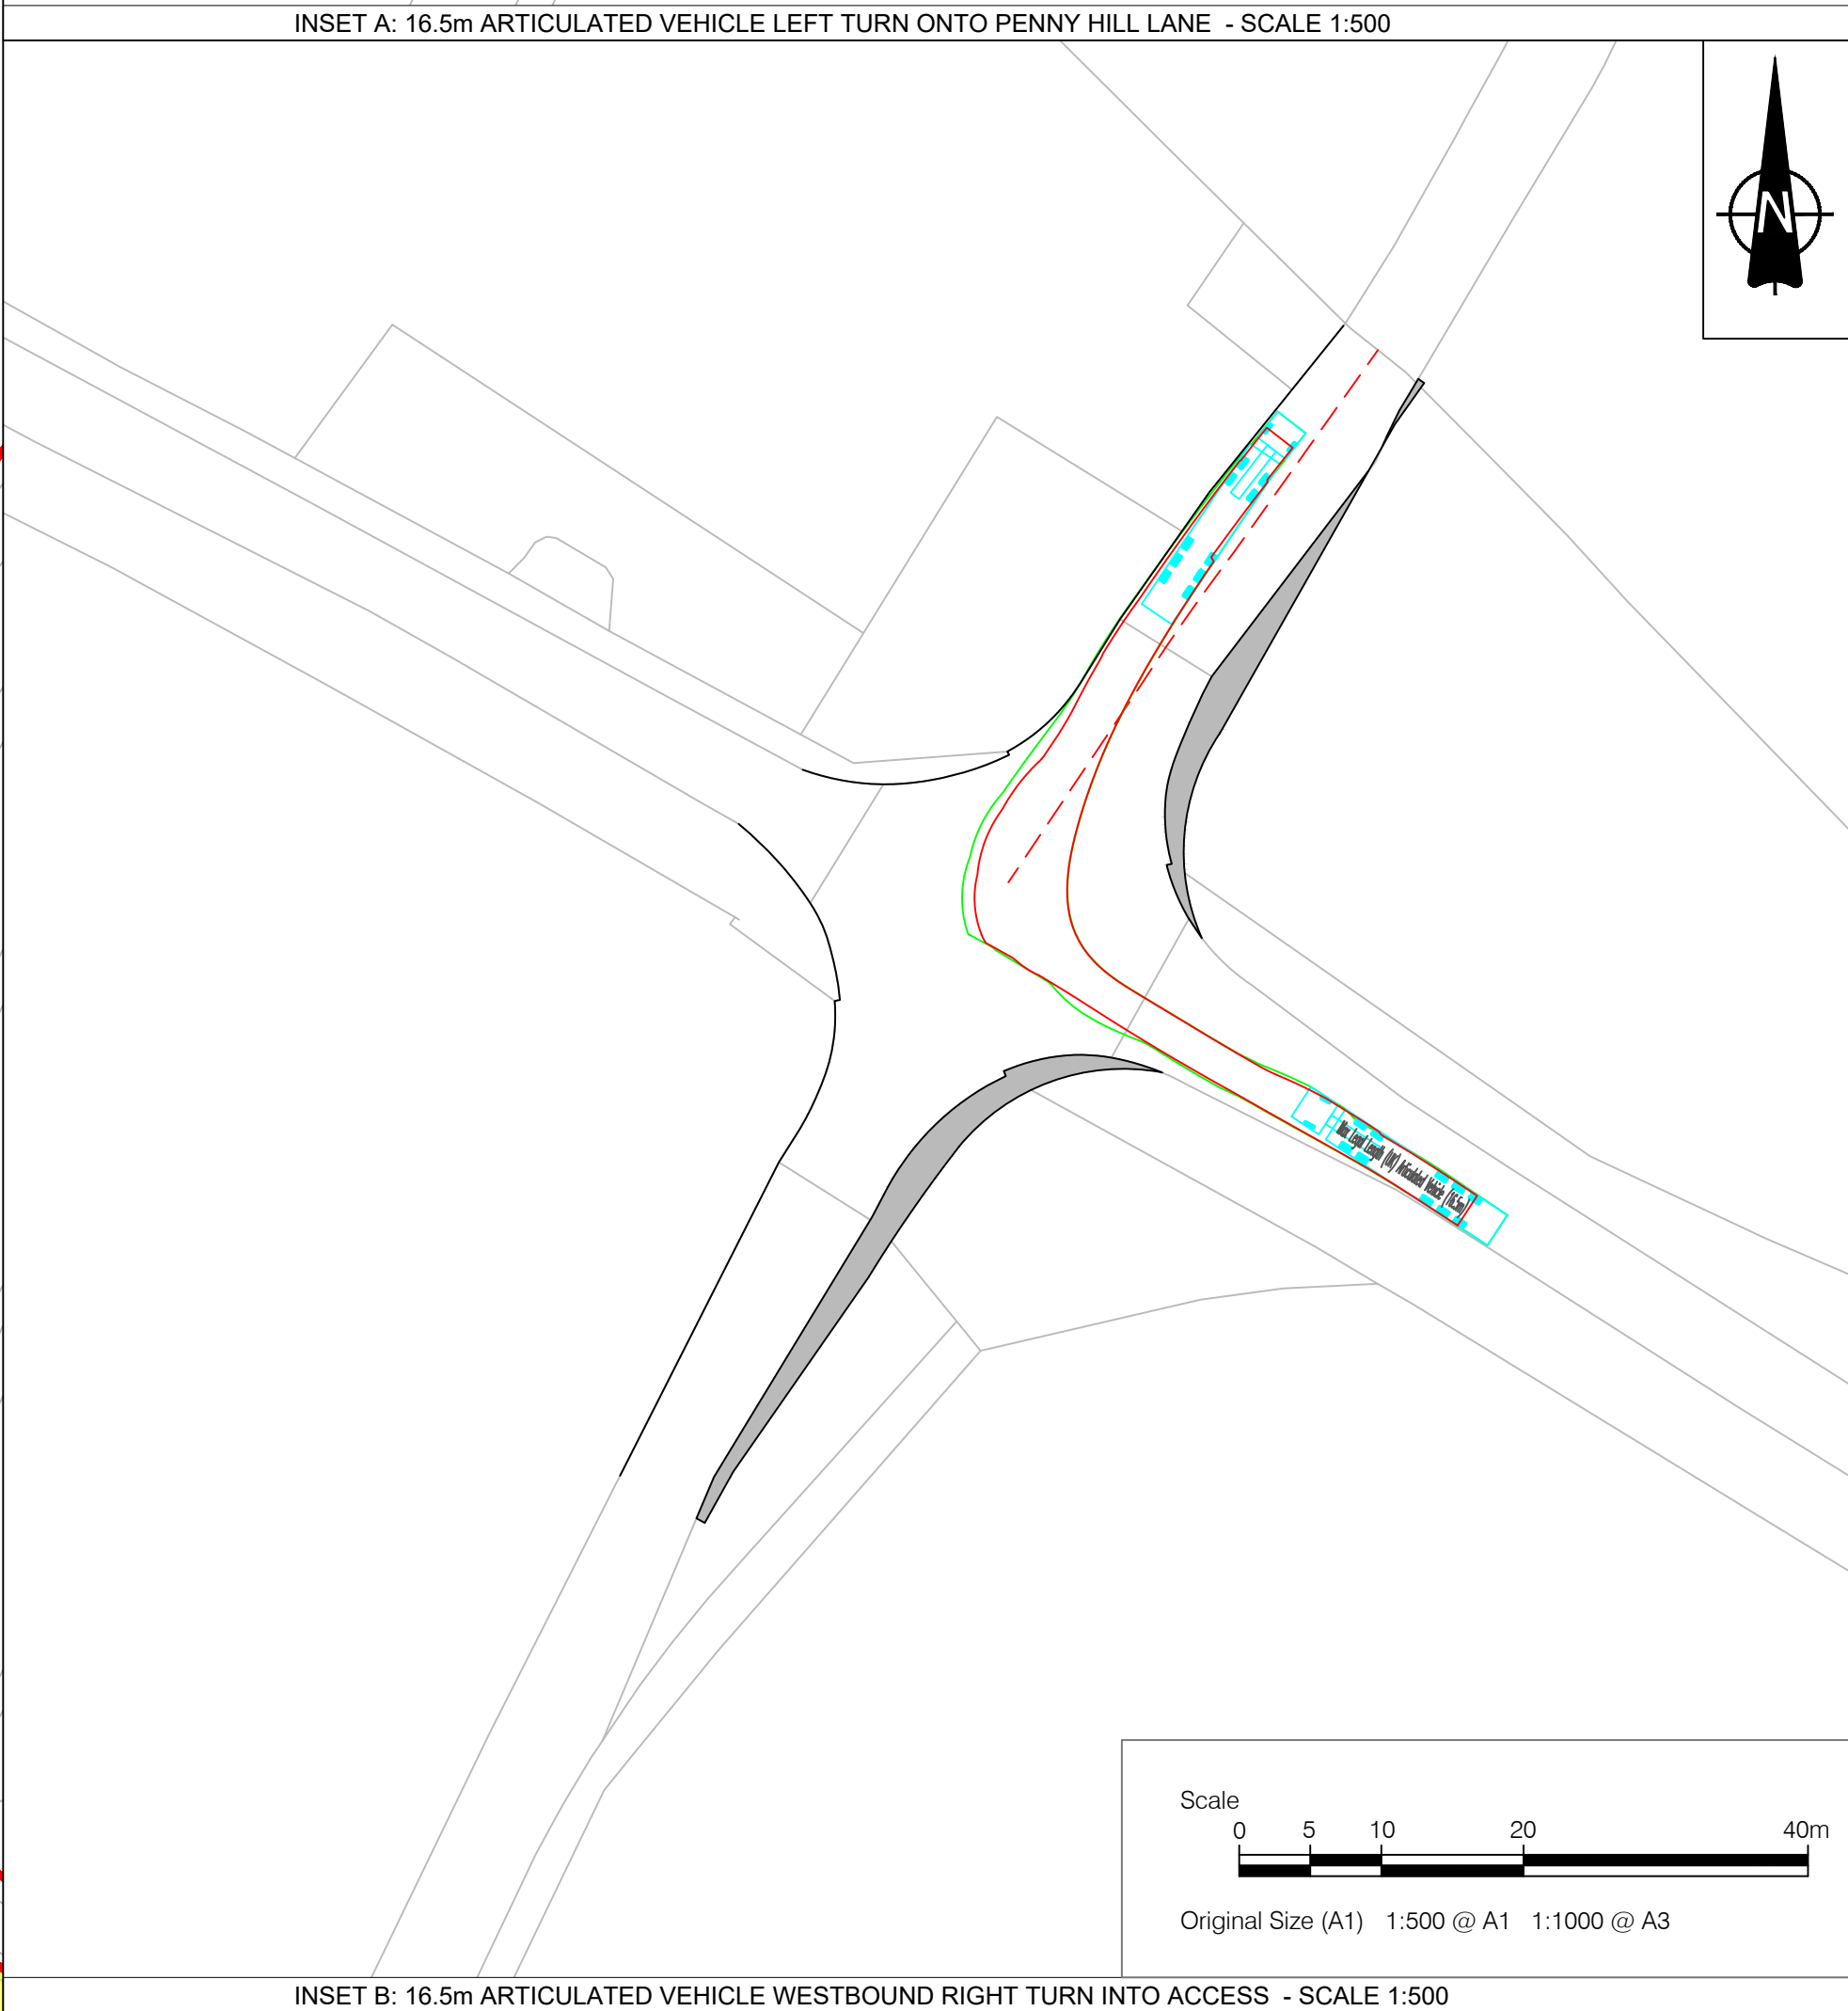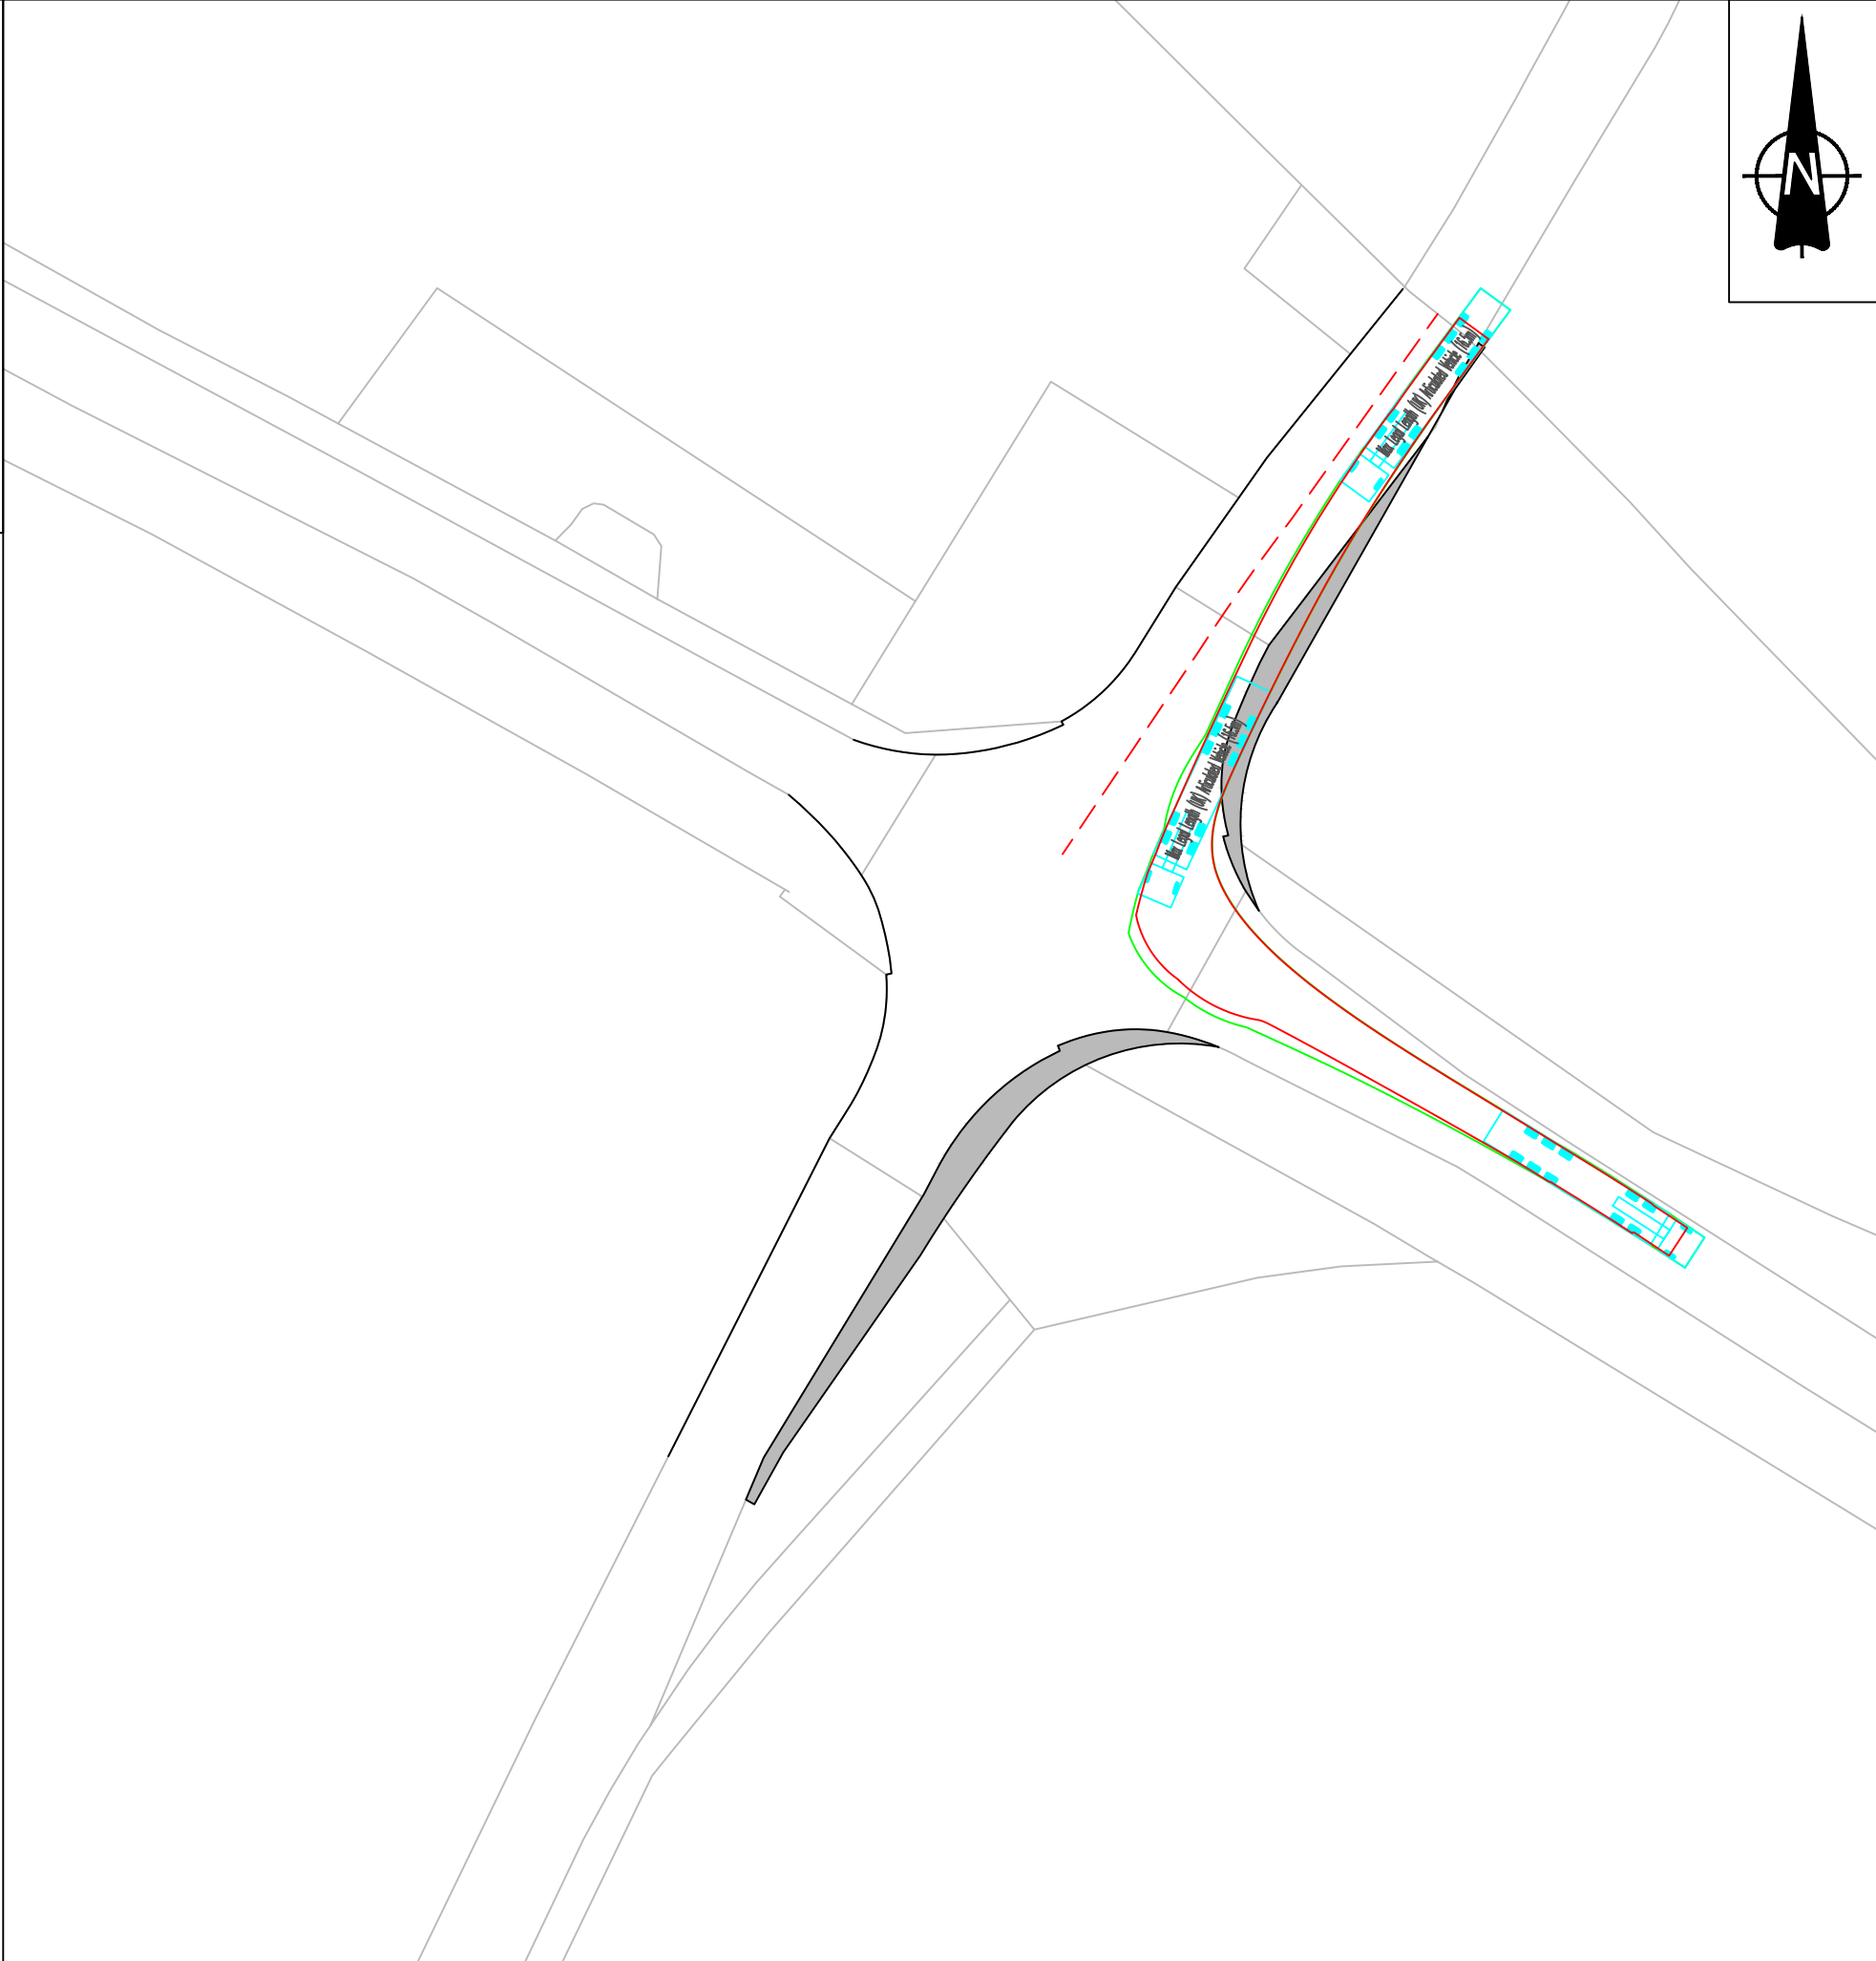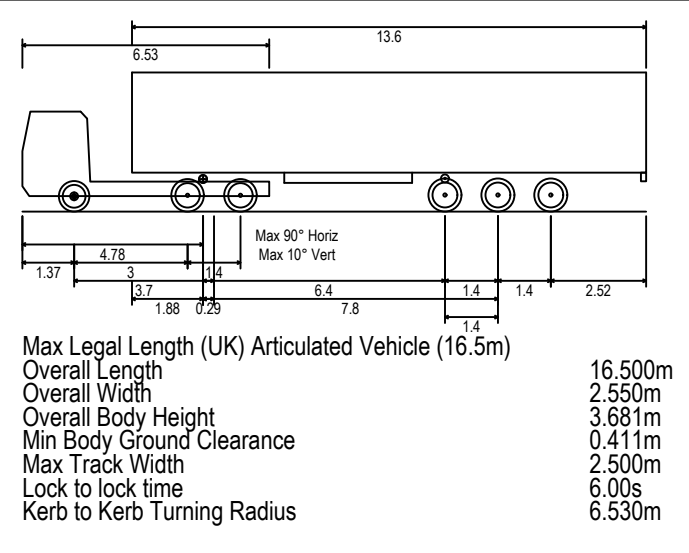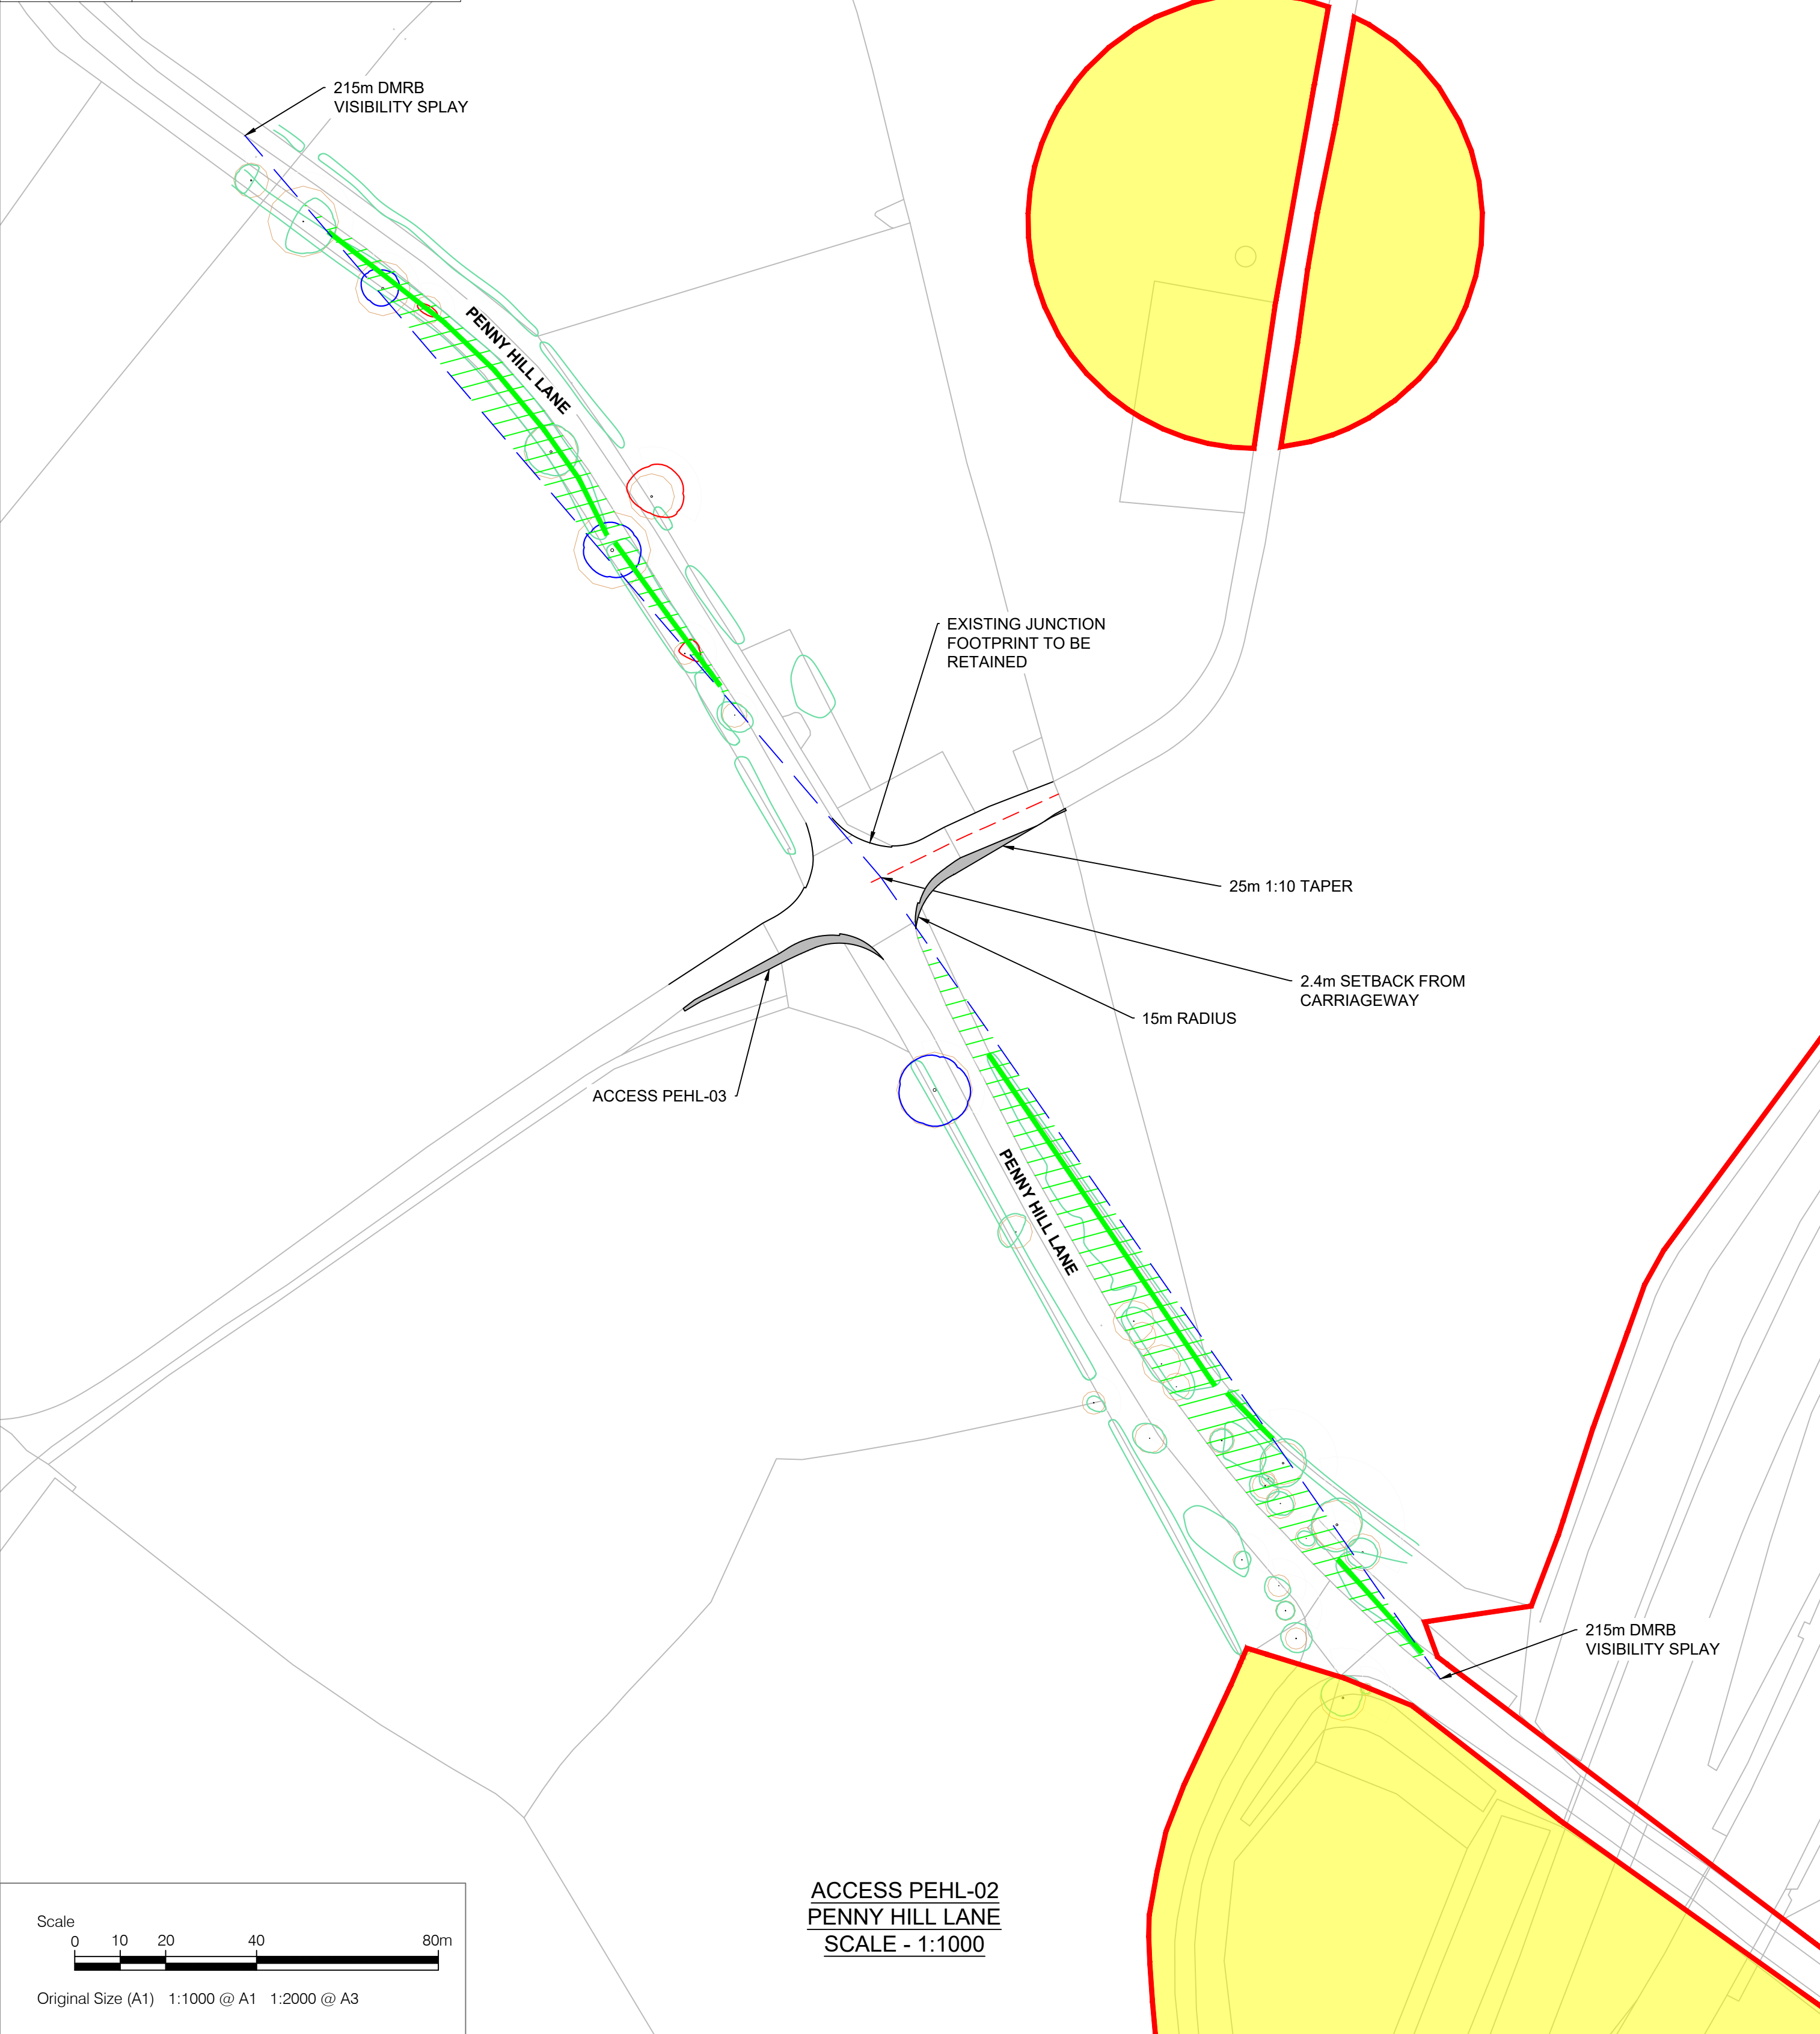

- NOTES**
- This drawing is to be read in conjunction with all other relevant documentation.
 - Do not scale from this drawing, use only printed dimensions.
 - All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
 - This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
 - Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
 - The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
 - Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
 - Junction visibility for the access is based upon DMRB CD109 Table 2.10.

- LEGEND**
- Extent of Access Footprint
 - Order Limits
 - Land Excluded from Order Limits
 - Vehicle Body
 - Vehicle Body Path
 - Vehicle Load
 - Vehicle Load Path
 - Vehicle Wheels Path
 - Edge of Road
 - Access Centreline
 - Junction Visibility
 - Vegetation to be Removed for Vis Splay
 - Indicative Hedgerow Removal Vis Splay
 - Indicative Hedgerow Removal for Bellmouth Access
 - Health and Safety Risk Identifier
 - Existing Public Right of Way

SHEET PLAN

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:

PV Area Access PEHL-02

Appendix 3 - Sheet 13 of 53

Whitestone Solar Farm


Regulation 5(2)(o)

DRAWING DATE: 03/06/2026	
SCALE: AS SHOWN	SHEET: Sheet 13 of 53
SIZE: A1	REVISION: 01
DOCUMENT REFERENCE: EN0110020/APP/5.12	
APPLICATION NUMBER: EN0110020	






WHITESTONE
solar farm

EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012 RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

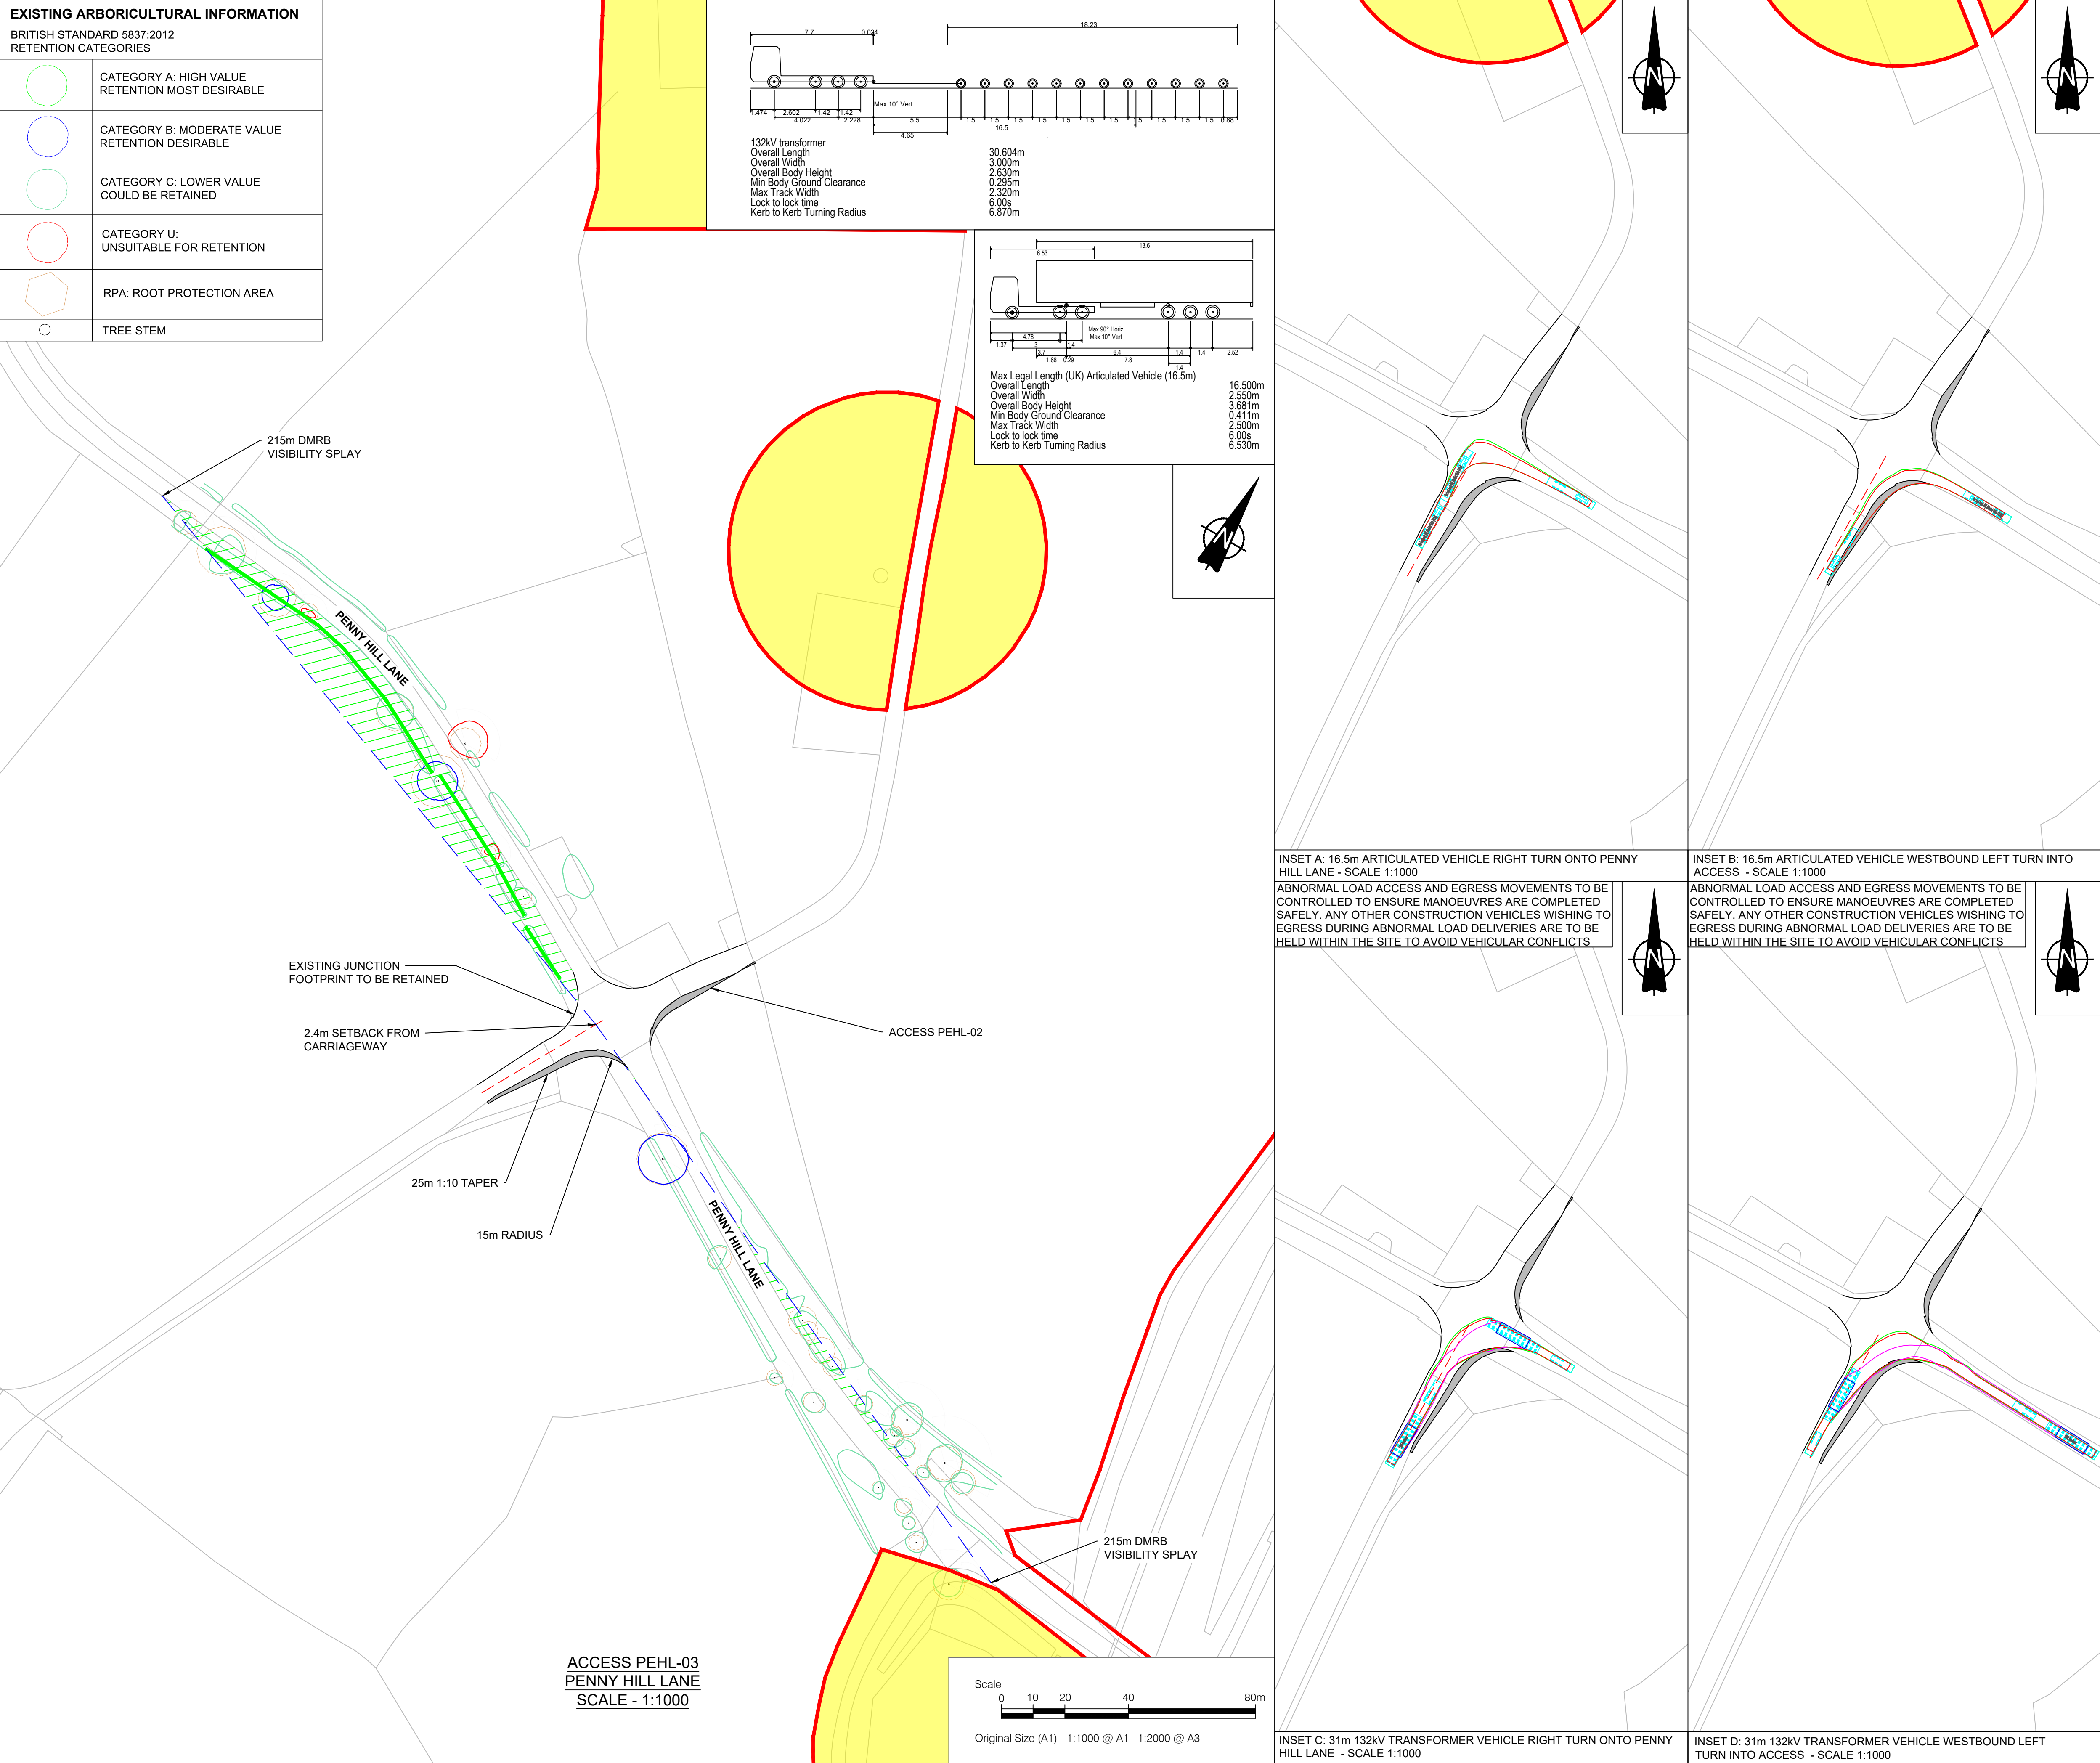

ACCESS PEHL-03
PENNY HILL LANE
SCALE - 1:1000

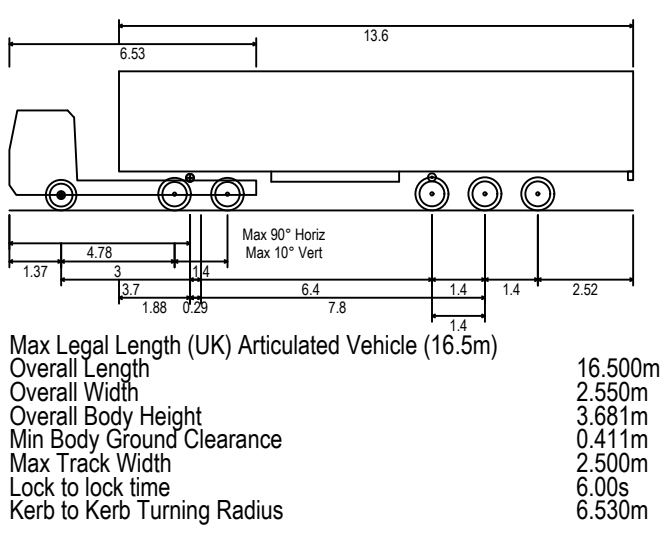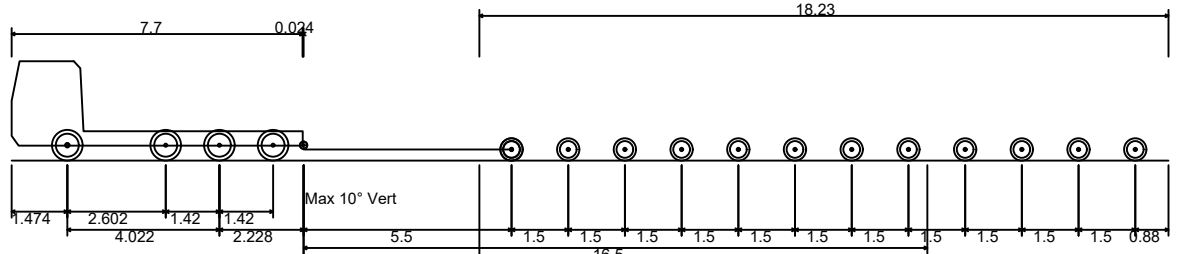


INSET A: 16.5m ARTICULATED VEHICLE RIGHT TURN ONTO PENNY HILL LANE - SCALE 1:1000
ABNORMAL LOAD ACCESS AND EGRESS MOVEMENTS TO BE CONTROLLED TO ENSURE MANOEUVRES ARE COMPLETED SAFELY. ANY OTHER CONSTRUCTION VEHICLES WISHING TO EGRESS DURING ABNORMAL LOAD DELIVERIES ARE TO BE HELD WITHIN THE SITE TO AVOID VEHICULAR CONFLICTS



INSET B: 16.5m ARTICULATED VEHICLE WESTBOUND LEFT TURN INTO ACCESS - SCALE 1:1000
ABNORMAL LOAD ACCESS AND EGRESS MOVEMENTS TO BE CONTROLLED TO ENSURE MANOEUVRES ARE COMPLETED SAFELY. ANY OTHER CONSTRUCTION VEHICLES WISHING TO EGRESS DURING ABNORMAL LOAD DELIVERIES ARE TO BE HELD WITHIN THE SITE TO AVOID VEHICULAR CONFLICTS



INSET C: 31m 132kV TRANSFORMER VEHICLE RIGHT TURN ONTO PENNY HILL LANE - SCALE 1:1000

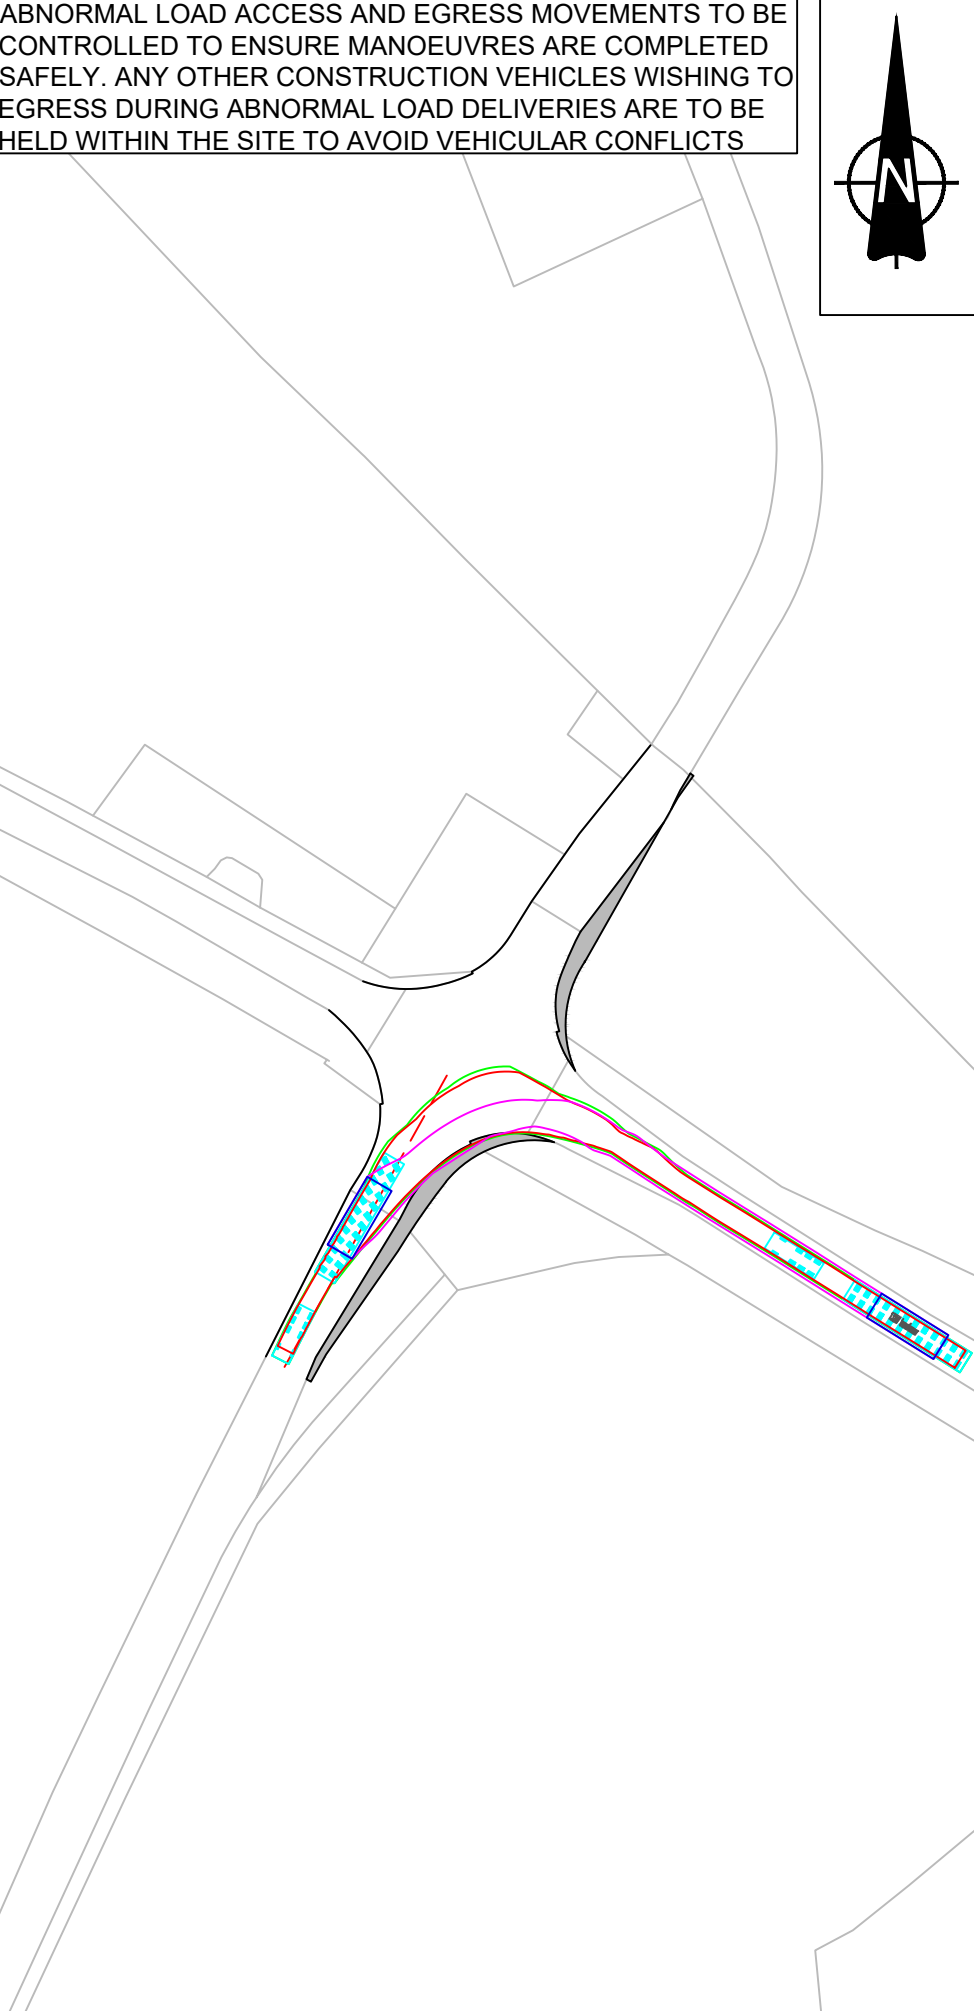


INSET D: 31m 132kV TRANSFORMER VEHICLE WESTBOUND LEFT TURN INTO ACCESS - SCALE 1:1000

- NOTES**
- This drawing is to be read in conjunction with all other relevant documentation.
 - Do not scale from this drawing, use only printed dimensions.
 - All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
 - This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
 - Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
 - The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
 - Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
 - Junction visibility for the access is based upon DMRB CD109 Table 2.10.

- LEGEND**
- Extent of Access Footprint
 - Order Limits
 - Land Excluded from Order Limits
 - Vehicle Body
 - Vehicle Body Path
 - Vehicle Load
 - Vehicle Load Path
 - Vehicle Wheels Path
 - Edge of Road
 - Access Centreline
 - Junction Visibility
 - Vegetation to be Removed for Vis Splay
 - Indicative Hedgerow Removal Vis Splay
 - Indicative Hedgerow Removal for Bellmouth Access
 - Health and Safety Risk Identifier
 - Existing Public Right of Way

SHEET PLAN

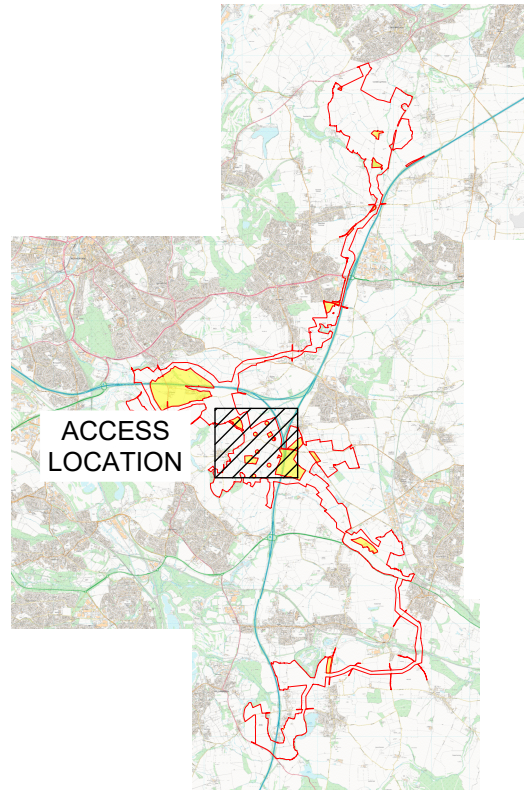

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:
PV Area Access PEHL-03
Appendix 3 - Sheet 14 of 53
Whitestone Solar Farm
Regulation 5(2)(o)

DRAWING DATE: 03/06/2026


SCALE: 1:1000
SIZE: A1
SHEET: Sheet 14 of 53
REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020




EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012 RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

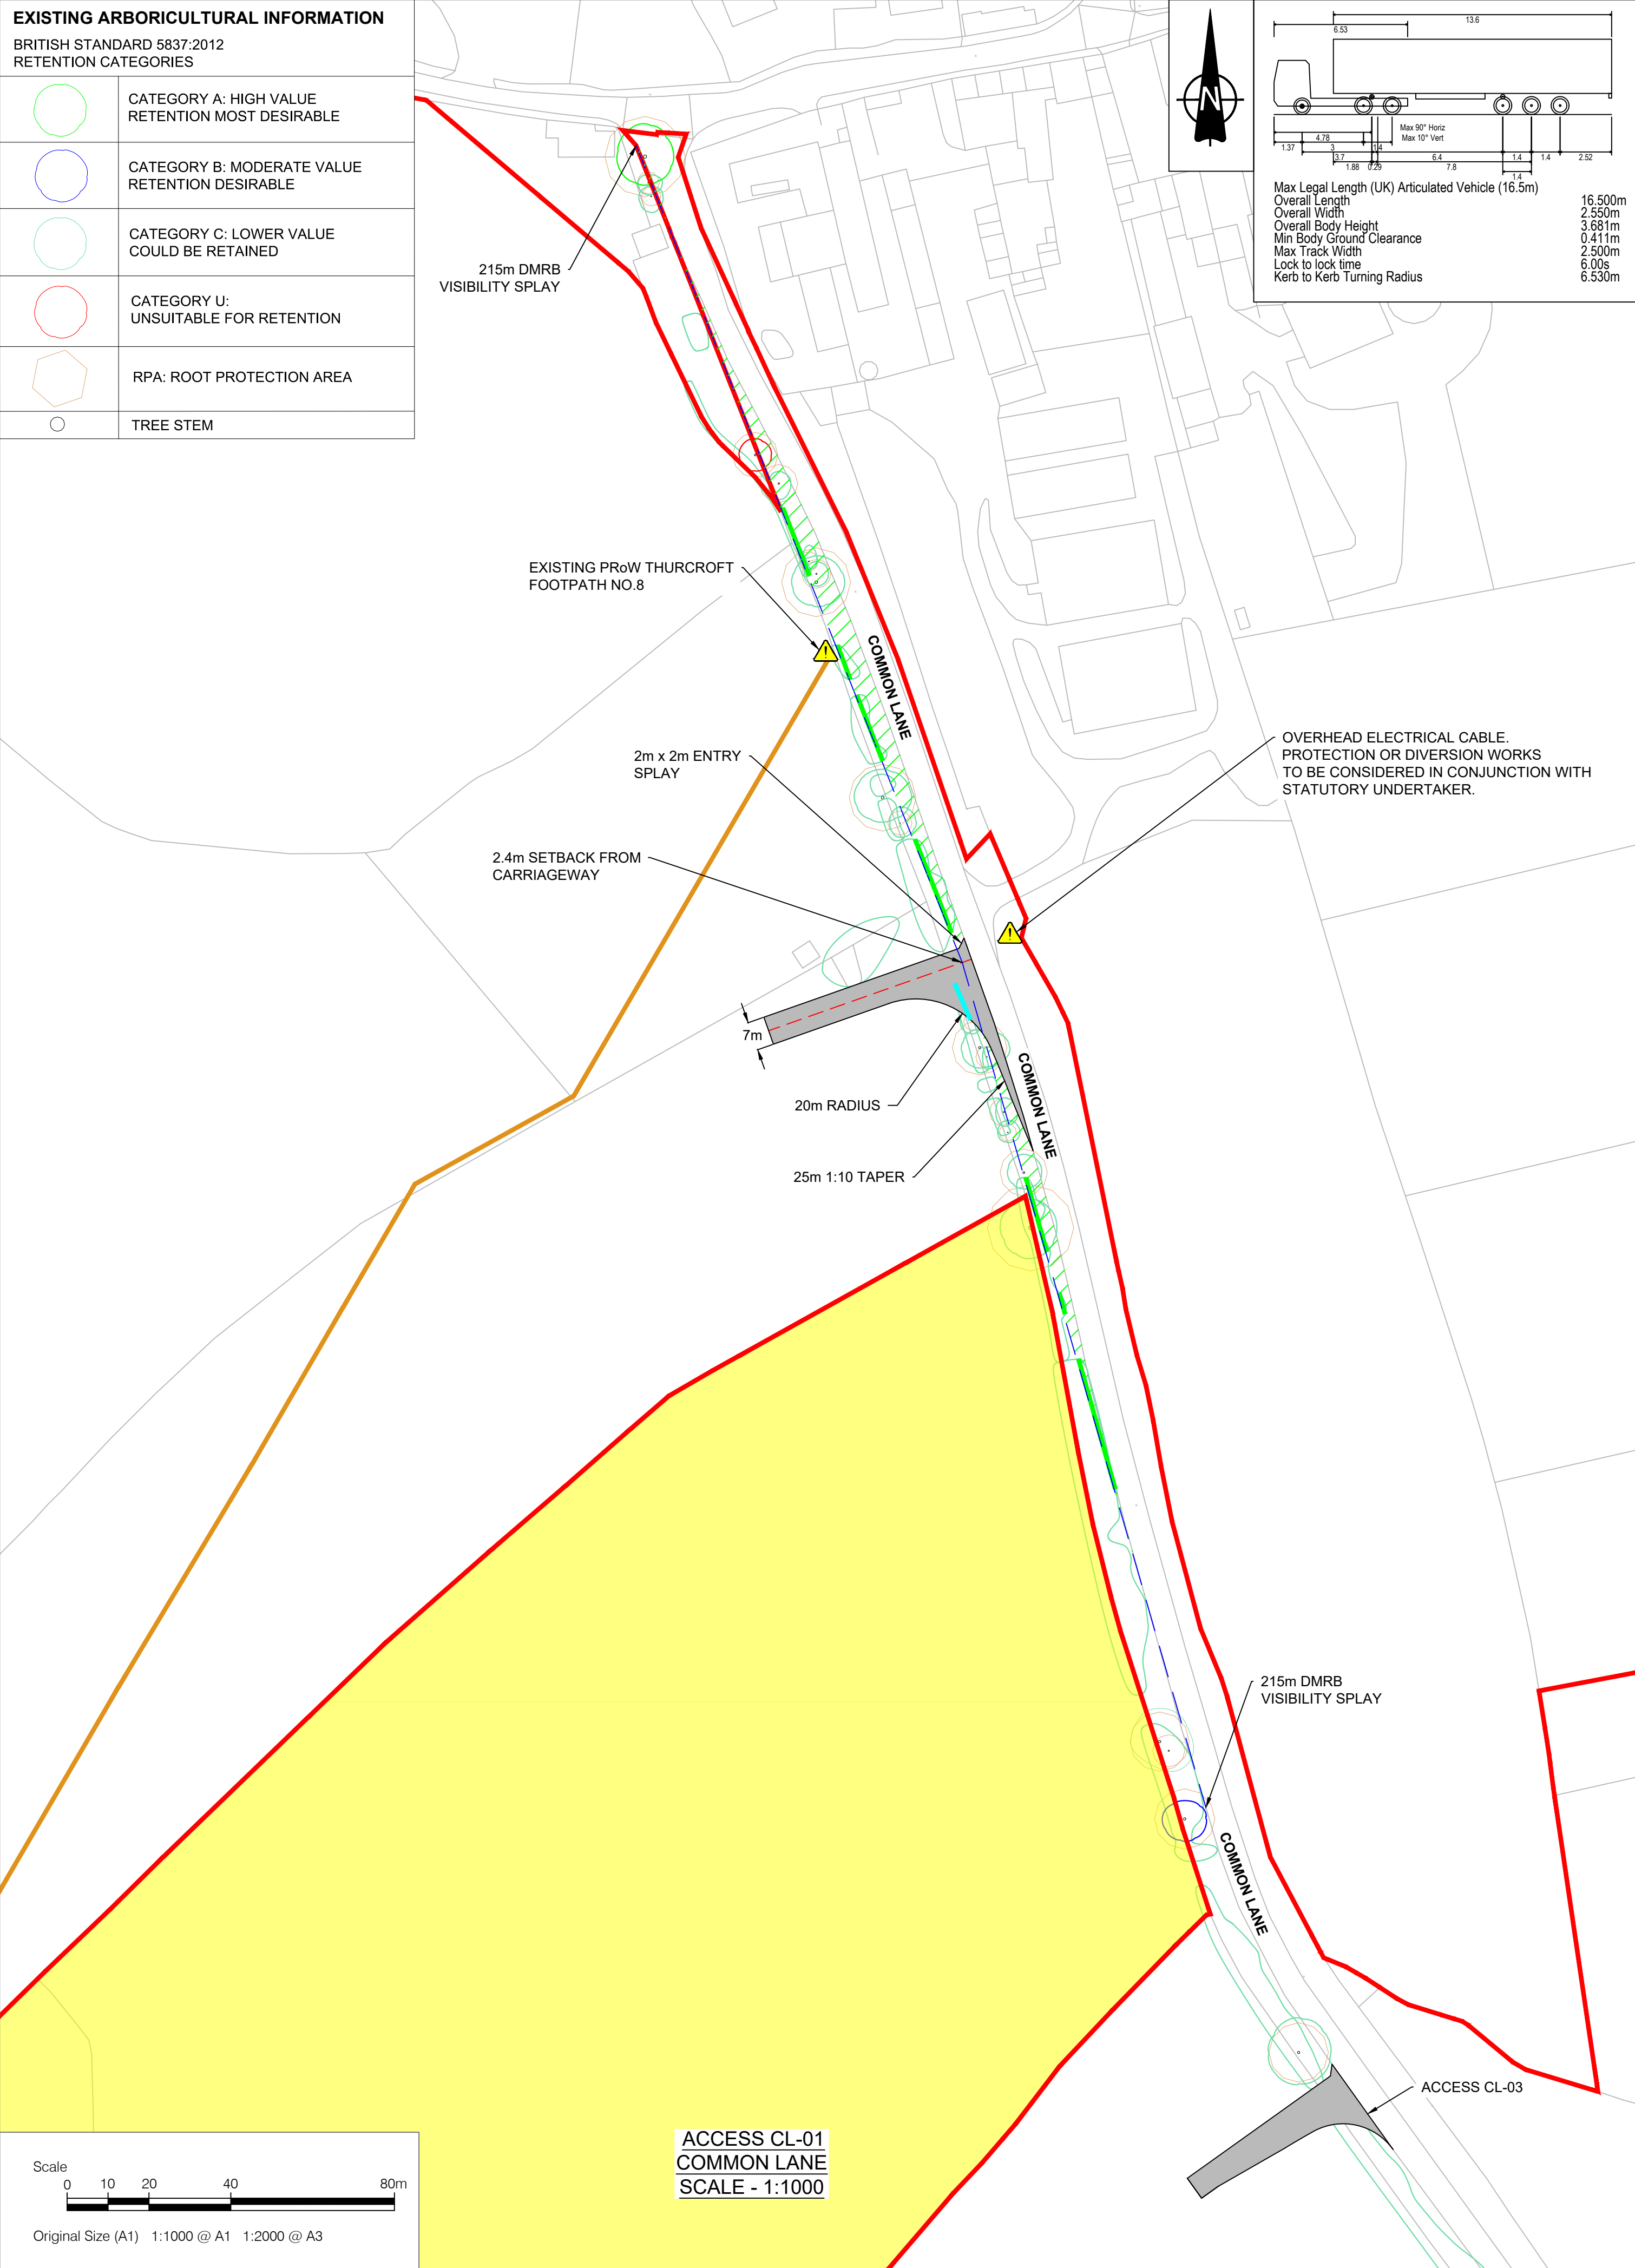

- NOTES**
- This drawing is to be read in conjunction with all other relevant documentation.
 - Do not scale from this drawing, use only printed dimensions.
 - All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
 - This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
 - Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
 - The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
 - Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
 - Junction visibility for the access is based upon DMRB CD109 Table 2.10.

- LEGEND**
- Extent of Access Footprint
 - Order Limits
 - Land Excluded from Order Limits
 - Vehicle Body
 - Vehicle Body Path
 - Vehicle Load
 - Vehicle Load Path
 - Vehicle Wheels Path
 - Edge of Road
 - Access Centreline
 - Junction Visibility
 - Vegetation to be Removed for Vis Splay
 - Indicative Hedgerow Removal Vis Splay
 - Indicative Hedgerow Removal for Bellmouth Access
 - Health and Safety Risk Identifier
 - Existing Public Right of Way

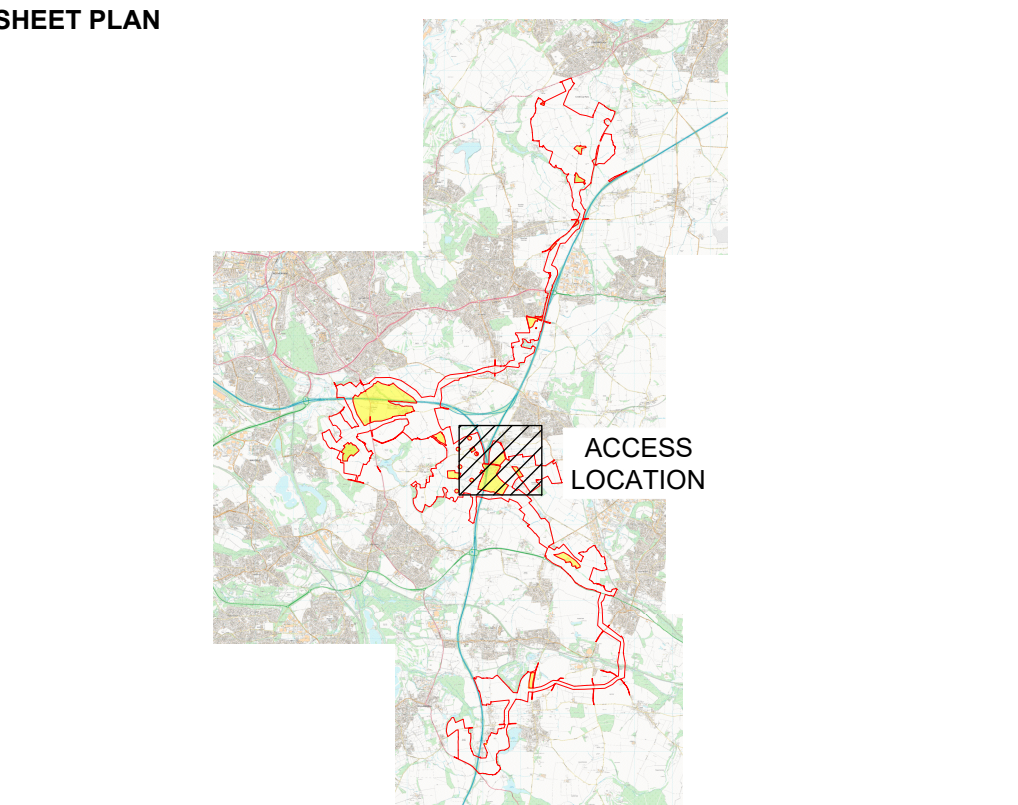

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:
PV Area Access CL-01
Appendix 3 - Sheet 15 of 53
Whitestone Solar Farm
Regulation 5(2)(o)


DRAWING DATE: 03/06/2026

SCALE: AS SHOWN	SHEET: Sheet 15 of 53
SIZE: A1	REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020



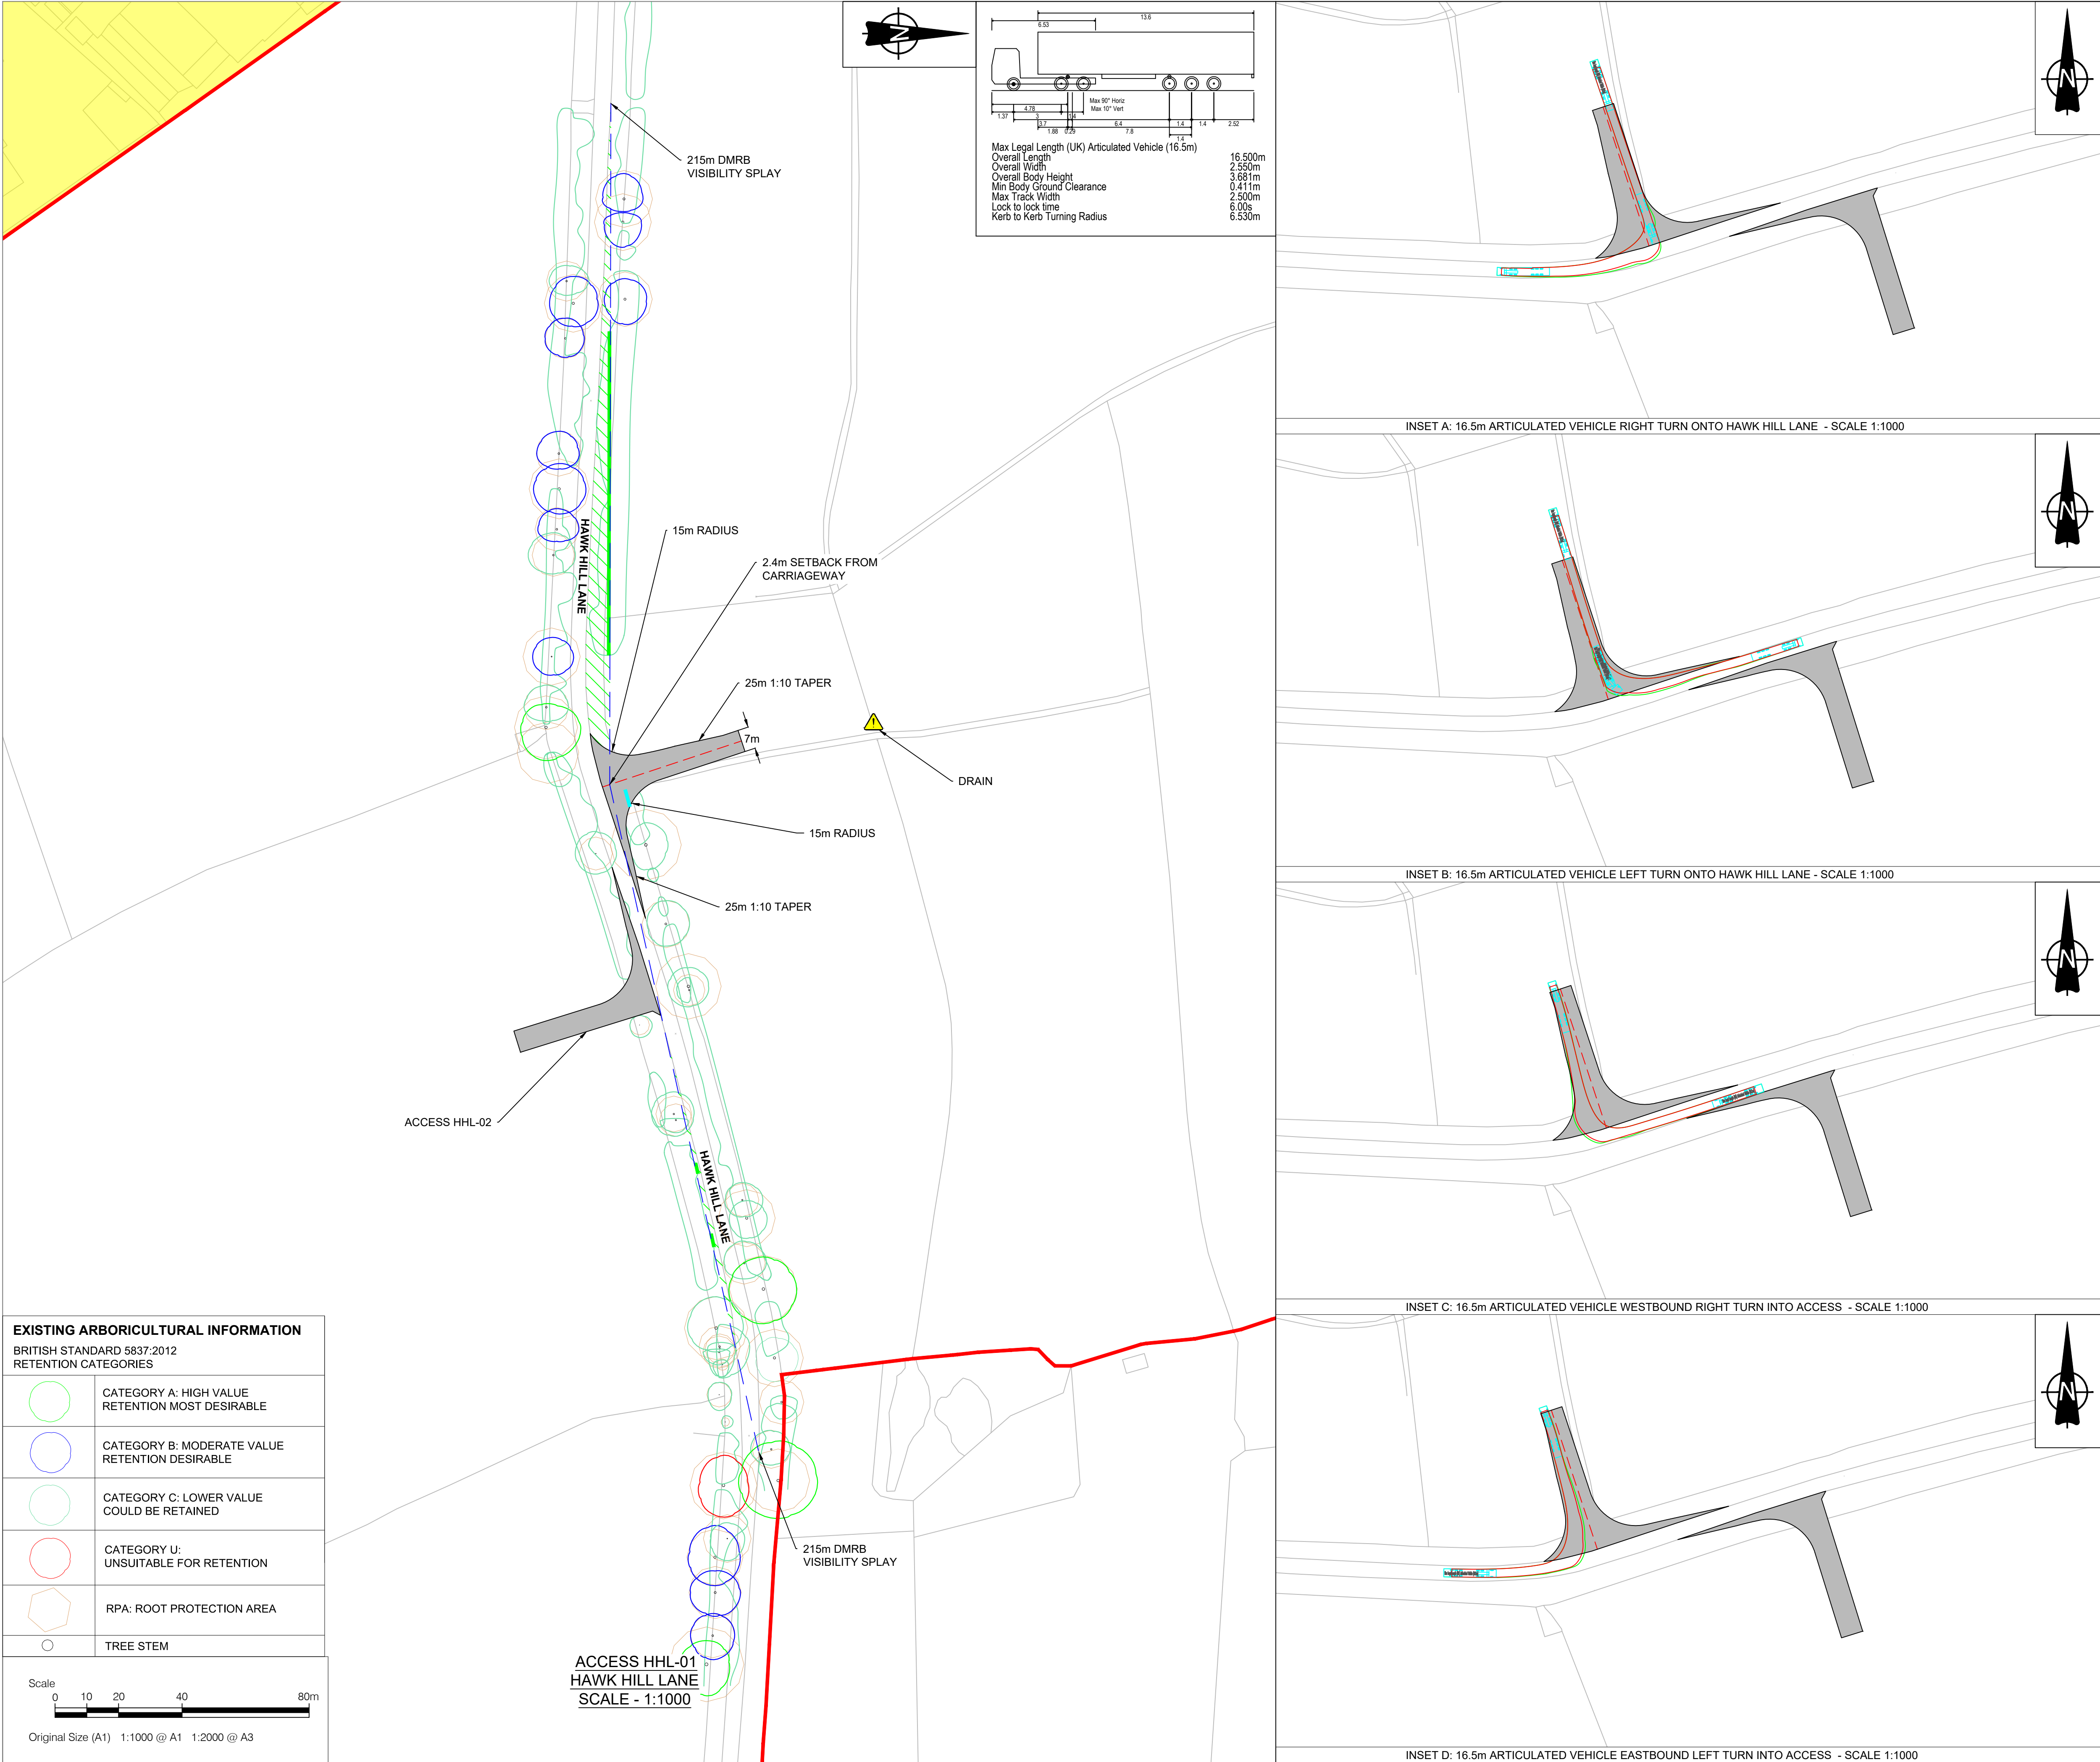

NOTES

- This drawing is to be read in conjunction with all other relevant documentation.
- Do not scale from this drawing, use only printed dimensions.
- All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
- This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
- Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
- The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
- Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
- Junction visibility for the access is based upon DMRB CD109 Table 2.10.

LEGEND

- Extent of Access Footprint
- Order Limits
- Land Excluded from Order Limits
- Vehicle Body
- Vehicle Body Path
- Vehicle Load
- Vehicle Load Path
- Vehicle Wheels Path
- Edge of Road
- Access Centreline
- Junction Visibility
- Vegetation to be Removed for Vis Splay
- Indicative Hedgerow Removal Vis Splay
- Indicative Hedgerow Removal for Bellmouth Access
- Health and Safety Risk Identifier
- Existing Public Right of Way

SHEET PLAN

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:
PV Area Access HHL-01
Appendix 3 - Sheet 16 of 53
Whitestone Solar Farm
Regulation 5(2)(o)

DRAWING DATE: 03/06/2026

SCALE: 1:1000

SHEET: Sheet 16 of 53

SIZE: A1

REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12


APPLICATION NUMBER: EN0110020

EXISTING ARBORICULTURAL INFORMATION
BRITISH STANDARD 5837:2012
RETENTION CATEGORIES

	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

Scale

Original Size (A1) 1:1000 @ A1 1:2000 @ A3

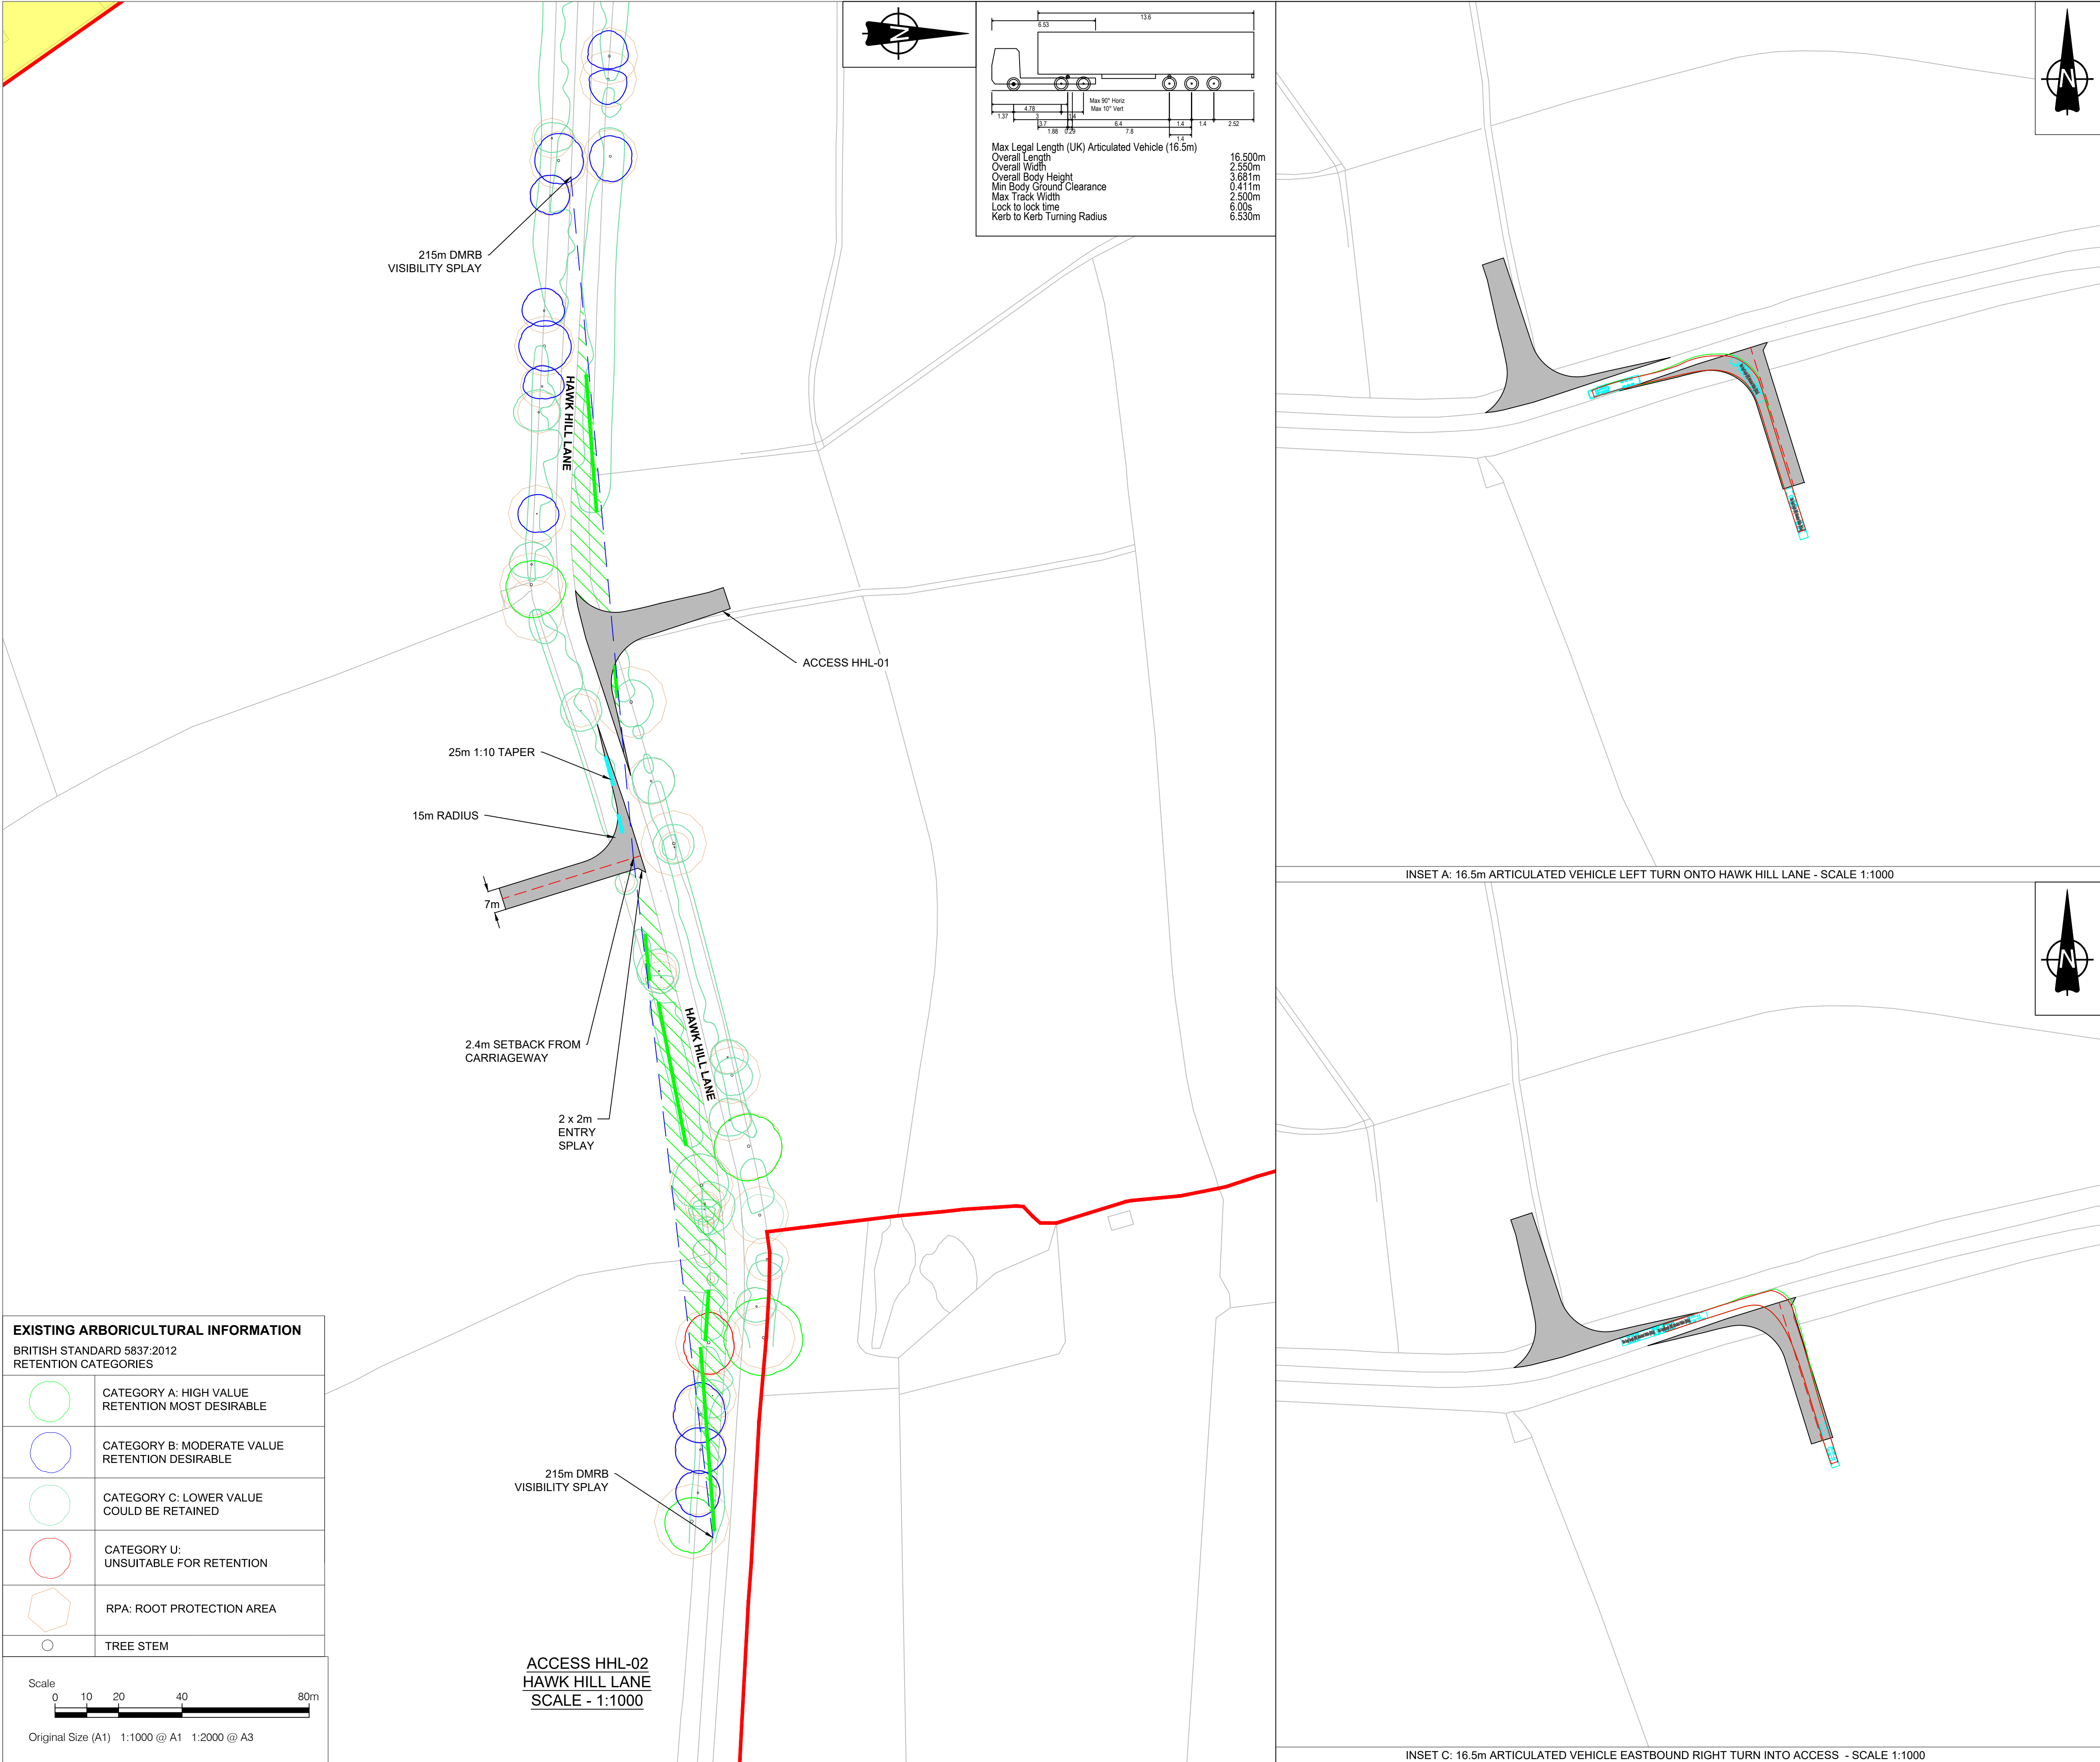

NOTES

- This drawing is to be read in conjunction with all other relevant documentation.
- Do not scale from this drawing, use only printed dimensions.
- All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
- This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
- Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
- The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
- Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
- Junction visibility for the access is based upon DMRB CD109 Table 2.10.

LEGEND

- Extent of Access Footprint
- Order Limits
- Land Excluded from Order Limits
- Vehicle Body
- Vehicle Body Path
- Vehicle Load
- Vehicle Load Path
- Vehicle Wheels Path
- Edge of Road
- Access Centreline
- Junction Visibility
- Vegetation to be Removed for Vis Splay
- Indicative Hedgerow Removal Vis Splay
- Indicative Hedgerow Removal for Bellmouth Access
- Health and Safety Risk Identifier
- Existing Public Right of Way

SHEET PLAN

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:

PV Area Access HHL-02

Appendix 3 - Sheet 17 of 53

Whitestone Solar Farm

Regulation 5(2)(o)


DRAWING DATE: 03/06/2026

SCALE: 1:1000	SHEET: Sheet 17 of 53
SIZE: A1	REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020

EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012 RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

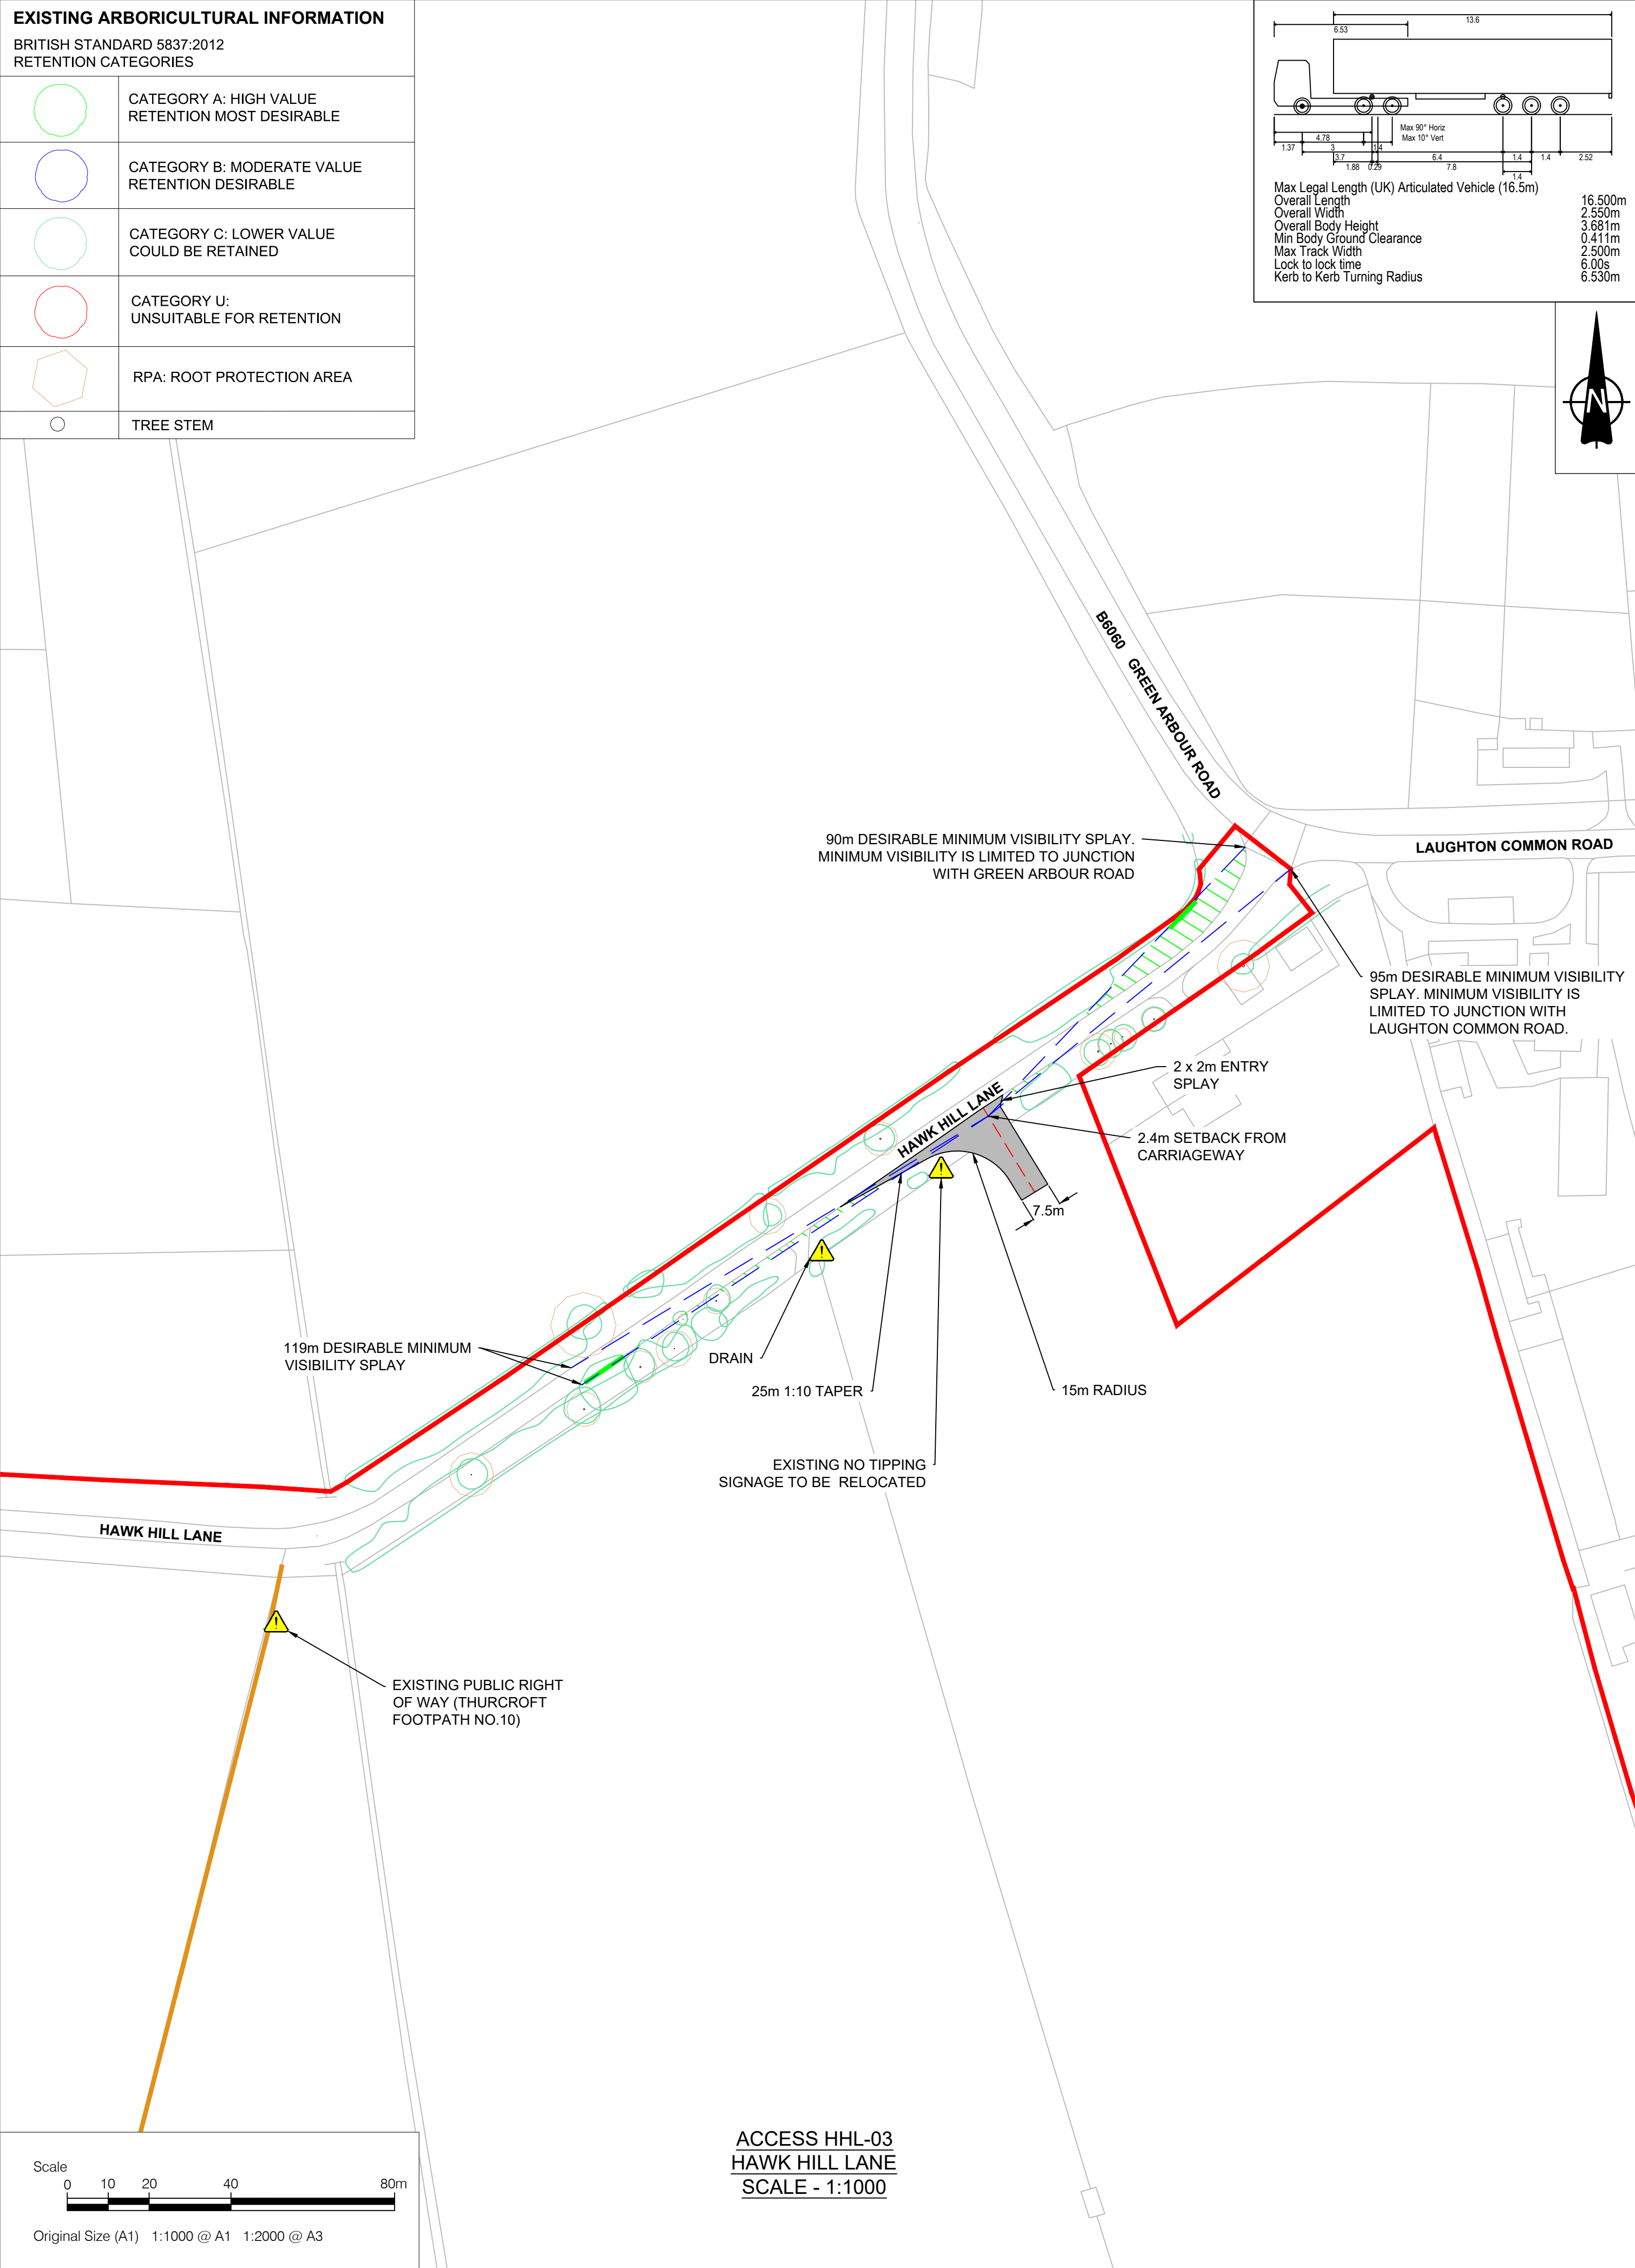


NOTES

- This drawing is to be read in conjunction with all other relevant documentation.
- Do not scale from this drawing, use only printed dimensions.
- All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
- This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
- Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
- The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
- Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
- Junction visibility for the access is based upon visibility parameters derived using the 85th percentile speed survey conducted between the 4th June 2025 to the 10th June 2025.

LEGEND

- Extent of Access Footprint
- Order Limits
- Land Excluded from Order Limits
- Vehicle Body
- Vehicle Body Path
- Vehicle Load
- Vehicle Load Path
- Vehicle Wheels Path
- Edge of Road
- Access Centreline
- Junction Visibility
- Vegetation to be Removed for Vis Splay
- Indicative Hedgerow Removal Vis Splay
- Indicative Hedgerow Removal for Bellmouth Access
- Health and Safety Risk Identifier
- Existing Public Right of Way

SHEET PLAN

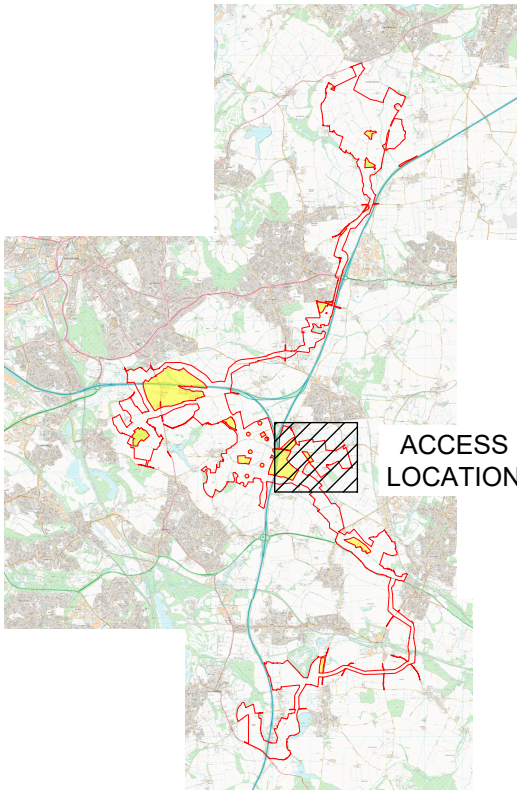

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:
PV Area Access HHL-03
Appendix 3 - Sheet 18 of 53
Whitestone Solar Farm
Regulation 5(2)(o)


DRAWING DATE: 03/06/2026

SCALE: AS SHOWN	SHEET: Sheet 18 of 53
SIZE: A1	REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020




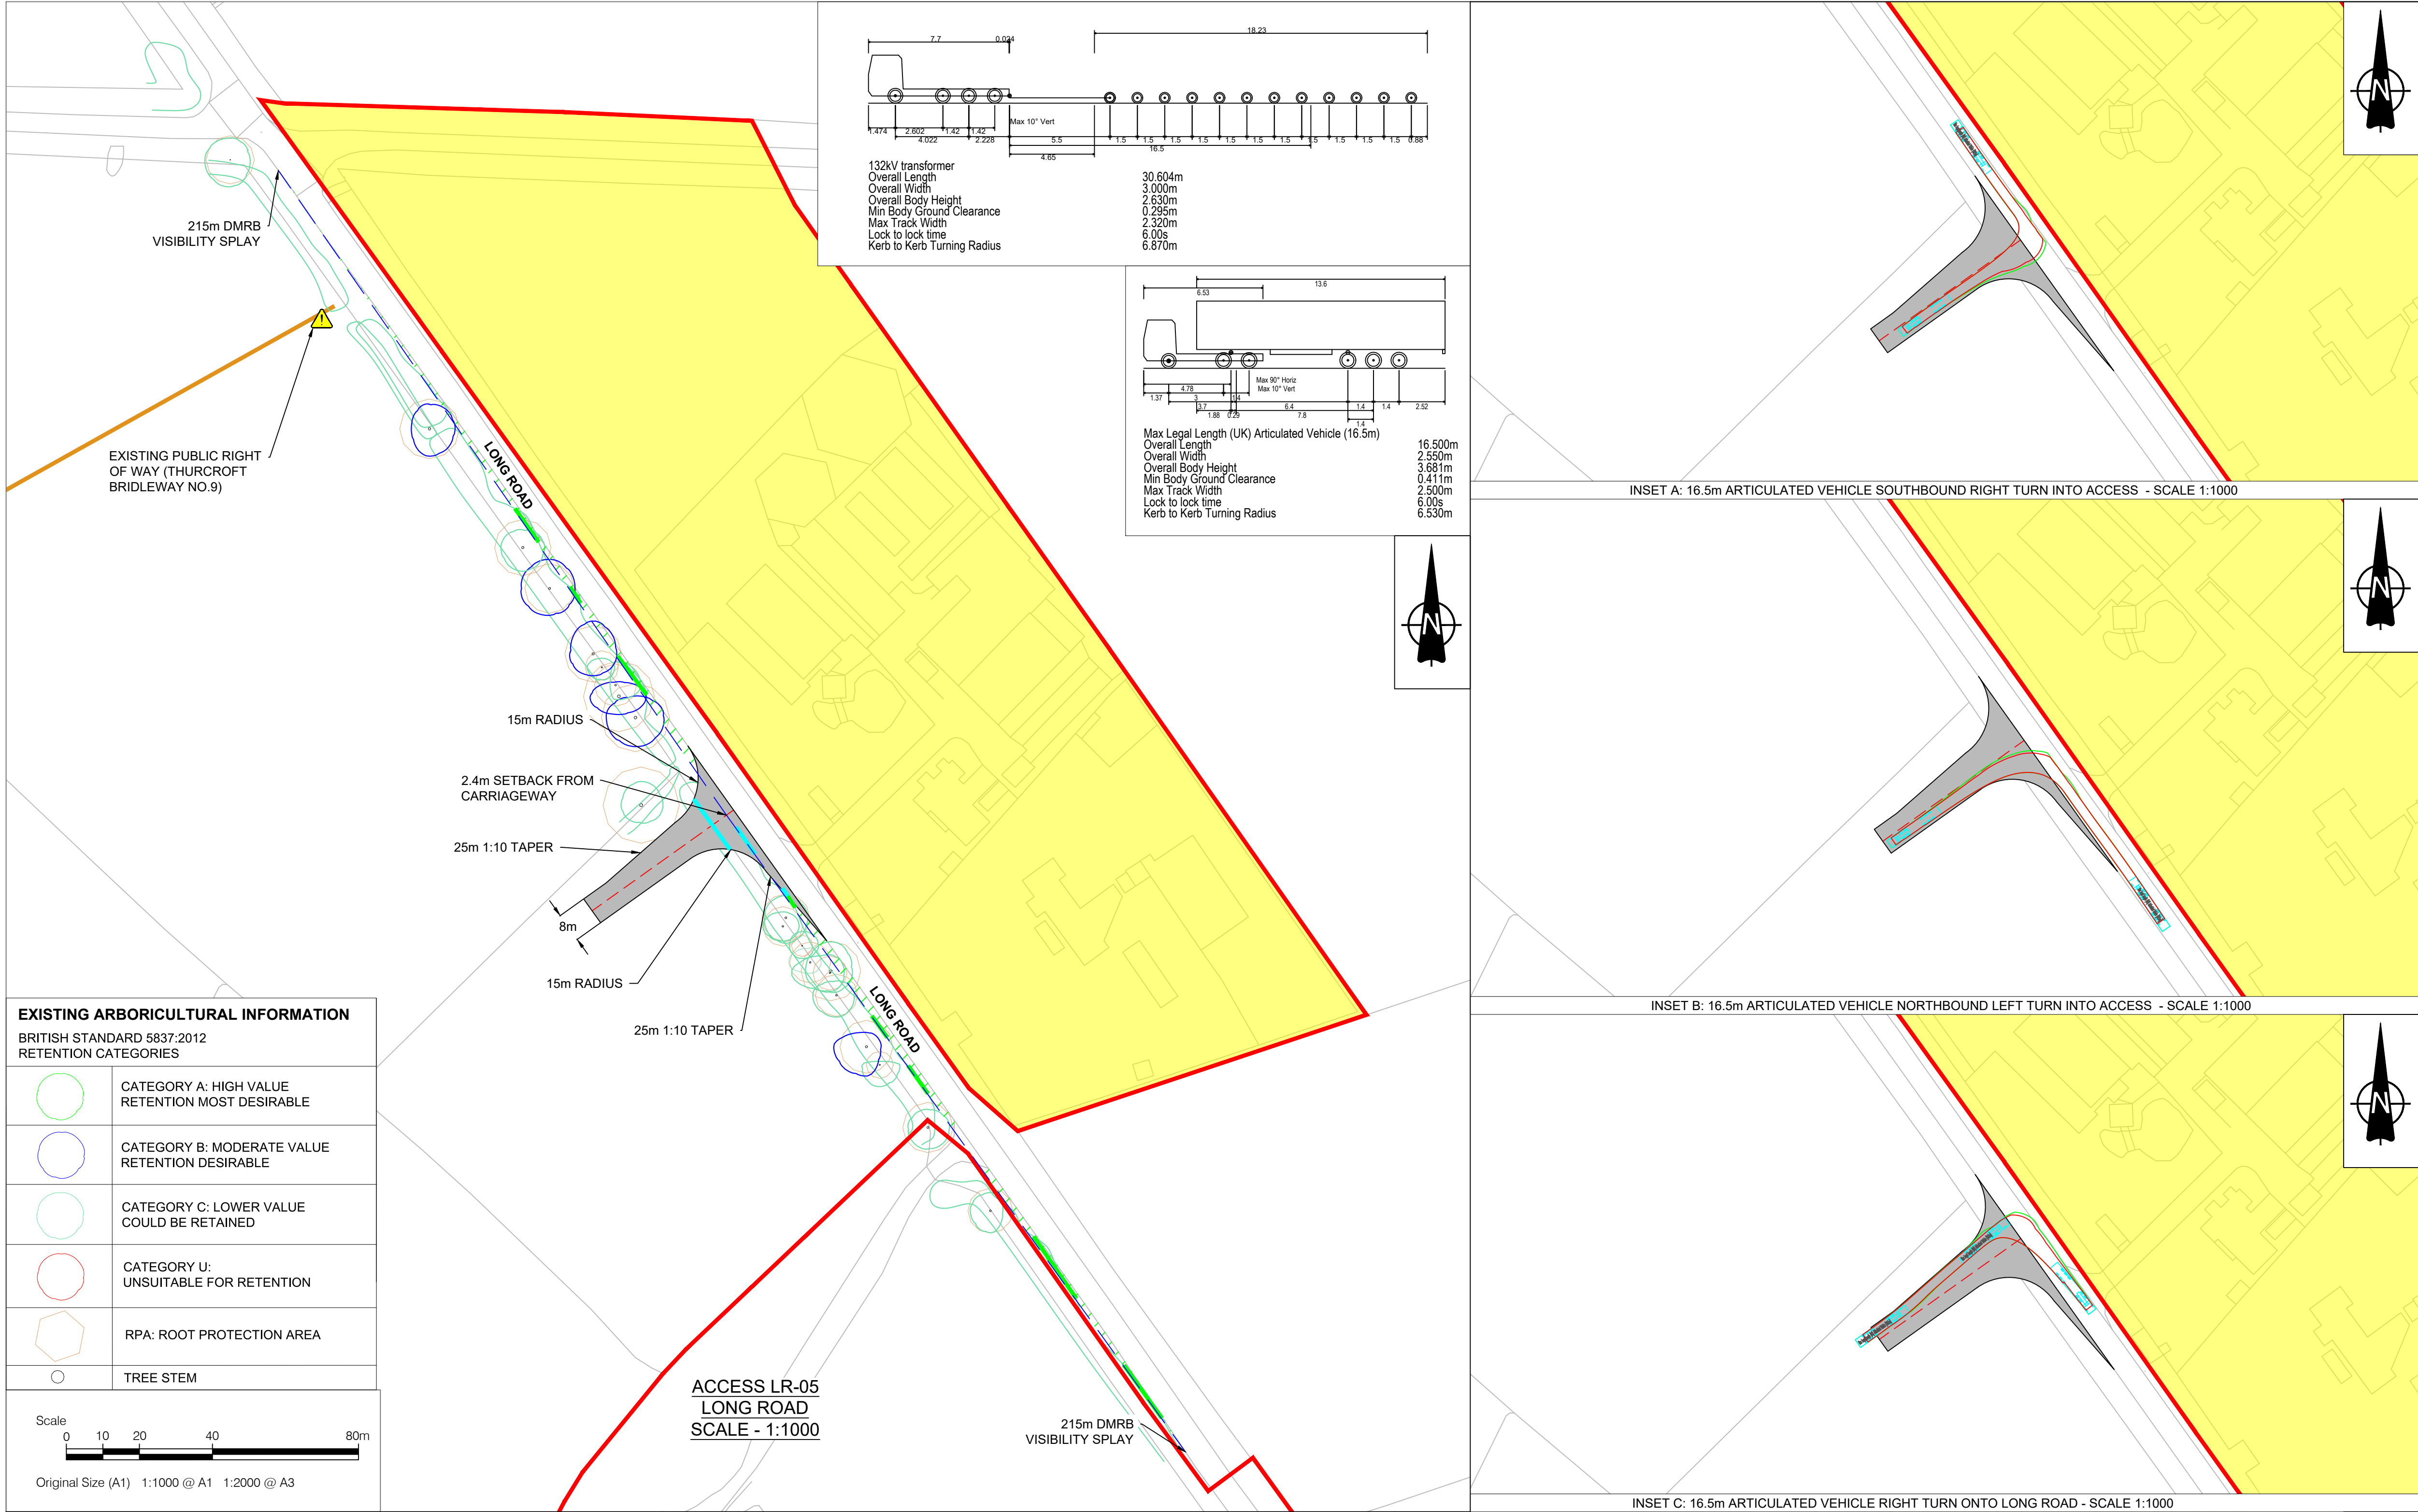

EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012	
RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM
Scale 0 10 20 40 80m	
Original Size (A1) 1:1000 @ A1 1:2000 @ A3	

- NOTES**
- This drawing is to be read in conjunction with all other relevant documentation.
 - Do not scale from this drawing, use only printed dimensions.
 - All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
 - This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
 - Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
 - The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
 - Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
 - Junction visibility for the access is based upon DMRB CD109 Table 2.10.

- LEGEND**
- Extent of Access Footprint
 - Order Limits
 - Land Excluded from Order Limits
 - Vehicle Body
 - Vehicle Body Path
 - Vehicle Load
 - Vehicle Load Path
 - Vehicle Wheels Path
 - Edge of Road
 - Access Centreline
 - Junction Visibility
 - Vegetation to be Removed for Vis Splay
 - Indicative Hedgerow Removal Vis Splay
 - Indicative Hedgerow Removal for Bellmouth Access
 - Health and Safety Risk Identifier
 - Existing Public Right of Way

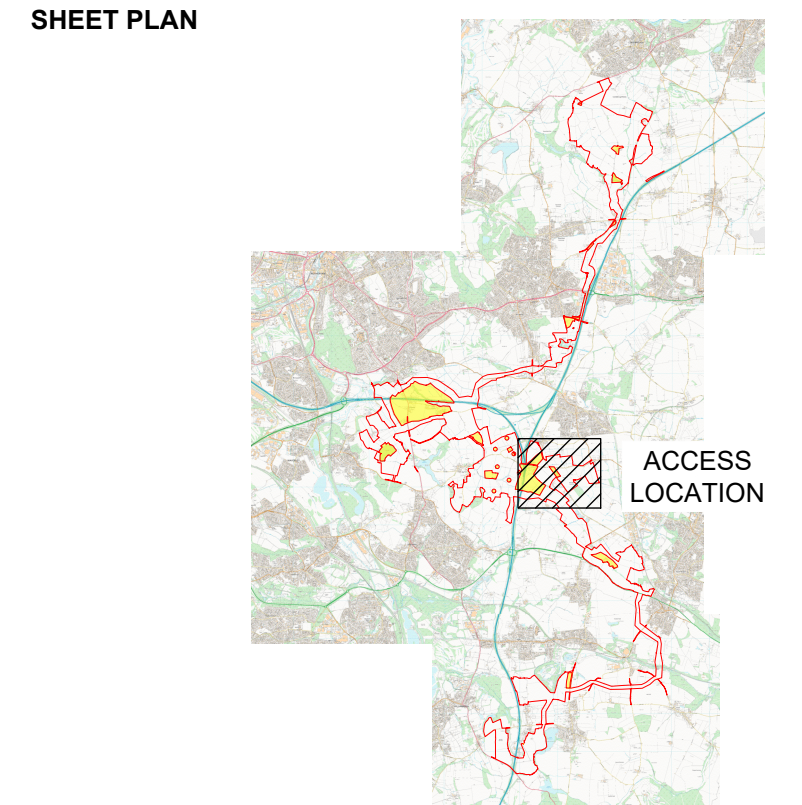

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:
PV Area Access LR-05
Appendix 3 - Sheet 19 of 53
Whitestone Solar Farm
Regulation 5(2)(o)

DRAWING DATE: 03/06/2026

SCALE: 1:1000
SIZE: A1

SHEET: Sheet 19 of 53
REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020




ABNORMAL LOAD ACCESS AND EGRESS MOVEMENTS TO BE CONTROLLED TO ENSURE MANOEUVRES ARE COMPLETED SAFELY. ANY OTHER CONSTRUCTION VEHICLES WISHING TO EGRESS DURING ABNORMAL LOAD DELIVERIES ARE TO BE HELD WITHIN THE SITE TO AVOID VEHICULAR CONFLICTS

INSET F: 31m 132kV TRANSFORMER VEHICLE NORTHBOUND LEFT TURN INTO ACCESS - SCALE 1:1000

ABNORMAL LOAD ACCESS AND EGRESS MOVEMENTS TO BE CONTROLLED TO ENSURE MANOEUVRES ARE COMPLETED SAFELY. ANY OTHER CONSTRUCTION VEHICLES WISHING TO EGRESS DURING ABNORMAL LOAD DELIVERIES ARE TO BE HELD WITHIN THE SITE TO AVOID VEHICULAR CONFLICTS


INSET E: 31m 132kV TRANSFORMER VEHICLE RIGHT TURN ONTO LONG ROAD - SCALE 1:1000

INSET D: 16.5m ARTICULATED VEHICLE LEFT TURN ONTO LONG ROAD - SCALE 1:1000

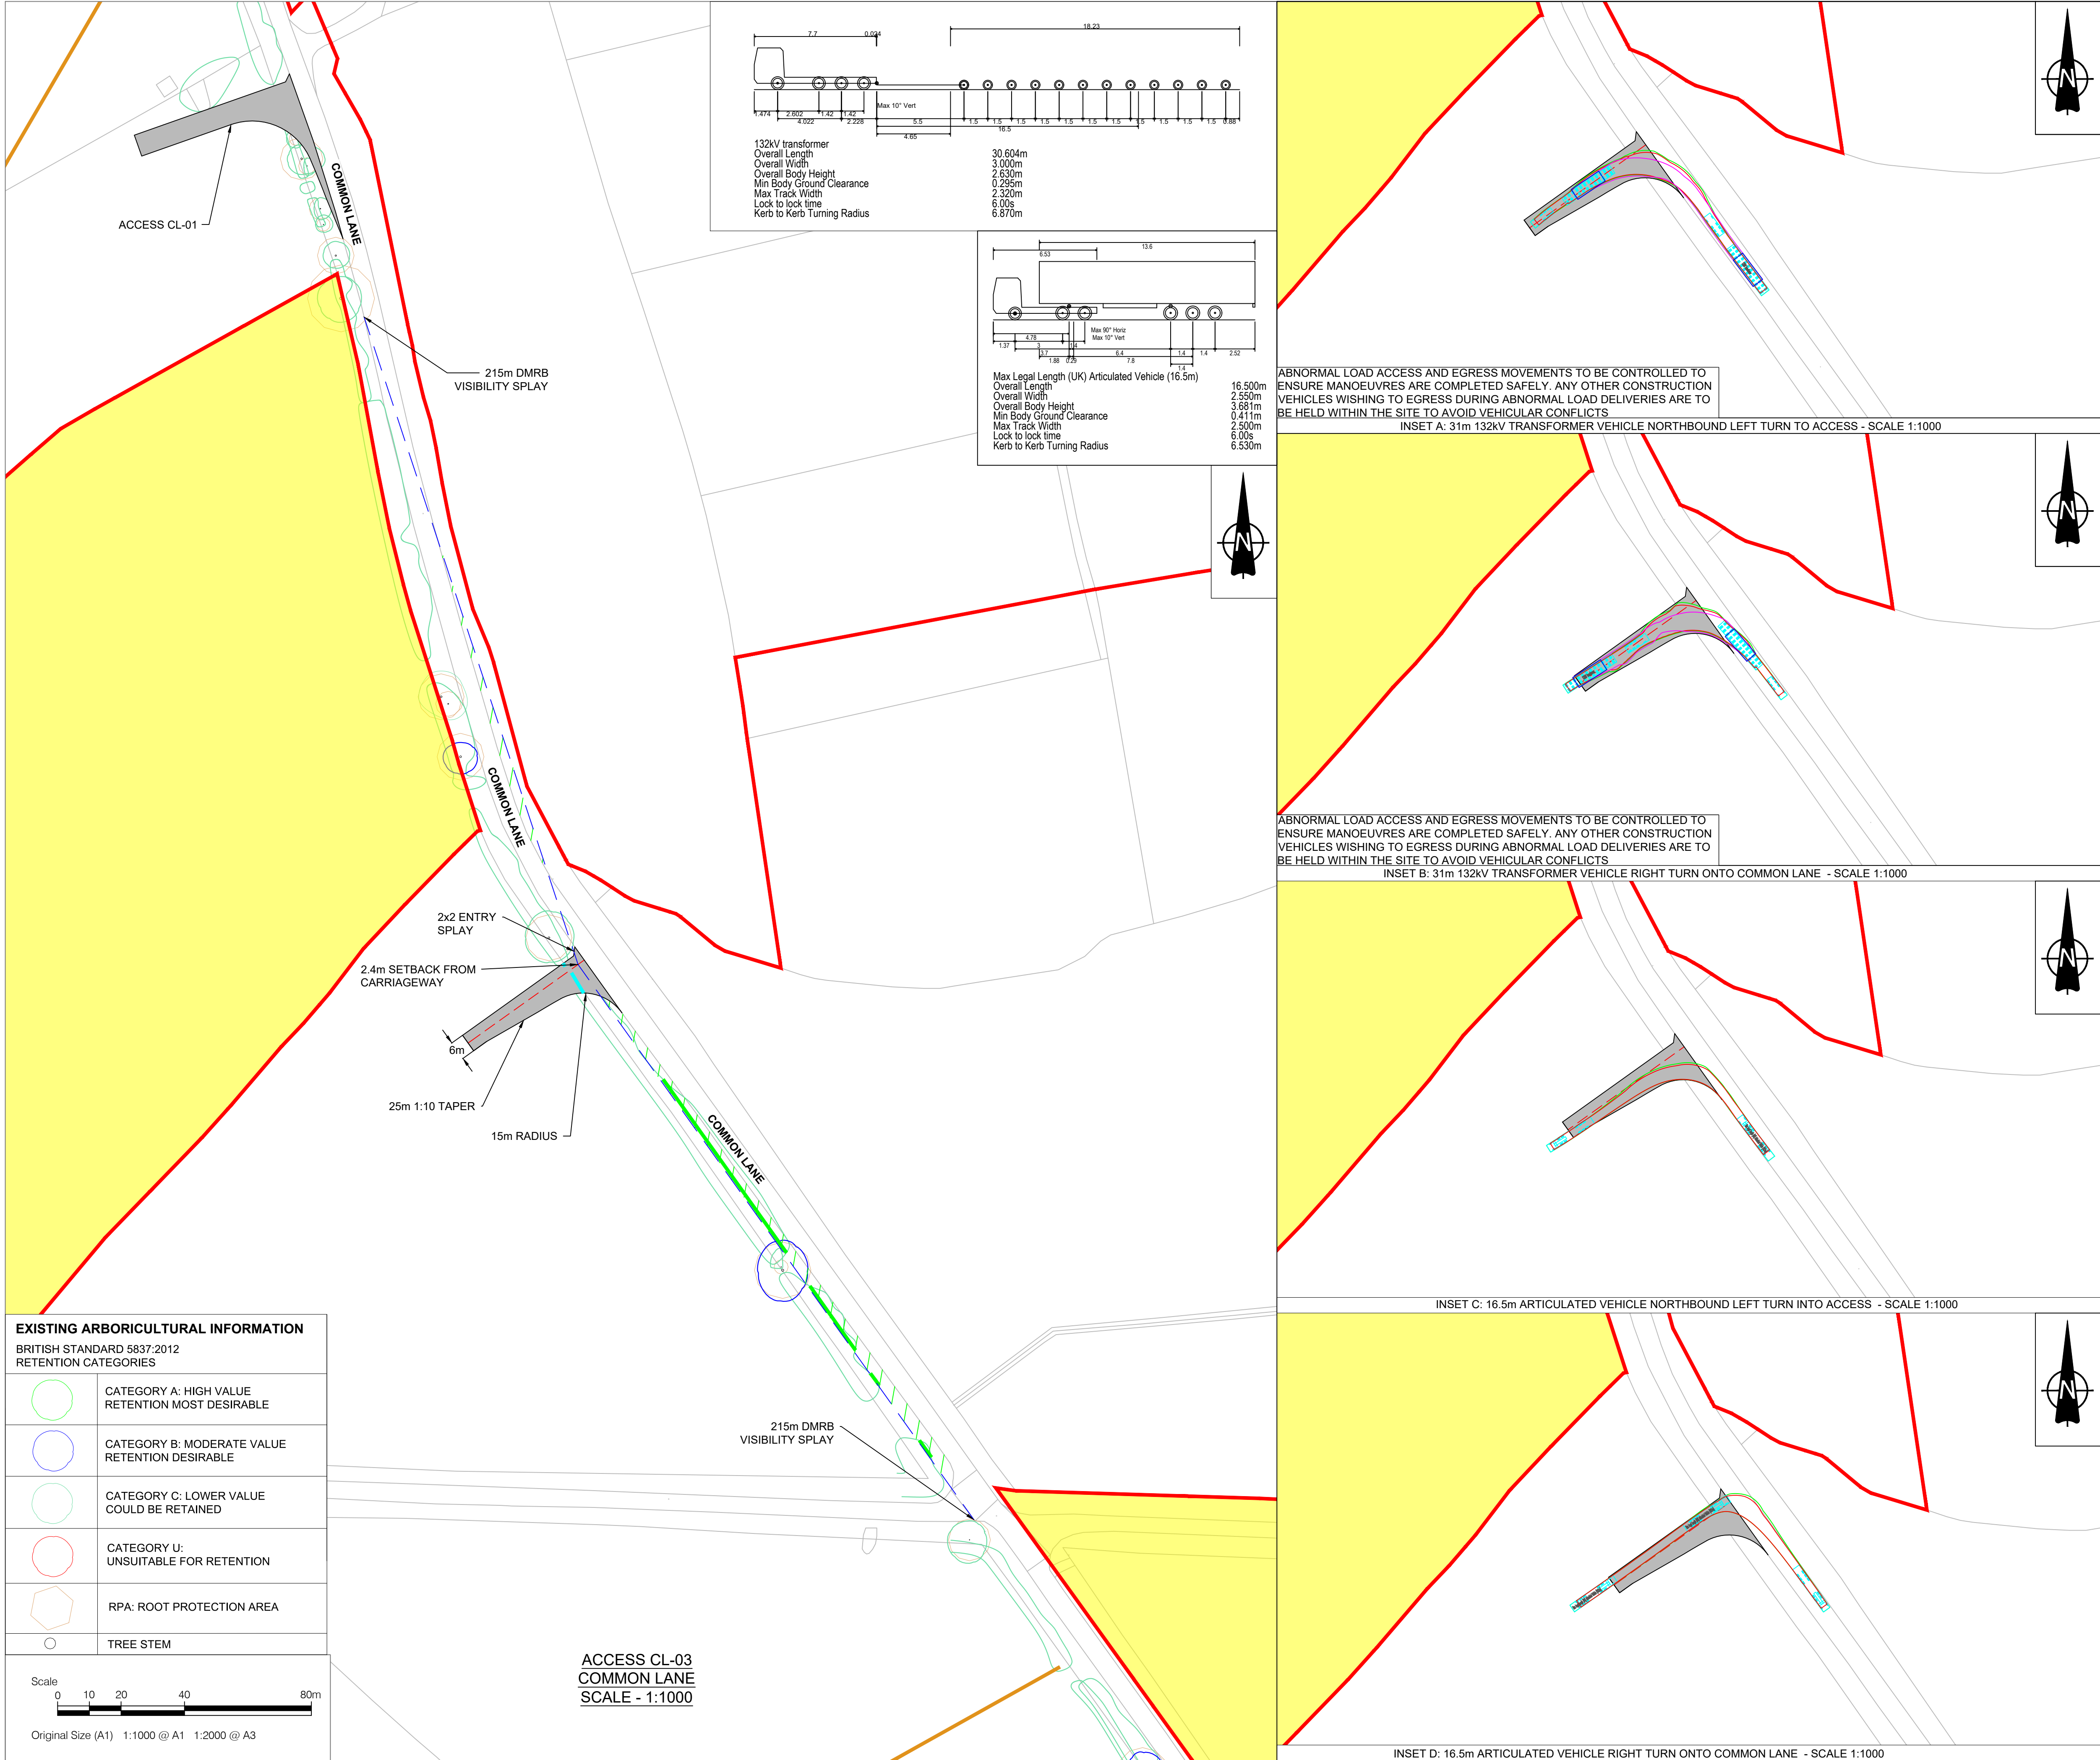

- NOTES**
- This drawing is to be read in conjunction with all other relevant documentation.
 - Do not scale from this drawing, use only printed dimensions.
 - All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
 - This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
 - Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
 - The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
 - Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
 - Junction visibility for the access is based upon DMRB CD109 Table 2.10.

- LEGEND**
- Extent of Access Footprint
 - Order Limits
 - Land Excluded from Order Limits
 - Vehicle Body
 - Vehicle Body Path
 - Vehicle Load
 - Vehicle Load Path
 - Vehicle Wheels Path
 - Edge of Road
 - Access Centreline
 - Junction Visibility
 - Vegetation to be Removed for Vis Splay
 - Indicative Hedgerow Removal Vis Splay
 - Indicative Hedgerow Removal for Bellmouth Access
 - Health and Safety Risk Identifier
 - Existing Public Right of Way

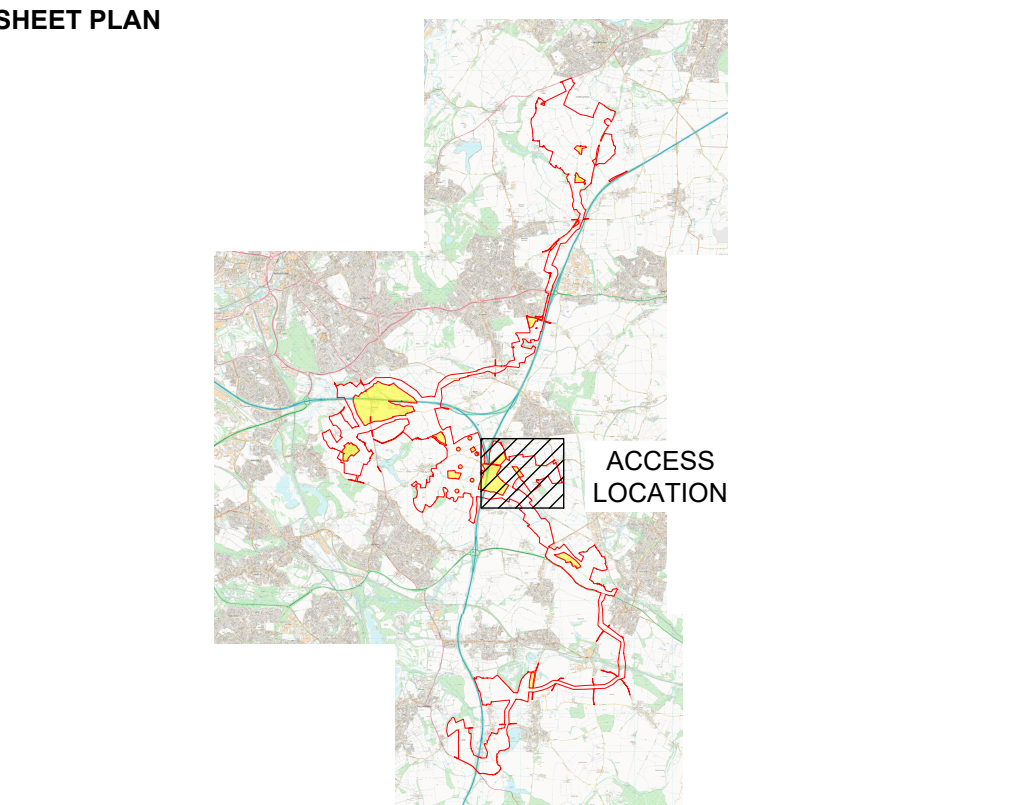

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:
PV Area Access CL-03
Appendix 3 - Sheet 20 of 53
Whitestone Solar Farm
Regulation 5(2)(o)

DRAWING DATE: 03/06/2026


SCALE: 1:1000
SIZE: A1

SHEET: Sheet 20 of 53
REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12


APPLICATION NUMBER: EN0110020



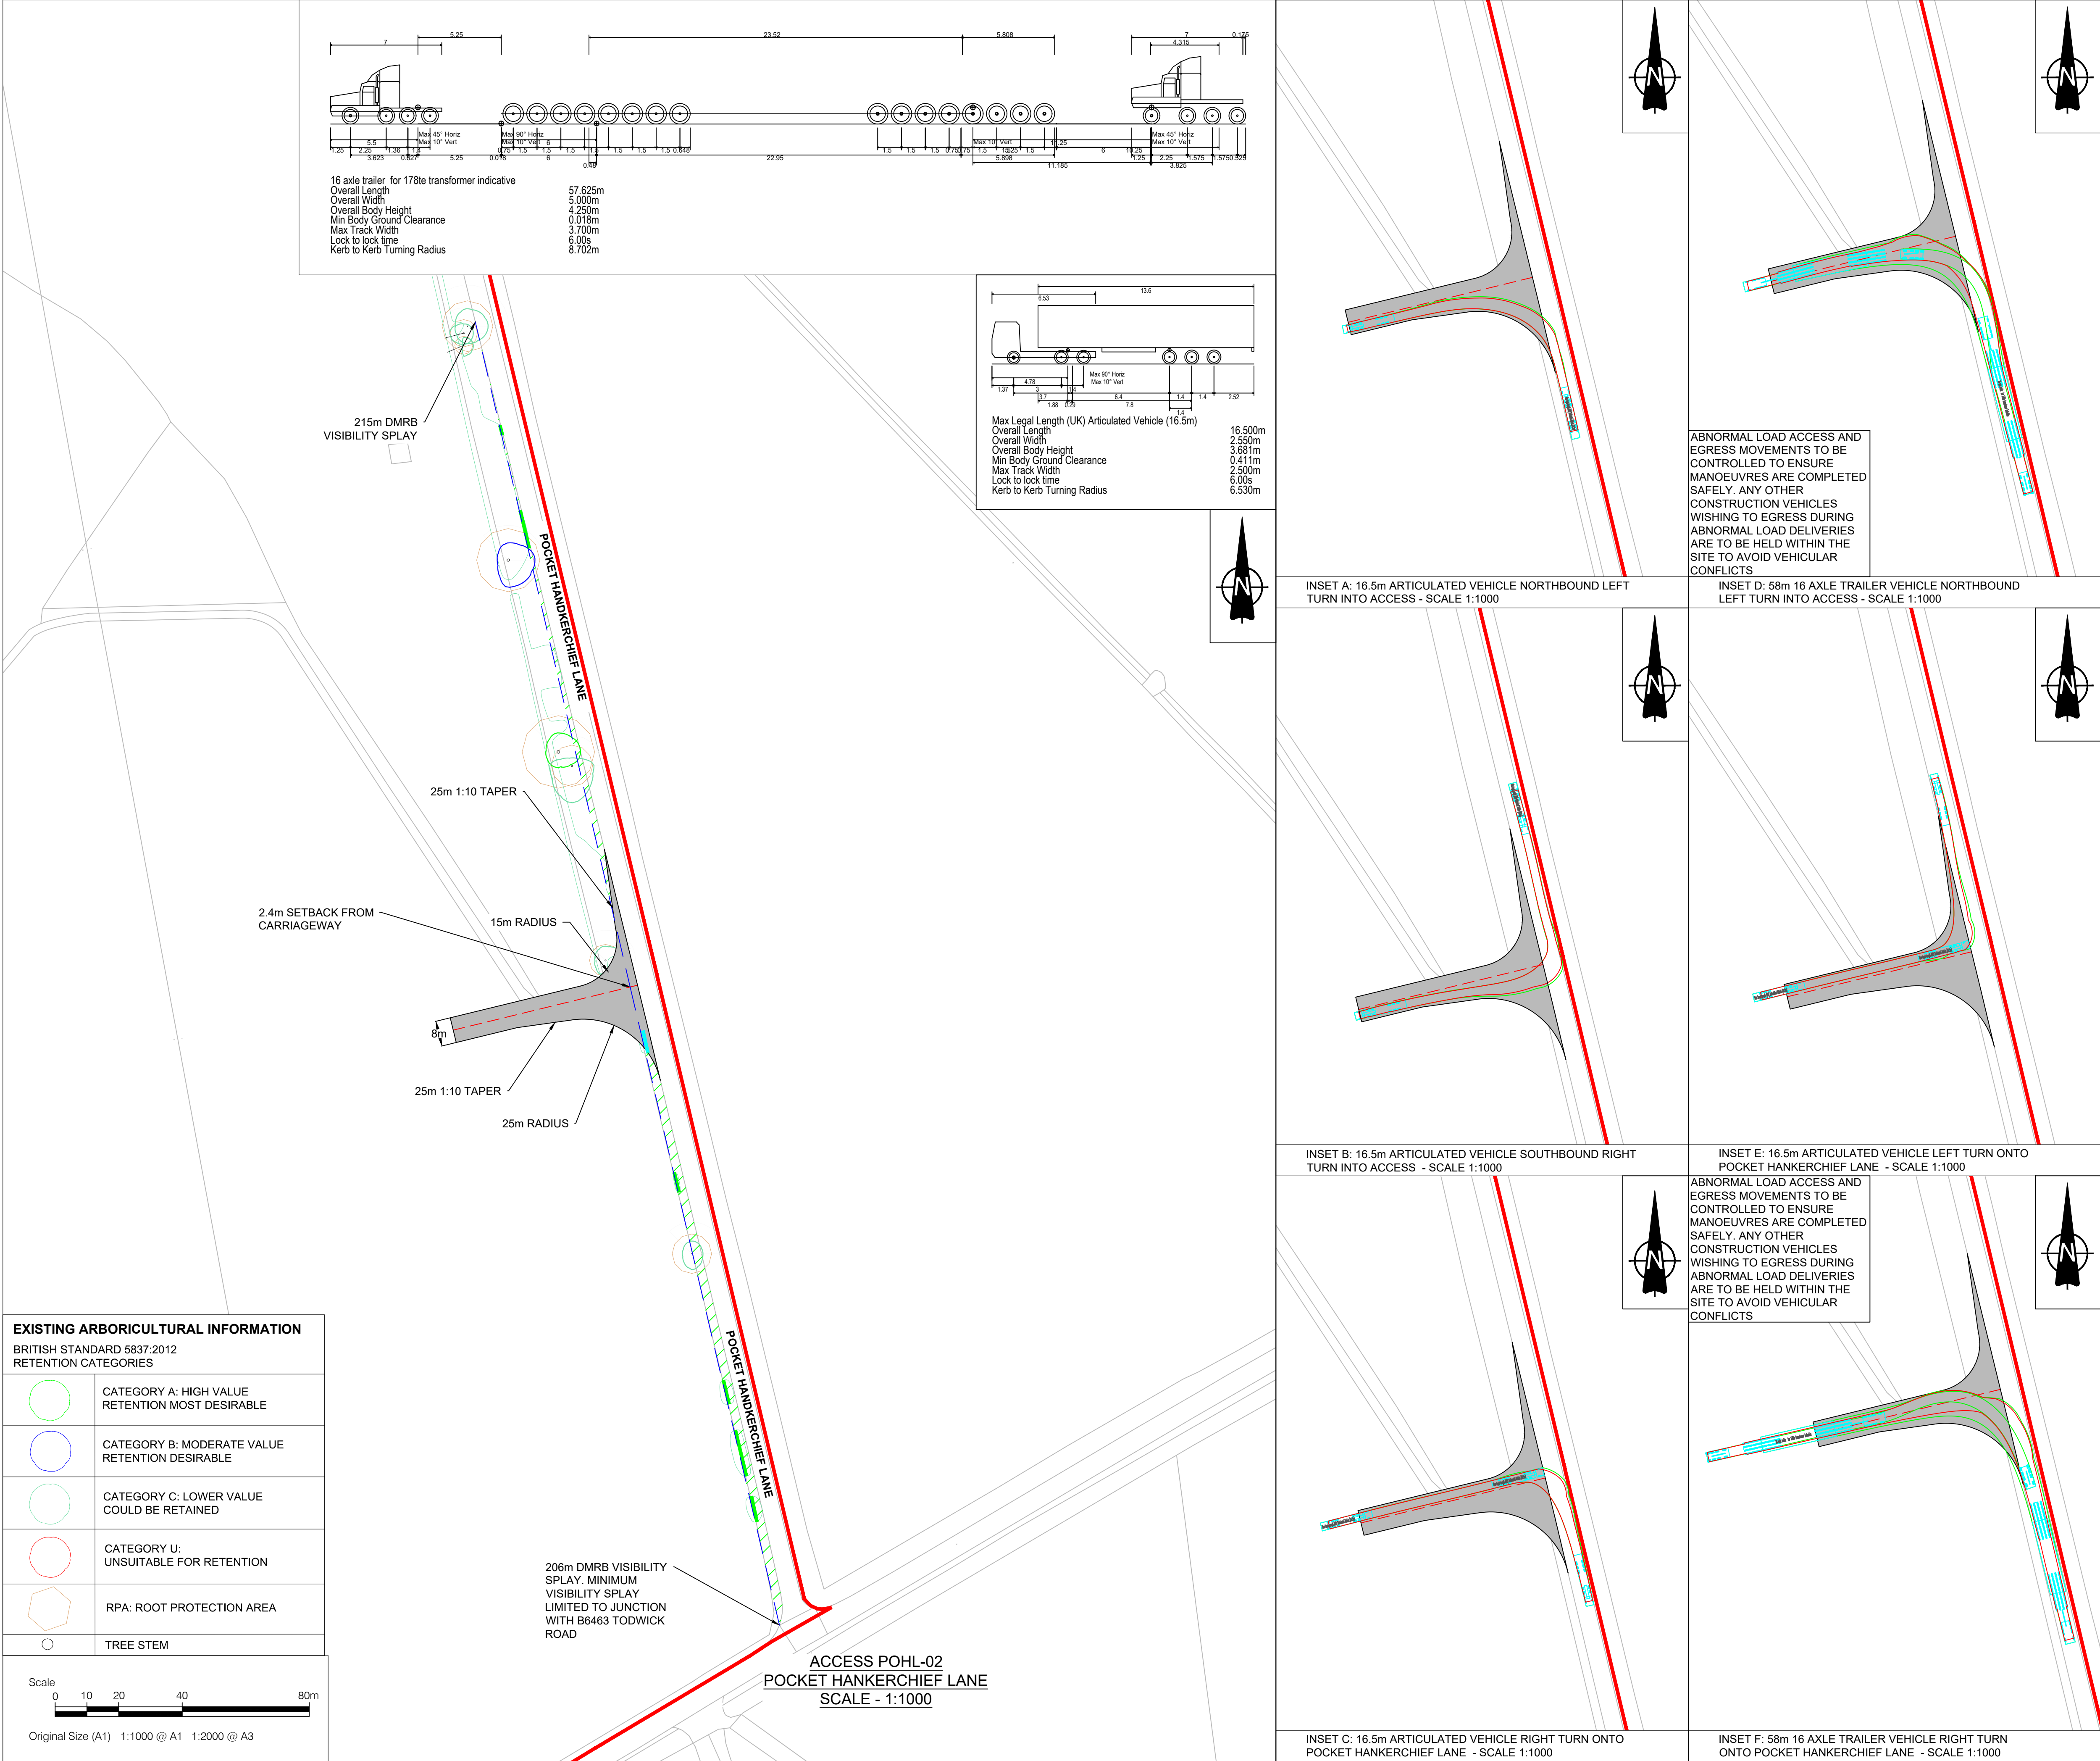



- NOTES**
1. This drawing is to be read in conjunction with all other relevant documentation.
 2. Do not scale from this drawing, use only printed dimensions.
 3. All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
 4. This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
 5. Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
 6. The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
 7. Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
 8. Junction visibility for the access is based upon DMRB CD109 Table 2.10.

- LEGEND**
- Extent of Access Footprint
 - Order Limits
 - Land Excluded from Order Limits
 - Vehicle Body
 - Vehicle Body Path
 - Vehicle Load
 - Vehicle Load Path
 - Vehicle Wheels Path
 - Edge of Road
 - Access Centreline
 - Junction Visibility
 - Vegetation to be Removed for Vis Splay
 - Indicative Hedgerow Removal Vis Splay
 - Indicative Hedgerow Removal for Bellmouth Access
 - Health and Safety Risk Identifier
 - Existing Public Right of Way

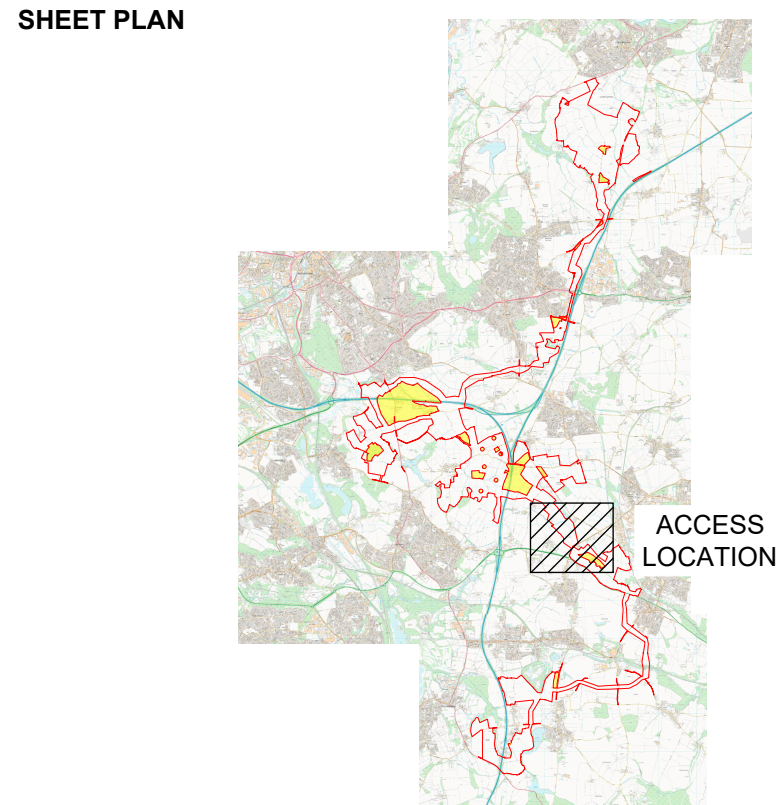


EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012	
RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM



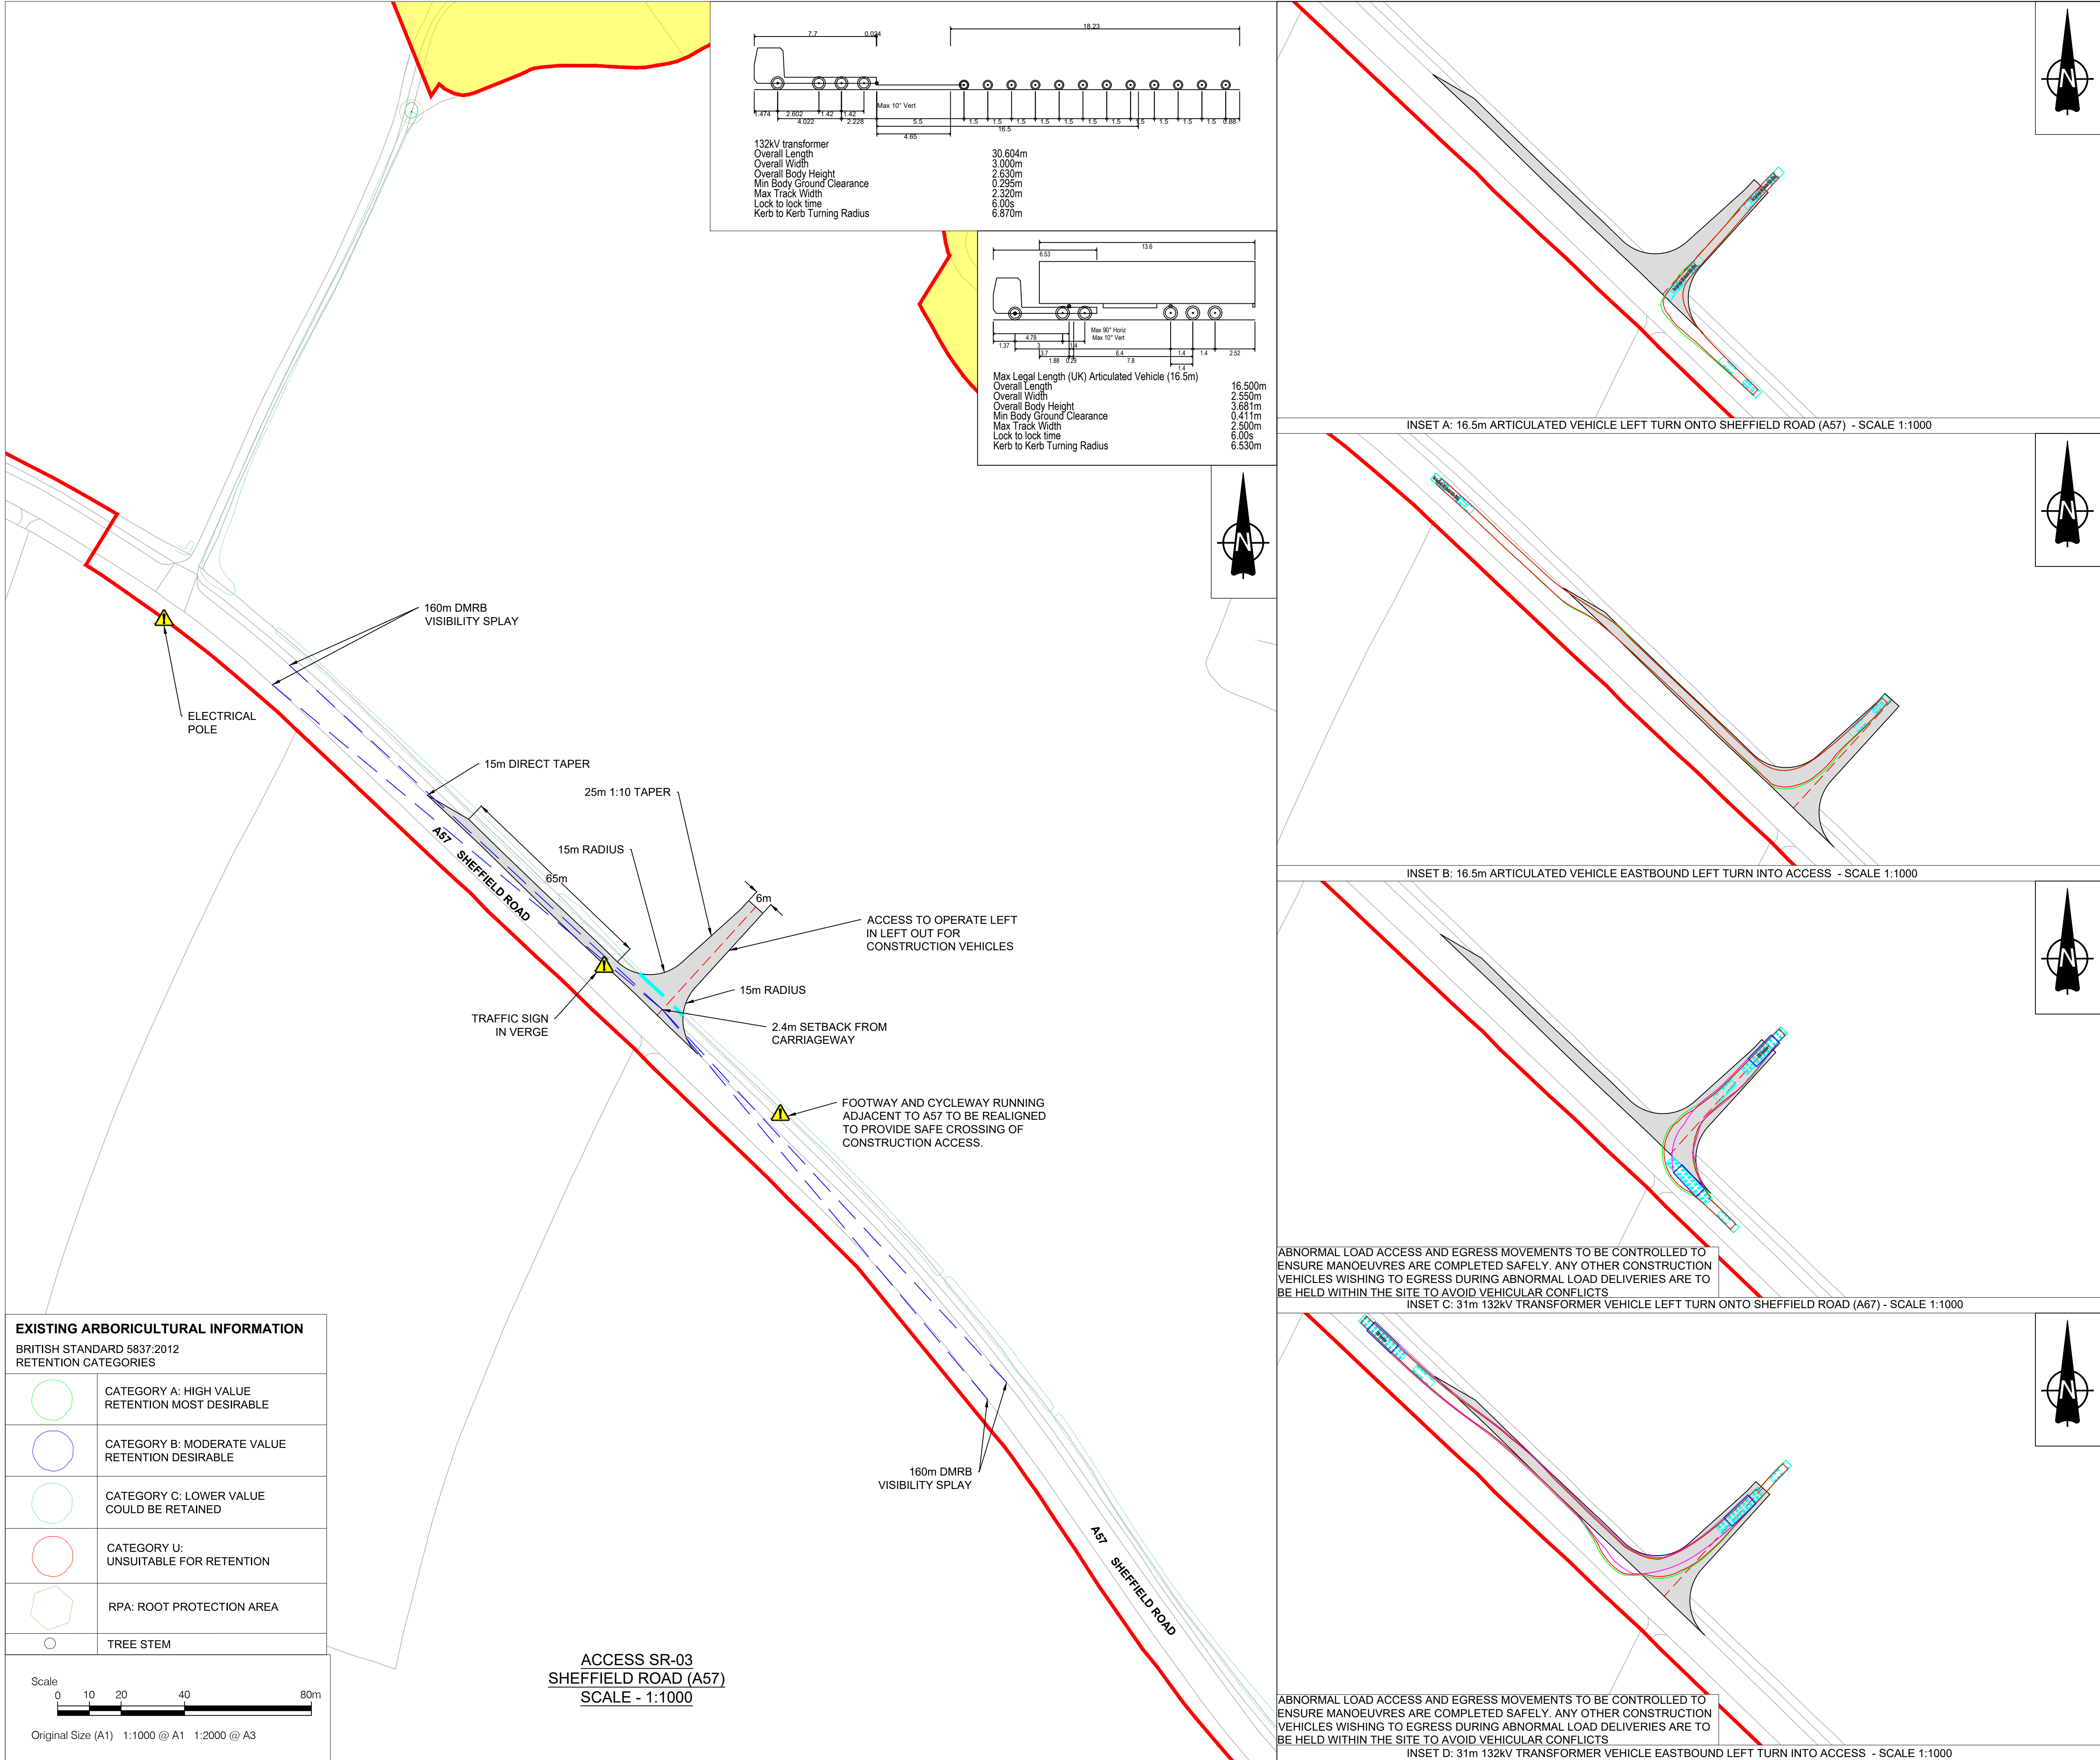


EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012 RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM



Sources: Esri, TomTom, Garmin, FAO, NOAA, USGS, © OpenStreetMap contributors, and the GIS User Community. Reproduced from Ordnance Survey digital map data © Crown copyright 2026. All rights reserved. License number 0000848182

- NOTES**
- This drawing is to be read in conjunction with all other relevant documentation.
 - Do not scale from this drawing, use only printed dimensions.
 - All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
 - This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
 - Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
 - The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
 - Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
 - Junction visibility for the access is based upon DMRB CD109 Table 2.10.

- LEGEND**
- Extent of Access Footprint
 - Order Limits
 - Land Excluded from Order Limits
 - Vehicle Body
 - Vehicle Body Path
 - Vehicle Load
 - Vehicle Load Path
 - Vehicle Wheels Path
 - Edge of Road
 - Access Centreline
 - Junction Visibility
 - Vegetation to be Removed for Vis Splay
 - Indicative Hedgerow Removal Vis Splay
 - Indicative Hedgerow Removal for Bellmouth Access
 - Health and Safety Risk Identifier
 - Existing Public Right of Way

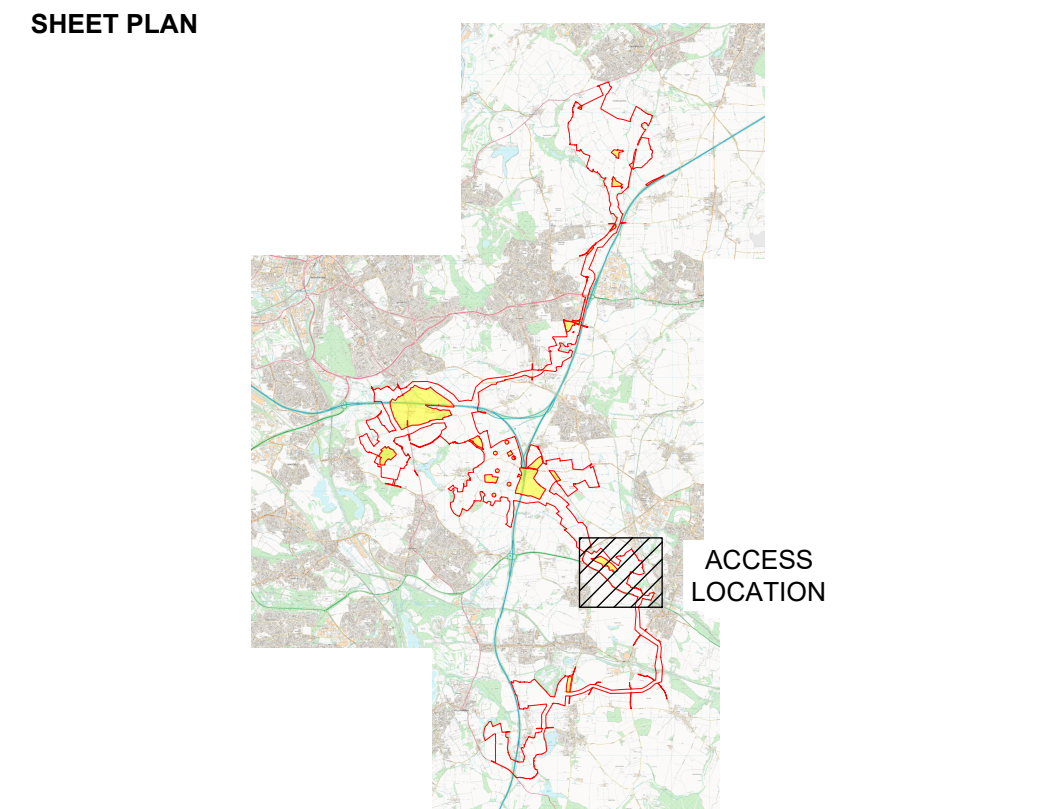

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:
PV Area Access SR-03
Appendix 3 - Sheet 22 of 53
Whitestone Solar Farm
Regulation 5(2)(o)

DRAWING DATE: 03/06/2026

SCALE: 1:1000
SIZE: A1


SHEET: Sheet 22 of 53
REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12


APPLICATION NUMBER: EN0110020



EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012 RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

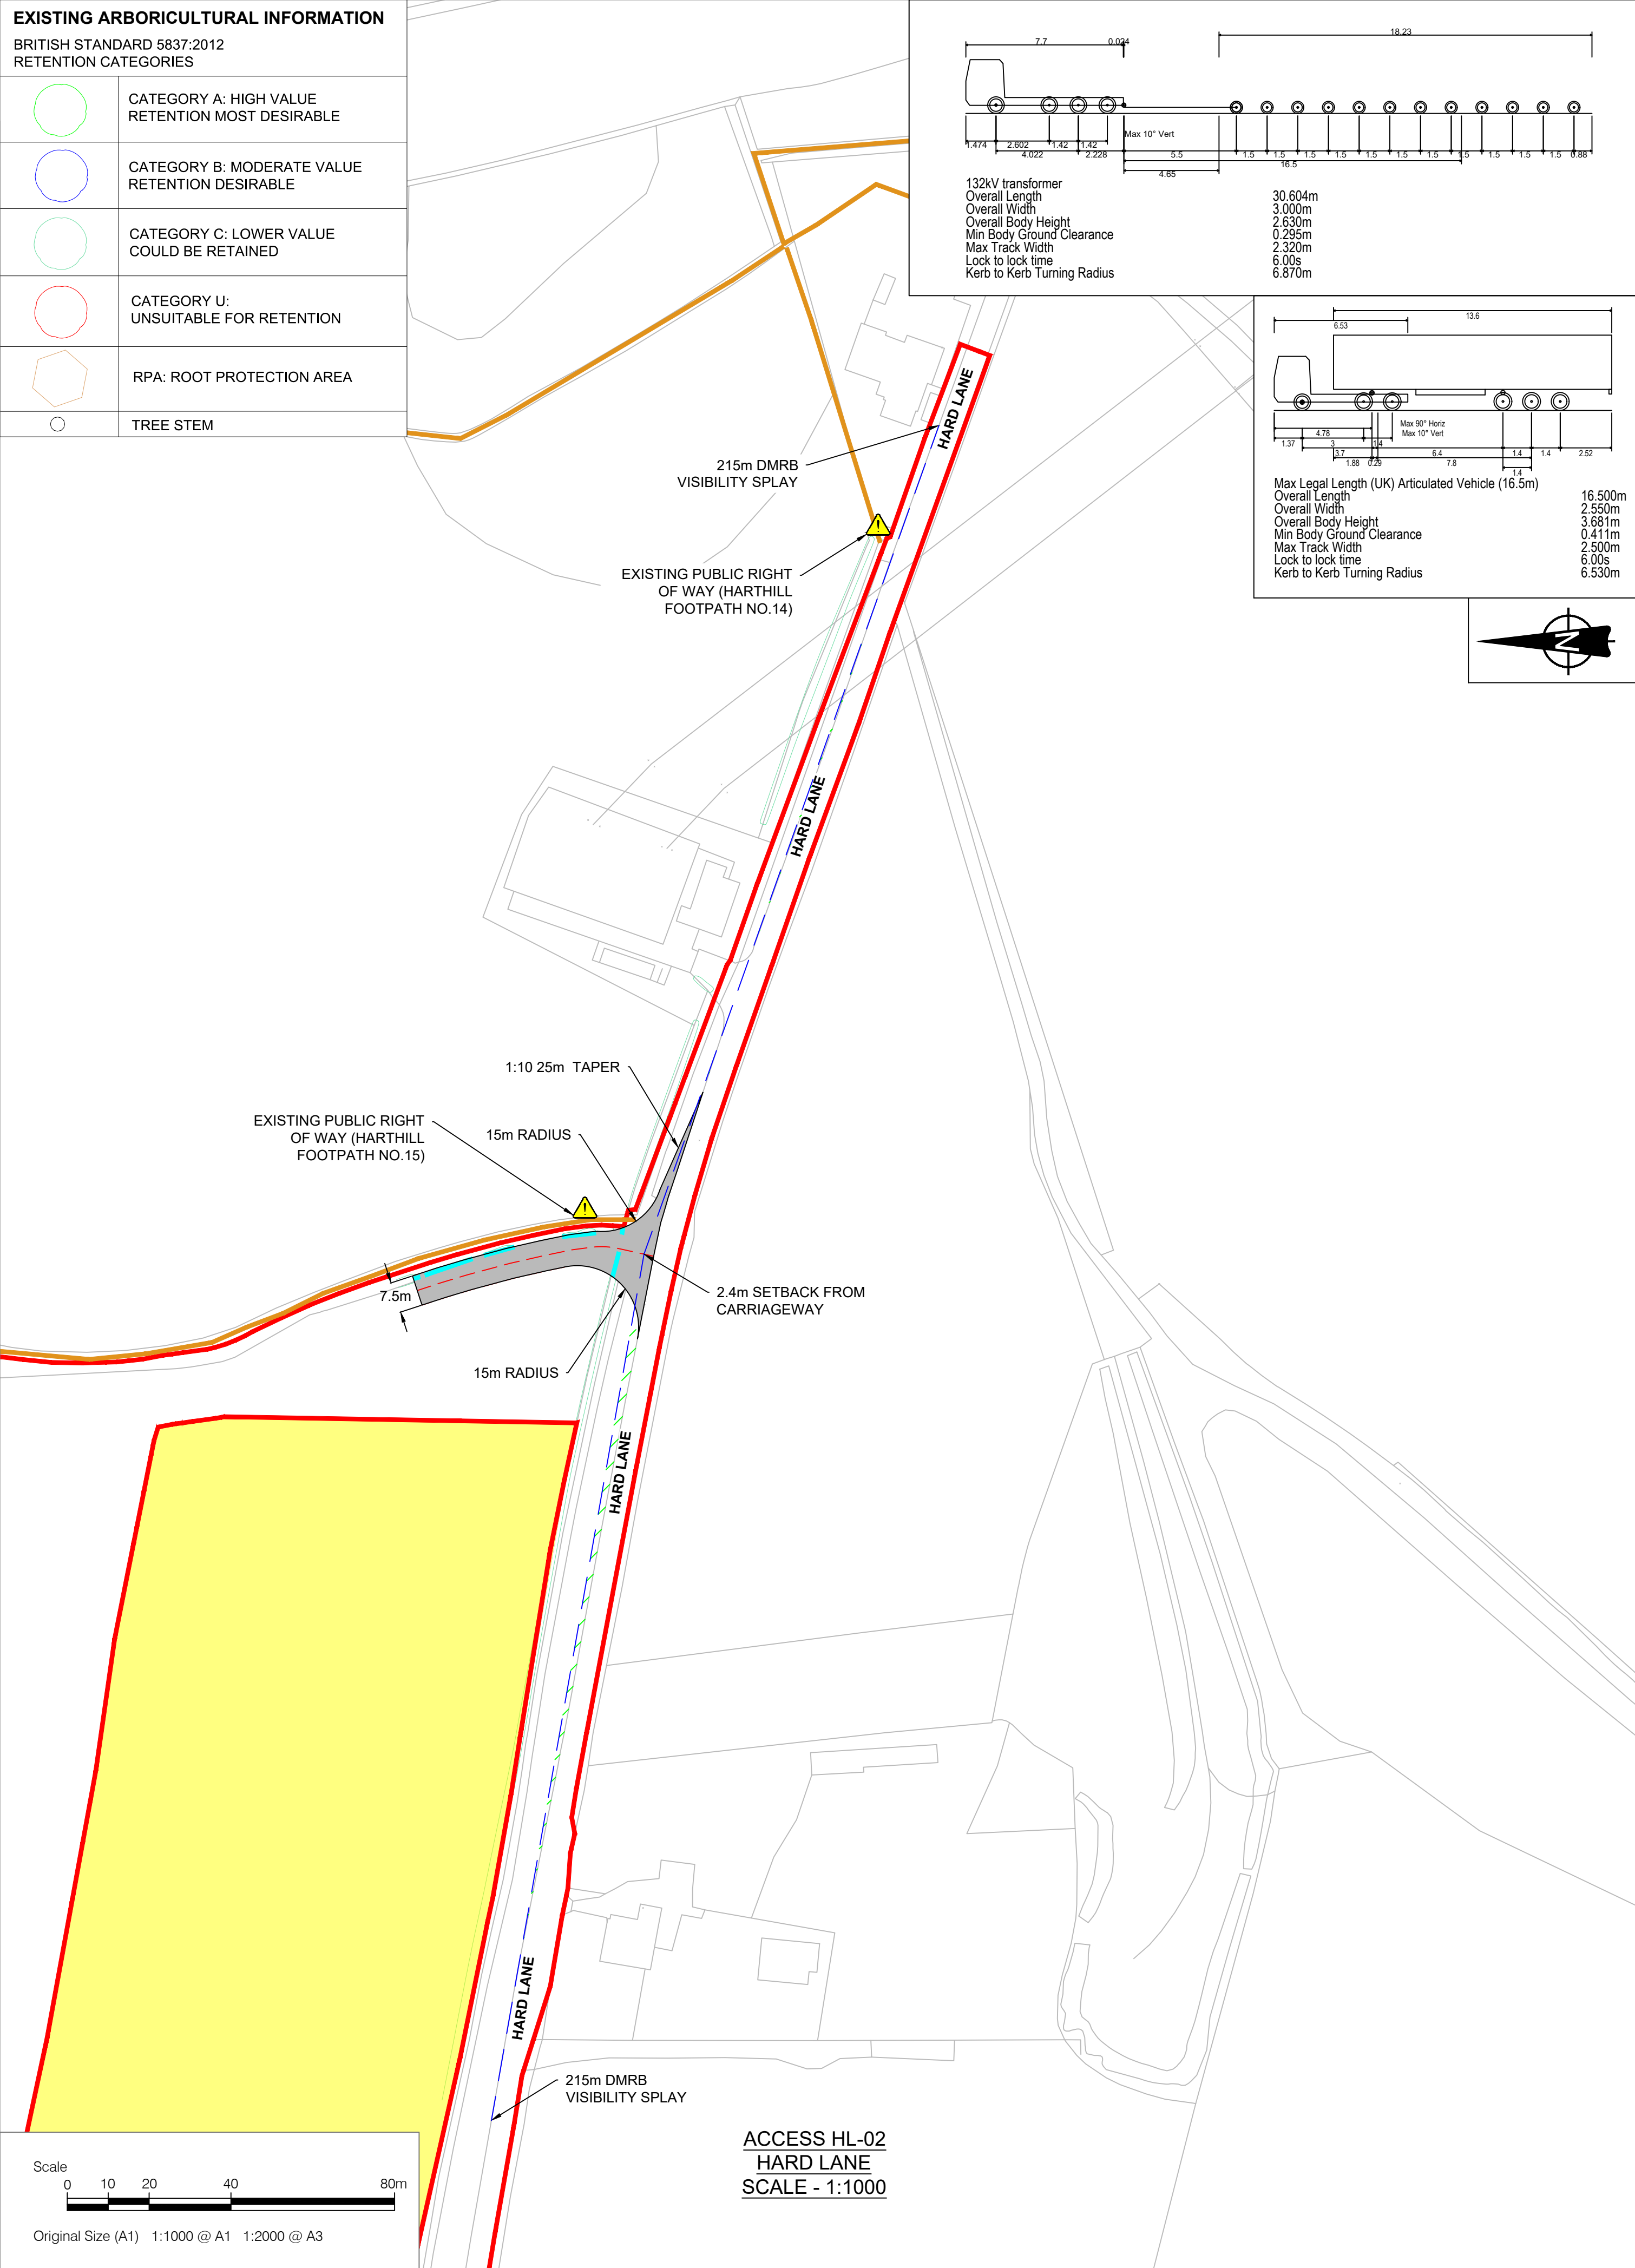


ABNORMAL LOAD ACCESS AND EGRESS MOVEMENTS TO BE CONTROLLED TO ENSURE MANOEUVRES ARE COMPLETED SAFELY. ANY OTHER CONSTRUCTION VEHICLES WISHING TO EGRESS DURING ABNORMAL LOAD DELIVERIES ARE TO BE HELD WITHIN THE SITE TO AVOID VEHICULAR CONFLICTS

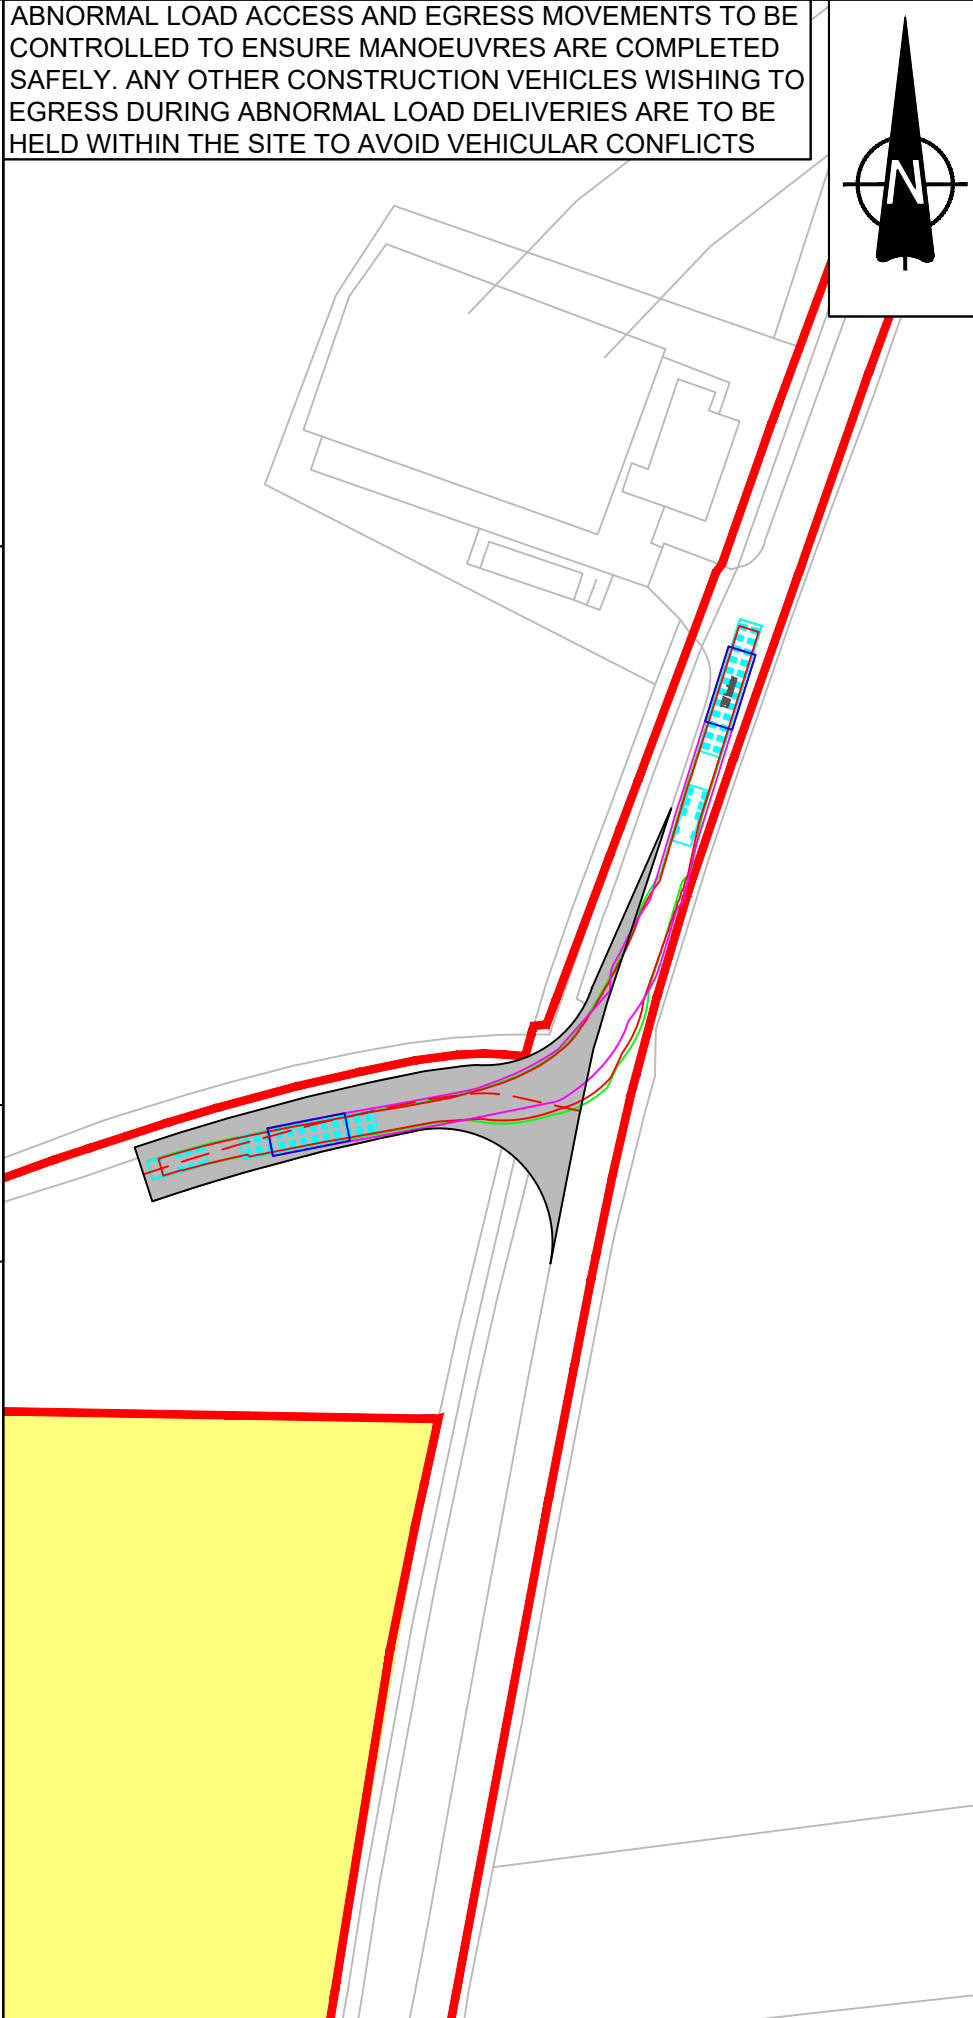


INSET A: 31m 132kV TRANSFORMER VEHICLE SOUTHBOUND RIGHT TURN INTO ACCESS - SCALE 1:1000

ABNORMAL LOAD ACCESS AND EGRESS MOVEMENTS TO BE CONTROLLED TO ENSURE MANOEUVRES ARE COMPLETED SAFELY. ANY OTHER CONSTRUCTION VEHICLES WISHING TO EGRESS DURING ABNORMAL LOAD DELIVERIES ARE TO BE HELD WITHIN THE SITE TO AVOID VEHICULAR CONFLICTS

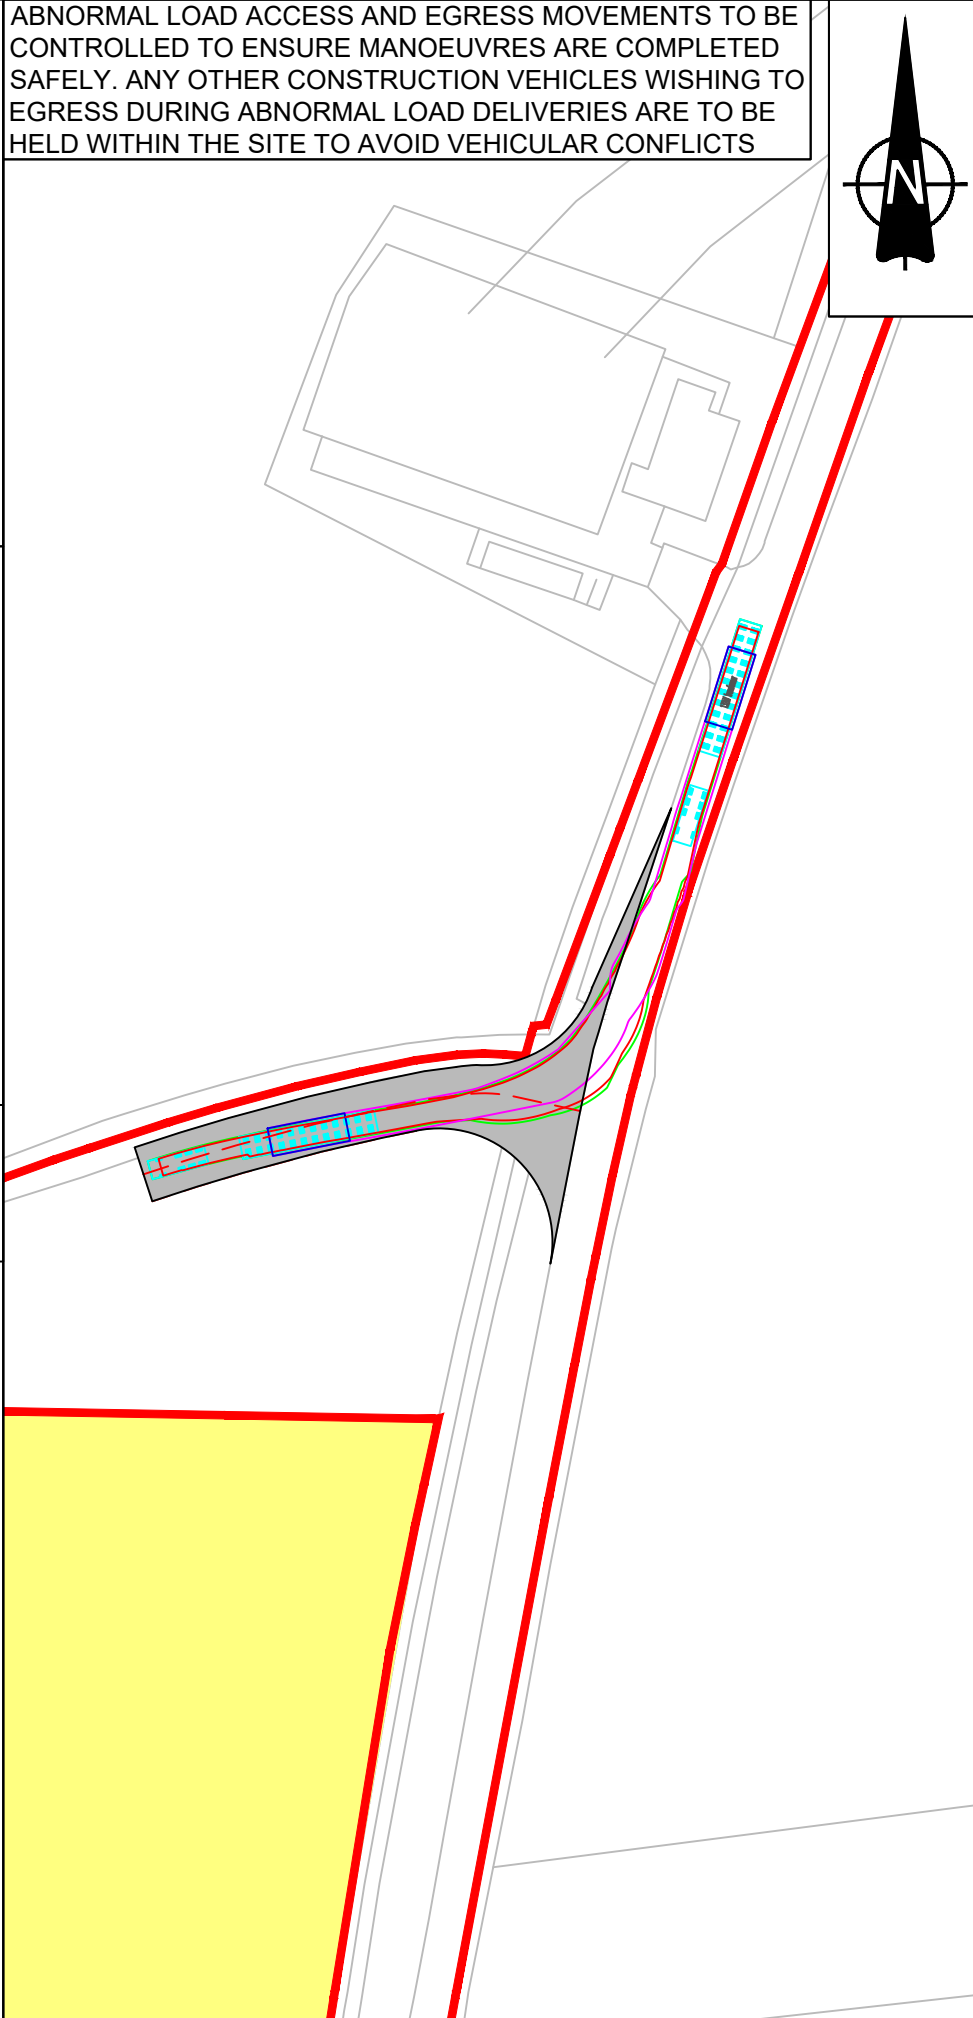


INSET B: 31m 132kV TRANSFORMER VEHICLE LEFT TURN ONTO HARD LANE - SCALE 1:1000

ABNORMAL LOAD ACCESS AND EGRESS MOVEMENTS TO BE CONTROLLED TO ENSURE MANOEUVRES ARE COMPLETED SAFELY. ANY OTHER CONSTRUCTION VEHICLES WISHING TO EGRESS DURING ABNORMAL LOAD DELIVERIES ARE TO BE HELD WITHIN THE SITE TO AVOID VEHICULAR CONFLICTS

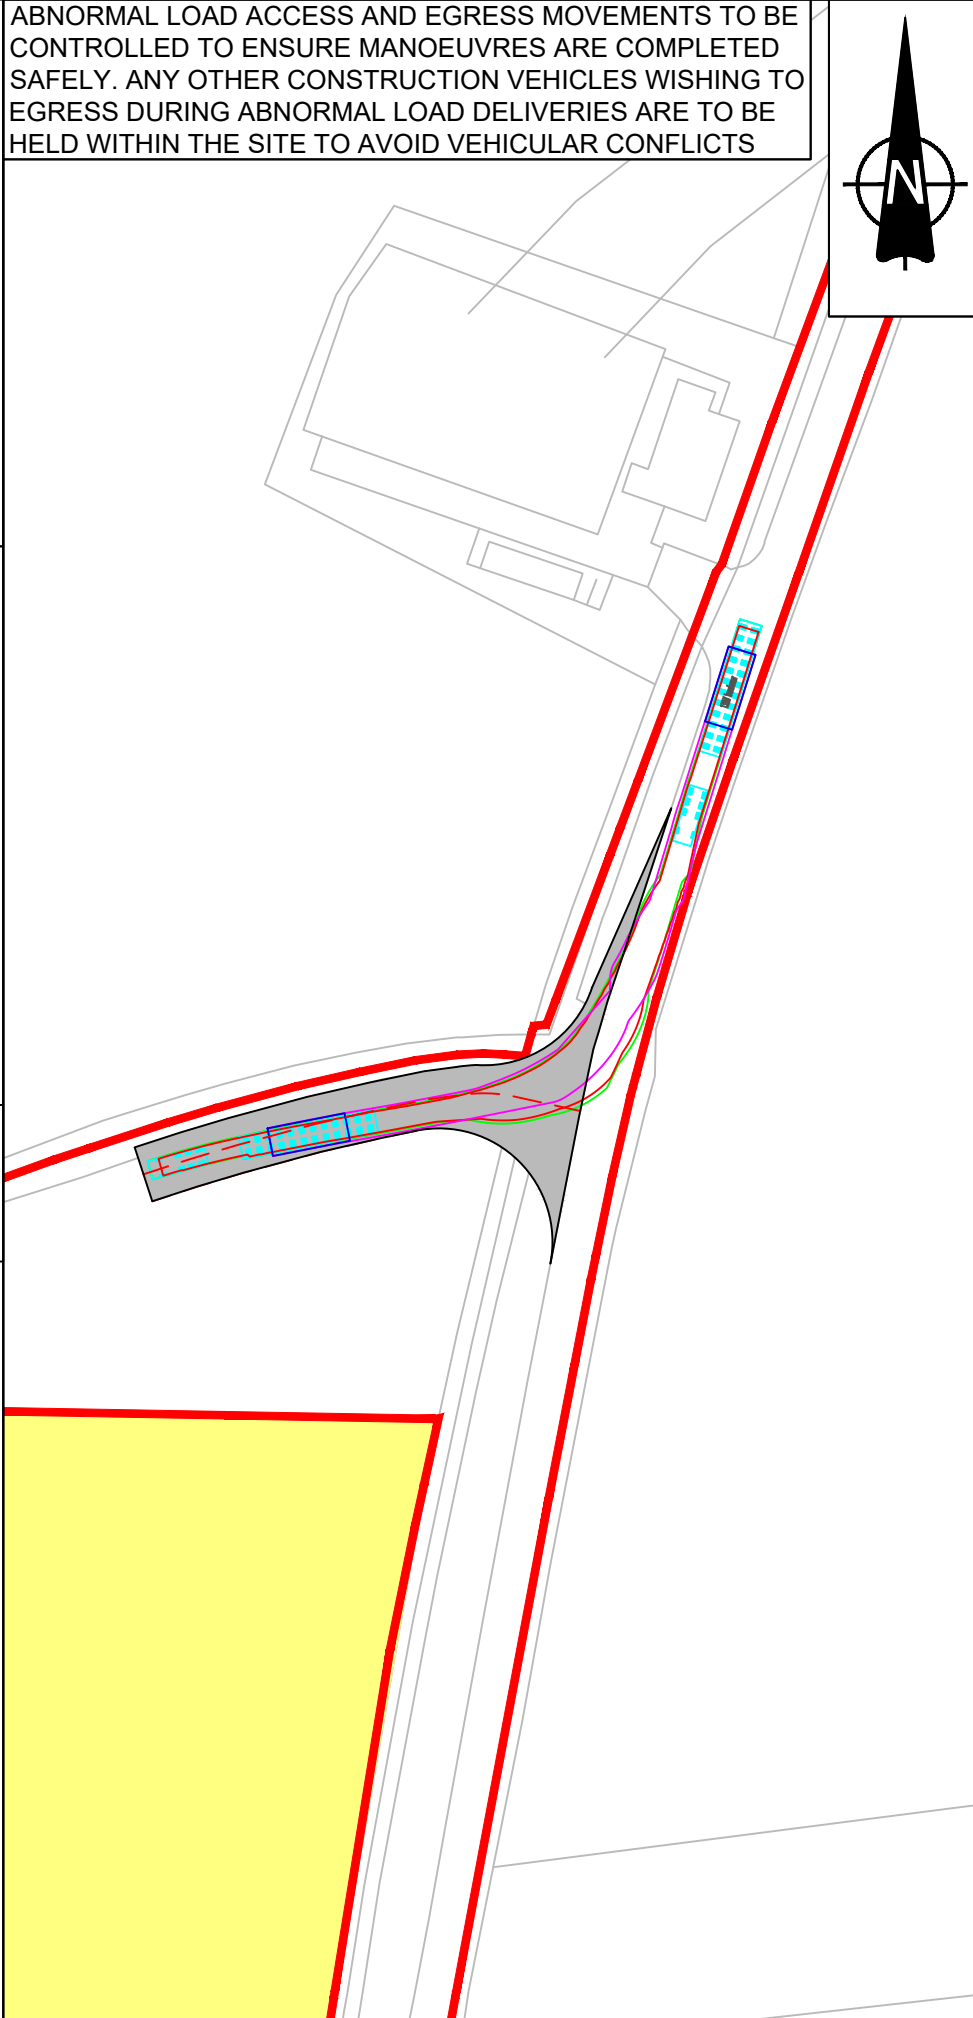

INSET C: 16.5m ARTICULATED VEHICLE LEFT TURN ONTO HARD LANE - SCALE 1:1000

ABNORMAL LOAD ACCESS AND EGRESS MOVEMENTS TO BE CONTROLLED TO ENSURE MANOEUVRES ARE COMPLETED SAFELY. ANY OTHER CONSTRUCTION VEHICLES WISHING TO EGRESS DURING ABNORMAL LOAD DELIVERIES ARE TO BE HELD WITHIN THE SITE TO AVOID VEHICULAR CONFLICTS

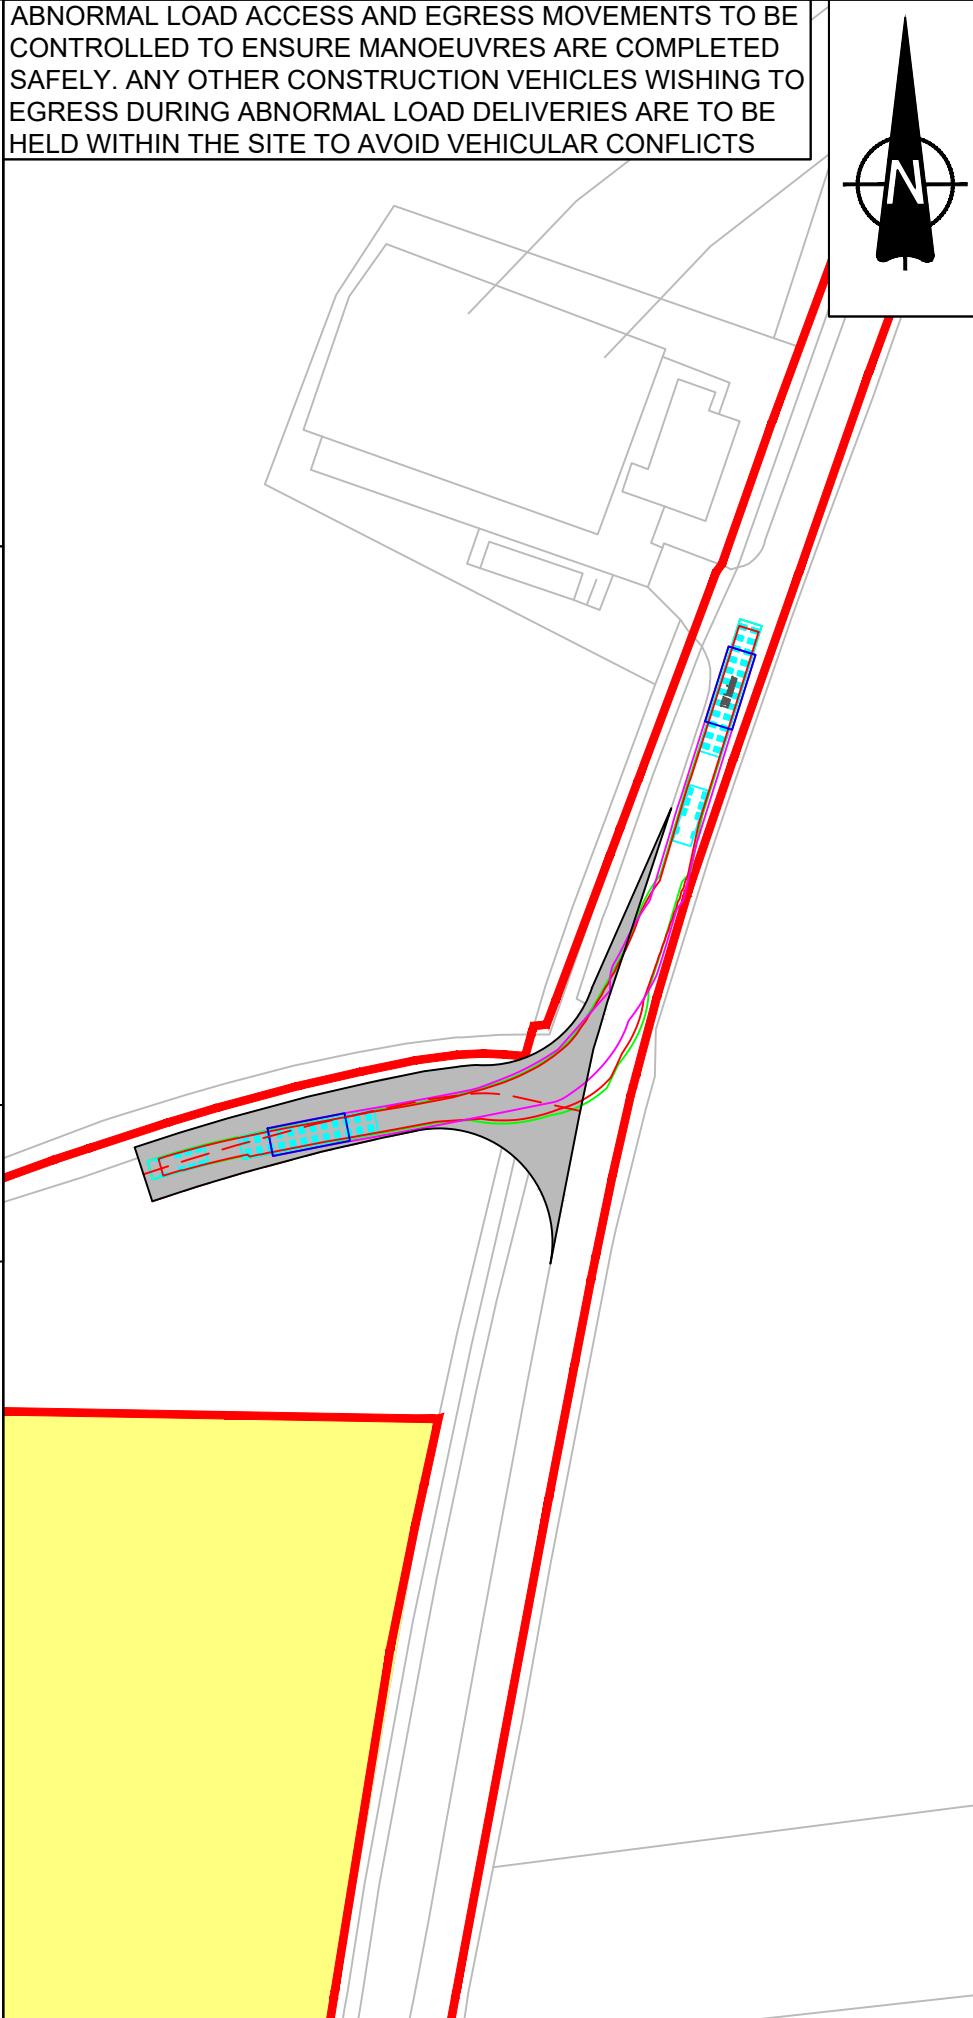

INSET D: 16.5m ARTICULATED VEHICLE SOUTHBOUND RIGHT TURN INTO ACCESS - SCALE 1:1000


NOTES

- This drawing is to be read in conjunction with all other relevant documentation.
- Do not scale from this drawing, use only printed dimensions.
- All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
- This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
- Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
- The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
- Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
- Junction visibility for the access is based upon DMRB CD109 Table 2.10.

LEGEND

- Extent of Access Footprint
- Order Limits
- Land Excluded from Order Limits
- Vehicle Body
- Vehicle Body Path
- Vehicle Load
- Vehicle Load Path
- Vehicle Wheels Path
- Edge of Road
- Access Centreline
- Junction Visibility
- Vegetation to be Removed for Vis Splay
- Indicative Hedgerow Removal Vis Splay
- Indicative Hedgerow Removal for Bellmouth Access
- Health and Safety Risk Identifier
- Existing Public Right of Way

SHEET PLAN

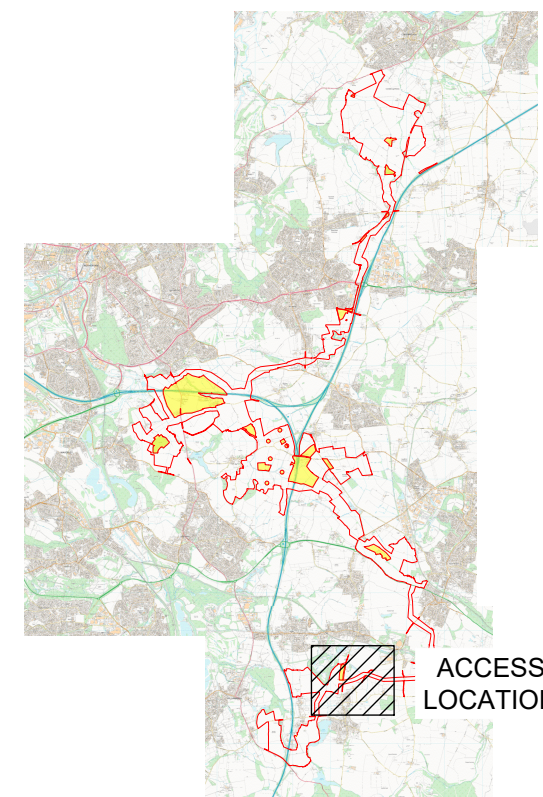

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:

PV Area Access HL-02
Appendix 3 - Sheet 23 of 53
Whitestone Solar Farm
Regulation 5(2)(o)

DRAWING DATE: 03/06/2026

SCALE: 1:1000

SIZE: A1




SHEET: Sheet 23 of 53

REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020



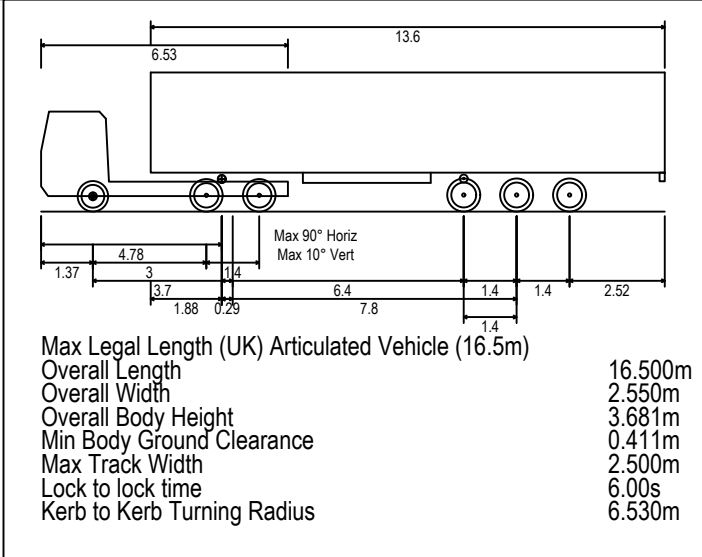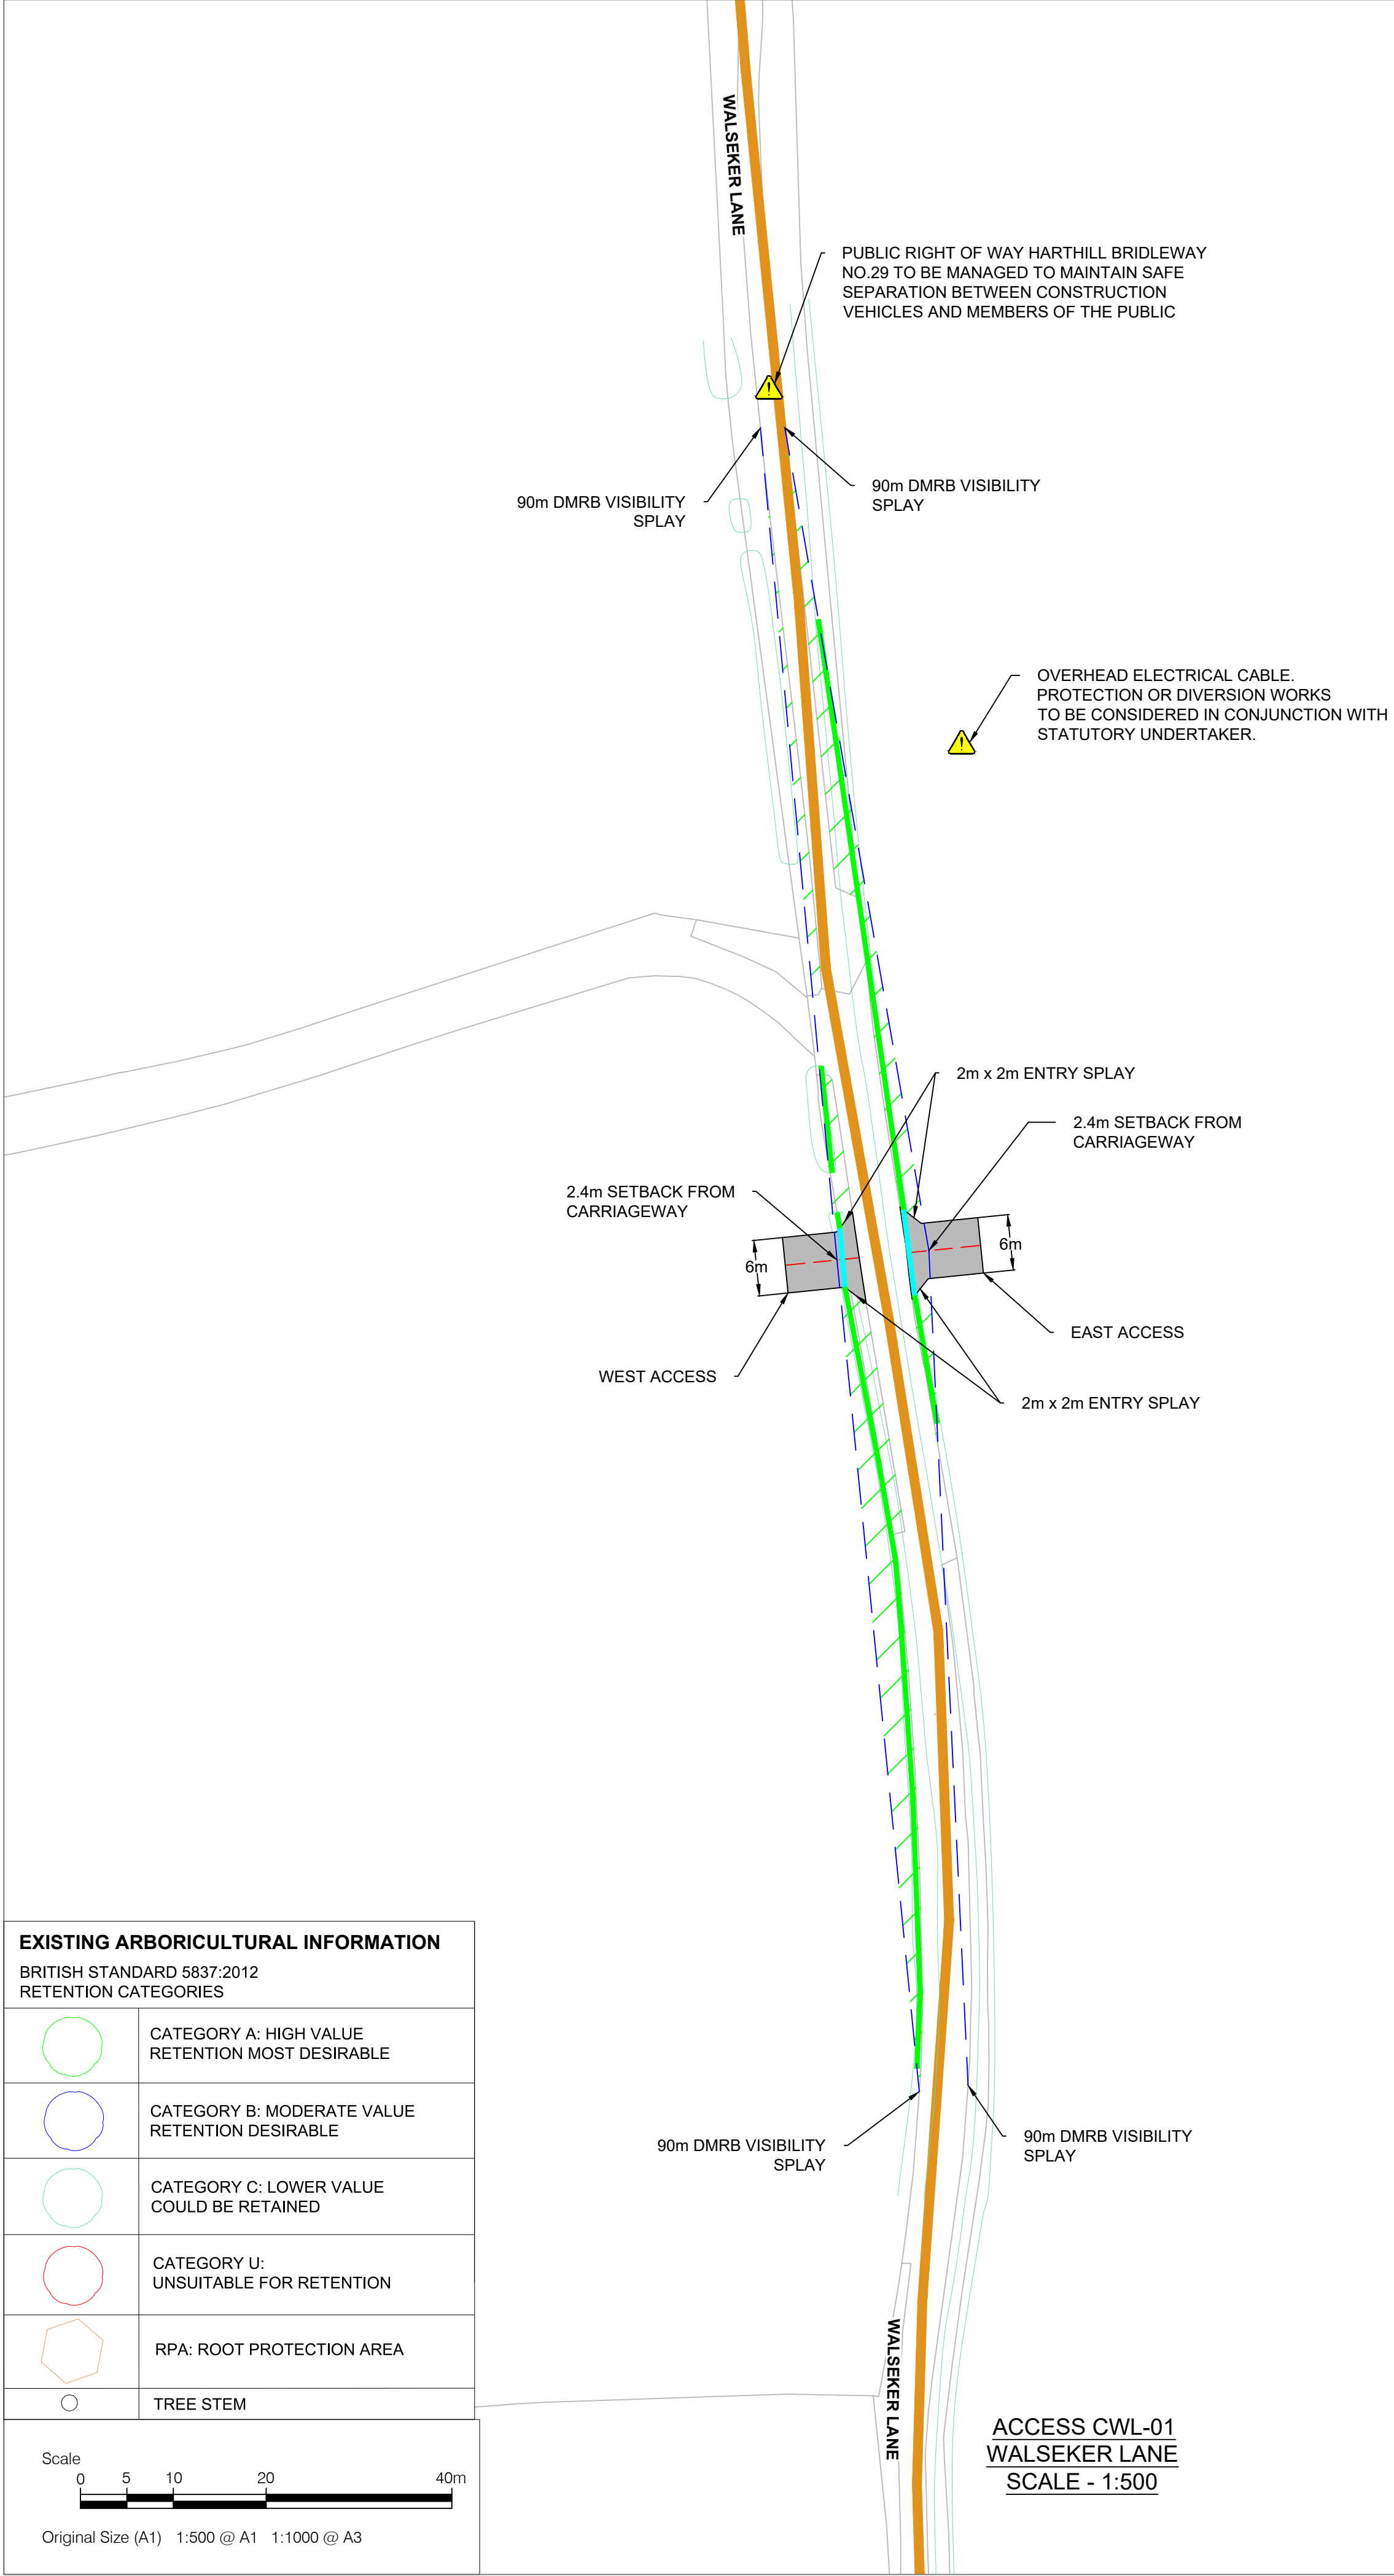

INSET A: 16.5m ARTICULATED VEHICLE HEADING WEST ACROSS WALSEKER LANE - SCALE 1:500

INSET B: 16.5m ARTICULATED VEHICLE HEADING EAST ACROSS WALSEKER LANE - SCALE 1:500




NOTES

1. This drawing is to be read in conjunction with all other relevant documentation.
2. Do not scale from this drawing, use only printed dimensions.
3. All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
4. This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
5. Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
6. The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
7. Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
8. Junction visibility for the access is based upon DMRB CD109 Table 2.10.

LEGEND


- Extent of Access Footprint
- Order Limits
- Land Excluded from Order Limits
- Vehicle Body
- Vehicle Body Path
- Vehicle Load
- Vehicle Load Path
- Vehicle Wheels Path
- Edge of Road
- Access Centreline
- Junction Visibility
- Vegetation to be Removed for Vis Splay
- Indicative Hedgerow Removal Vis Splay
- Indicative Hedgerow Removal for Bellmouth Access
- Health and Safety Risk Identifier
- Existing Public Right of Way

SHEET PLAN

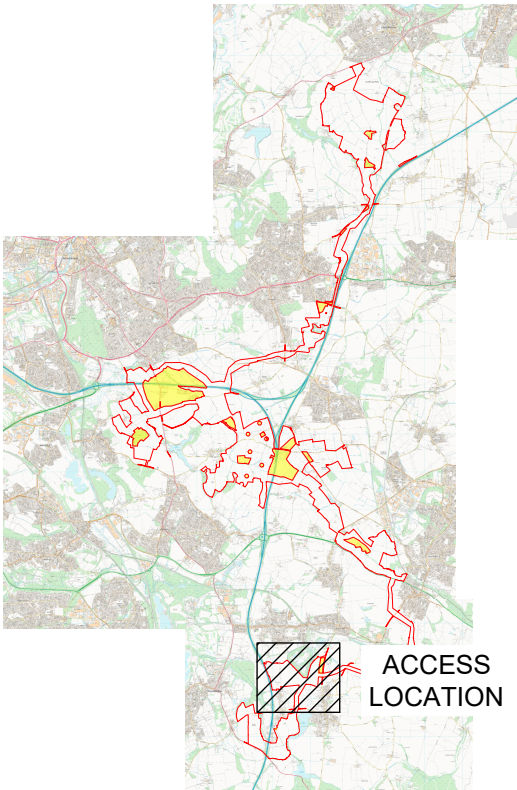

EXISTING ARBORICULTURAL INFORMATION
BRITISH STANDARD 5837:2012
RETENTION CATEGORIES

	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM



TITLE:

PV Area Access CWL-01
Appendix 3 - Sheet 24 of 53
Whitestone Solar Farm
Regulation 5(2)(o)

DRAWING DATE: 03/06/2026

SCALE: 1:500

SIZE: A1


SHEET: Sheet 24 of 53

REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020



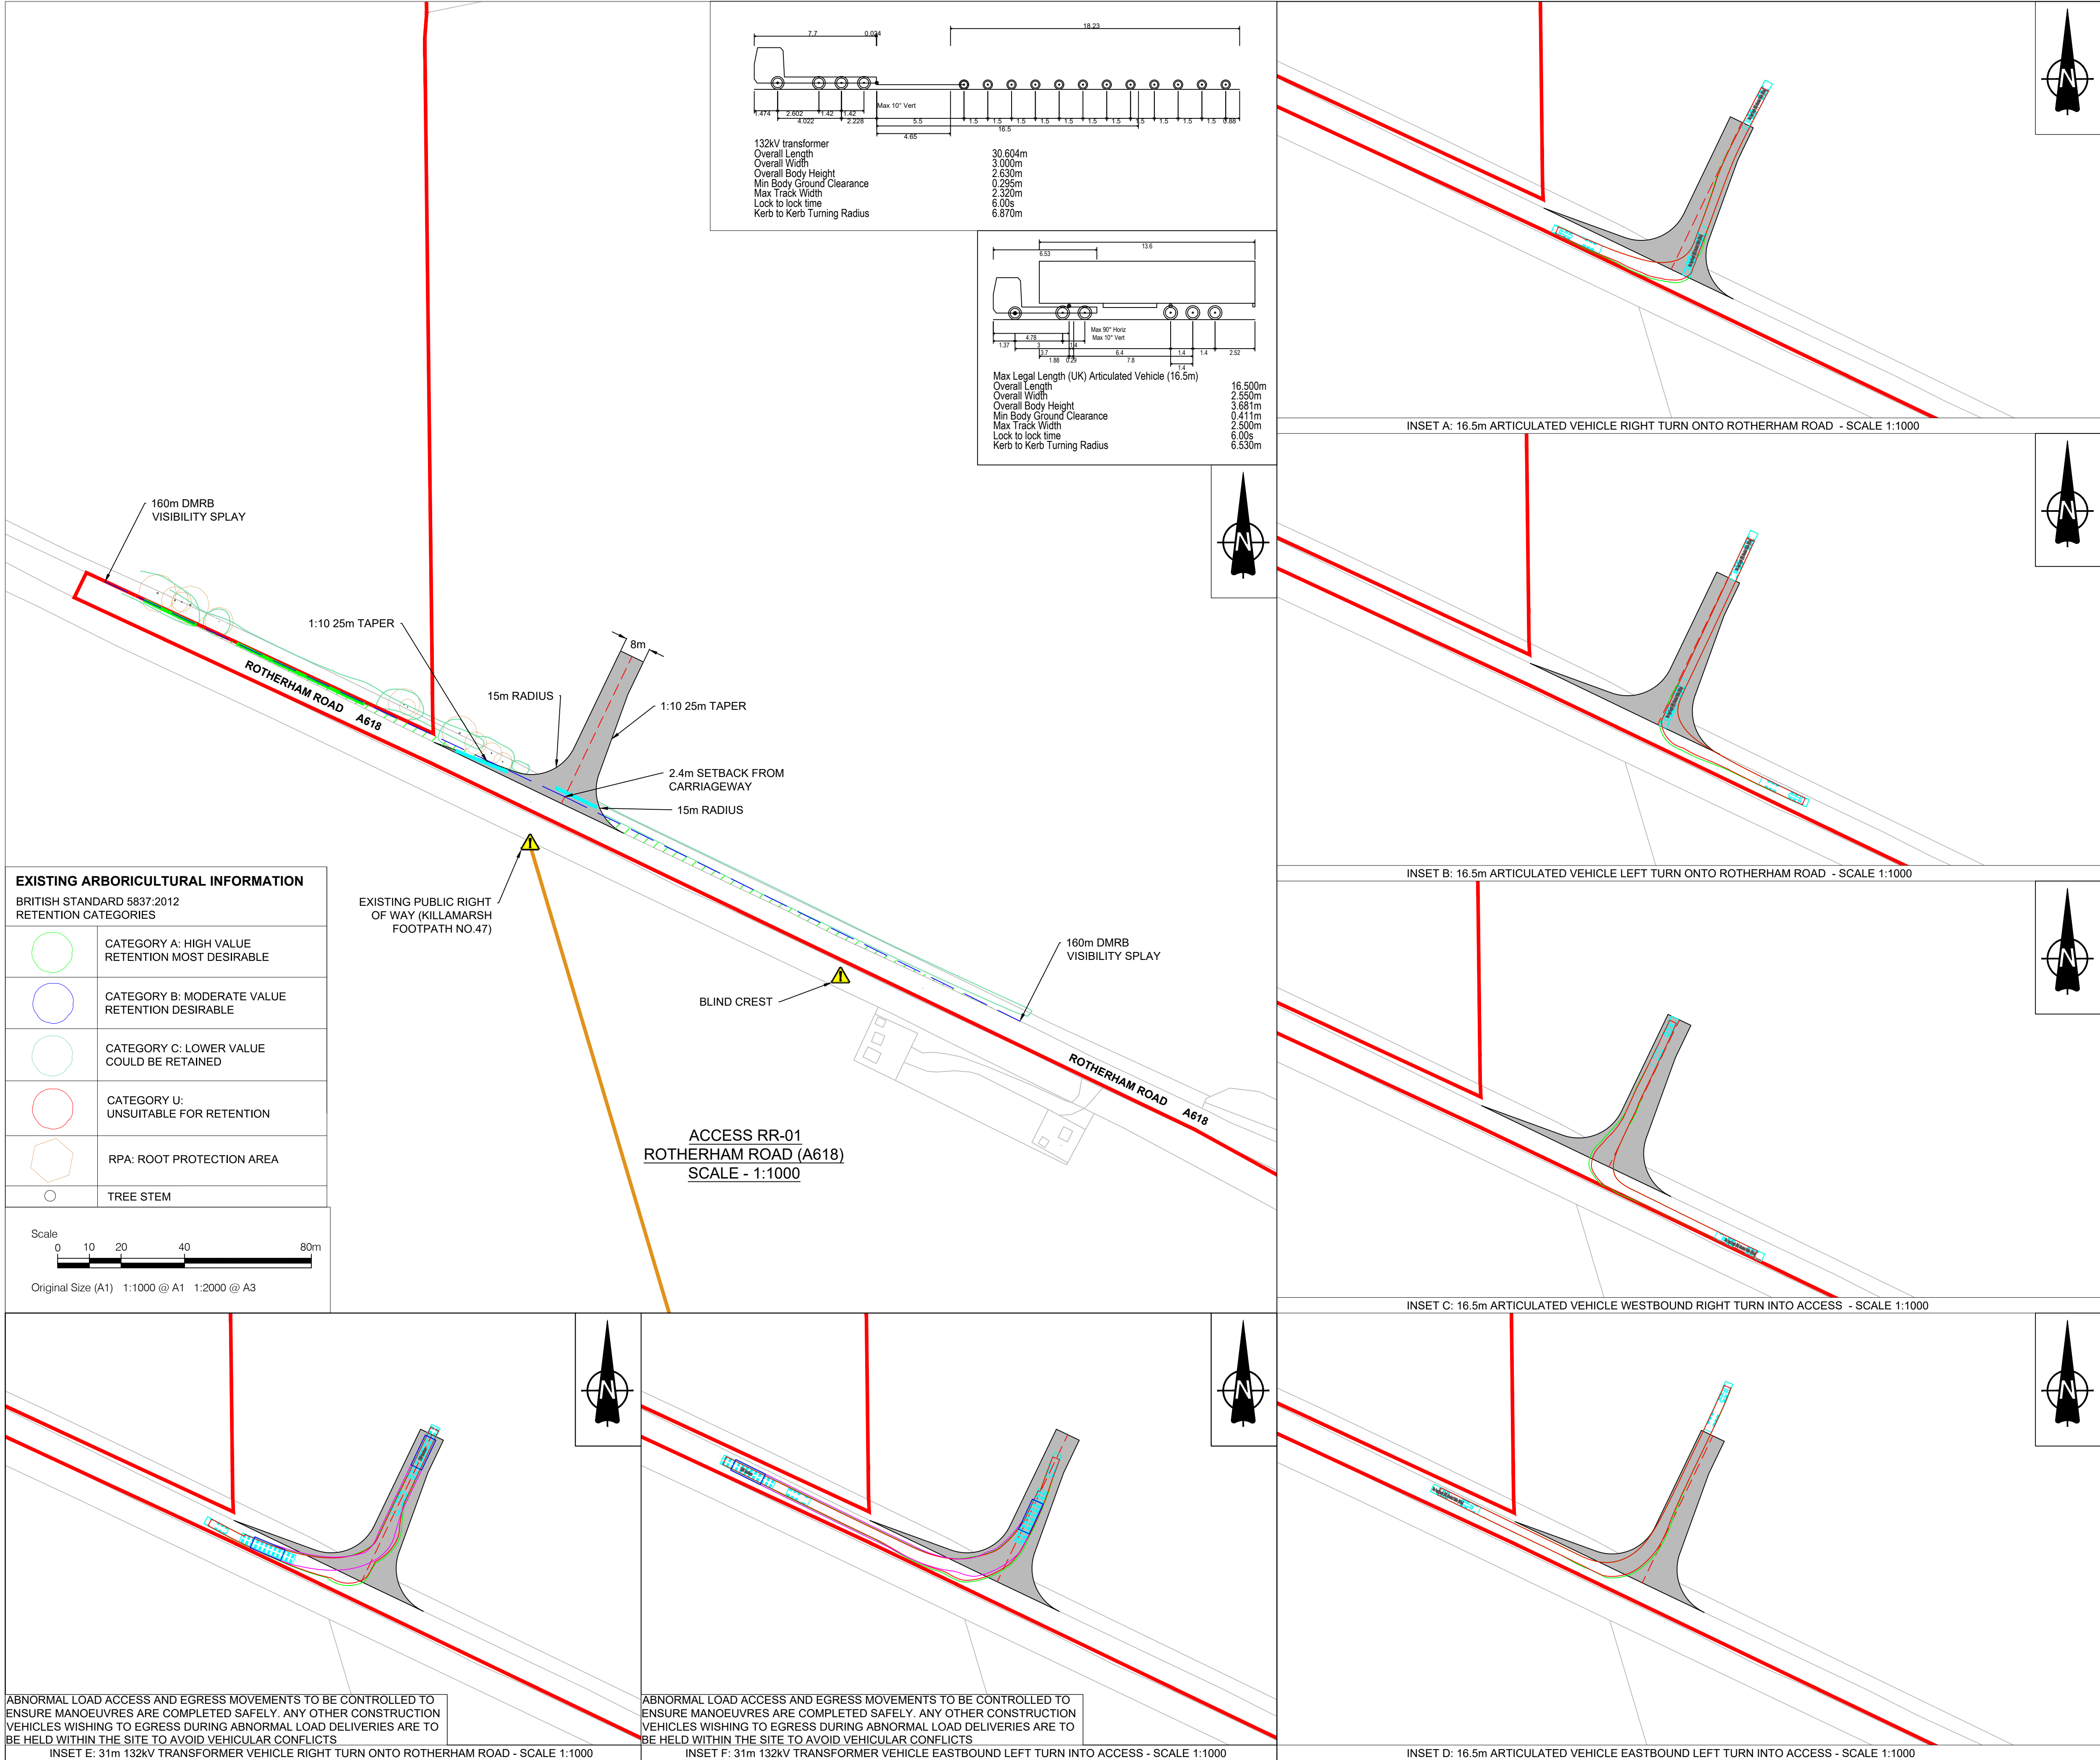

EXISTING ARBORICULTURAL INFORMATION

BRITISH STANDARD 5837:2012

RETENTION CATEGORIES

	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

Scale

0

10

20

40

80m

Original Size (A1) 1:1000 @ A1 1:2000 @ A3

NOTES

1.

This drawing is to be read in conjunction with all other relevant documentation.

2.

Do not scale from this drawing, use only printed dimensions.

3.

All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.

4.

This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.

5.

Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.

6.

The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.

7.

Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.

8.

Junction visibility for the access is based upon DMRB CD109 Table 2.10.

LEGEND

Extent of Access Footprint

Order Limits

Land Excluded from Order Limits

Vehicle Body

Vehicle Body Path

Vehicle Load

Vehicle Load Path

Vehicle Wheels Path

Edge of Road

Access Centreline

Junction Visibility

Vegetation to be Removed for Vis Splay

Indicative Hedgerow Removal Vis Splay

Indicative Hedgerow Removal for Bellmouth Access

Health and Safety Risk Identifier

Existing Public Right of Way

SHEET PLAN

ACCESS LOCATION

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:

PV Area Access RR-01

Appendix 3 - Sheet 26 of 53

Whitestone Solar Farm

Regulation 5(2)(o)

DRAWING DATE: 03/06/2026

SCALE: 1:1000



SIZE: A1

SHEET: Sheet 26 of 53

REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020

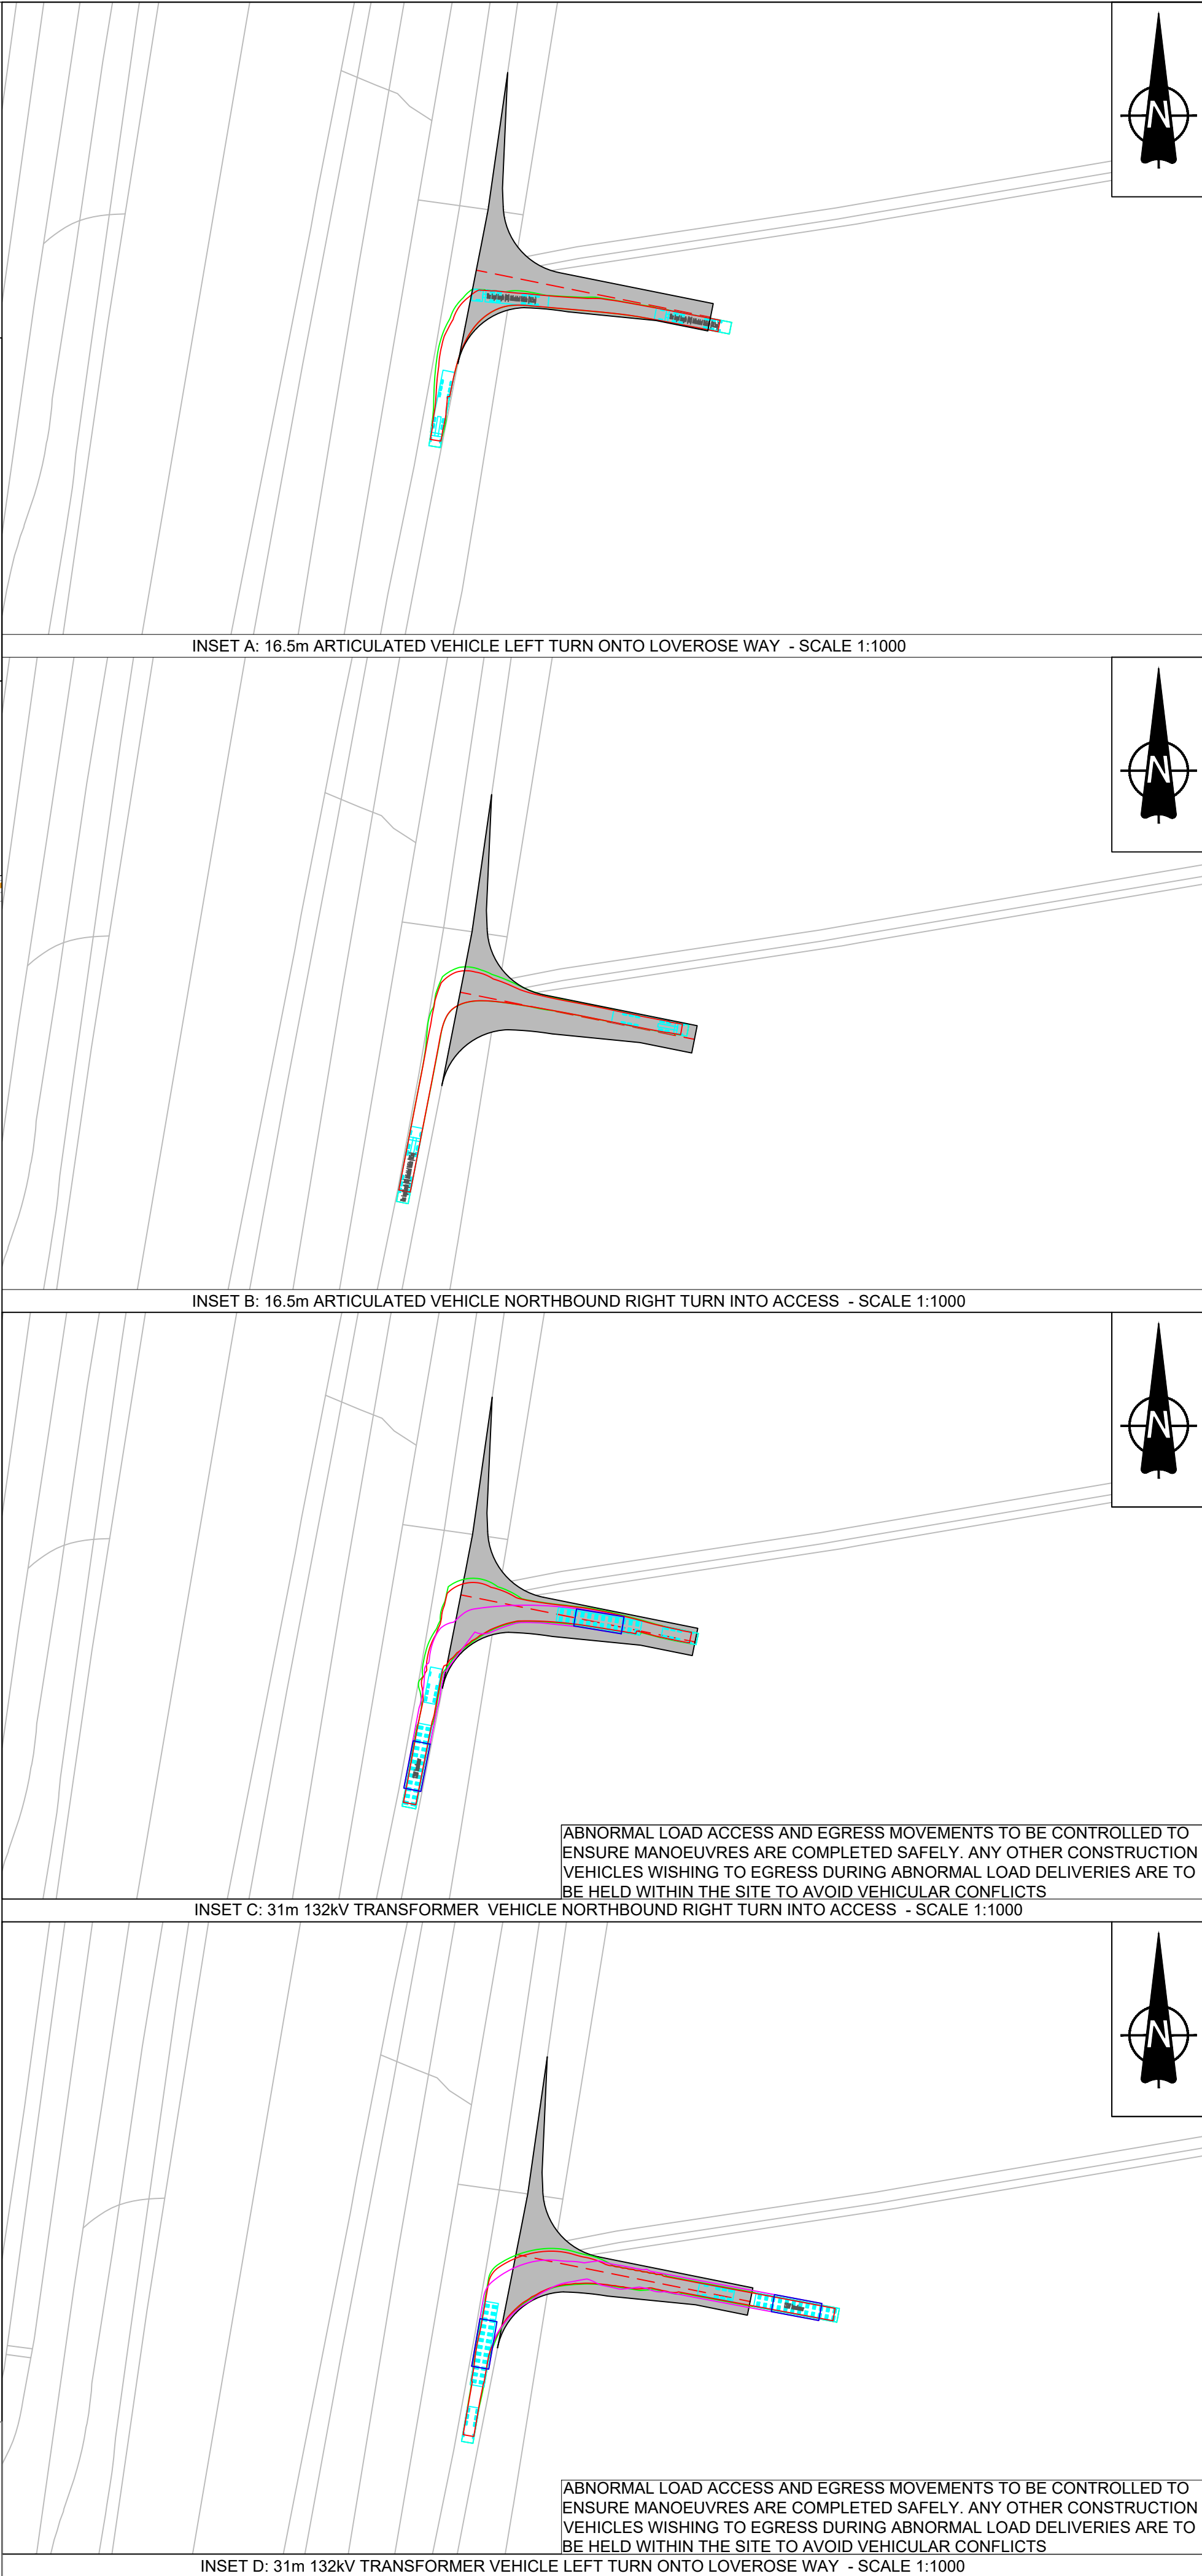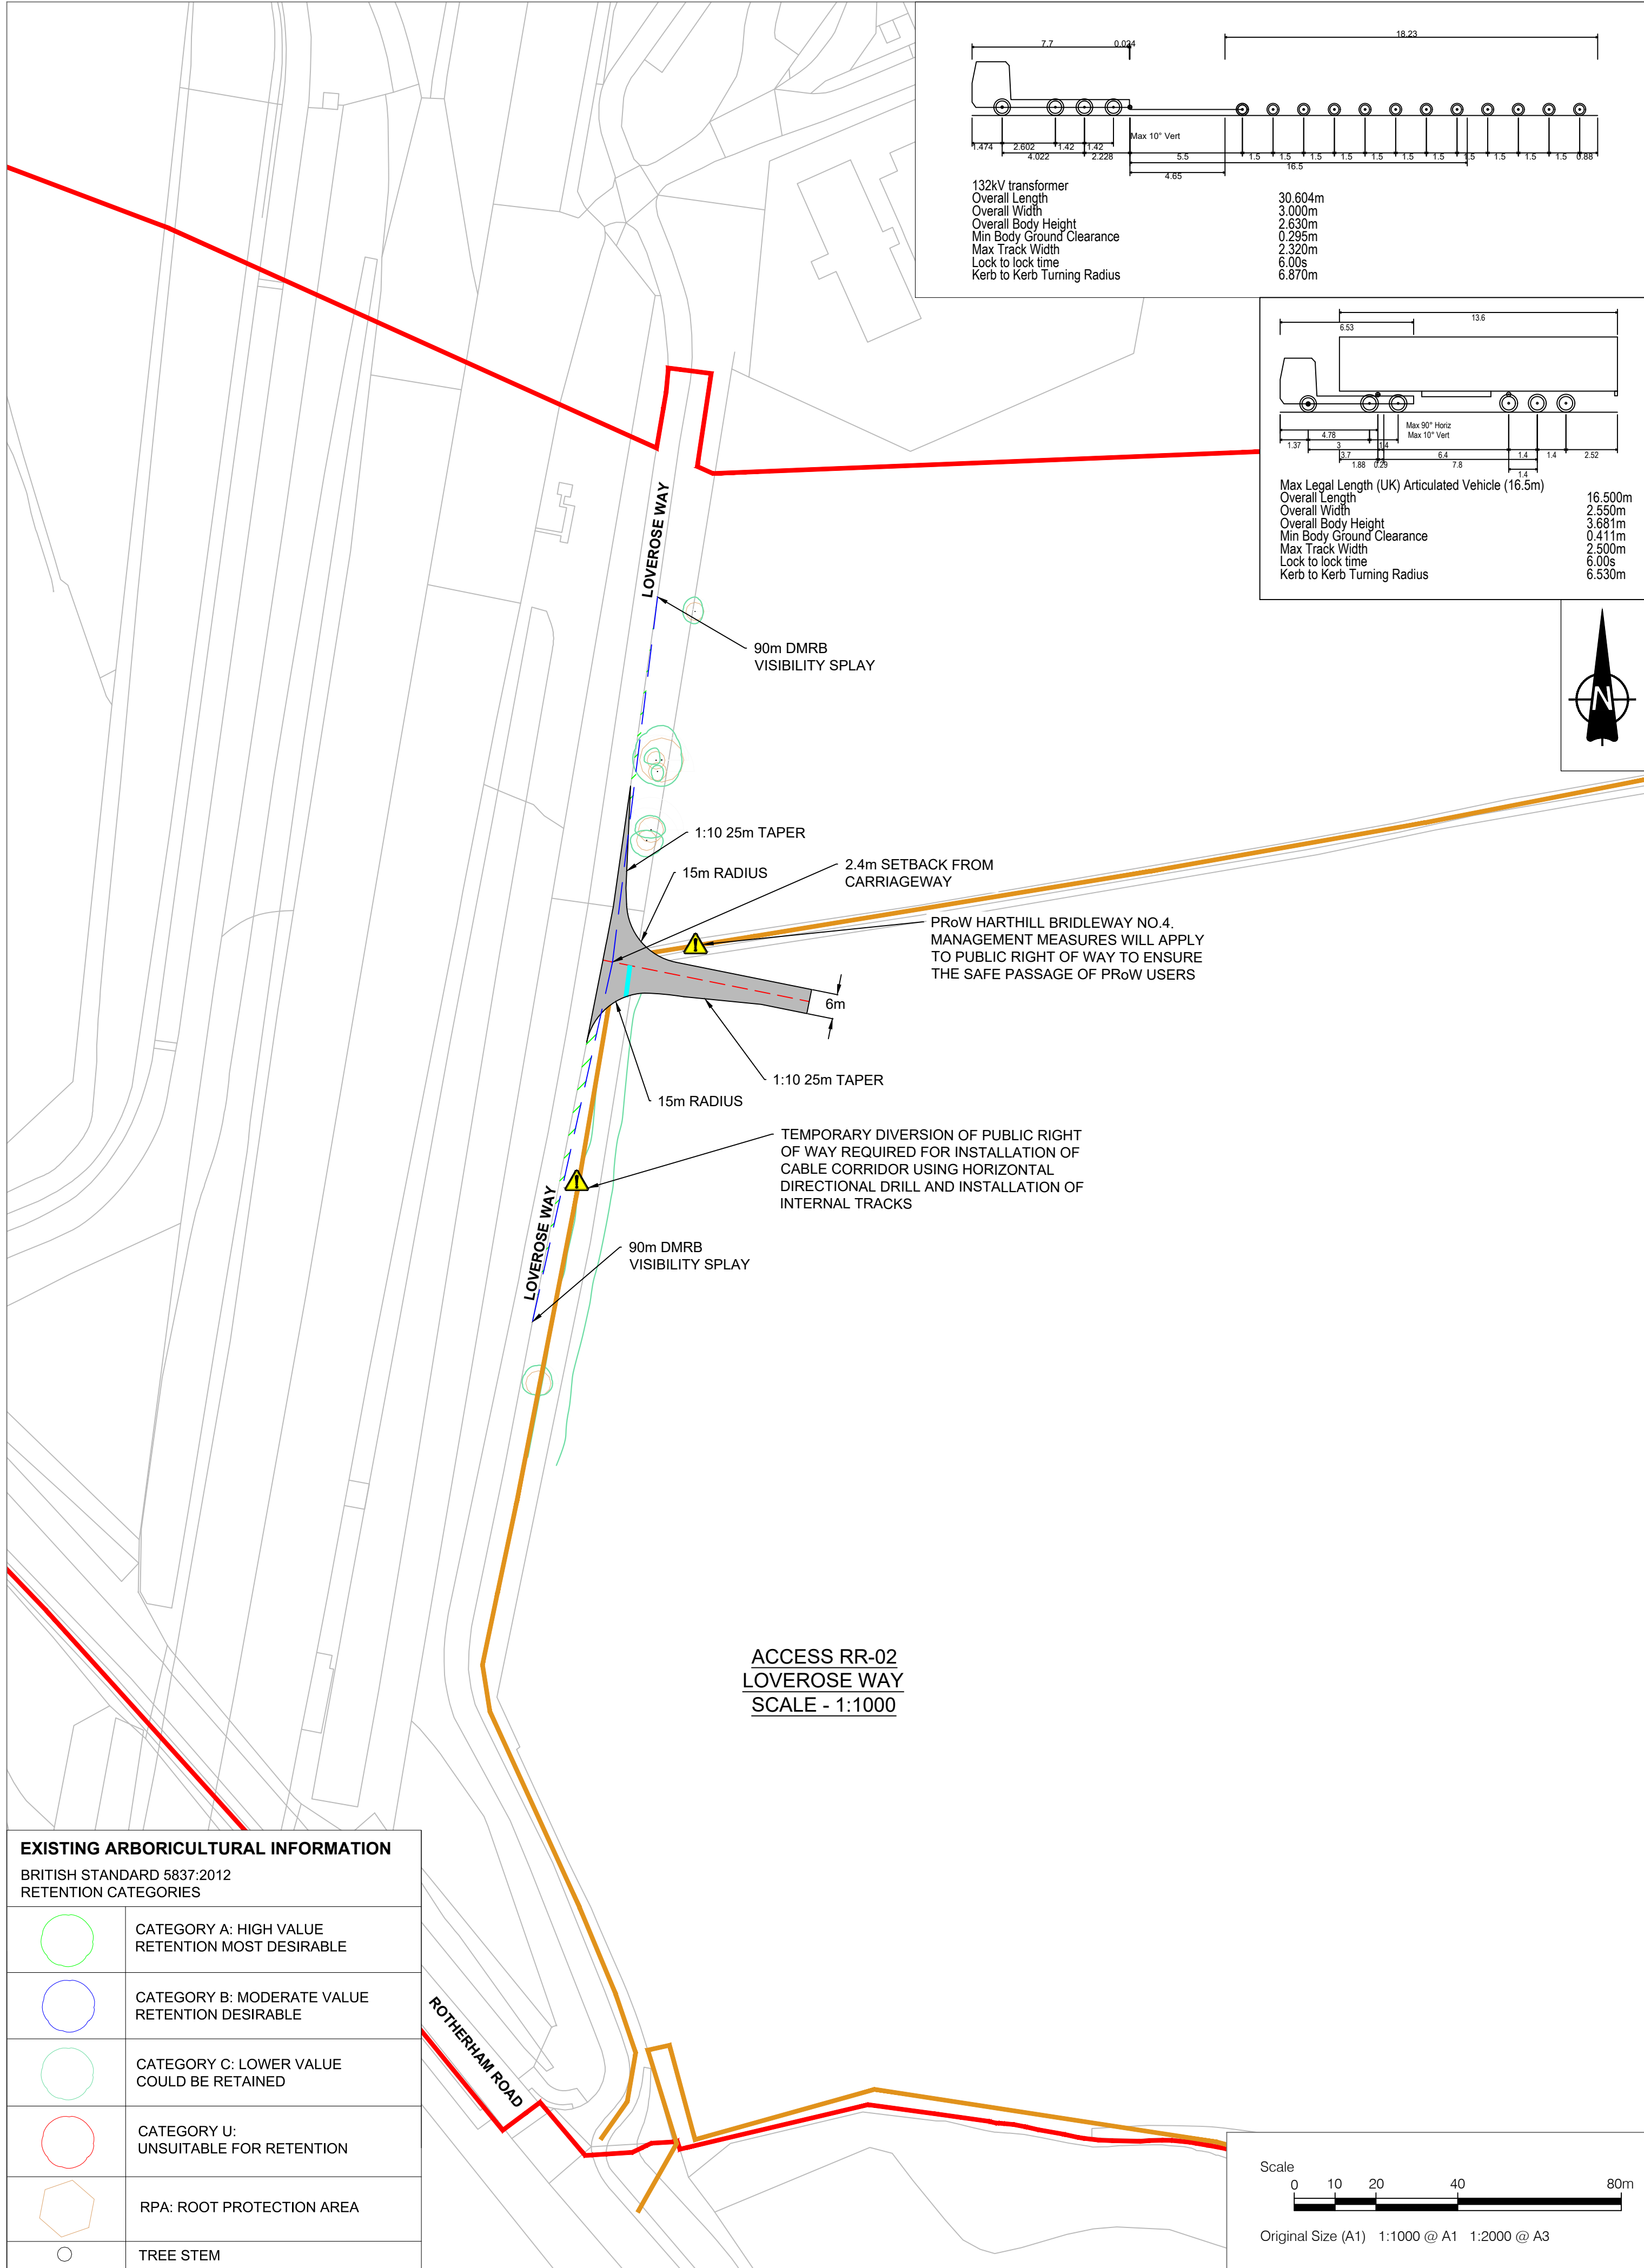


NOTES

- This drawing is to be read in conjunction with all other relevant documentation.
- Do not scale from this drawing, use only printed dimensions.
- All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
- This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
- Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
- The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
- Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
- Junction visibility for the access is based upon DMRB CD109 Table 2.10.

LEGEND

- Extent of Access Footprint
- Order Limits
- Land Excluded from Order Limits
- Vehicle Body
- Vehicle Body Path
- Vehicle Load
- Vehicle Load Path
- Vehicle Wheels Path
- Edge of Road
- Access Centreline
- Junction Visibility
- Vegetation to be Removed for Vis Splay
- Indicative Hedgerow Removal Vis Splay
- Indicative Hedgerow Removal for Bellmouth Access
- Health and Safety Risk Identifier
- Existing Public Right of Way

SHEET PLAN

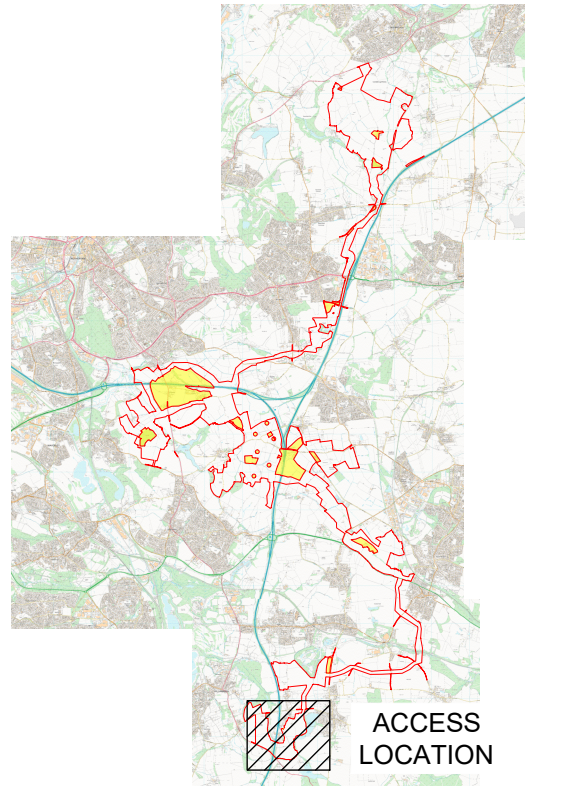

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:

PV Area Access RR-02
Appendix 3 - Sheet 27 of 53
Whitestone Solar Farm
Regulation 5(2)(o)

DRAWING DATE: 03/06/2026

SCALE: 1:1000

SHEET: Sheet 27 of 53

SIZE: A1





REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020




EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012 RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

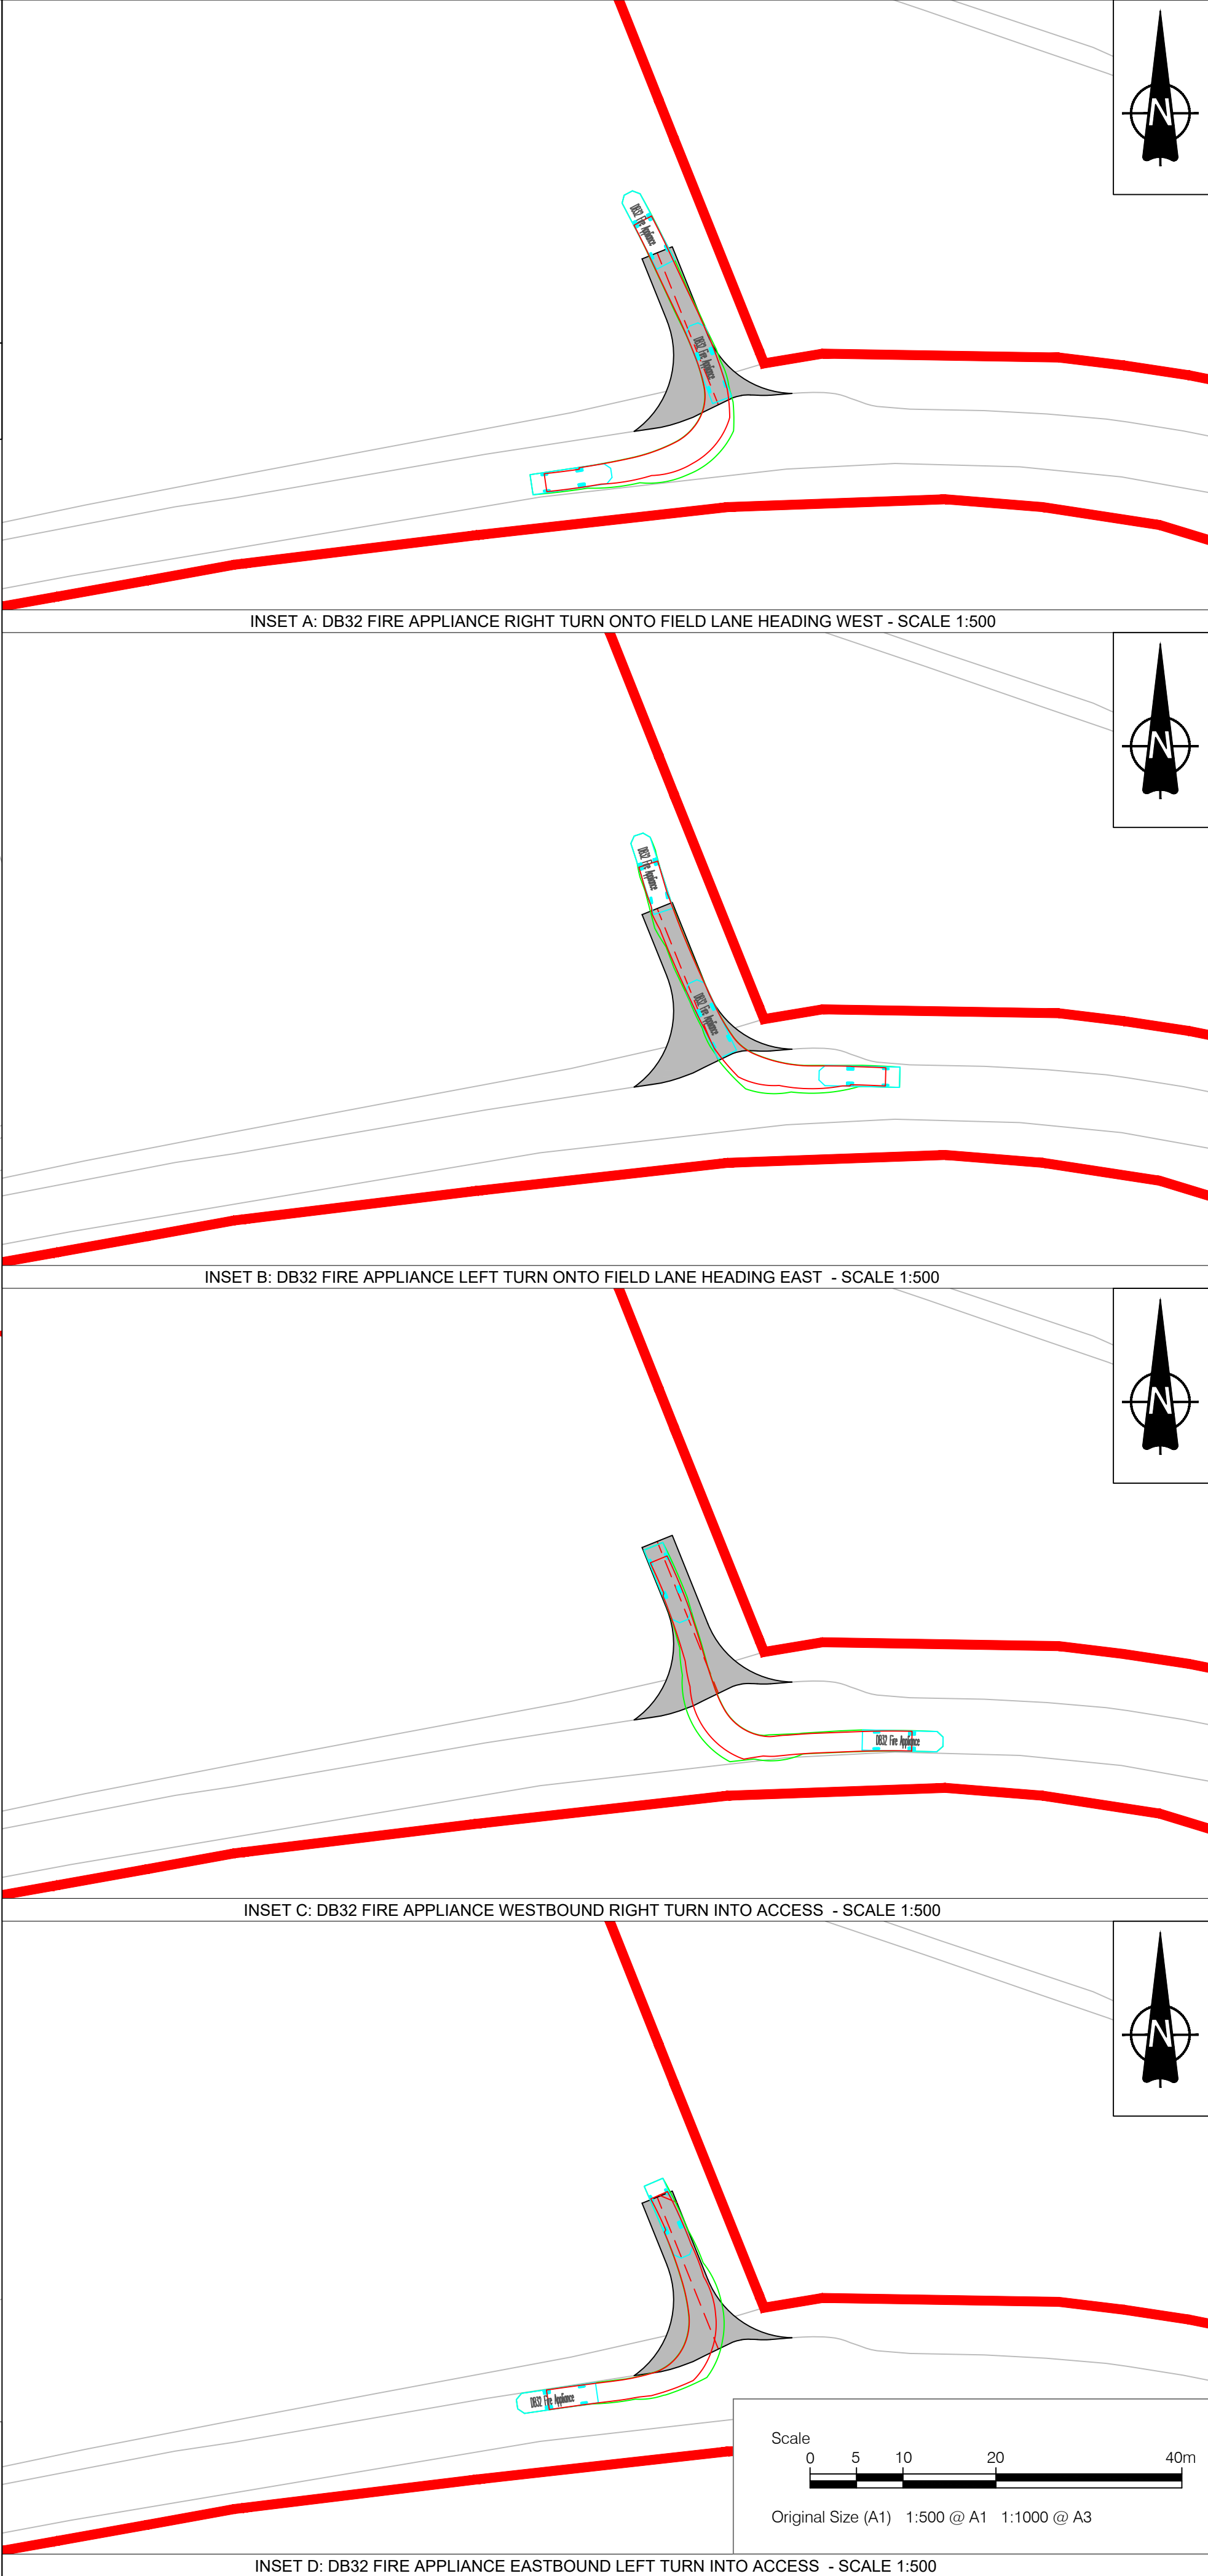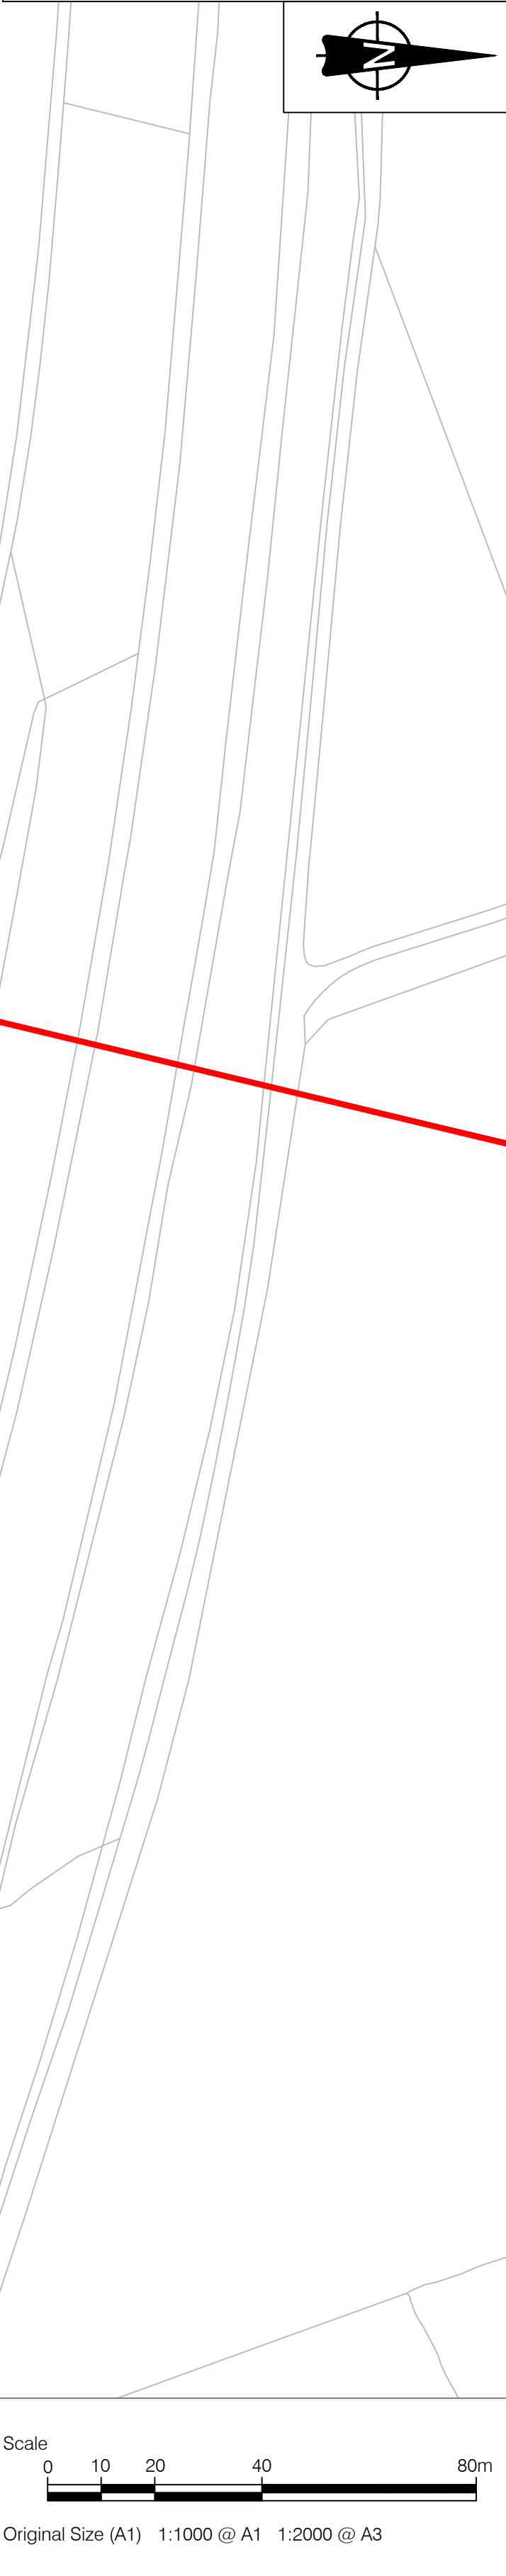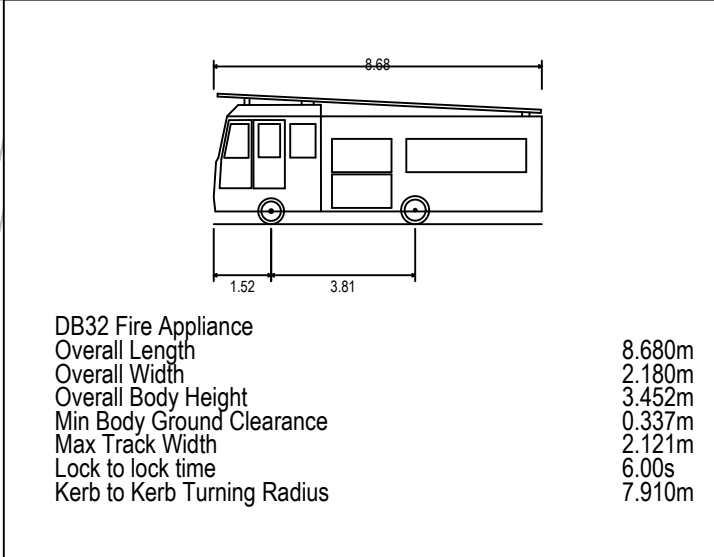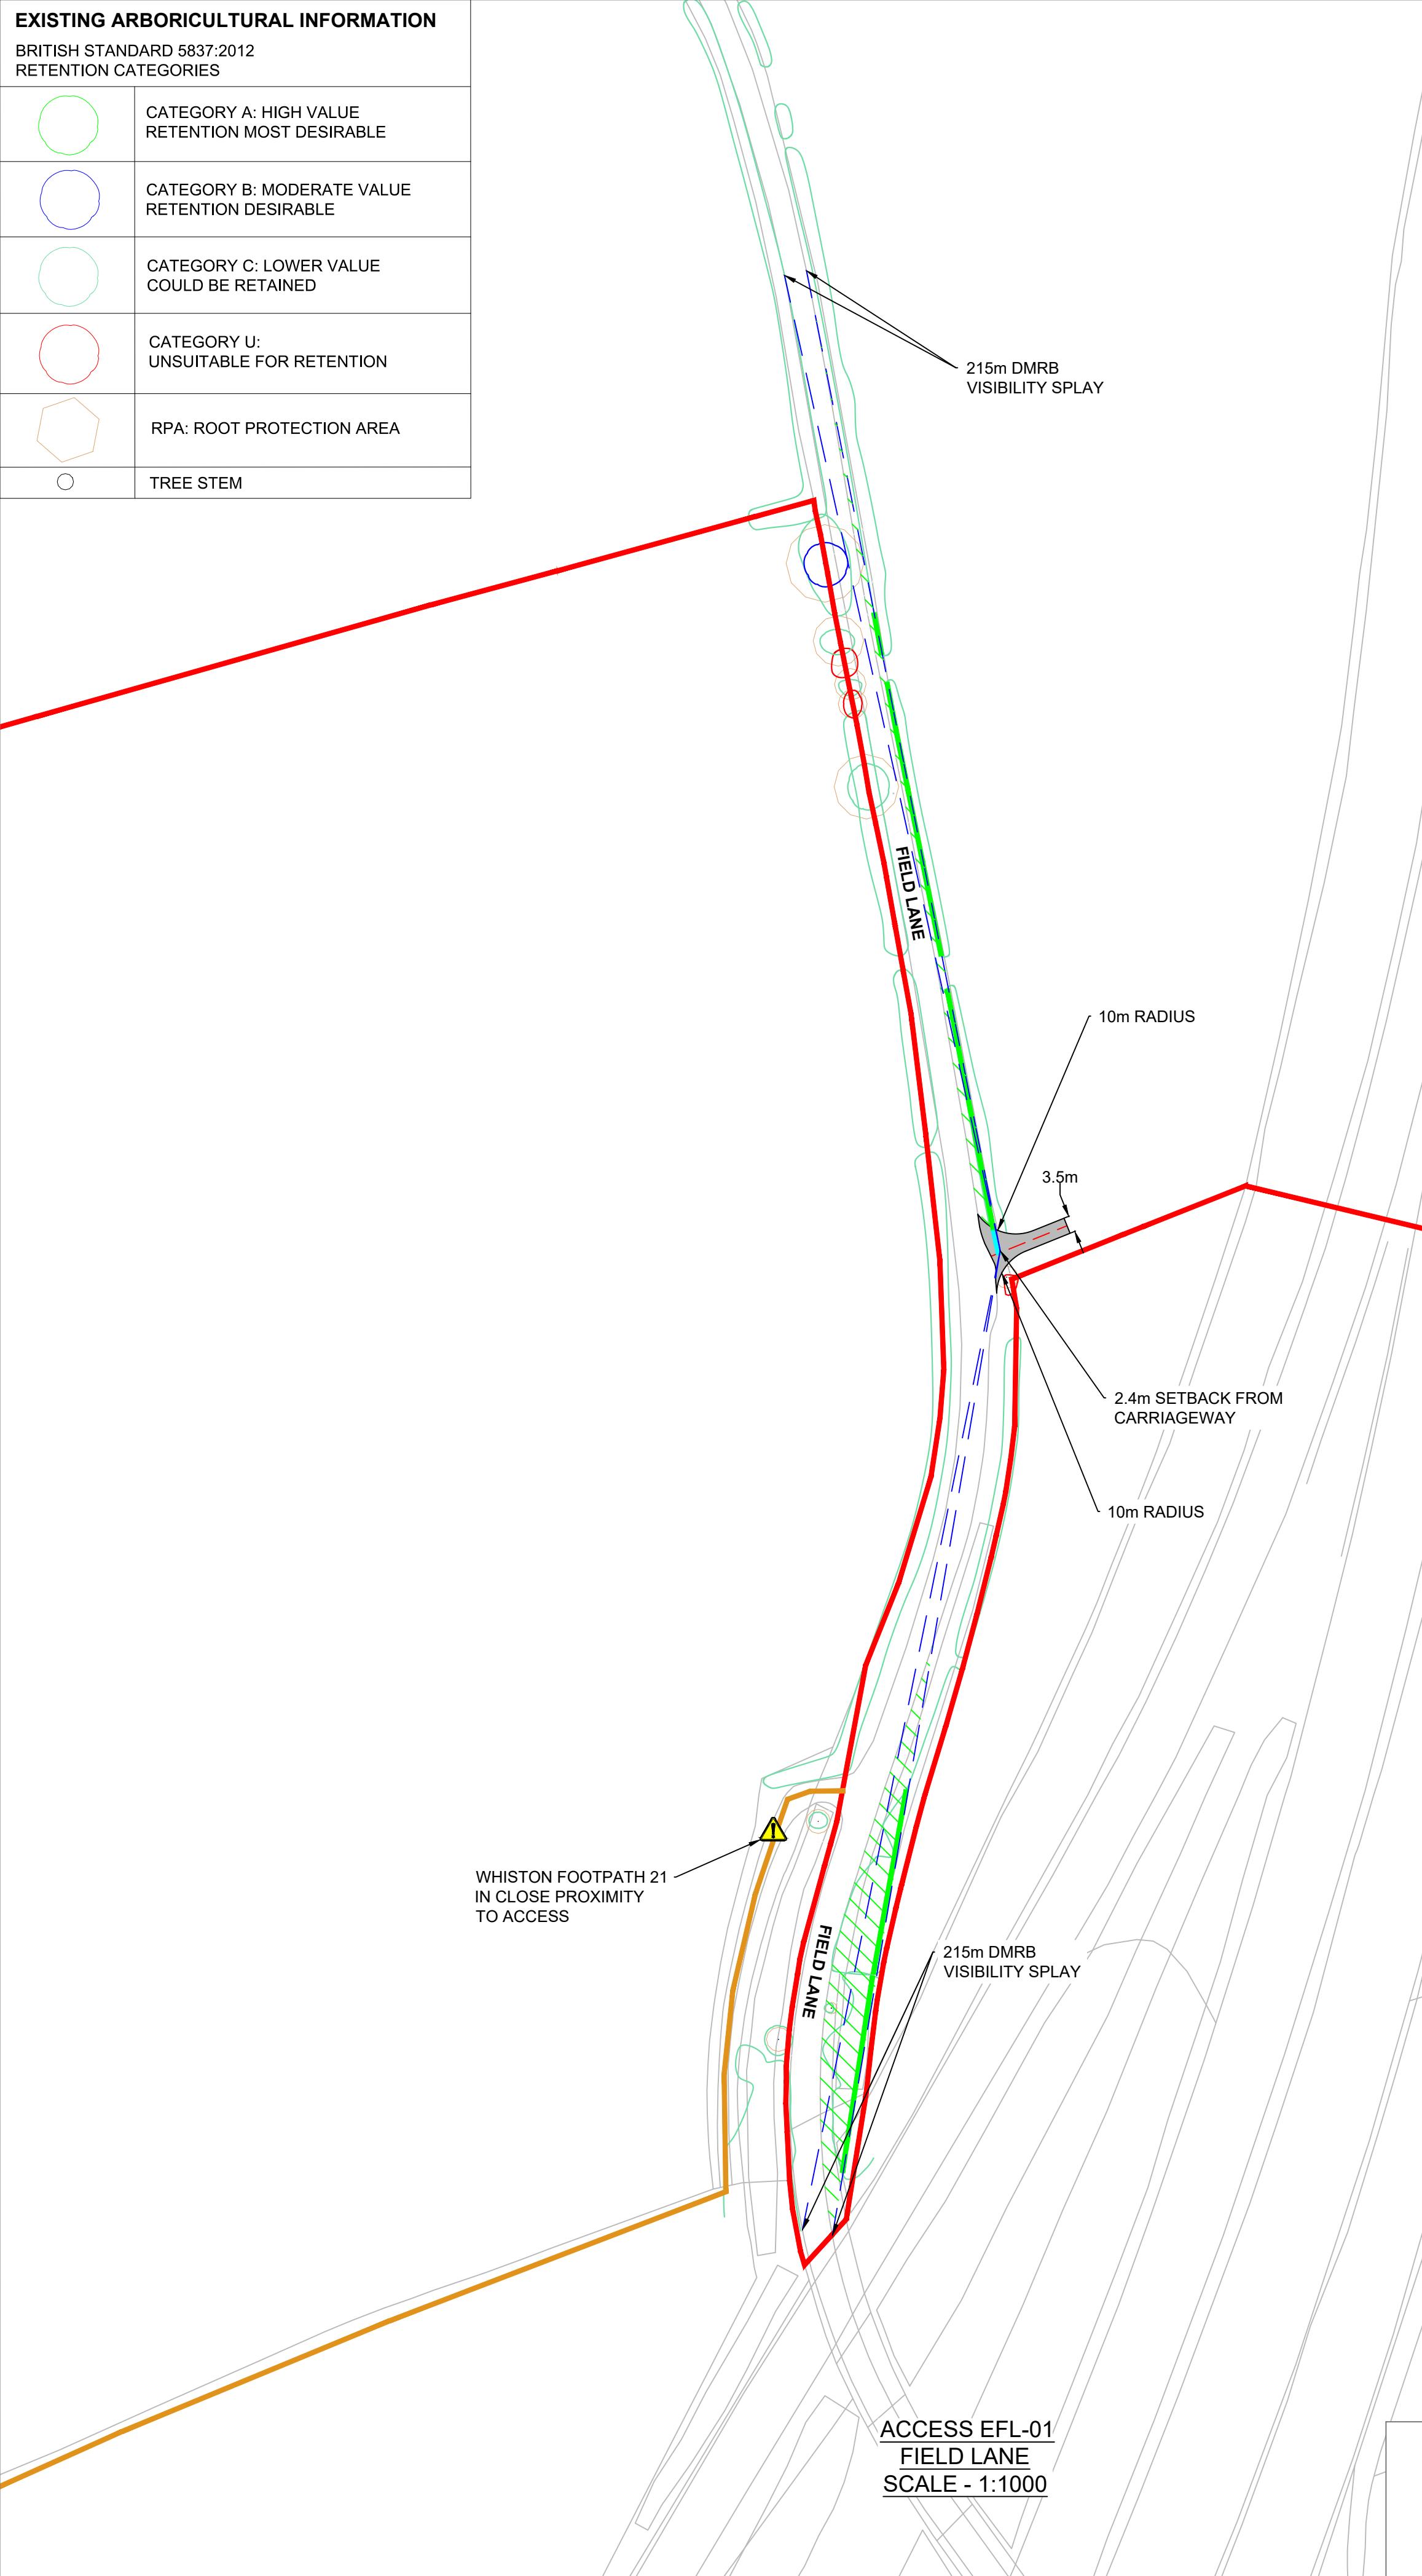

- NOTES**
- This drawing is to be read in conjunction with all other relevant documentation.
 - Do not scale from this drawing, use only printed dimensions.
 - All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
 - This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
 - Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
 - The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
 - Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
 - Junction visibility for the access is based upon DMRB CD109 Table 2.10.

- LEGEND**
- Extent of Access Footprint
 - Order Limits
 - Land Excluded from Order Limits
 - Vehicle Body
 - Vehicle Body Path
 - Vehicle Load
 - Vehicle Load Path
 - Vehicle Wheels Path
 - Edge of Road
 - Access Centreline
 - Junction Visibility
 - Vegetation to be Removed for Vis Splay
 - Indicative Hedgerow Removal Vis Splay
 - Indicative Hedgerow Removal for Bellmouth Access
 - Health and Safety Risk Identifier
 - Existing Public Right of Way

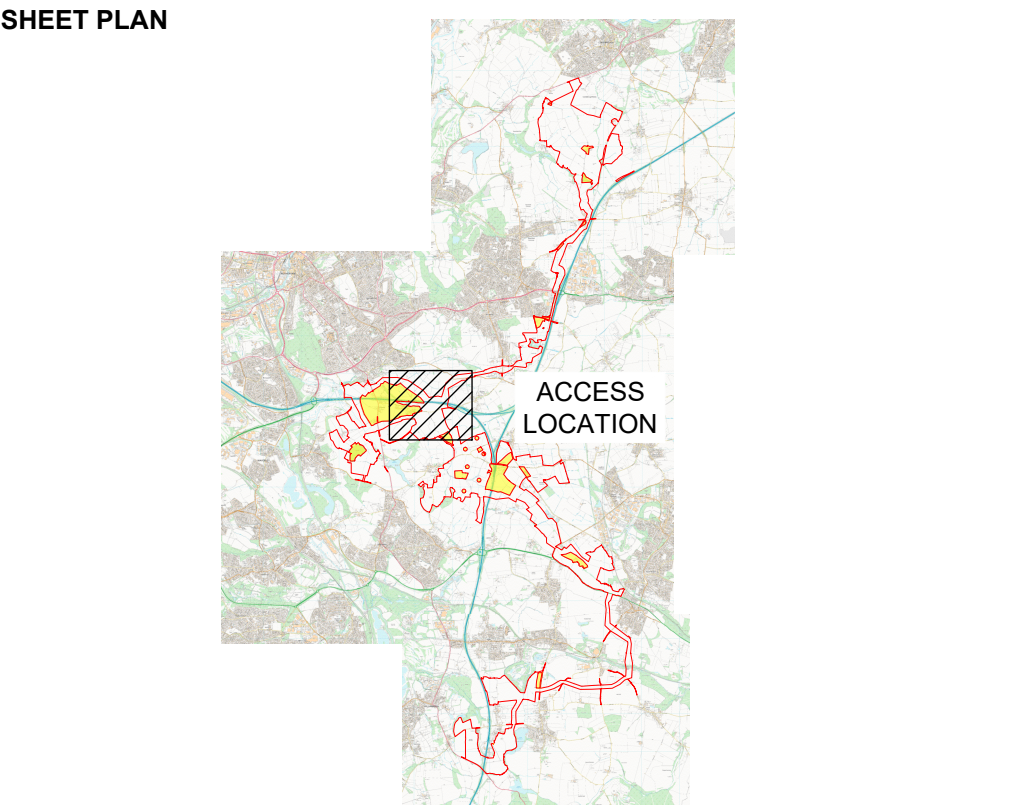

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:
PV Area Access EFL-01
Appendix 3 - Sheet 28 of 53
Whitestone Solar Farm
Regulation 5(2)(o)

DRAWING DATE: 03/06/2026


SCALE: AS SHOWN	SHEET: Sheet 28 of 53
SIZE: A1	REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12


APPLICATION NUMBER: EN0110020



EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012 RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

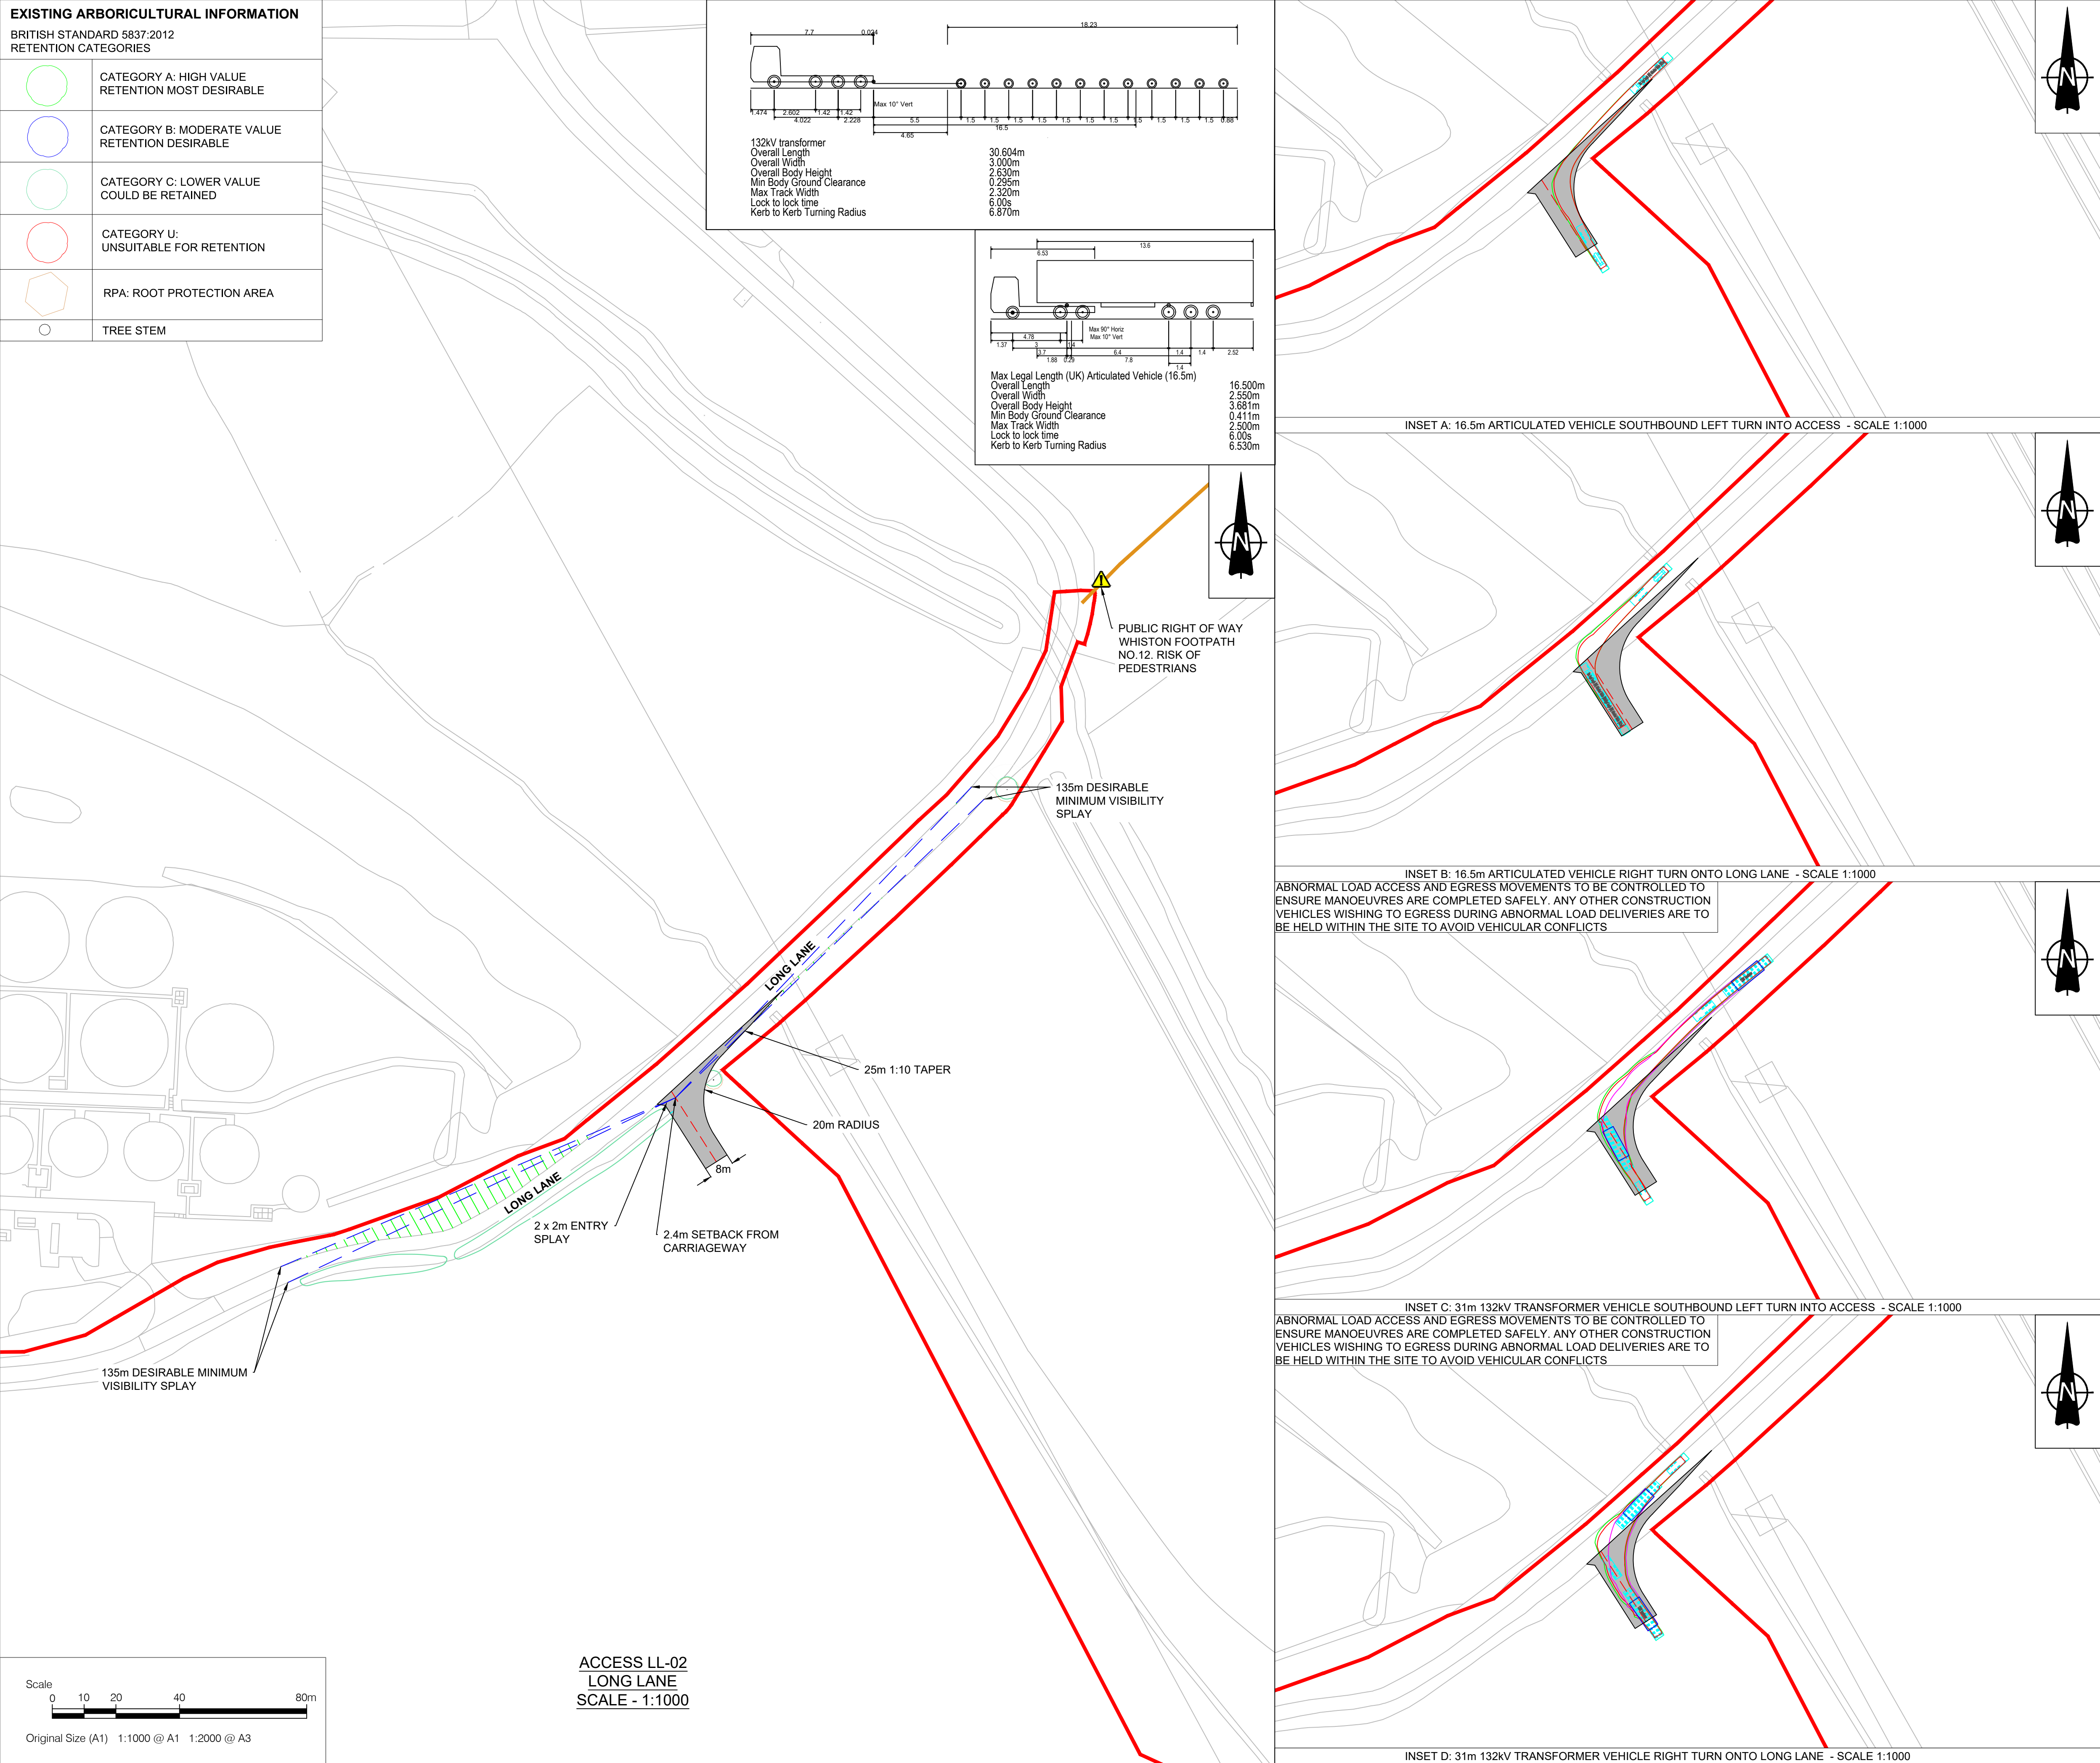

ACCESS LL-02
LONG LANE
SCALE - 1:1000



Sources: Esri, TomTom, Garmin, FAO, NOAA, USGS, © OpenStreetMap contributors, and the GIS User Community. Reproduced from Ordnance Survey digital map data © Crown copyright 2026. All rights reserved. License number 0000848182


NOTES

1. This drawing is to be read in conjunction with all other relevant documentation.
2. Do not scale from this drawing, use only printed dimensions.
3. All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
4. This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
5. Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
6. The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
7. Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
8. Junction visibility for the access is based upon visibility parameters derived using the 85th percentile speed survey conducted between the 4th June 2025 to the 10th June 2025.

LEGEND

- Extent of Access Footprint
- Order Limits
- Land Excluded from Order Limits
- Vehicle Body
- Vehicle Body Path
- Vehicle Load
- Vehicle Load Path
- Vehicle Wheels Path
- Edge of Road
- Access Centreline
- Junction Visibility
- Vegetation to be Removed for Vis Splay
- Indicative Hedgerow Removal Vis Splay
- Indicative Hedgerow Removal for Bellmouth Access
- Health and Safety Risk Identifier
- Existing Public Right of Way

SHEET PLAN

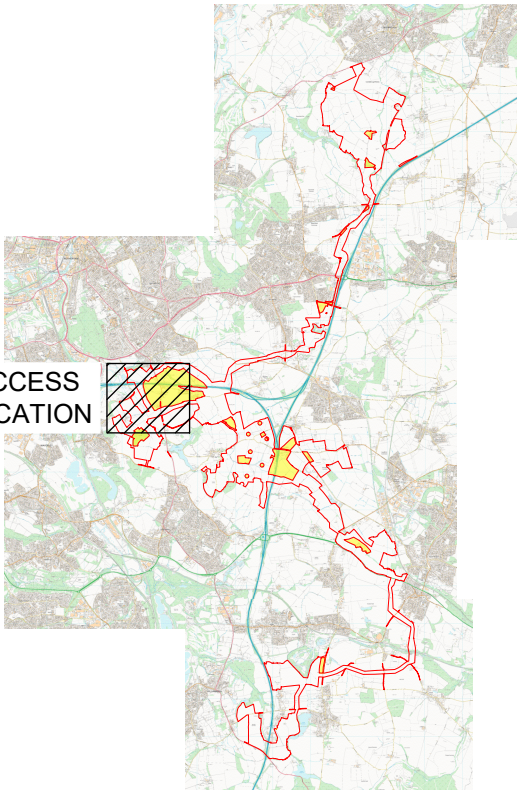

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:
PV Area Access LL-02
Appendix 3 - Sheet 29 of 53
Whitestone Solar Farm
Regulation 5(2)(o)


DRAWING DATE: 03/06/2026

SCALE: 1:1000	SHEET: Sheet 29 of 53
SIZE: A1	REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12


APPLICATION NUMBER: EN0110020



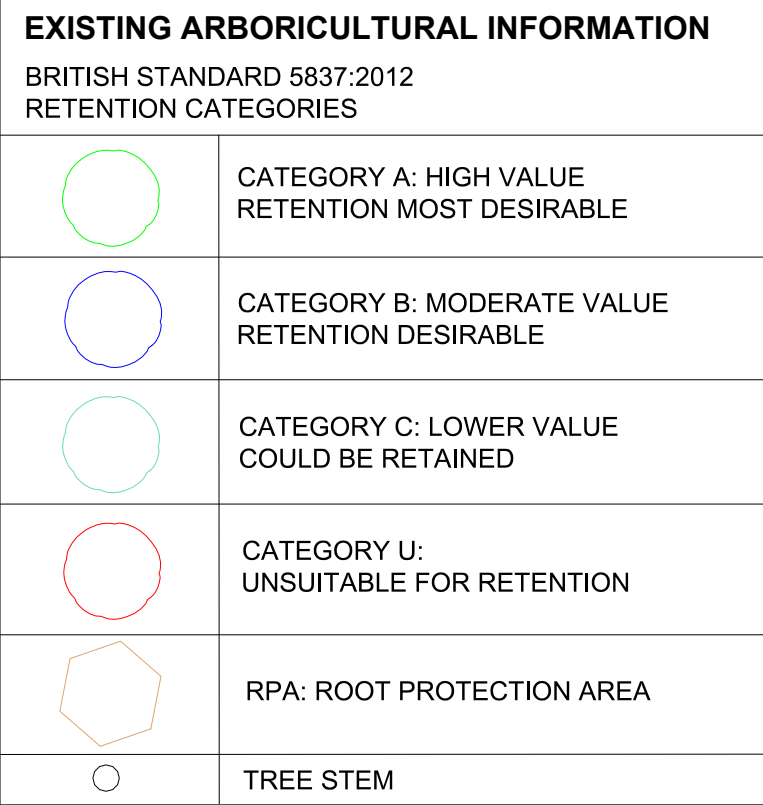


ACCESS CC-01
COMMON LANE
SCALE - 1:1000


ABNORMAL LOAD ACCESS AND EGRESS MOVEMENTS TO BE CONTROLLED TO ENSURE MANOEUVRES ARE COMPLETED SAFELY. ANY OTHER CONSTRUCTION VEHICLES WISHING TO EGRESS DURING ABNORMAL LOAD DELIVERIES ARE TO BE HELD WITHIN THE SITE TO AVOID VEHICULAR CONFLICTS

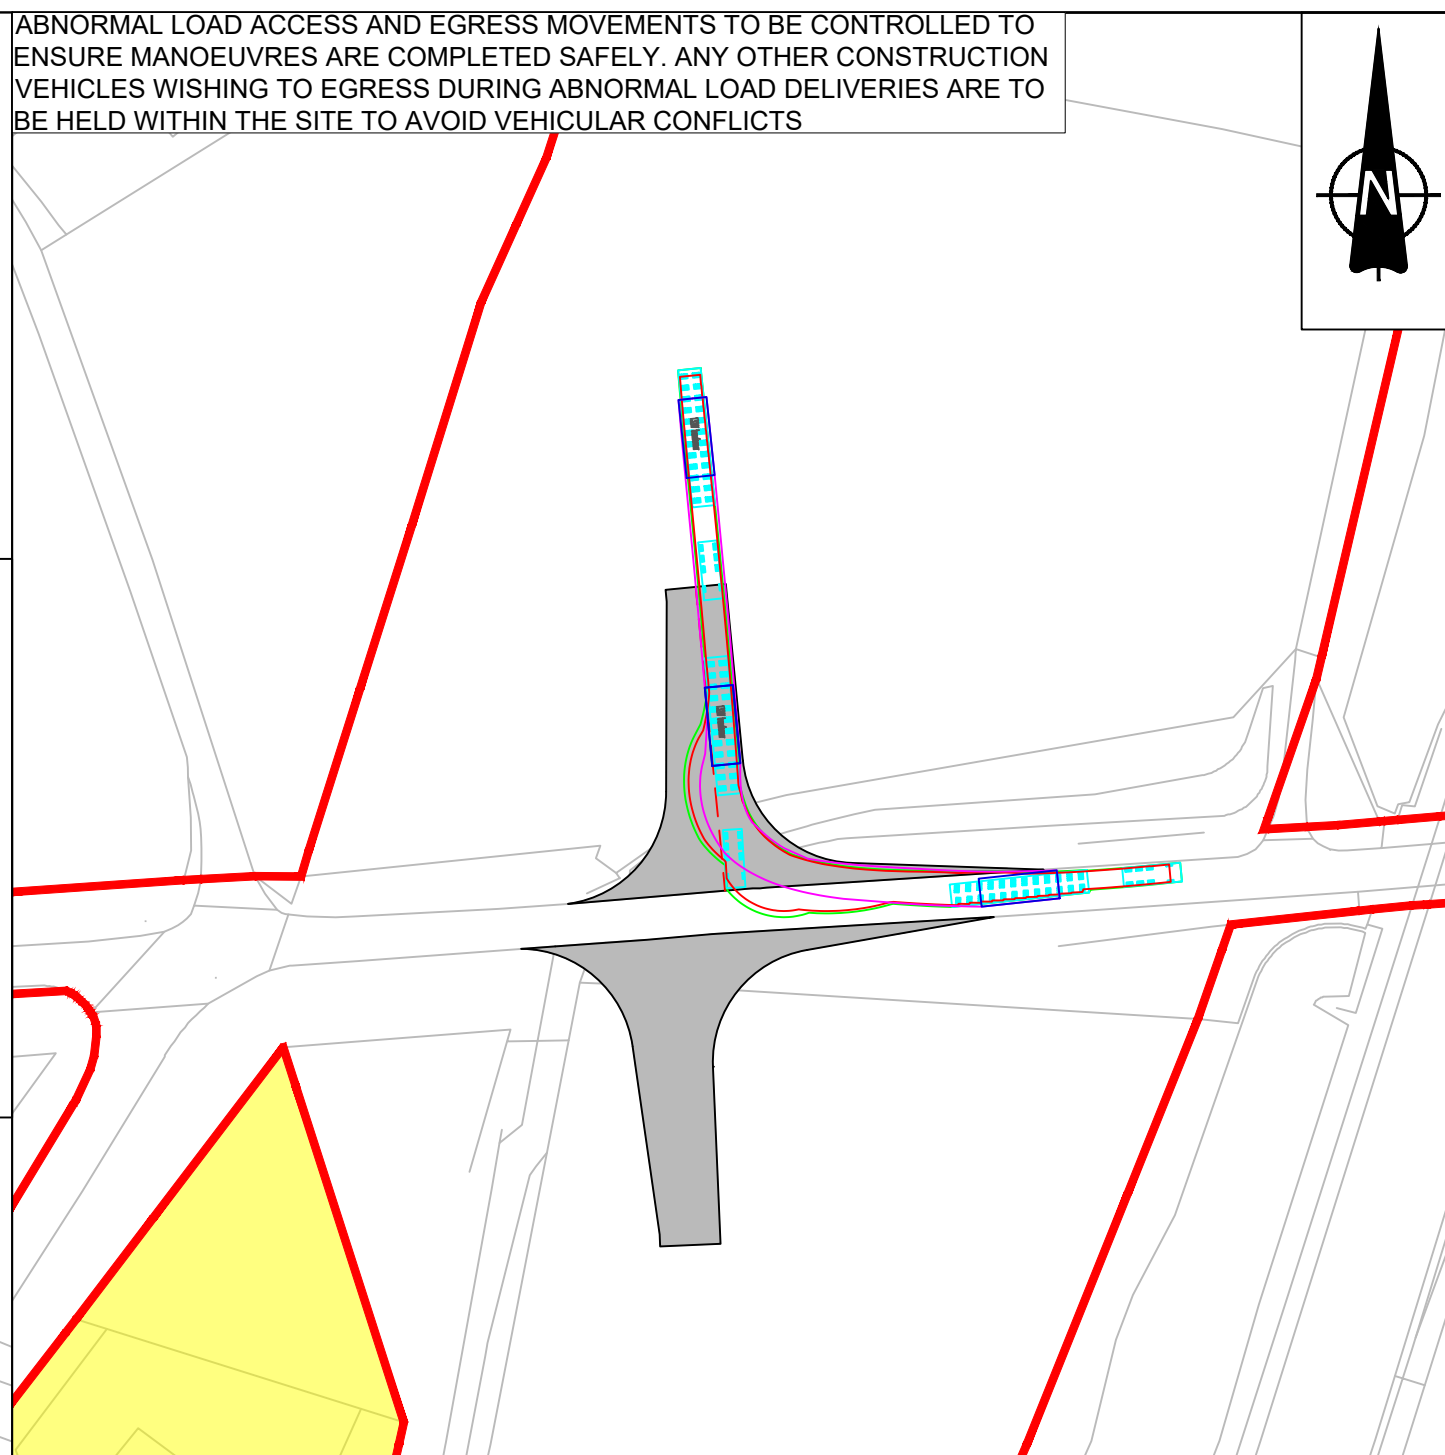

INSET A: 31m 132kV TRANSFORMER VEHICLE TURNING LEFT OUT OF ACCESS ONTO COMMON LANE
HEADING EAST - SCALE 1:1000

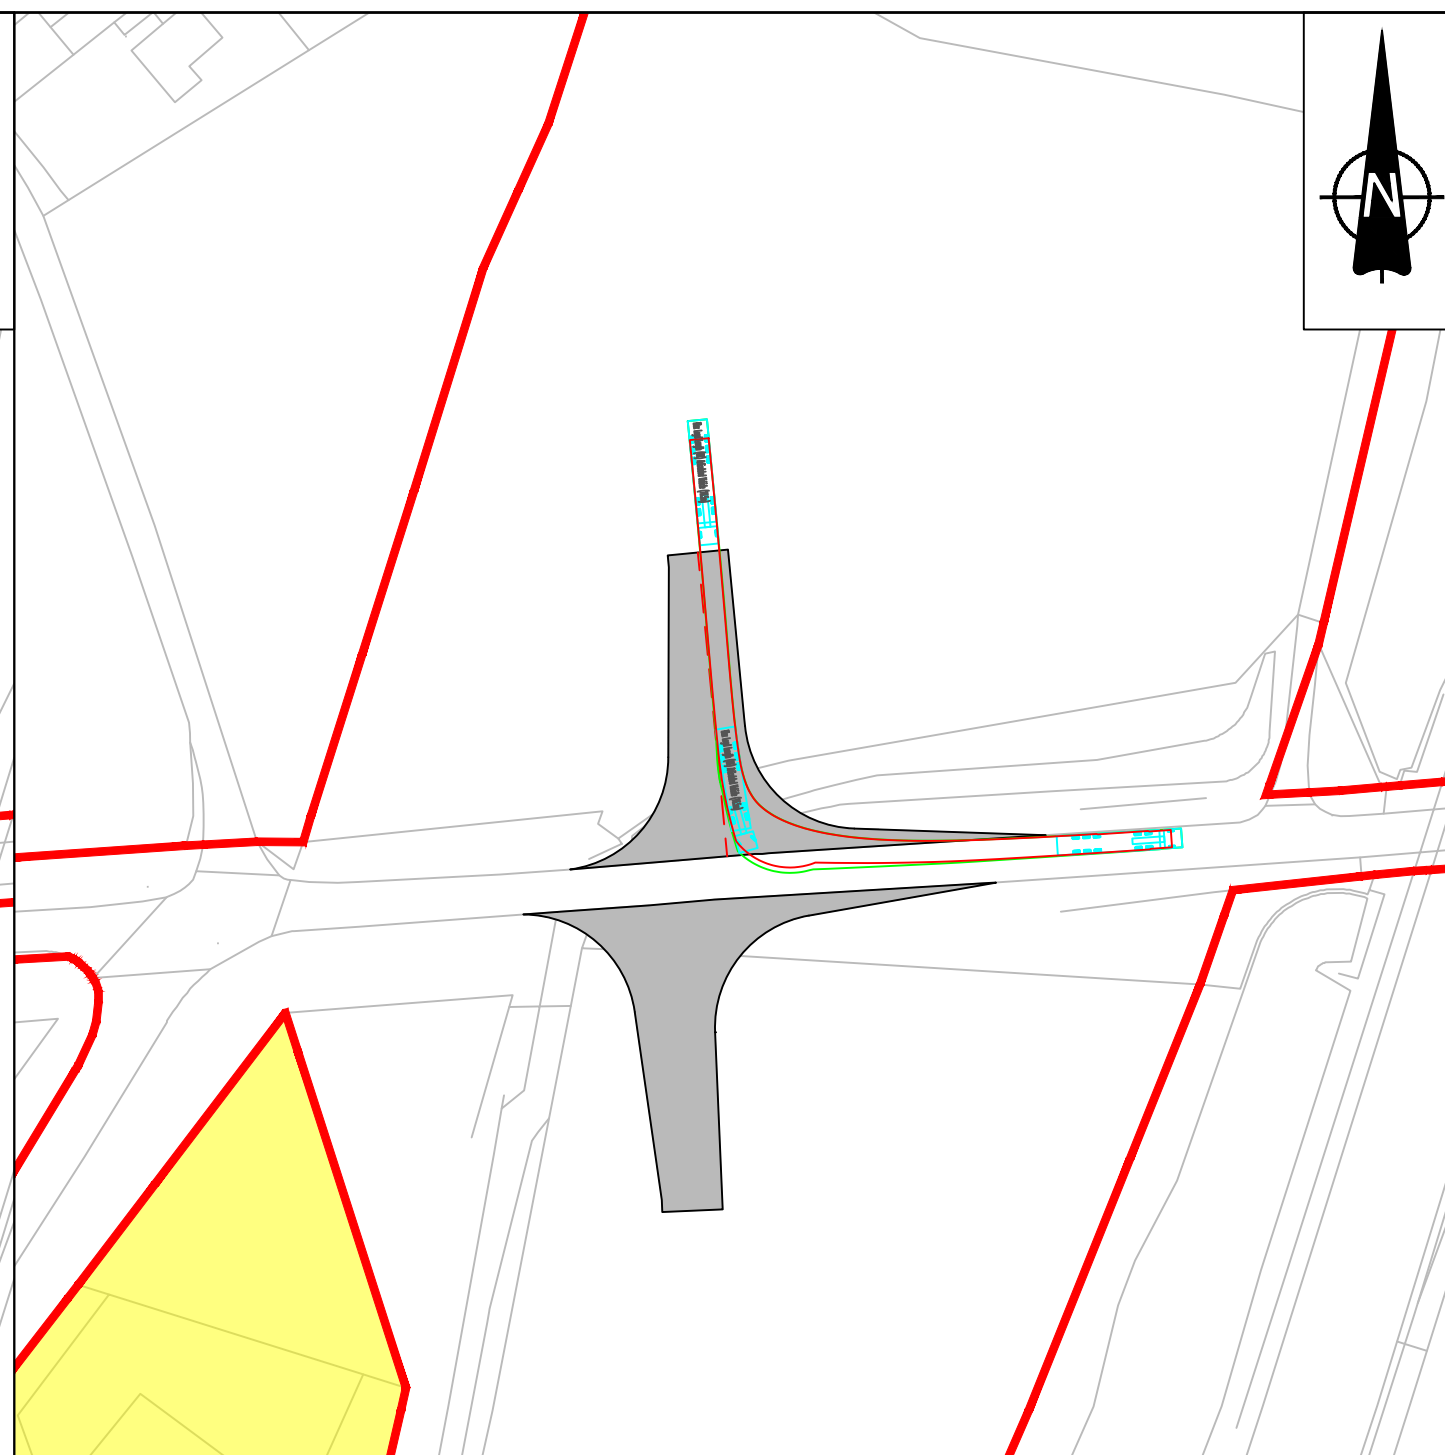


INSET B: 16.5m ARTICULATED VEHICLE TURNING LEFT OUT OF ACCESS ONTO COMMON LANE HEADING EAST - SCALE 1:1000

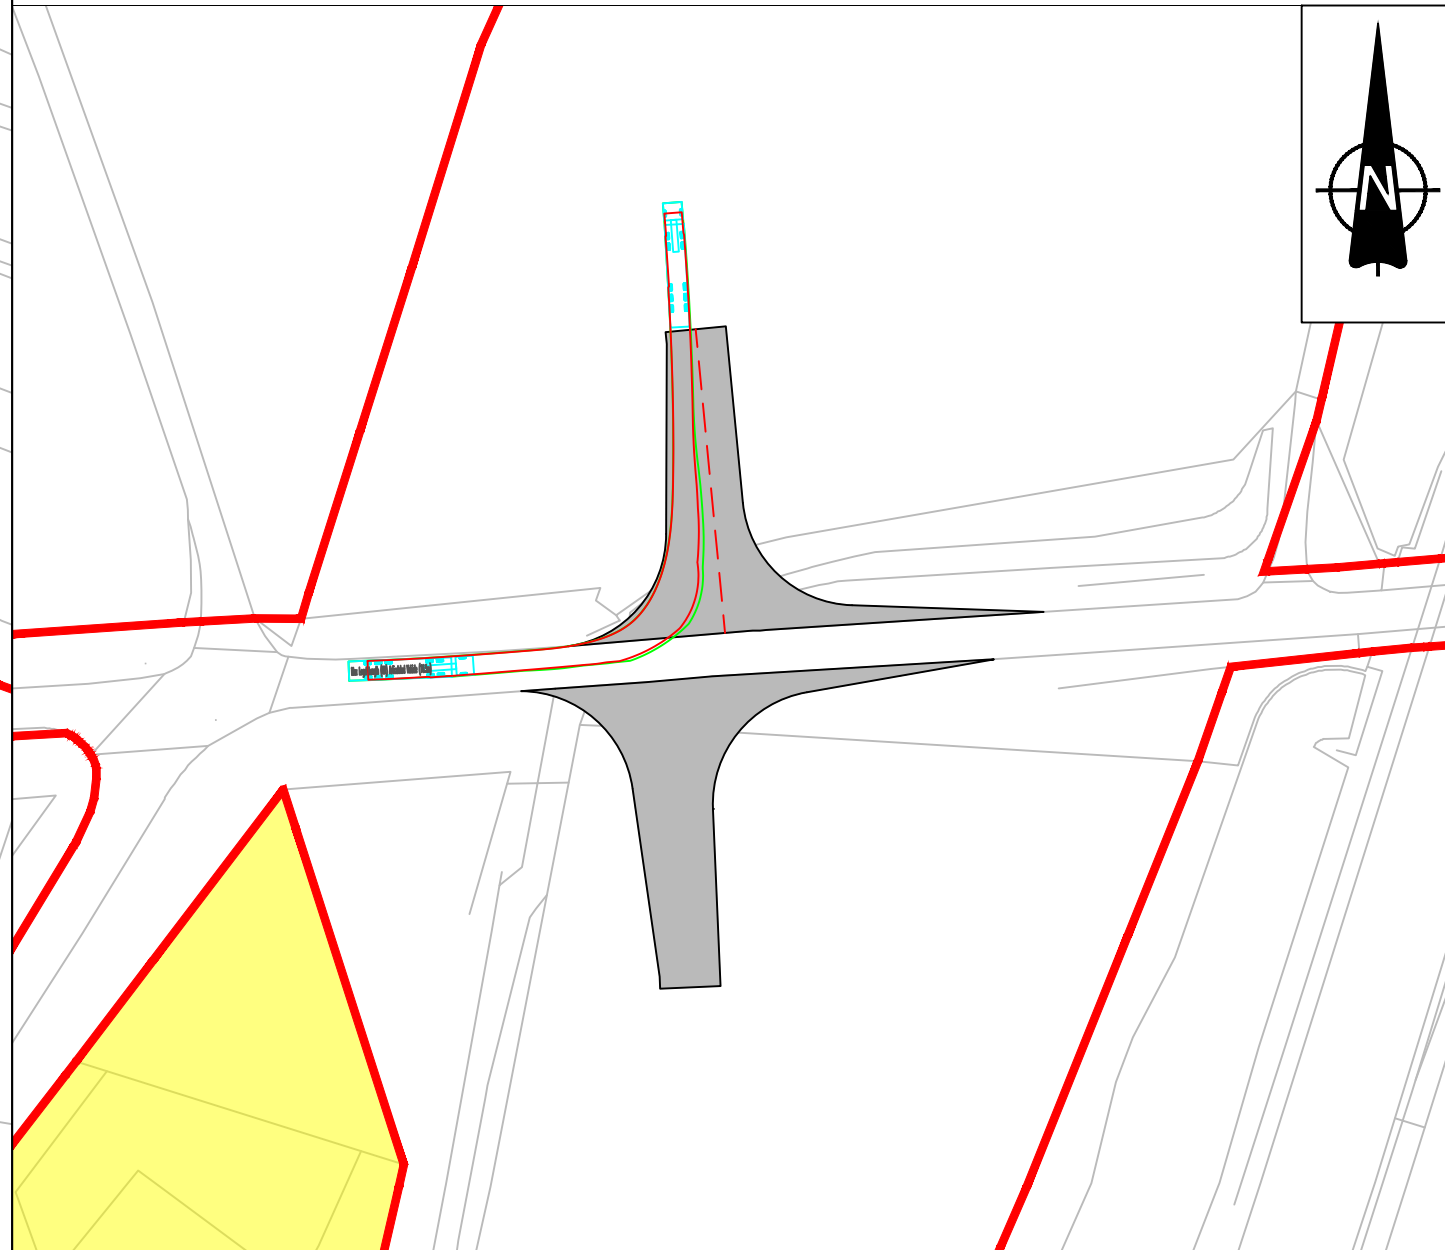


INSET C: 16.5m ARTICULATED VEHICLE HEADING EAST ON COMMON LANE AND TURNING LEFT INTO ACCESS - SCALE 1:1000


ABNORMAL LOAD ACCESS AND EGRESS MOVEMENTS TO BE CONTROLLED TO ENSURE MANOEUVRES ARE COMPLETED SAFELY. ANY OTHER CONSTRUCTION VEHICLES WISHING TO EGRESS DURING ABNORMAL LOAD DELIVERIES ARE TO BE HELD WITHIN THE SITE TO AVOID VEHICULAR CONFLICTS

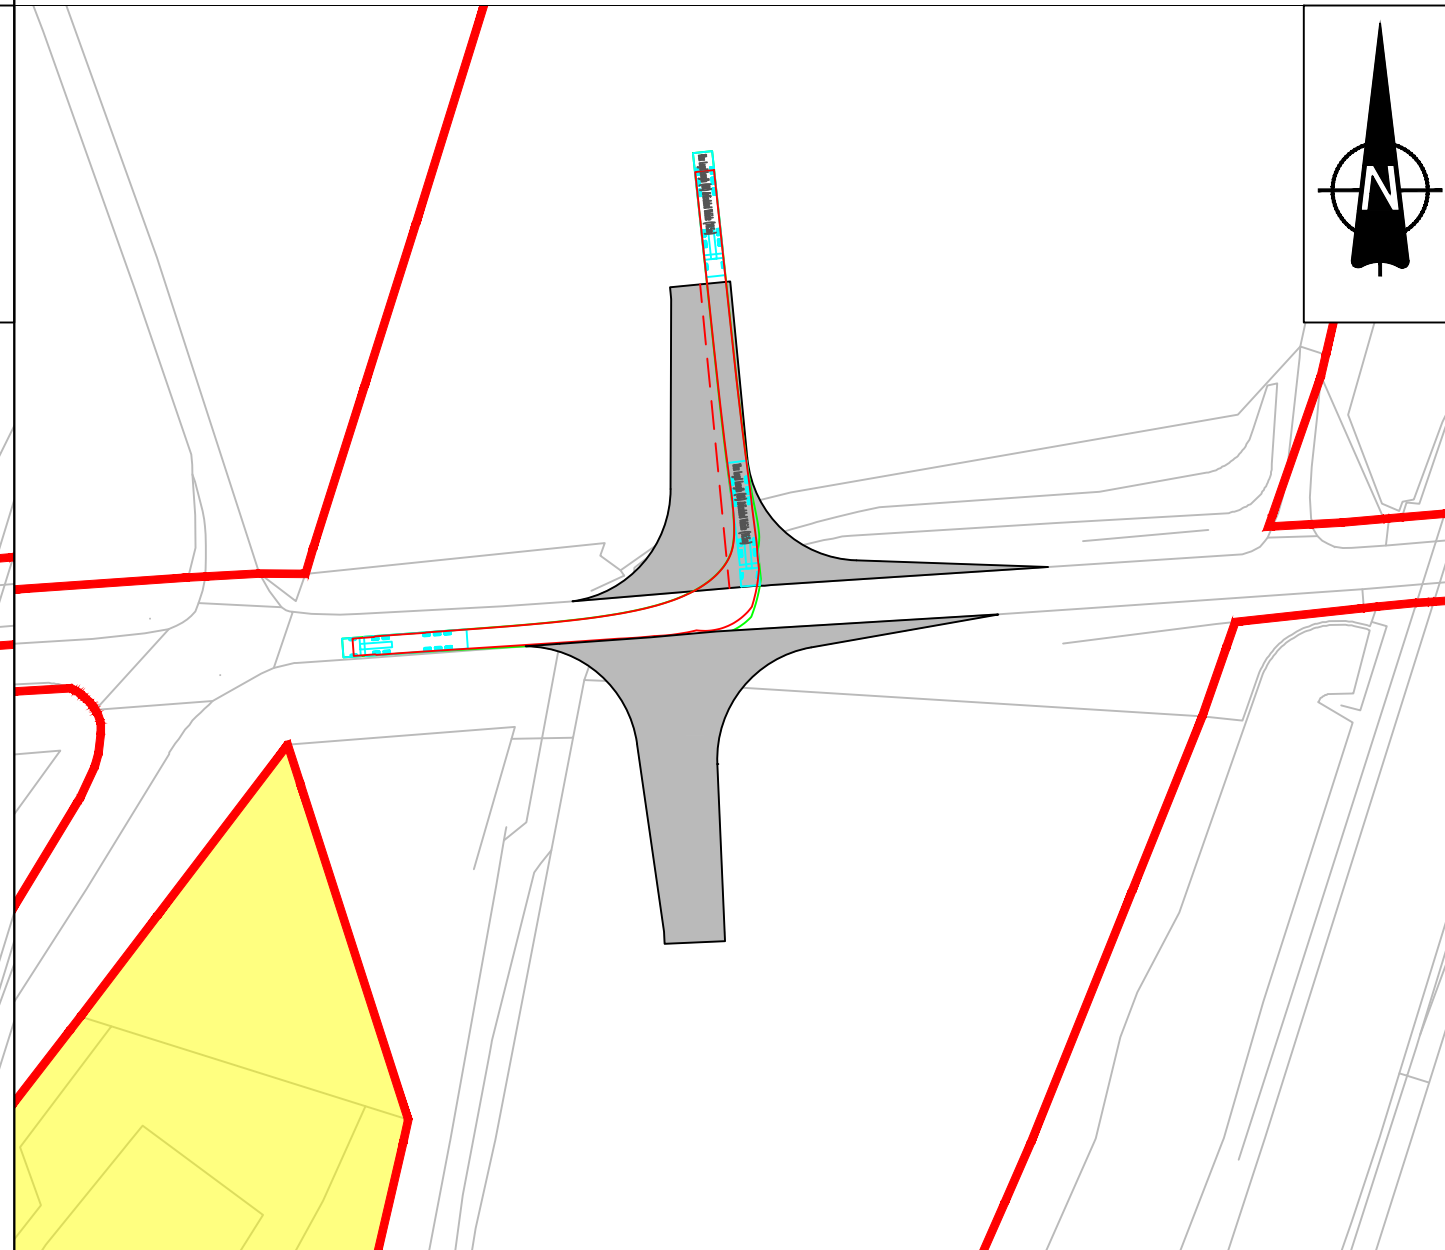

INSET D: 16.5m ARTICULATED VEHICLE TURNING RIGHT OUT OF ACCESS ONTO COMMON LANE
HEADING WEST - SCALE 1:1000

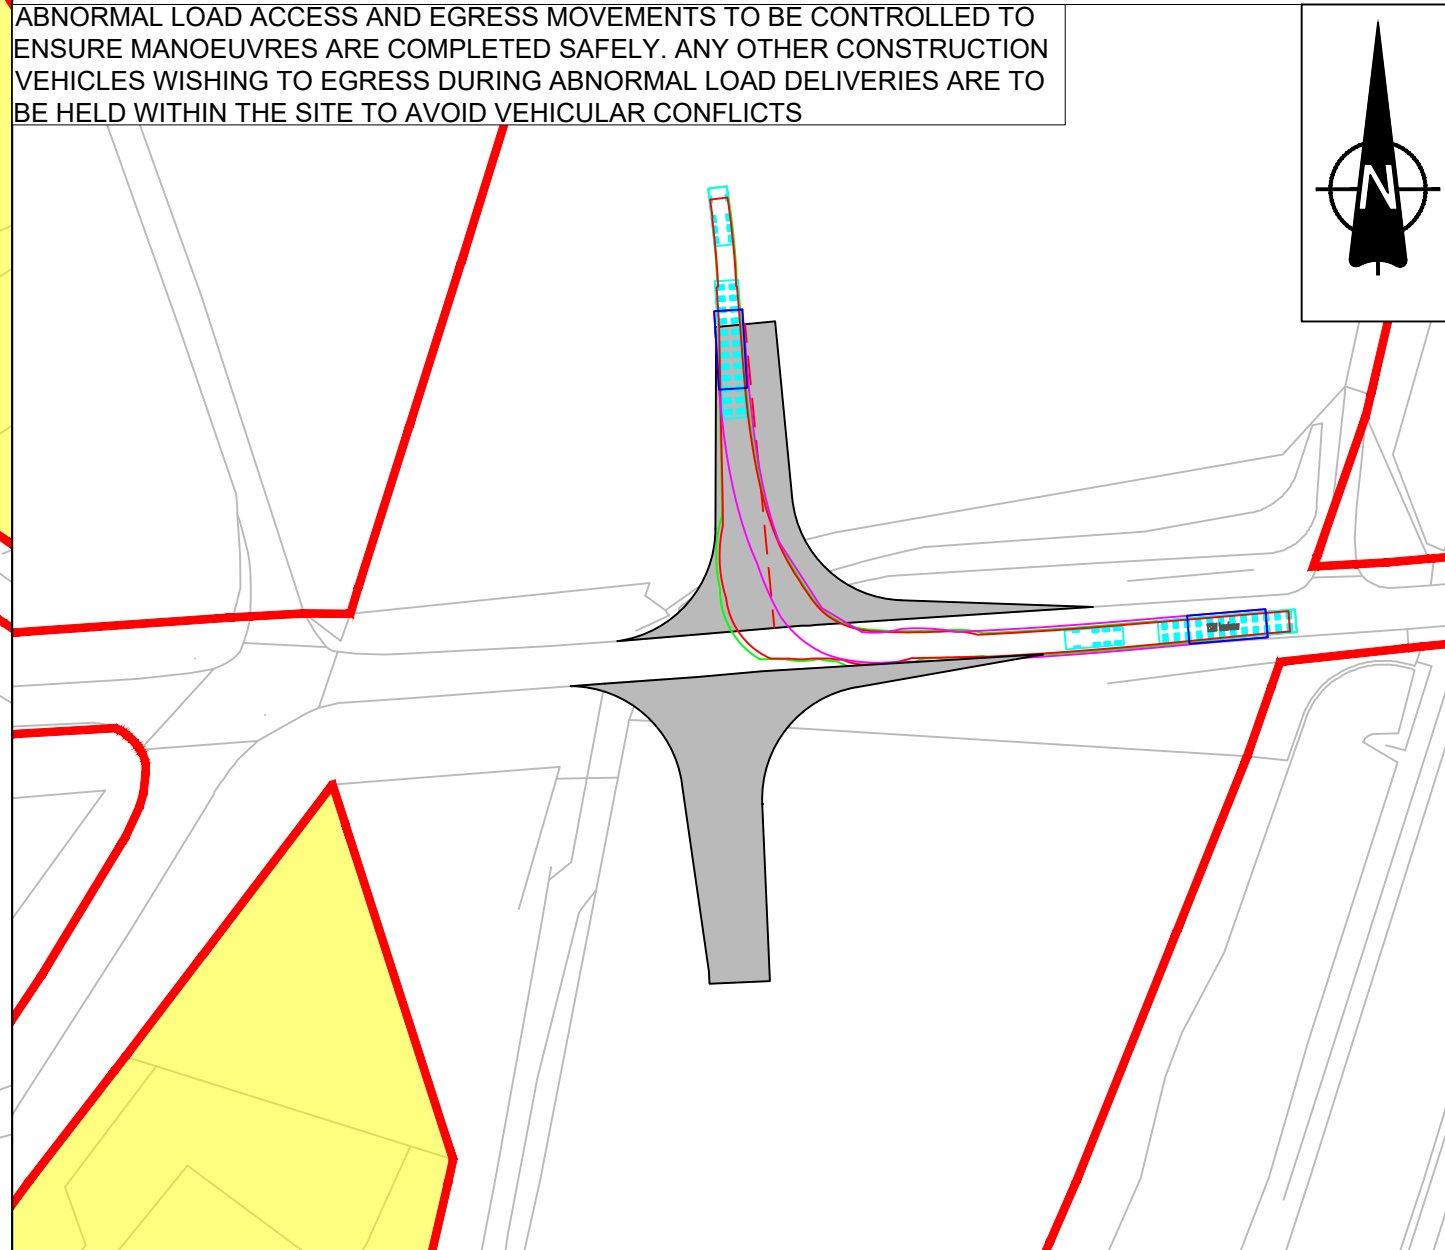

INSET E: 31m 132kV TRANSFORMER VEHICLE HEADING WEST ON COMMON LANE AND TURNING RIGHT INTO ACCESS - SCALE 1:1000

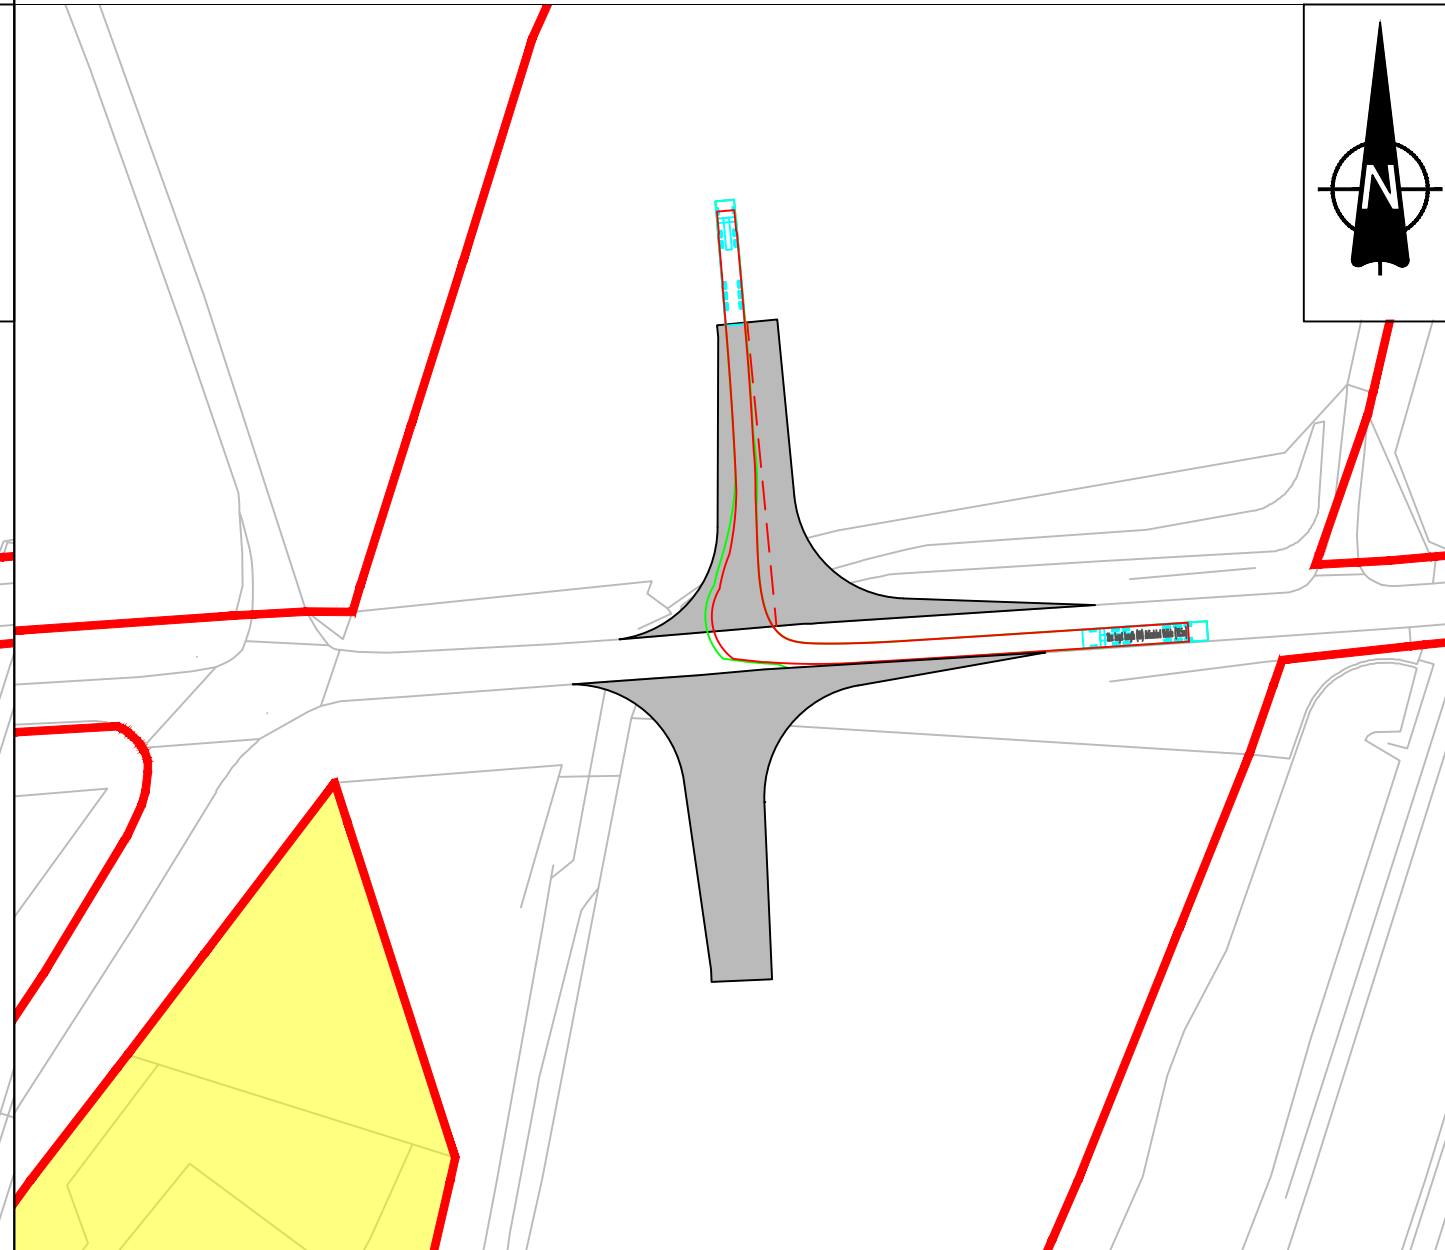

INSET F: 16.5m ARTICULATED VEHICLE HEADING WEST ON COMMON LANE AND TURNING RIGHT INTO ACCESS - SCALE 1:1000


NOTES

1. This drawing is to be read in conjunction with all other relevant documentation.
2. Do not scale from this drawing, use only printed dimensions.
3. All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
4. This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
5. Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required Junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
6. The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
7. Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
8. Junction visibility for the access is based upon DMRB CD109 Table 2.10.

LEGEND

-  Extent of Access Footprint
-  Order Limits
-  Land Excluded from Order Limits
-  Vehicle Body
-  Vehicle Body Path
-  Vehicle Load
-  Vehicle Load Path
-  Vehicle Wheels Path
-  Edge of Road
-  Access Centreline
-  Junction Visibility
-  Vegetation to be Removed for Vis Splay
-  Indicative Hedgerow Removal Vis Splay
-  Indicative Hedgerow Removal for Bellmouth Access
-  Health and Safety Risk Identifier
-  Existing Public Right of Way

SHEET PLAN

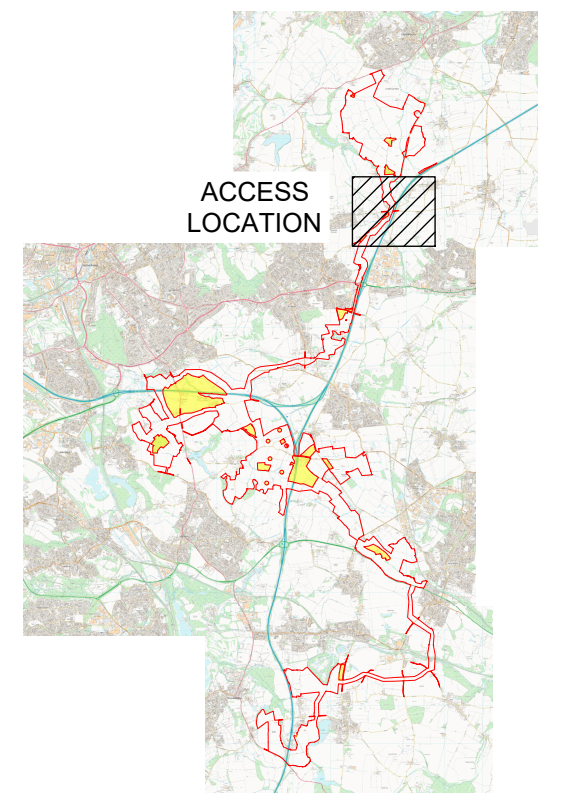

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:
Cable Corridor Area Access CC-01
Appendix 3 - Sheet 30 of 53
Whitestone Solar Farm
Regulation 5(2)(o)

DRAWING DATE: 03/06/2026

SCALE: 1:1000

SHEET: Sheet 30 of 53


SIZE: A1

REVIS


DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020




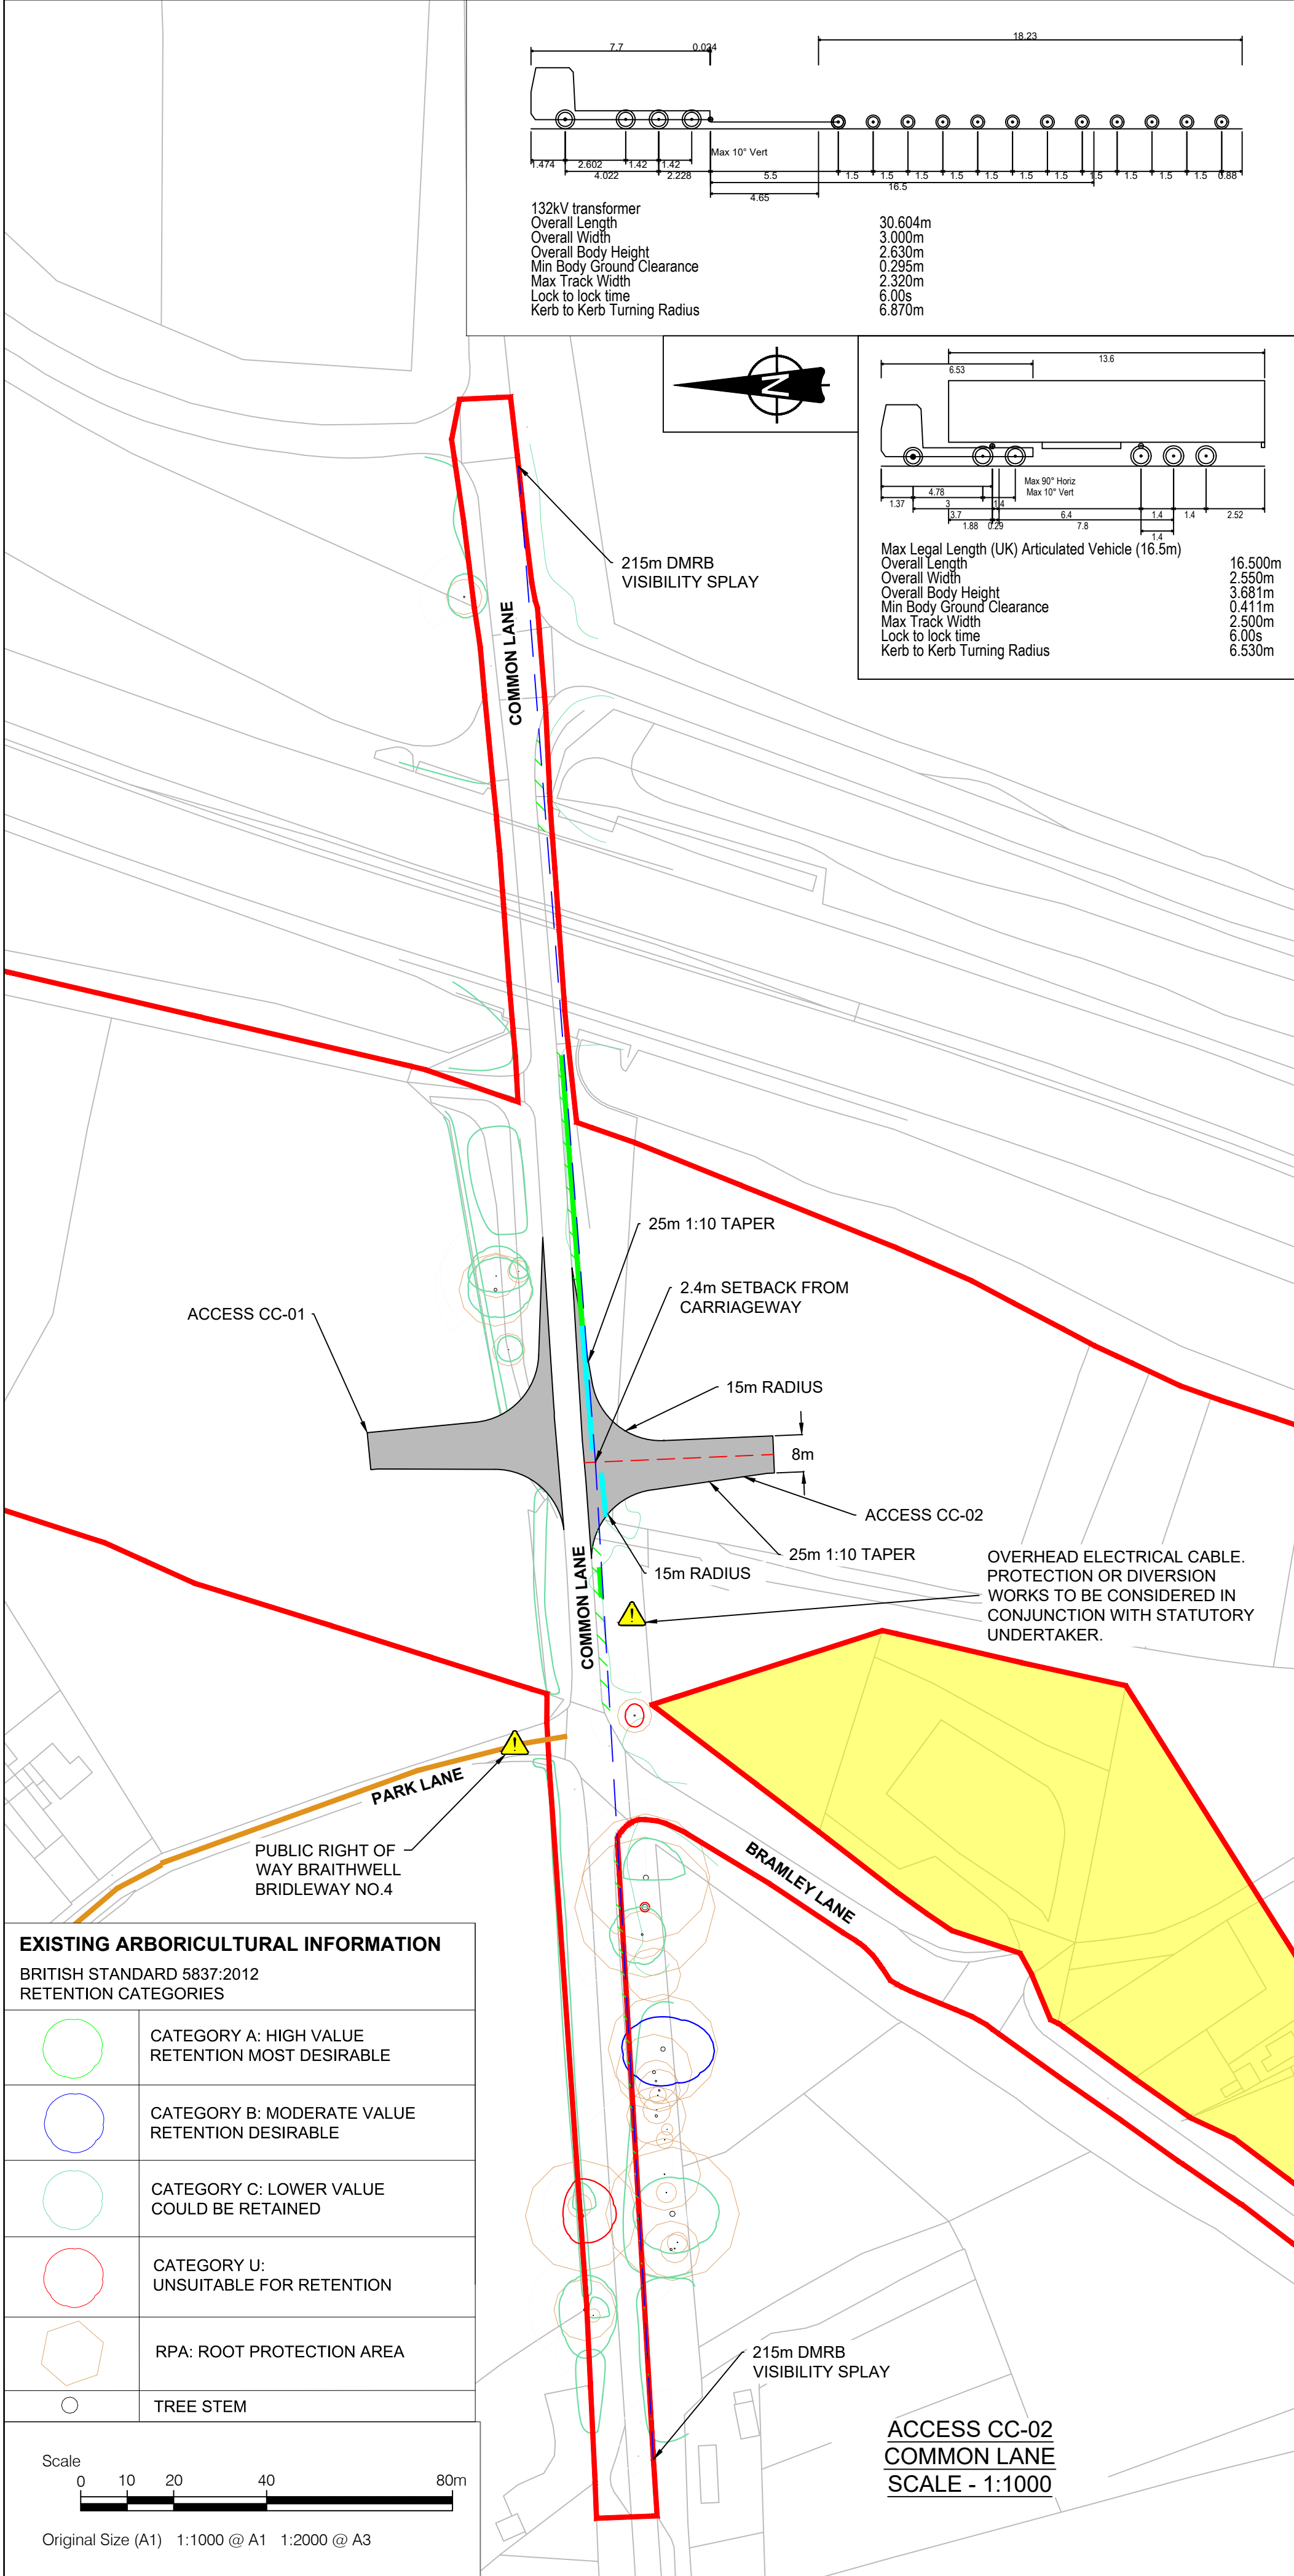

ABNORMAL LOAD ACCESS AND EGRESS MOVEMENTS TO BE CONTROLLED TO ENSURE MANOEUVRES ARE COMPLETED SAFELY. ANY OTHER CONSTRUCTION VEHICLES WISHING TO EGRESS DURING ABNORMAL LOAD DELIVERIES ARE TO BE HELD WITHIN THE SITE TO AVOID VEHICULAR CONFLICTS

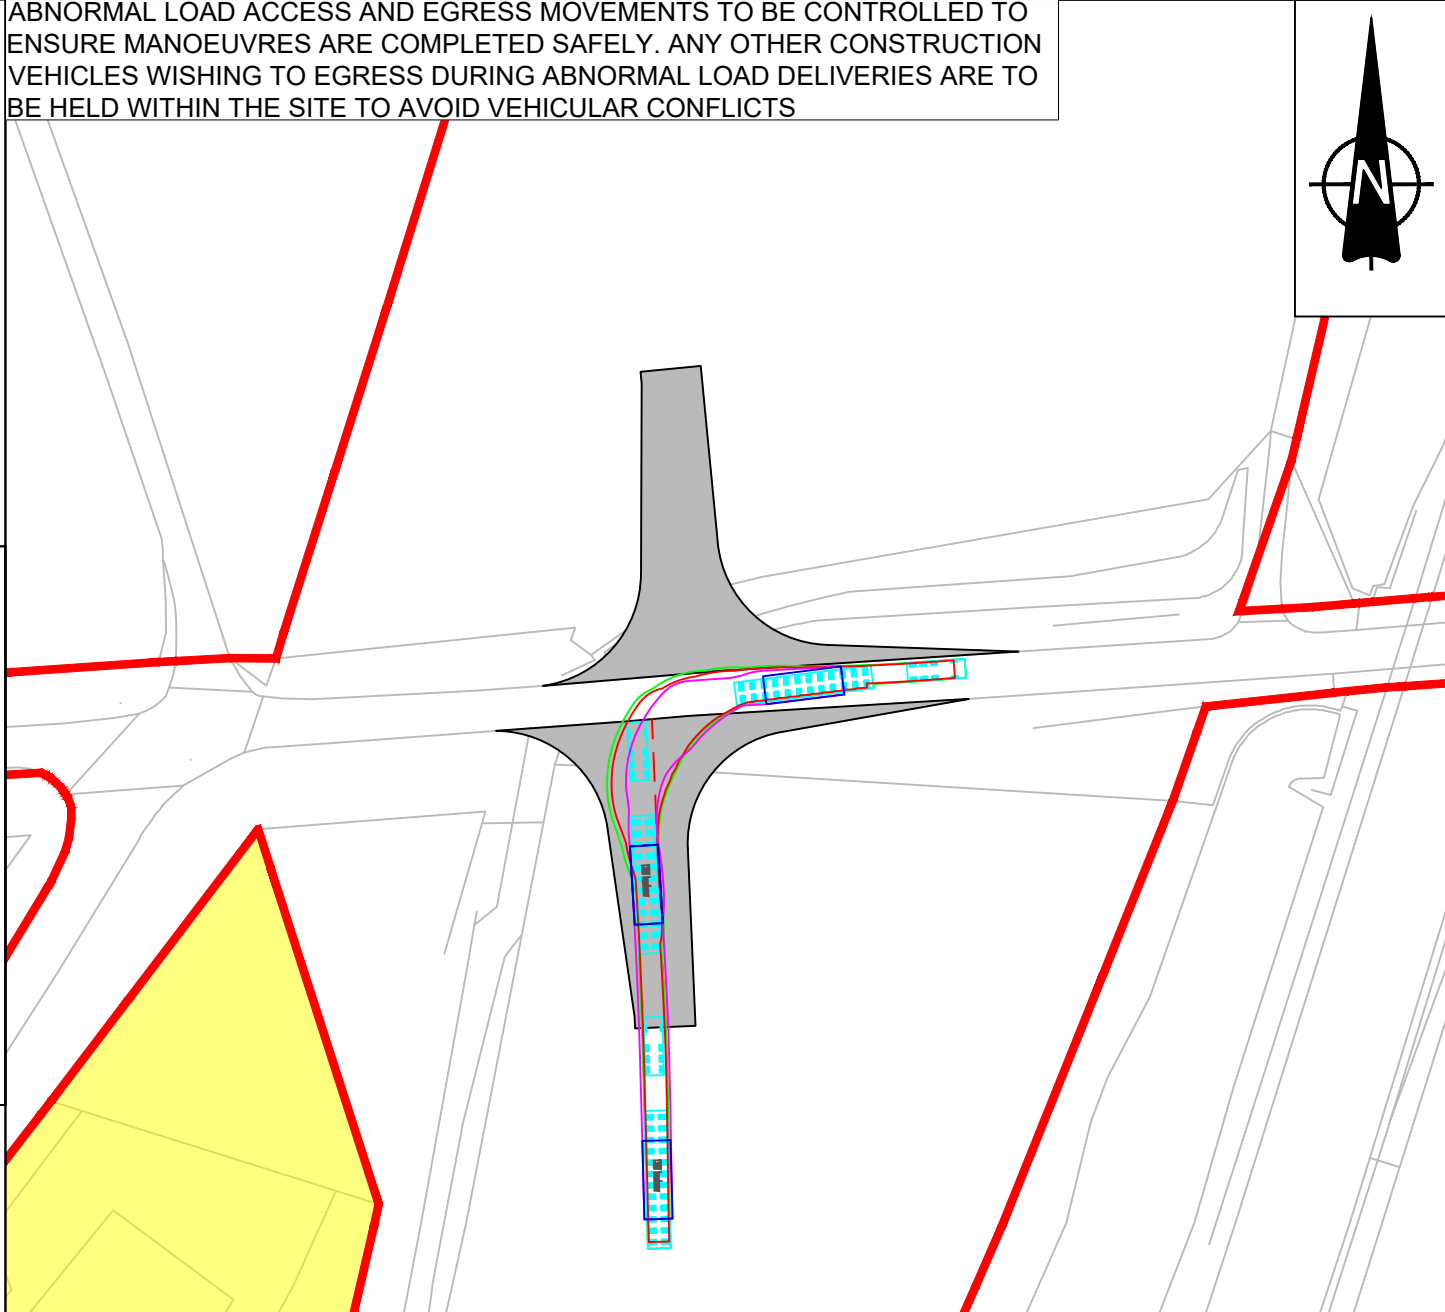


INSET A: 31m 132kV TRANSFORMER VEHICLE TURNING RIGHT OUT OF ACCESS ONTO COMMON LANE
HEADING EAST - SCALE 1:1000

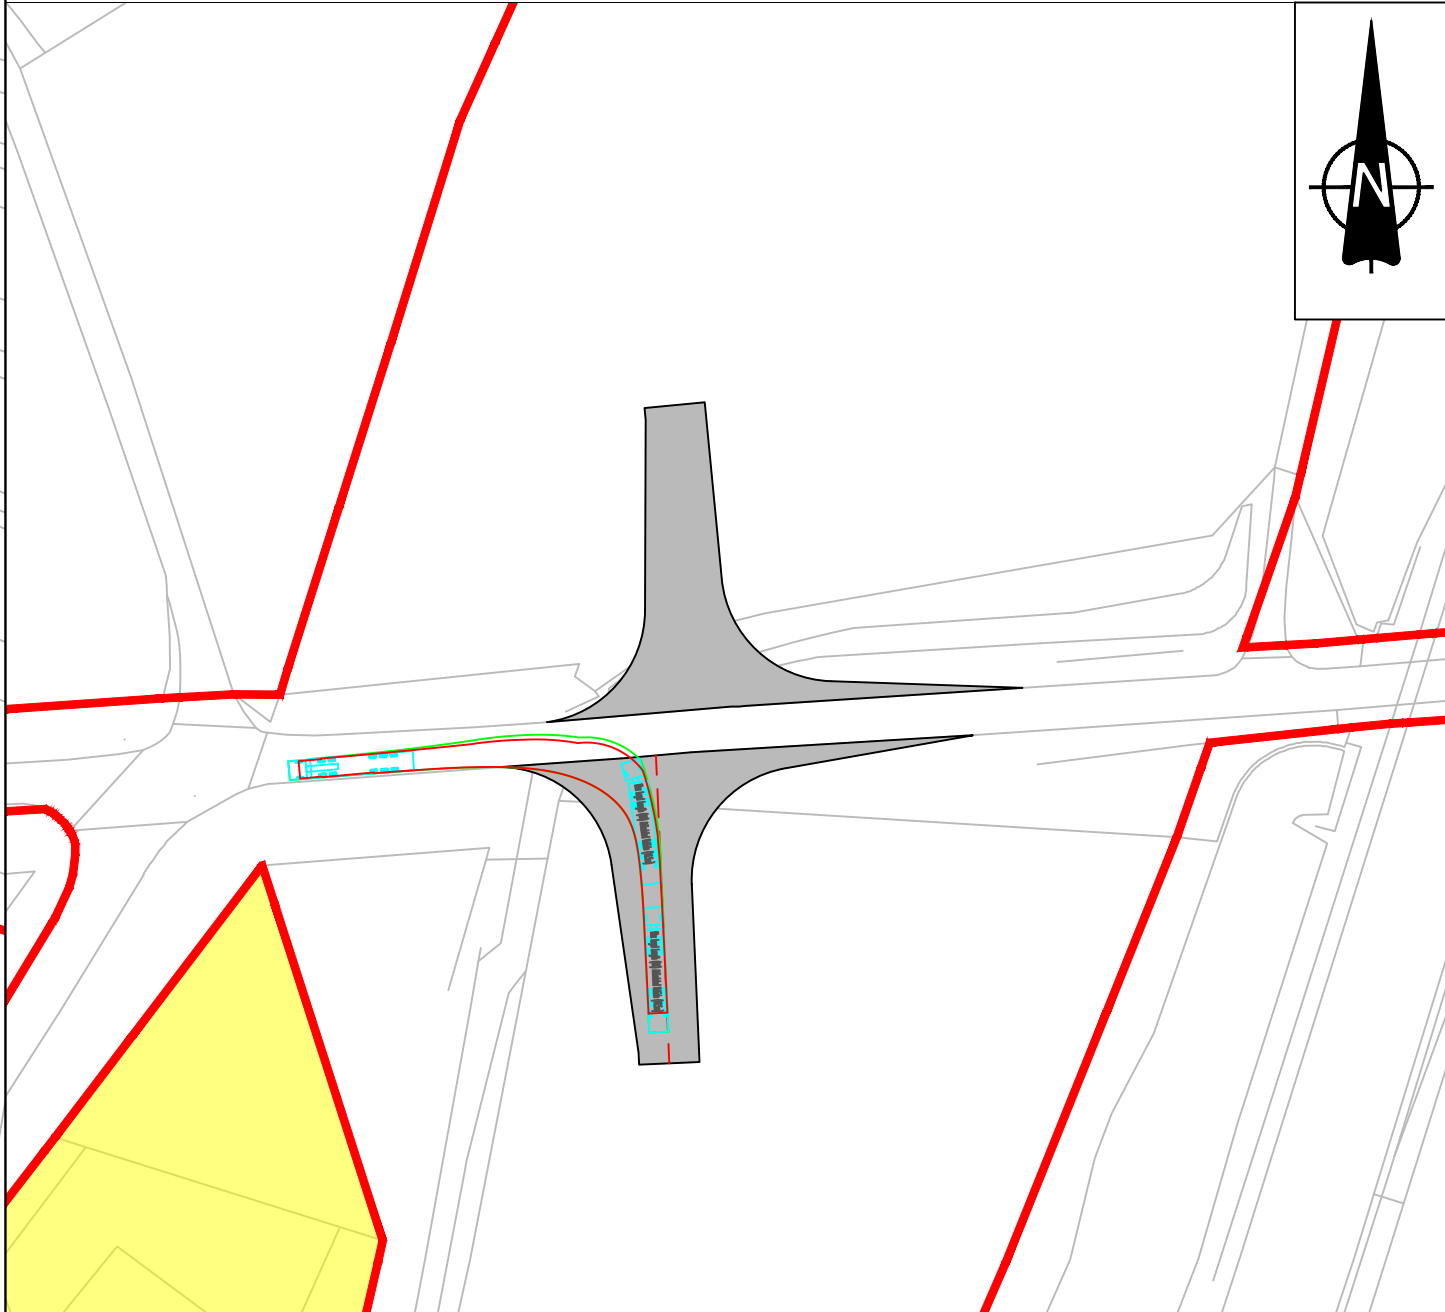


INSET C: 16.5m ARTICULATED VEHICLE TURNING LEFT OUT OF ACCESS ONTO COMMON LANE HEADING
WEST - SCALE 1:1000


ABNORMAL LOAD ACCESS AND EGRESS MOVEMENTS TO BE CONTROLLED TO ENSURE MANOEUVRES ARE COMPLETED SAFELY. ANY OTHER CONSTRUCTION VEHICLES WISHING TO EGRESS DURING ABNORMAL LOAD DELIVERIES ARE TO BE HELD WITHIN THE SITE TO AVOID VEHICULAR CONFLICTS

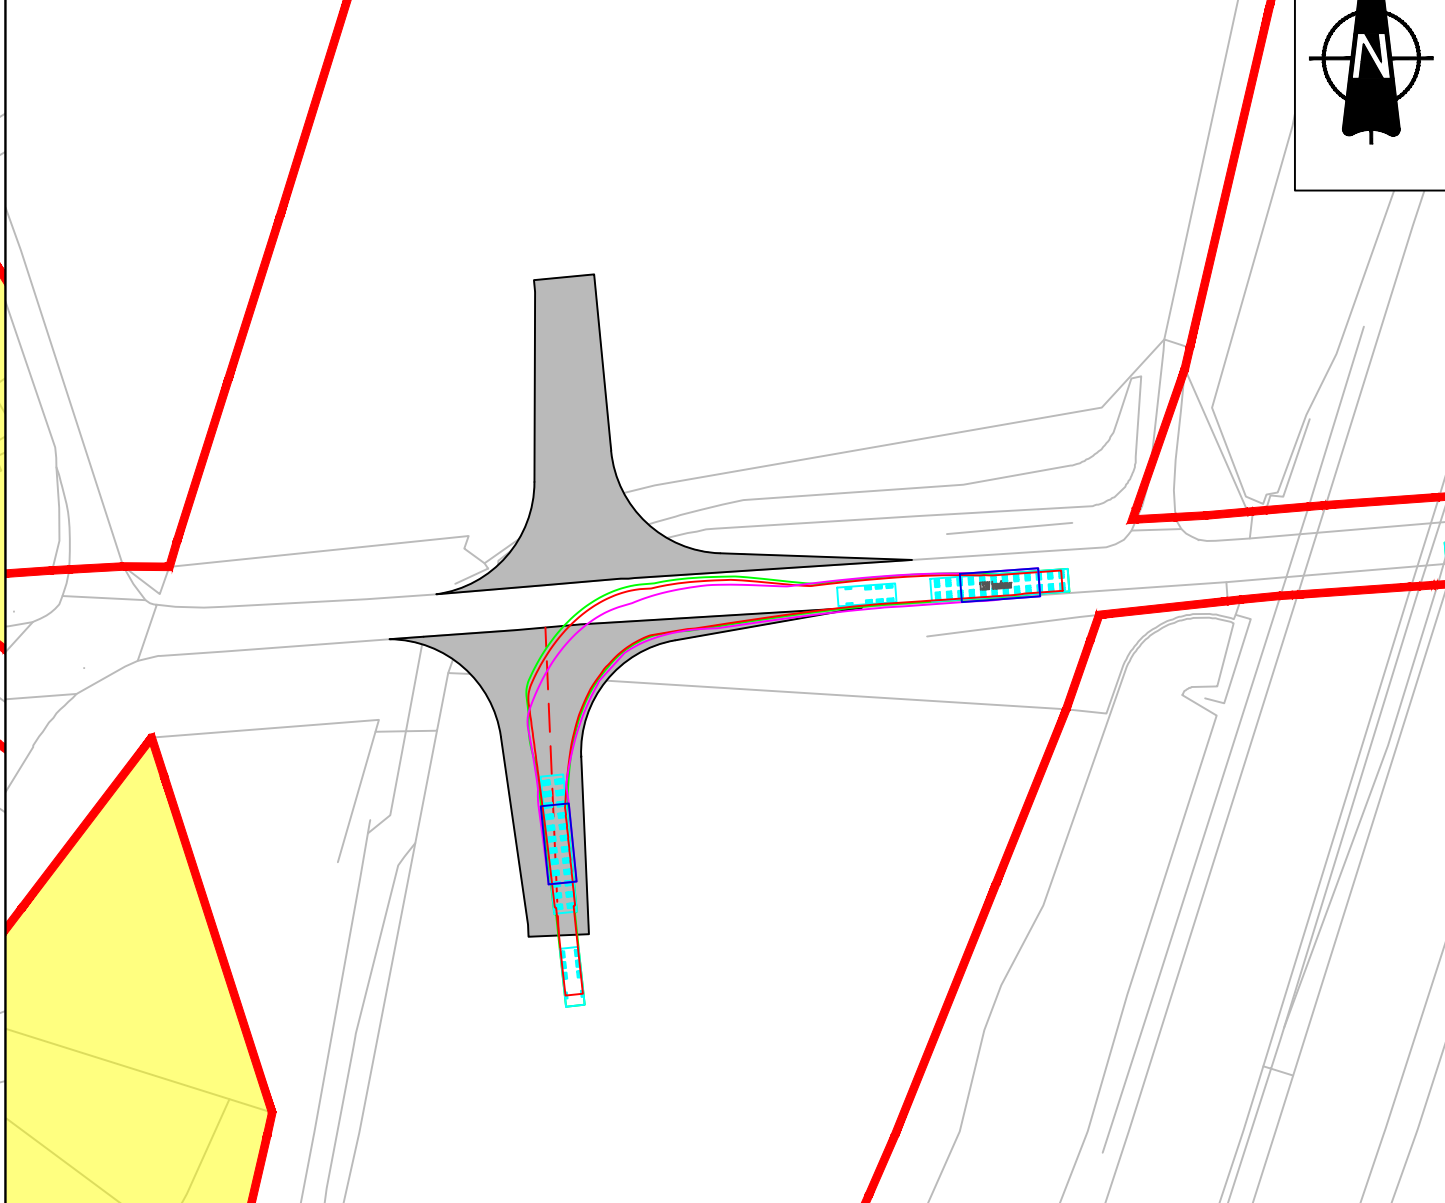


INSET E: 31m 132kV TRANSFORMER VEHICLE HEADING WEST ON COMMON LANE AND TURNING LEFT
INTO ACCESS - SCALE 1:1000

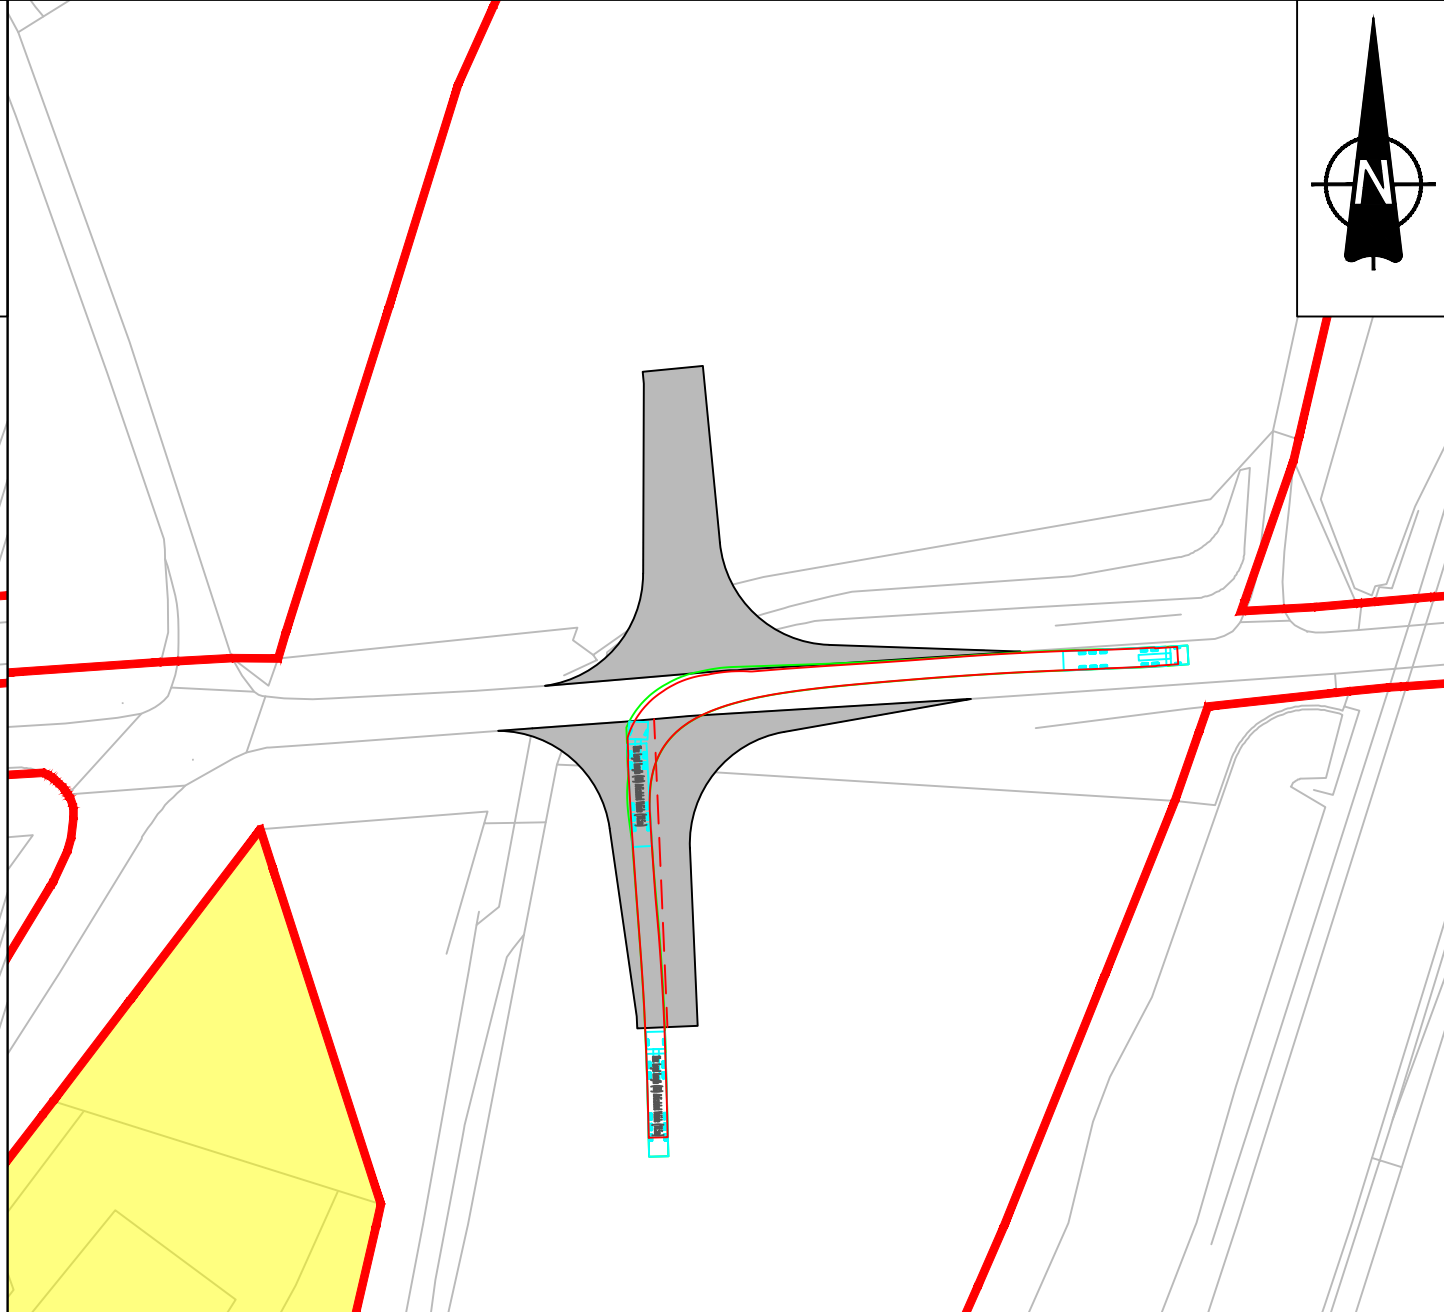

INSET B: 16.5m ARTICULATED VEHICLE TURNING RIGHT OUT OF ACCESS ONTO COMMON LANE
HEADING EAST - SCALE 1:1000

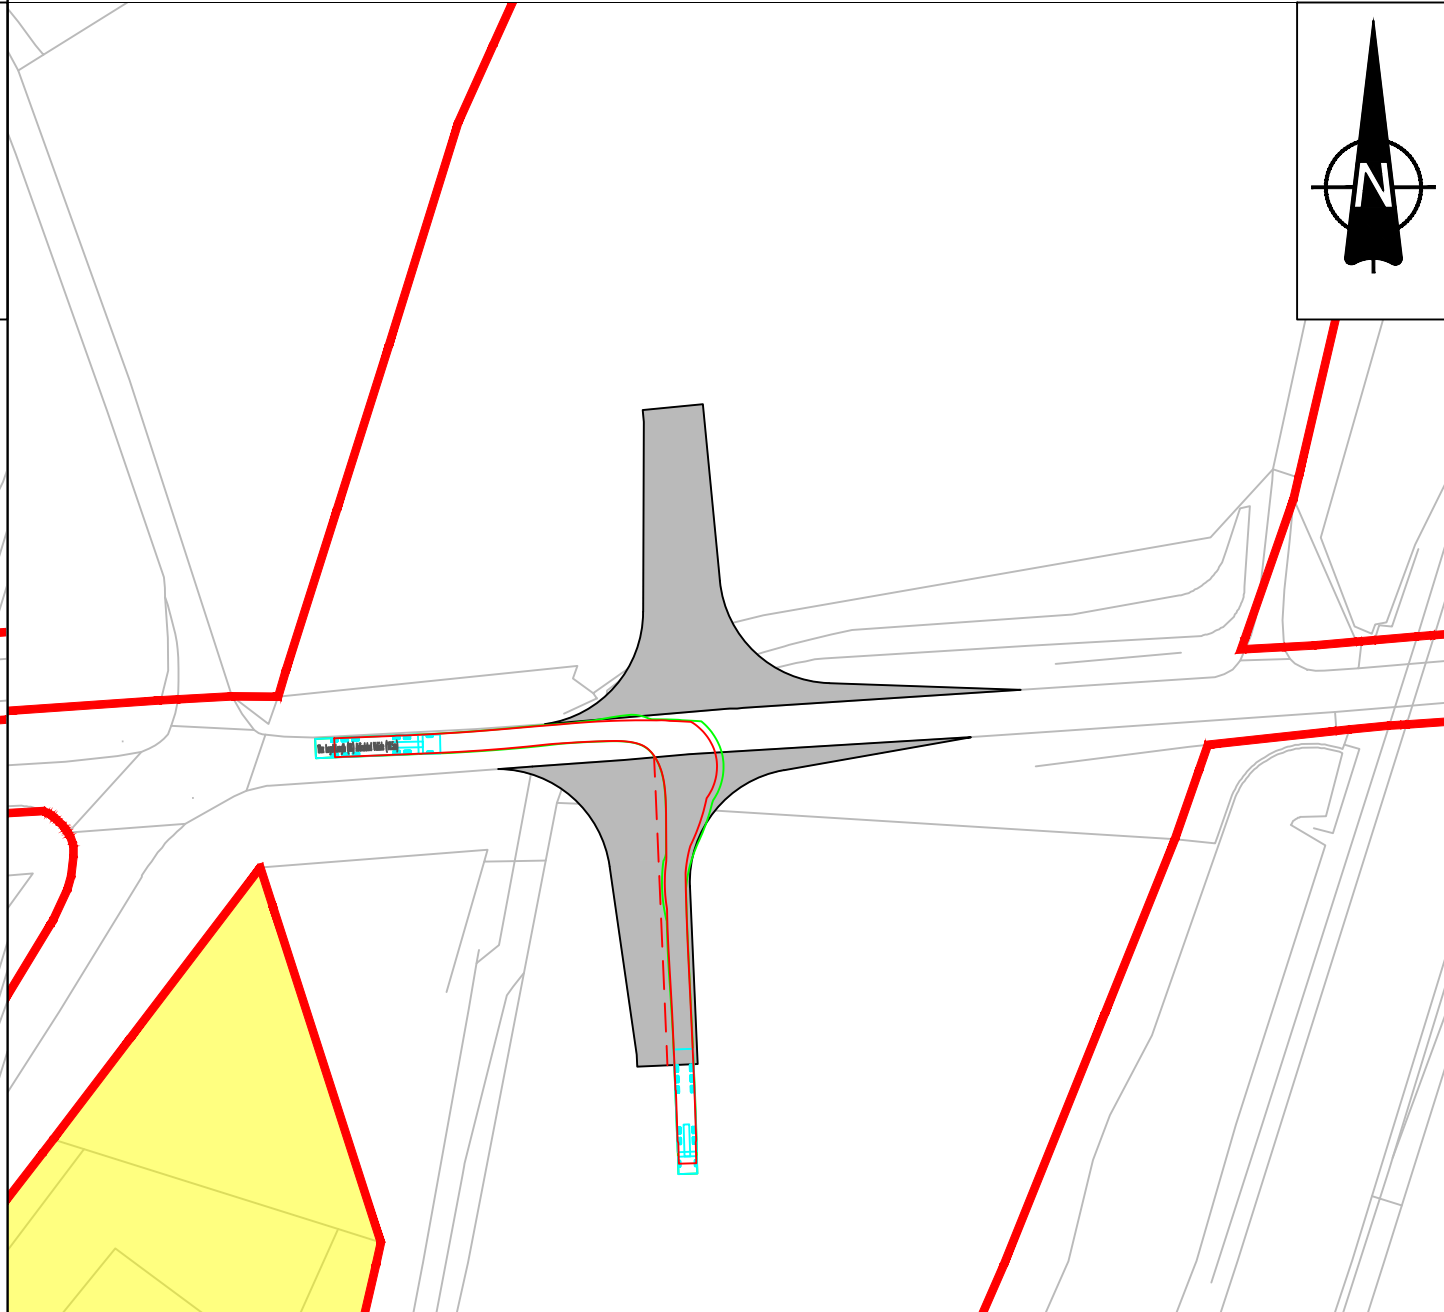

INSET D: 16.5m ARTICULATED VEHICLE HEADING EAST ON COMMON LANE AND TURNING RIGHT INTO
ACCESS - SCALE 1:1000

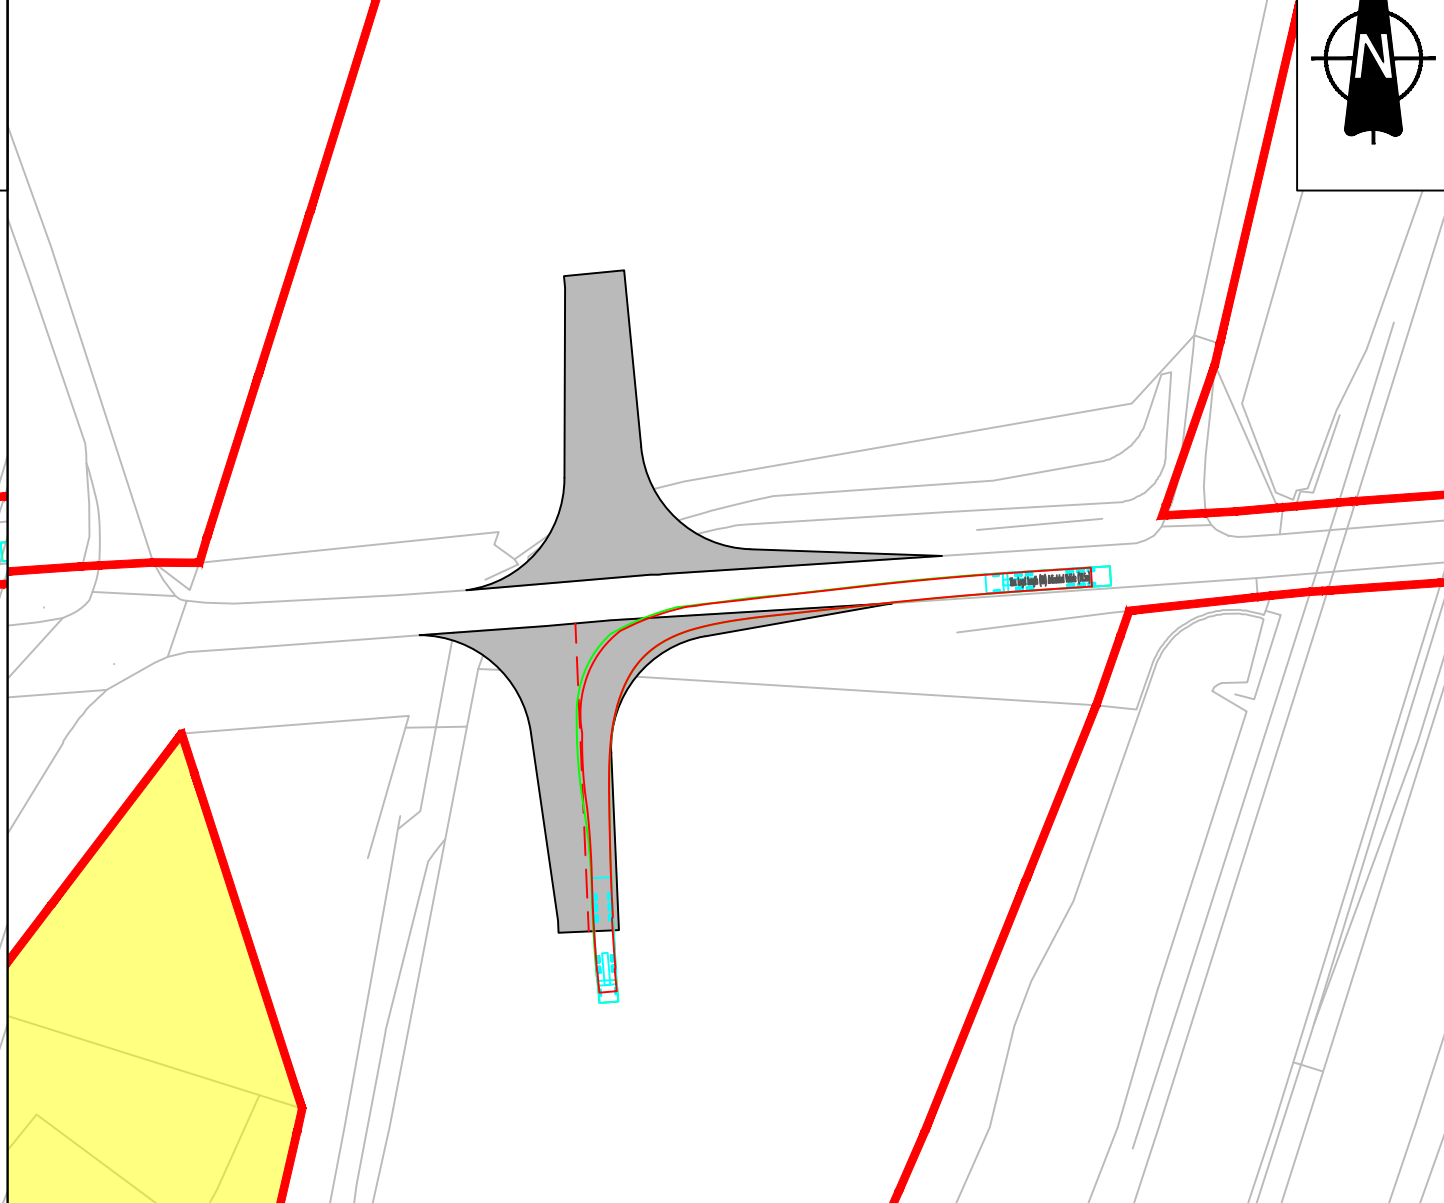

INSET F: 16.5m ARTICULATED VEHICLE HEADING WEST ON COMMON LANE AND TURNING LEFT INTO
ACCESS - SCALE 1:1000


NOTES

- This drawing is to be read in conjunction with all other relevant documentation.
- Do not scale from this drawing, use only printed dimensions.
- All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
- This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
- Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
- The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
- Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
- Junction visibility for the access is based upon DMRB CD109 Table 2.10.

LEGEND

- Extent of Access Footprint
- Order Limits
- Land Excluded from Order Limits
- Vehicle Body
- Vehicle Body Path
- Vehicle Load
- Vehicle Load Path
- Vehicle Wheels Path
- Edge of Road
- Access Centreline
- Junction Visibility
- Vegetation to be Removed for Vis Splay
- Indicative Hedgerow Removal Vis Splay
- Indicative Hedgerow Removal for Bellmouth Access
- Health and Safety Risk Identifier
- Existing Public Right of Way

SHEET PLAN

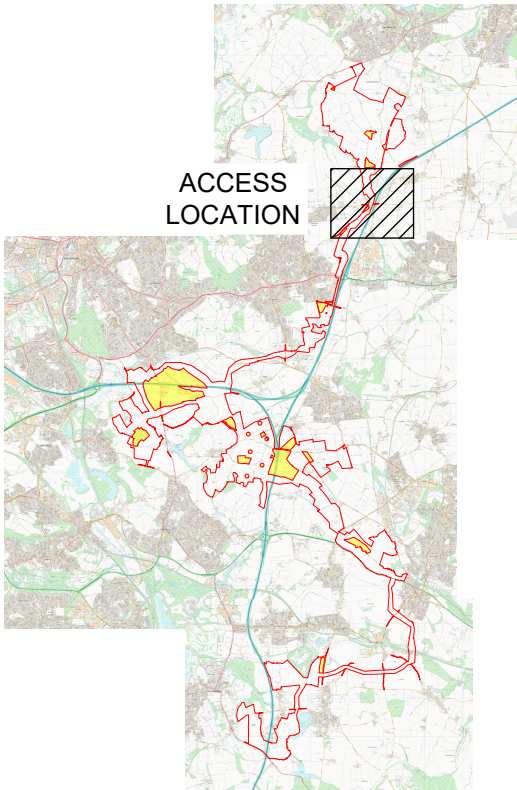

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:
Cable Corridor Area Access CC-02
Appendix 3 - Sheet 31 of 53
Whitestone Solar Farm
Regulation 5(2)(o)


DRAWING DATE: 03/06/2026

SCALE: 1:1000
SIZE: A1
SHEET: Sheet 31 of 53
REVISION: 01









DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020



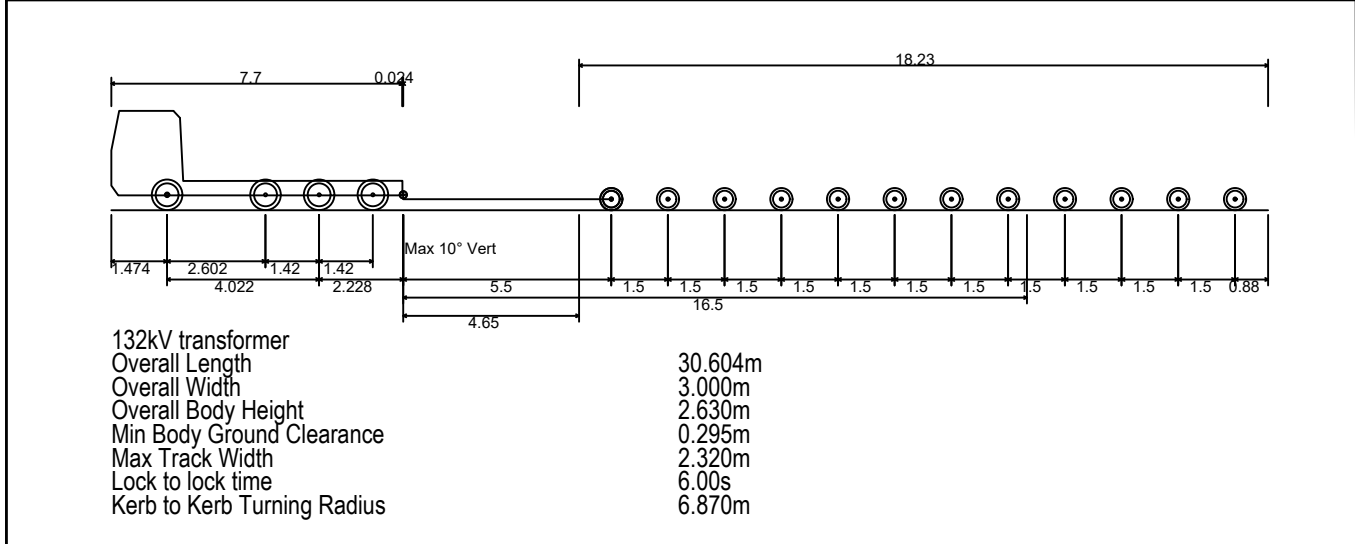

EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012	
RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

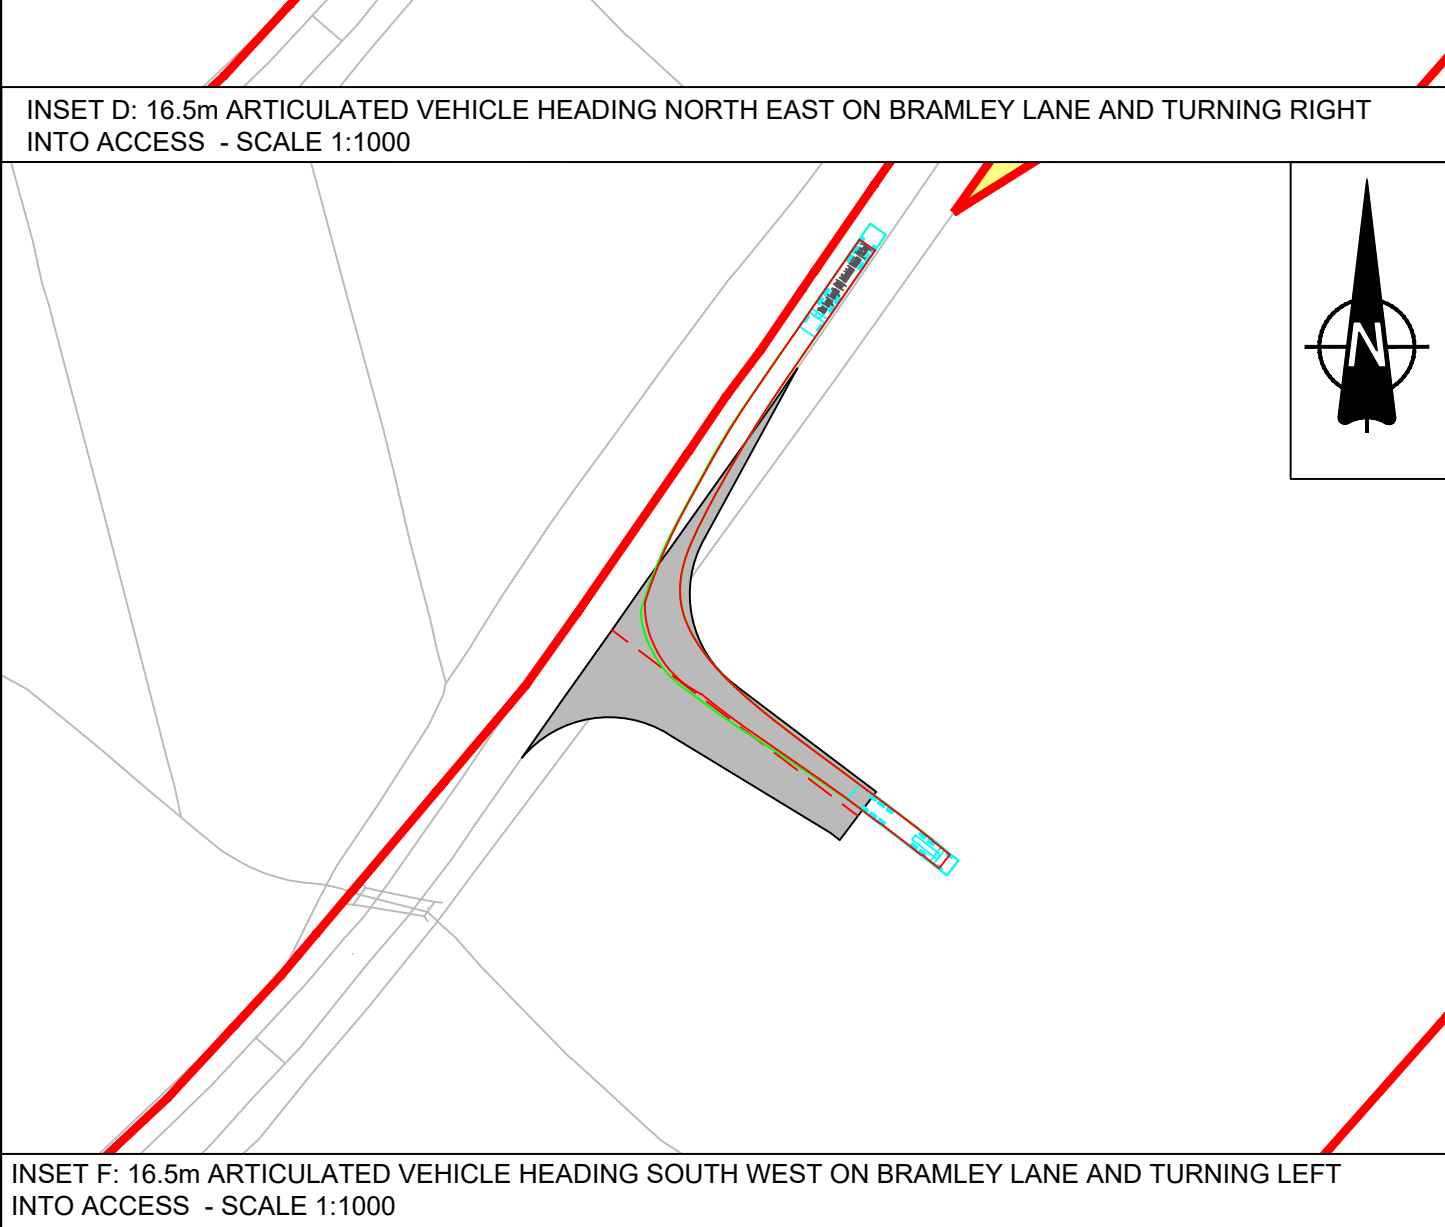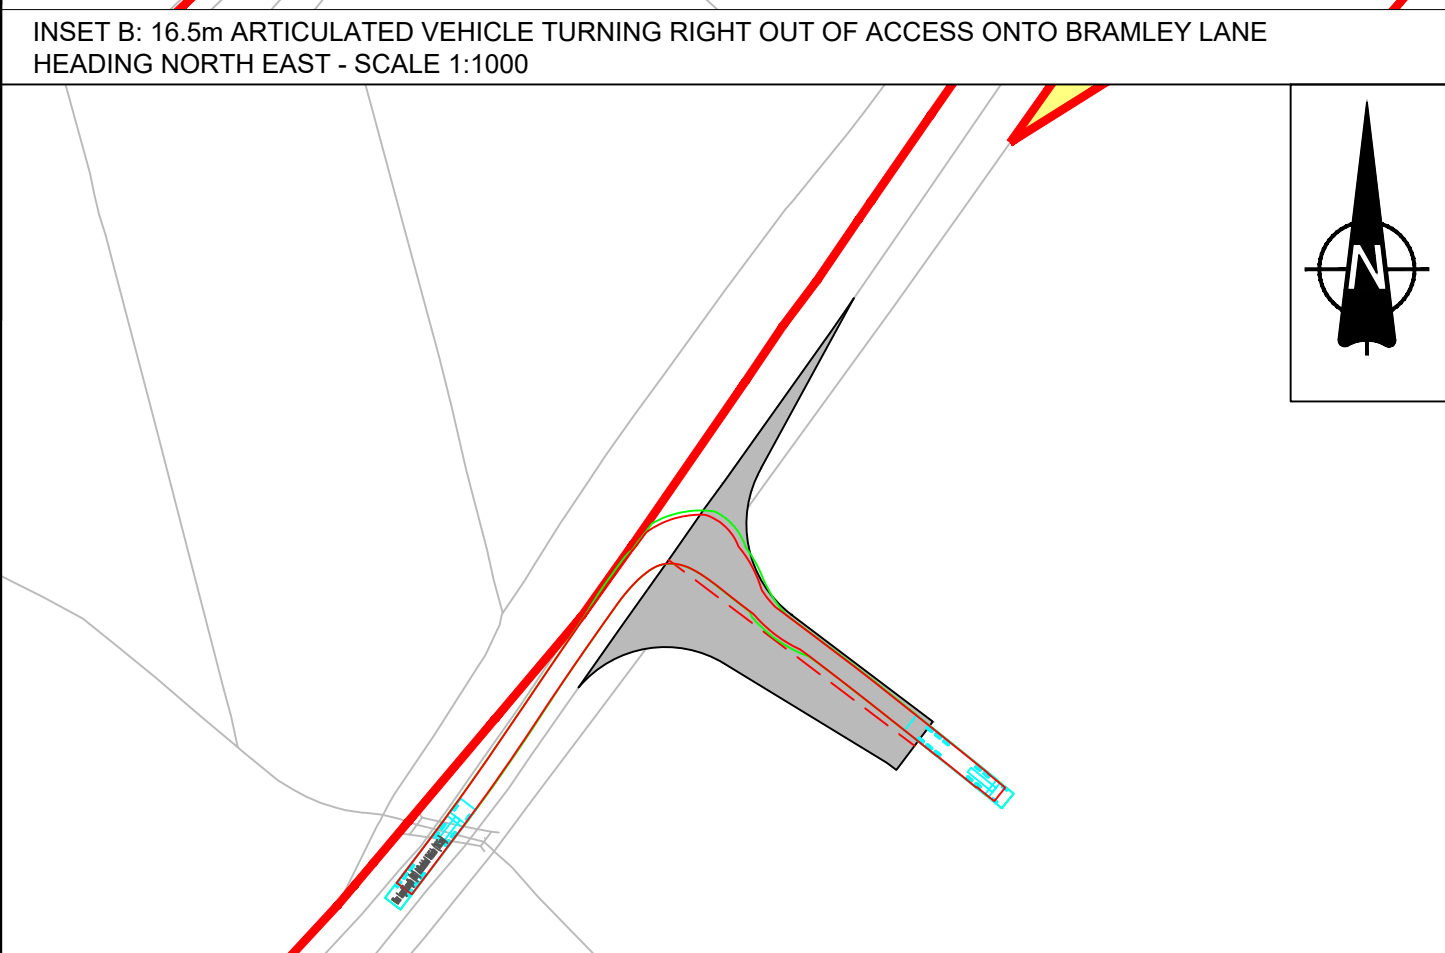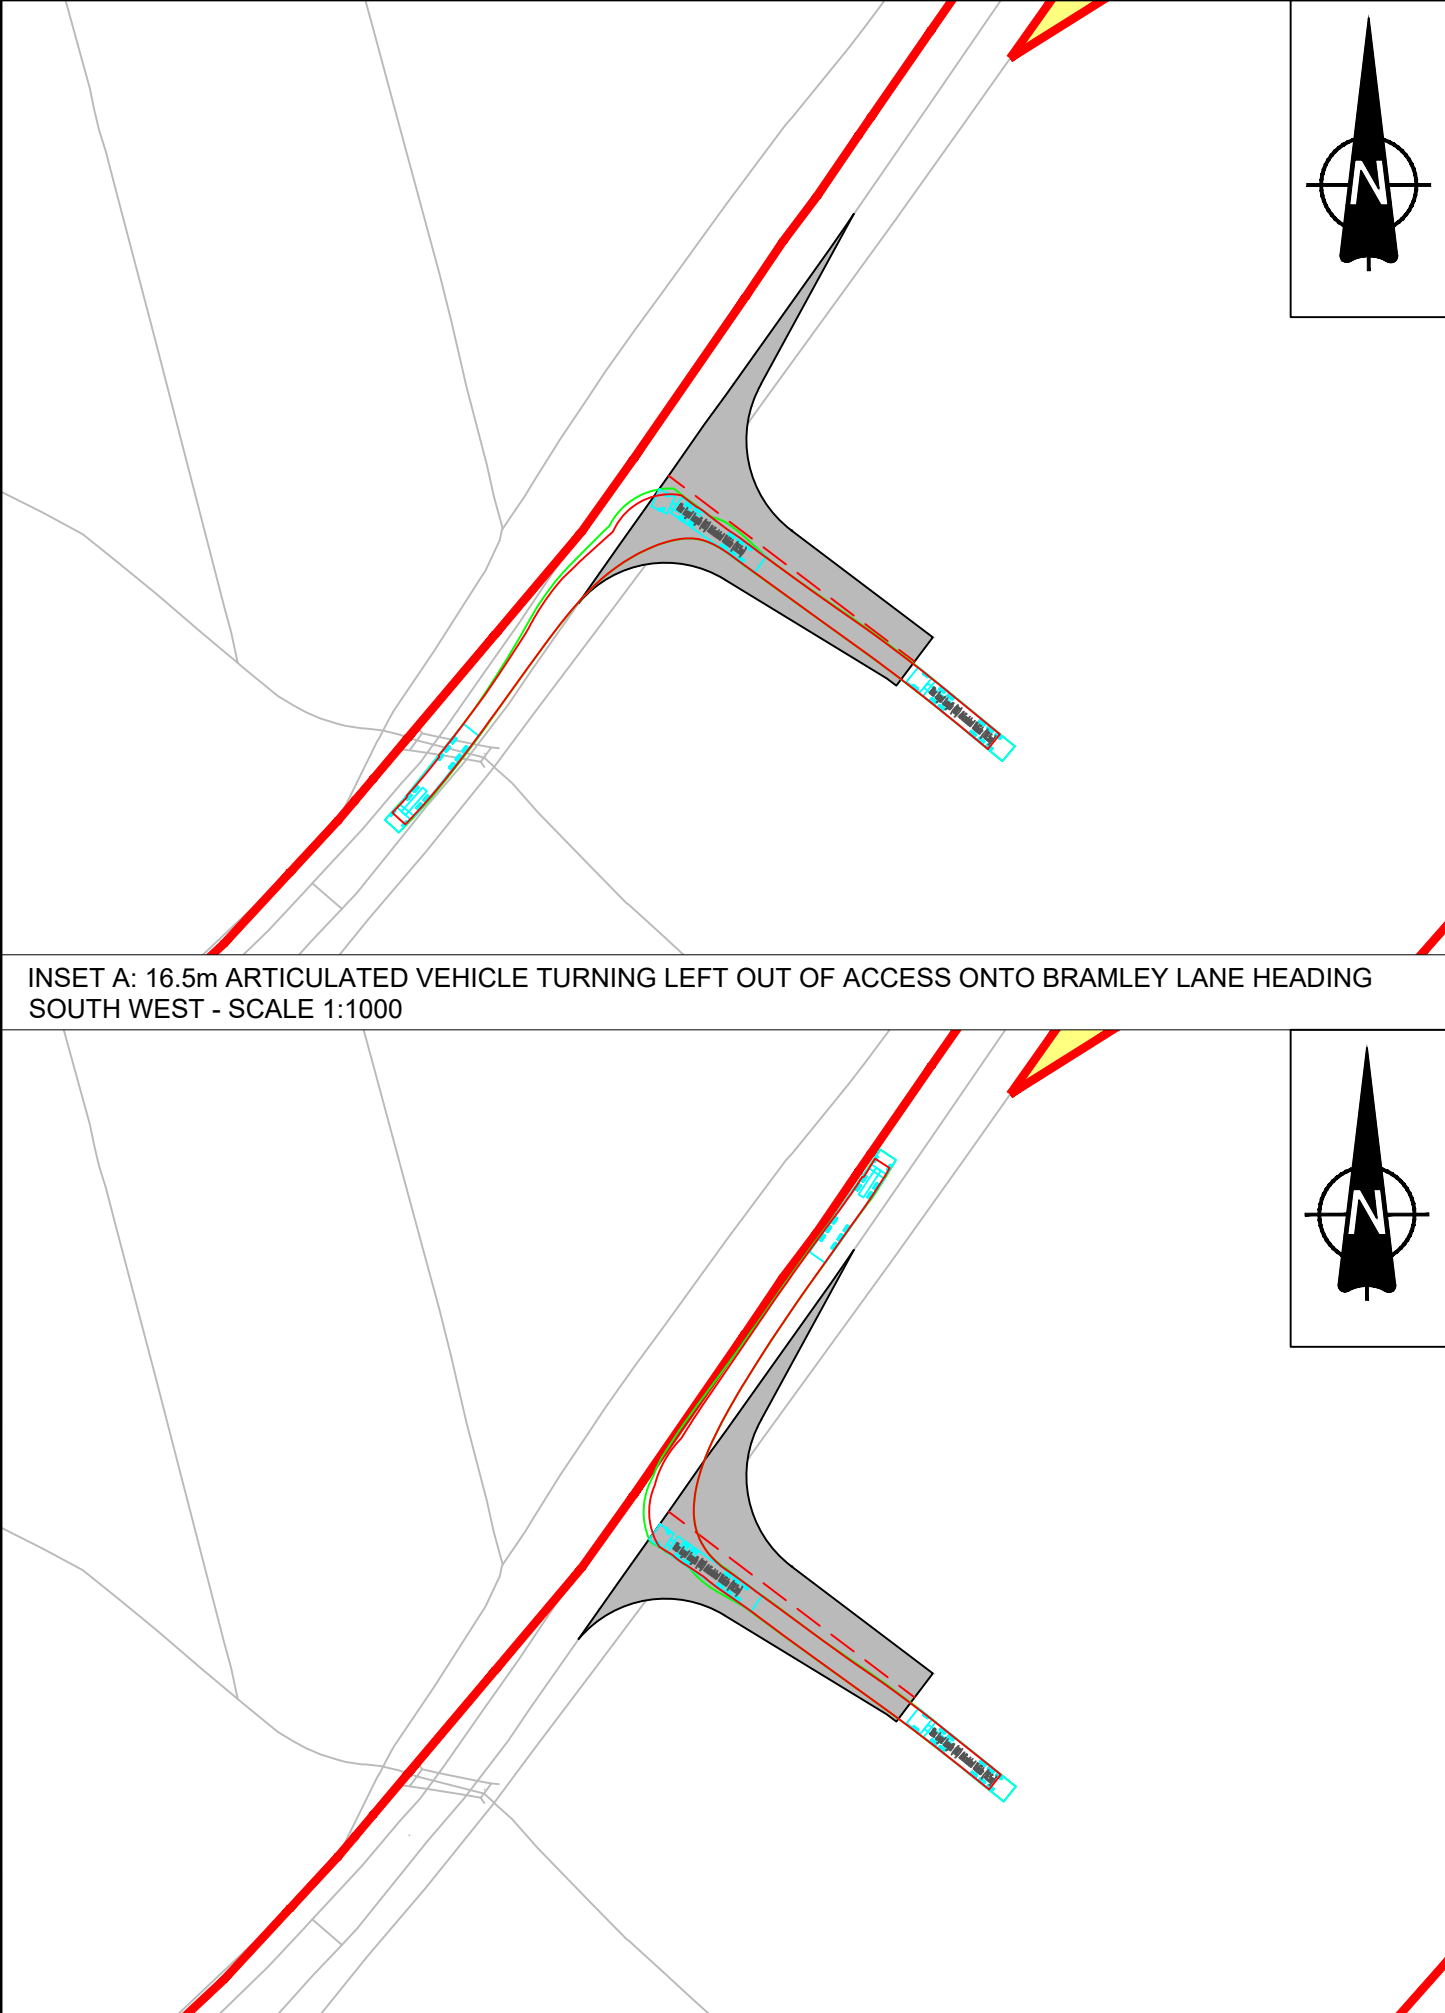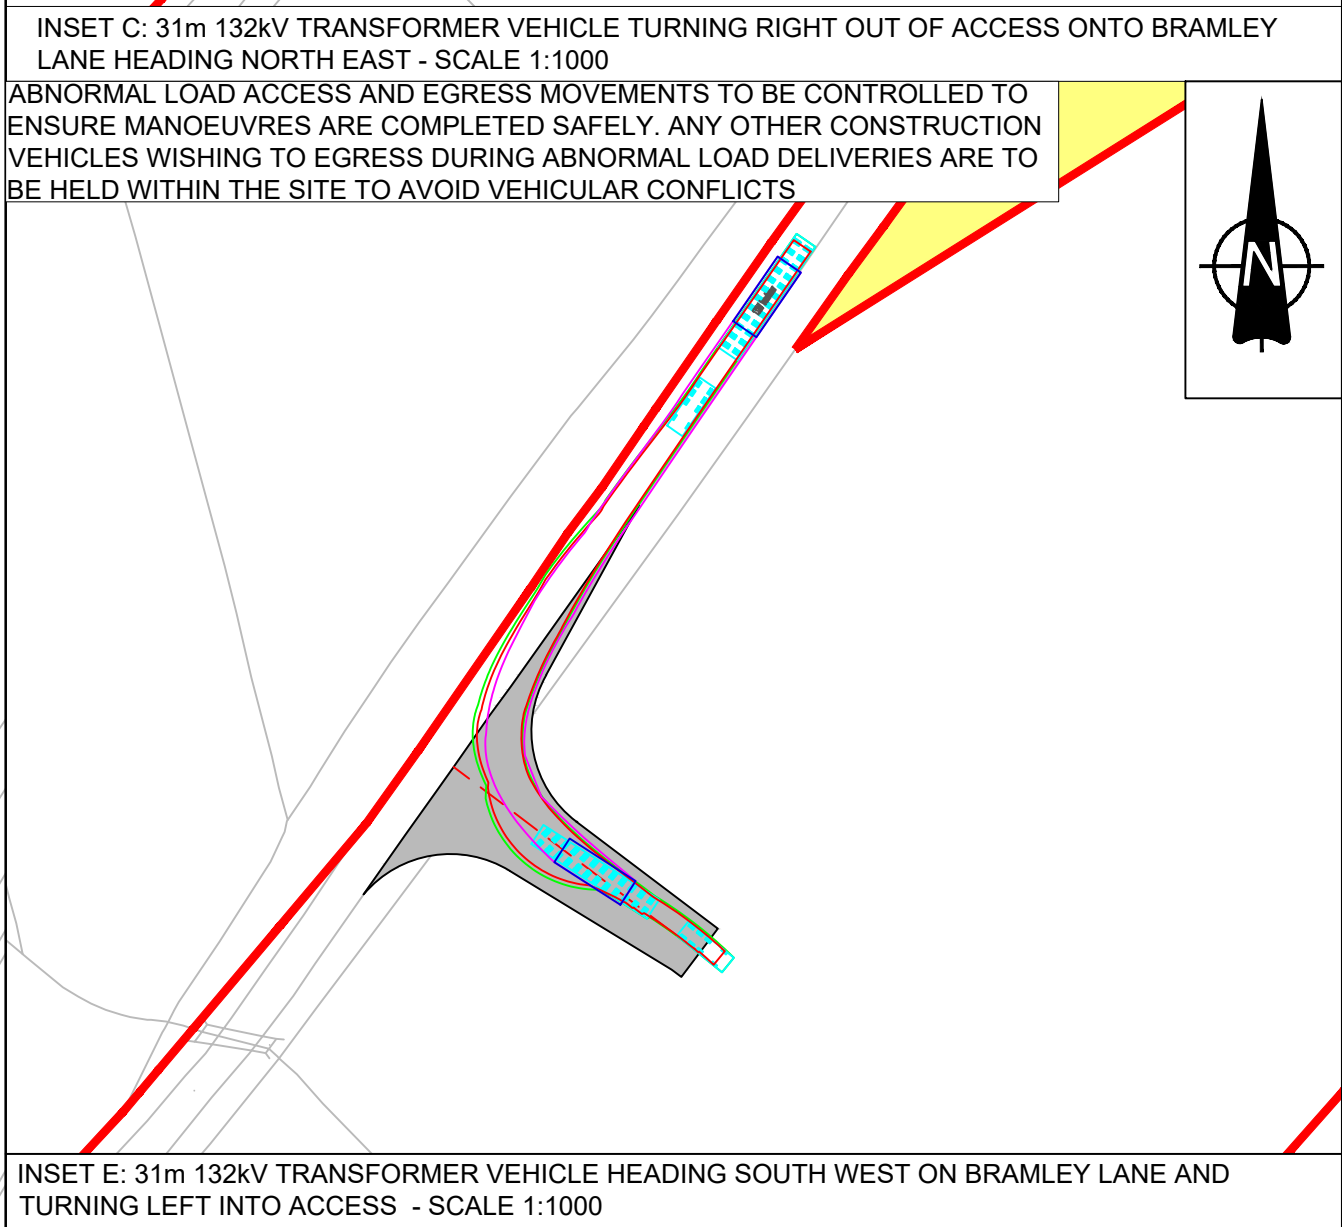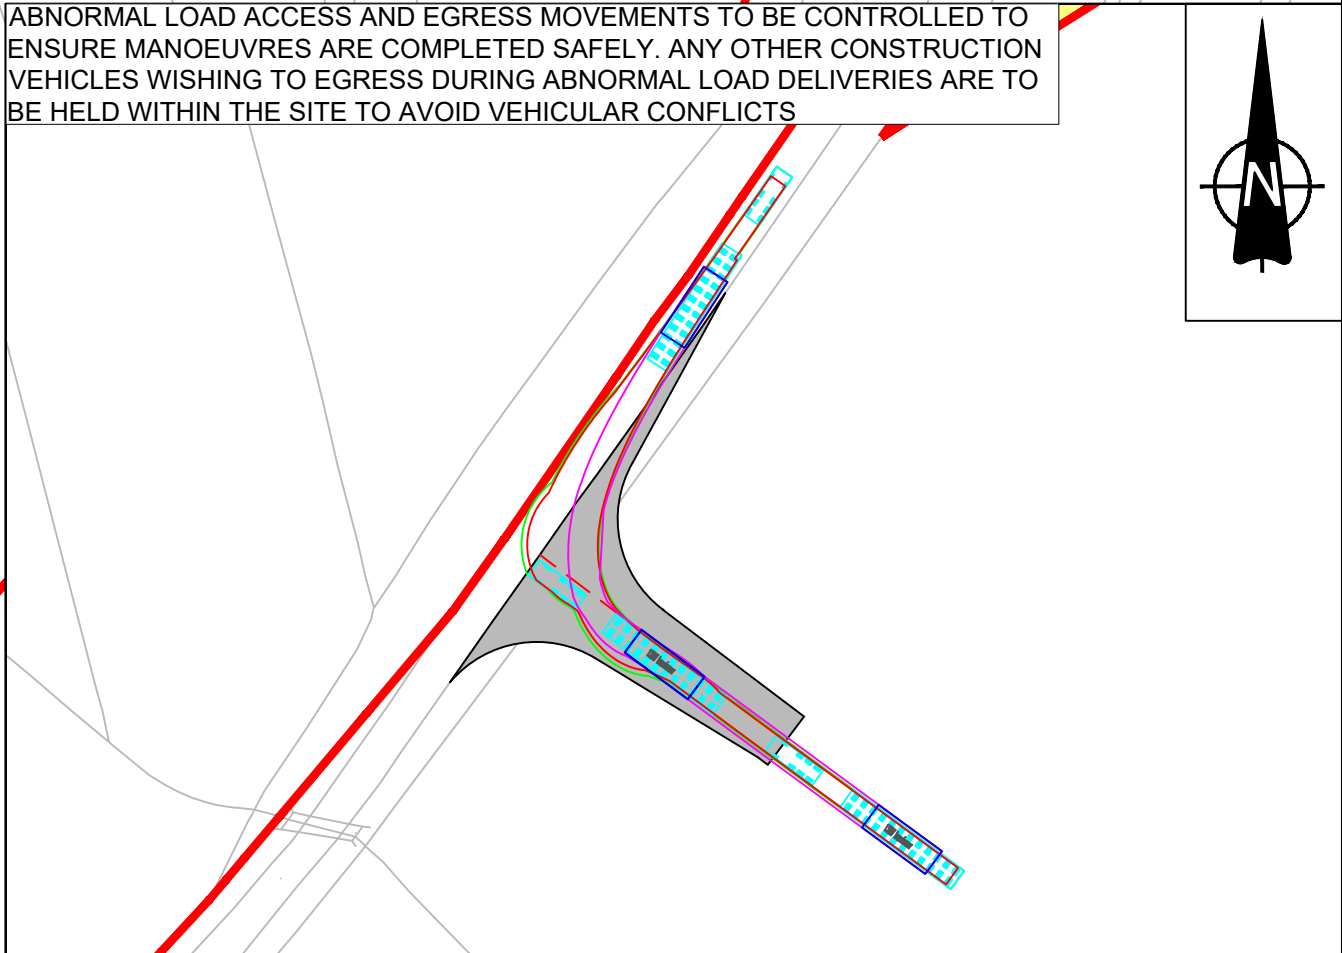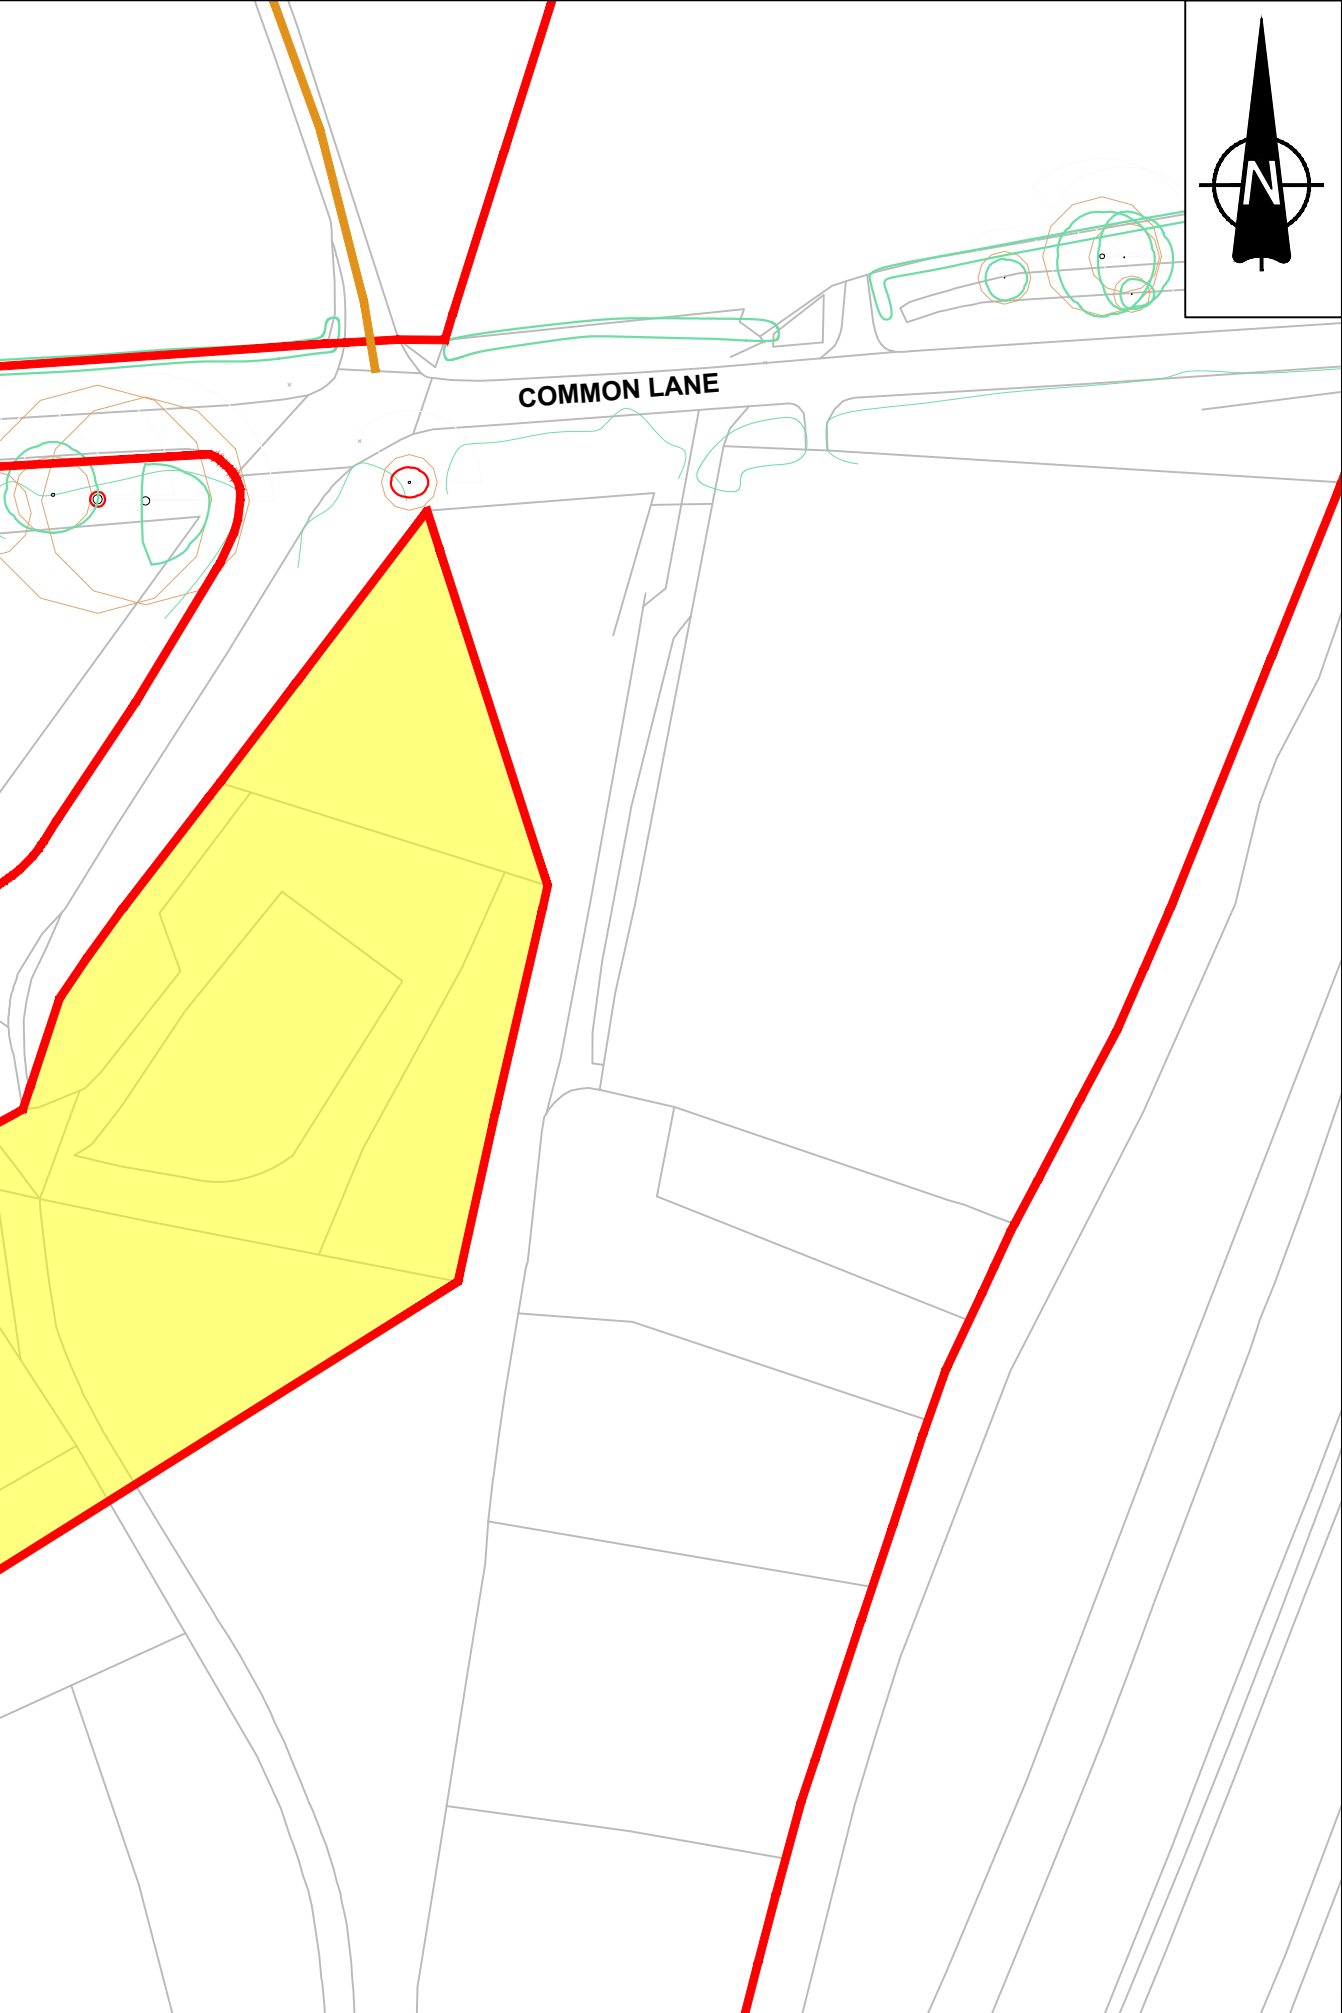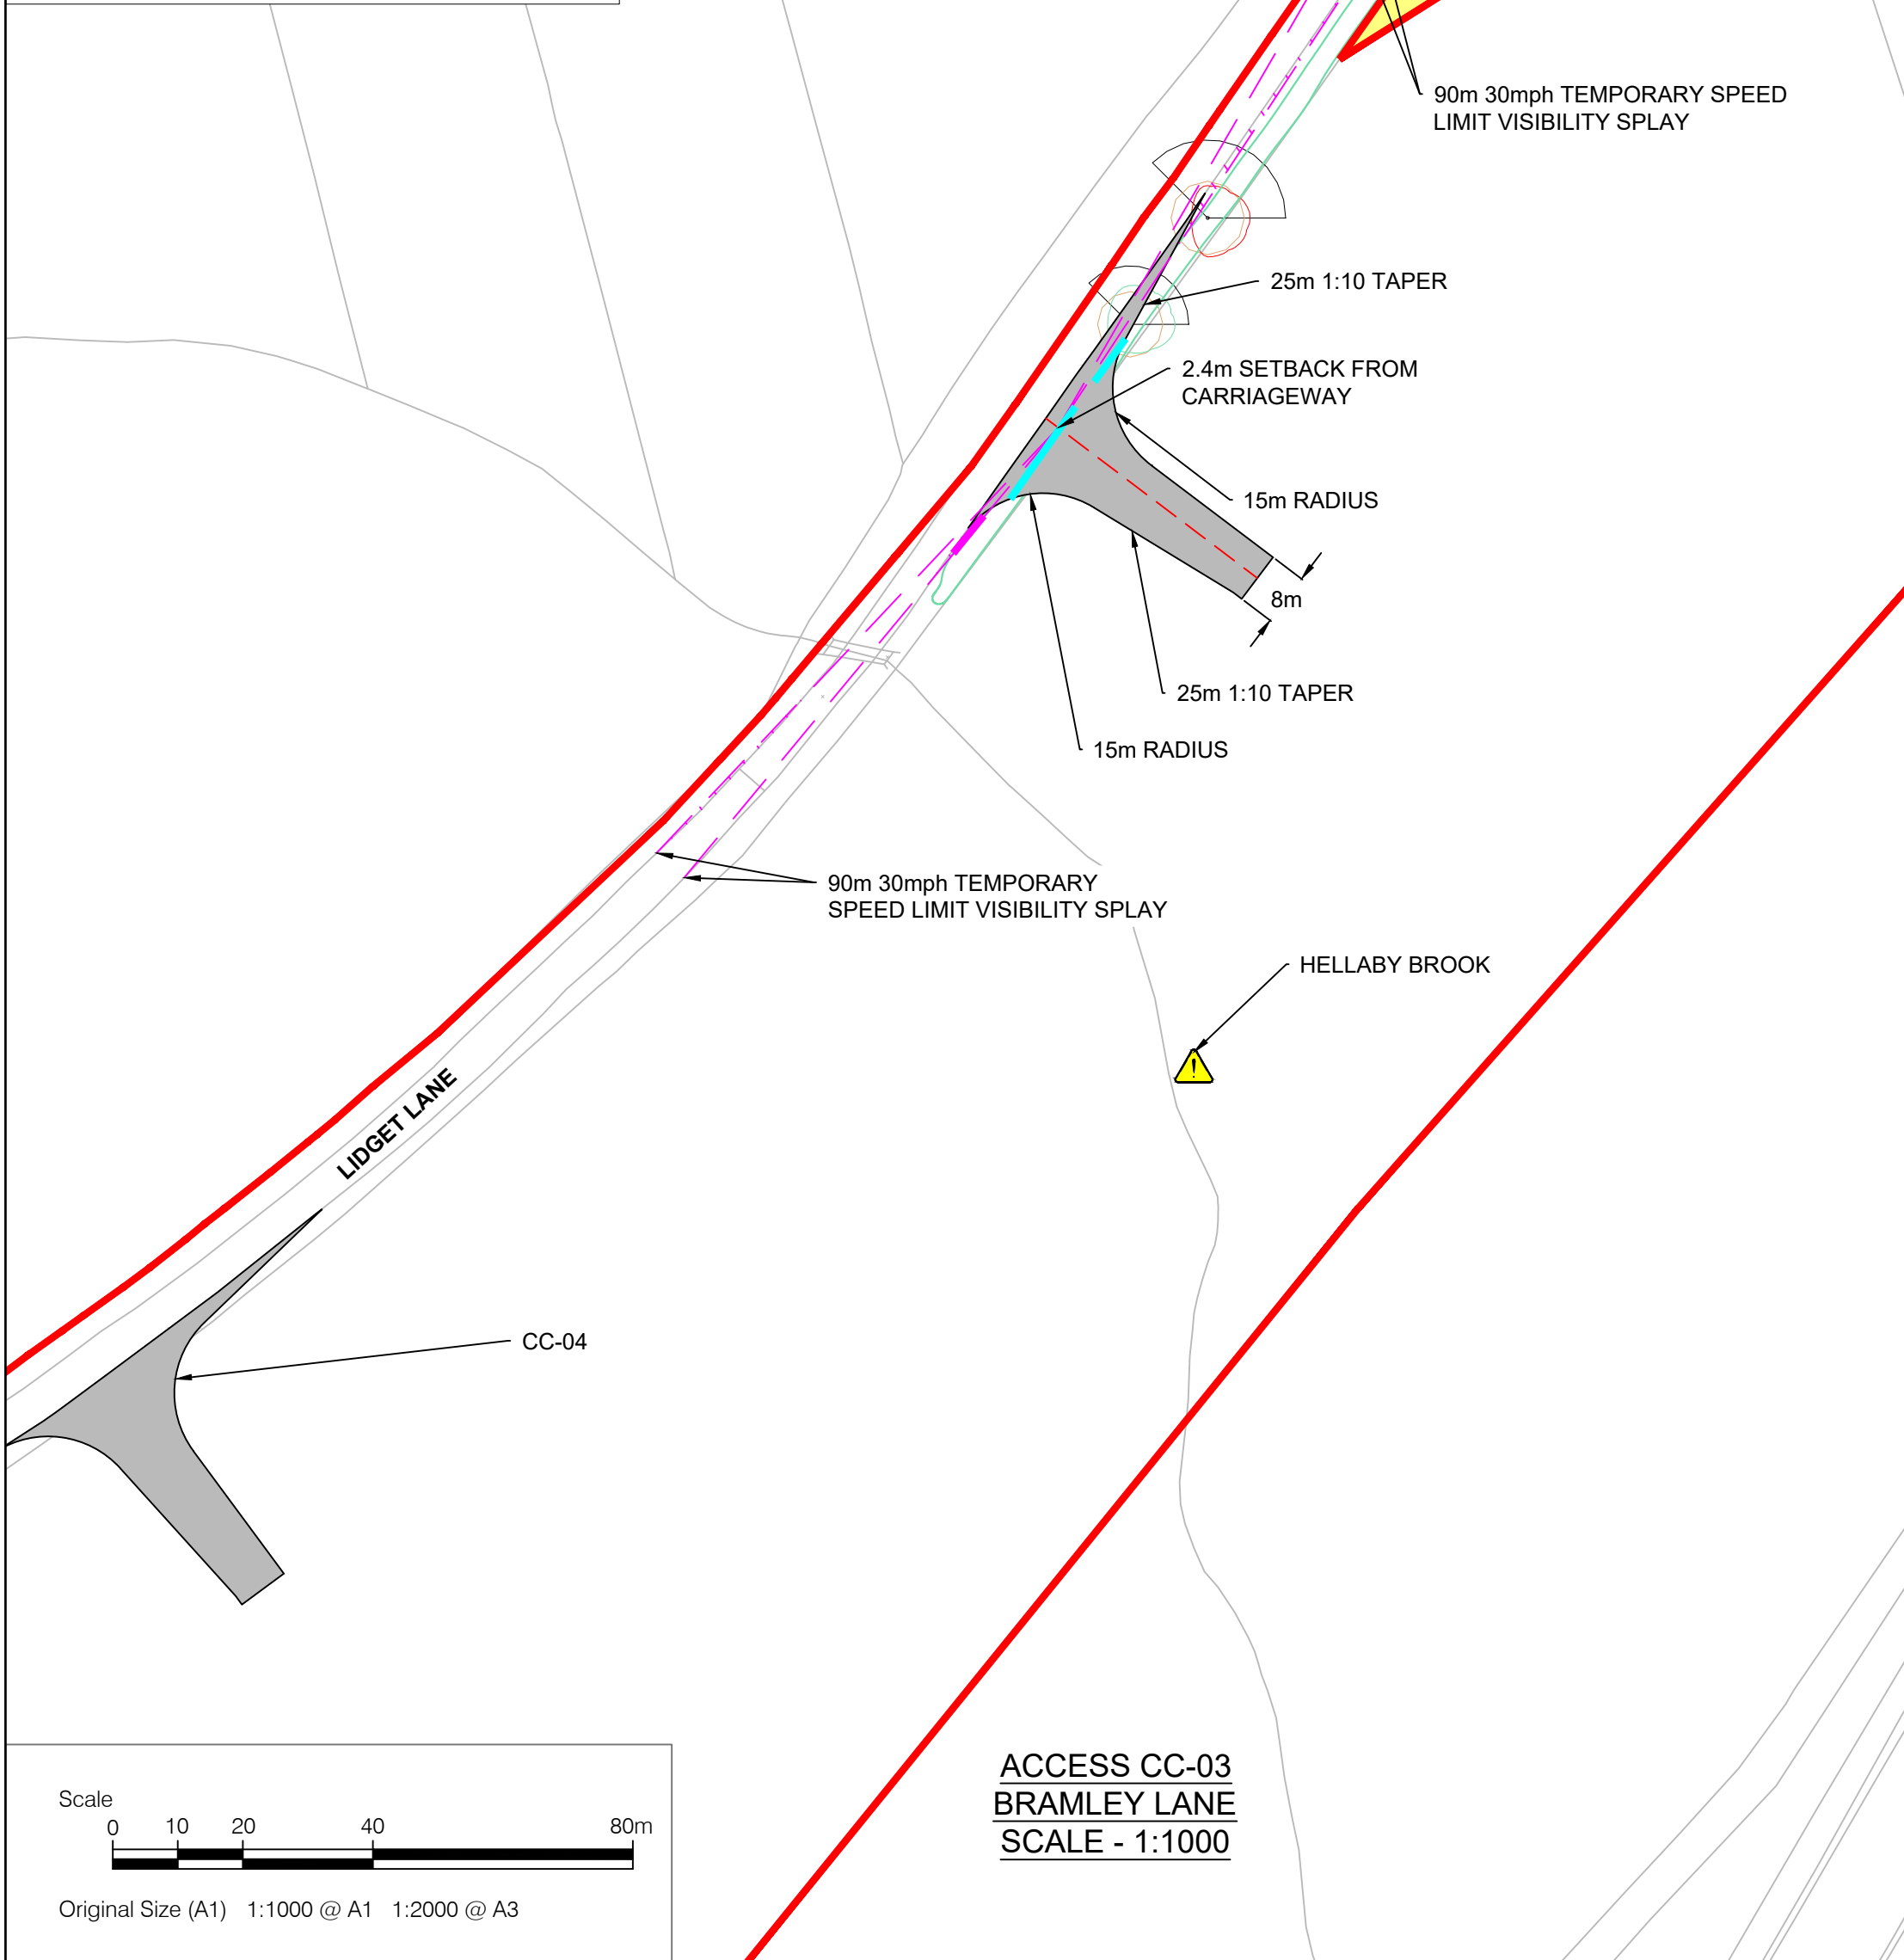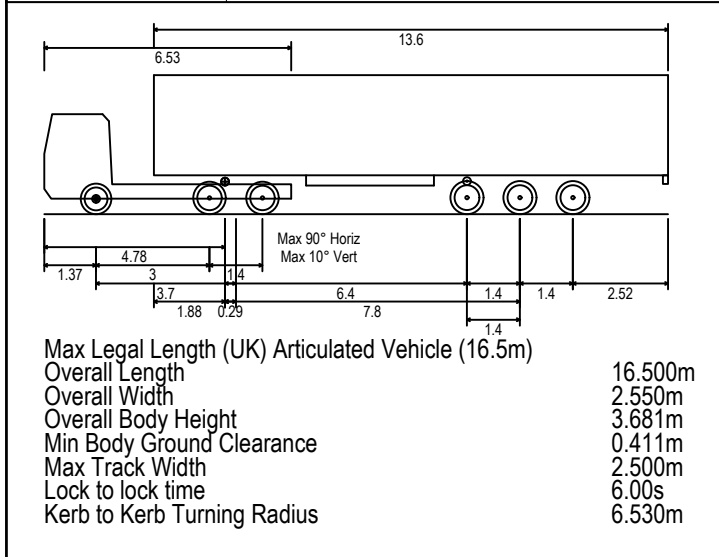


NOTES

- This drawing is to be read in conjunction with all other relevant documentation.
- Do not scale from this drawing, use only printed dimensions.
- All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
- This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
- Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
- The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
- Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
- Junction visibility for the access is based upon DMRB CD109 Table 2.10 on the basis of a 30mph temporary speed limit being enforced.

LEGEND

- Extent of Access Footprint
- Order Limits
- Land Excluded from Order Limits
- Vehicle Body
- Vehicle Body Path
- Vehicle Load
- Vehicle Load Path
- Vehicle Wheels Path
- Edge of Road
- Access Centreline
- Junction Visibility 30mph Temporary Speed Limit
- Vegetation to be Removed 30mph Temporary Speed Limit Vis Splay
- Indicative Hedgerow Removal 30mph Temporary Speed Limit
- Indicative Hedgerow Removal for Bellmouth Access
- Health and Safety Risk Identifier
- Existing Public Right of Way

SHEET PLAN

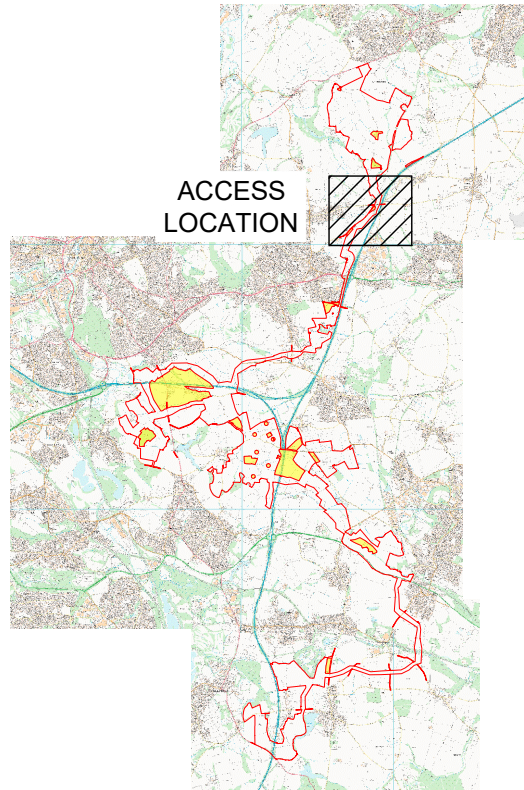

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:
Cable Corridor Area Access CC-03
Appendix 3 - Sheet 32 of 53
Whitestone Solar Farm
Regulation 5(2)(o)




DRAWING DATE: 03/06/2026

SCALE: 1:1000
SIZE: A1
SHEET: Sheet 32 of 53
REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12


APPLICATION NUMBER: EN0110020








WHITESTONE
solar farm

	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

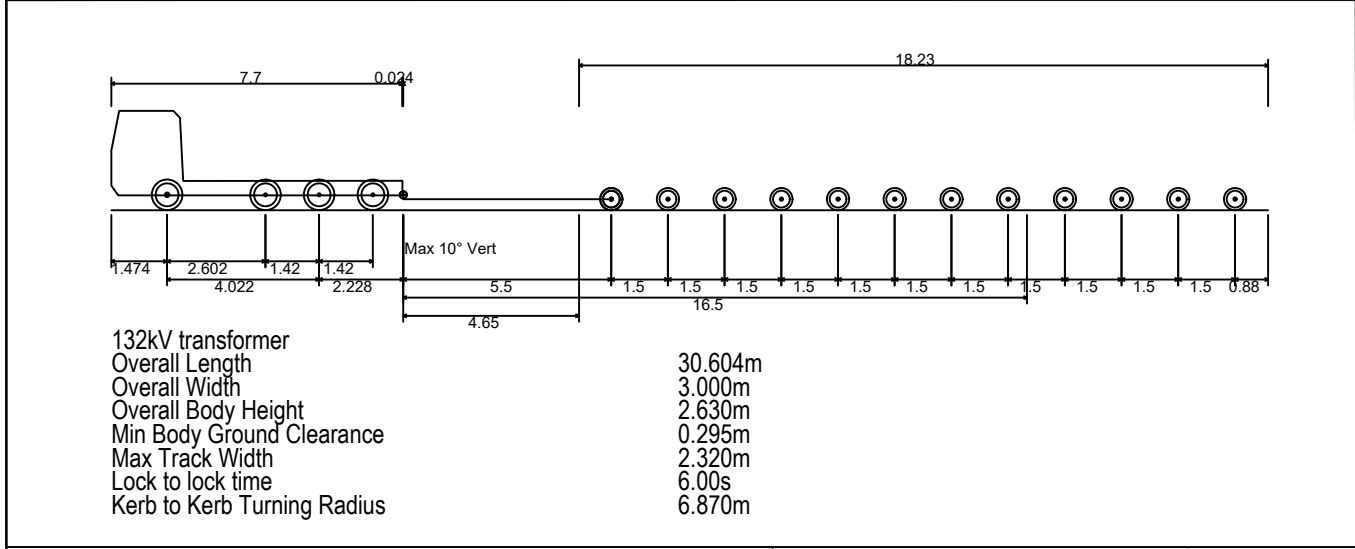

EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012	
RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

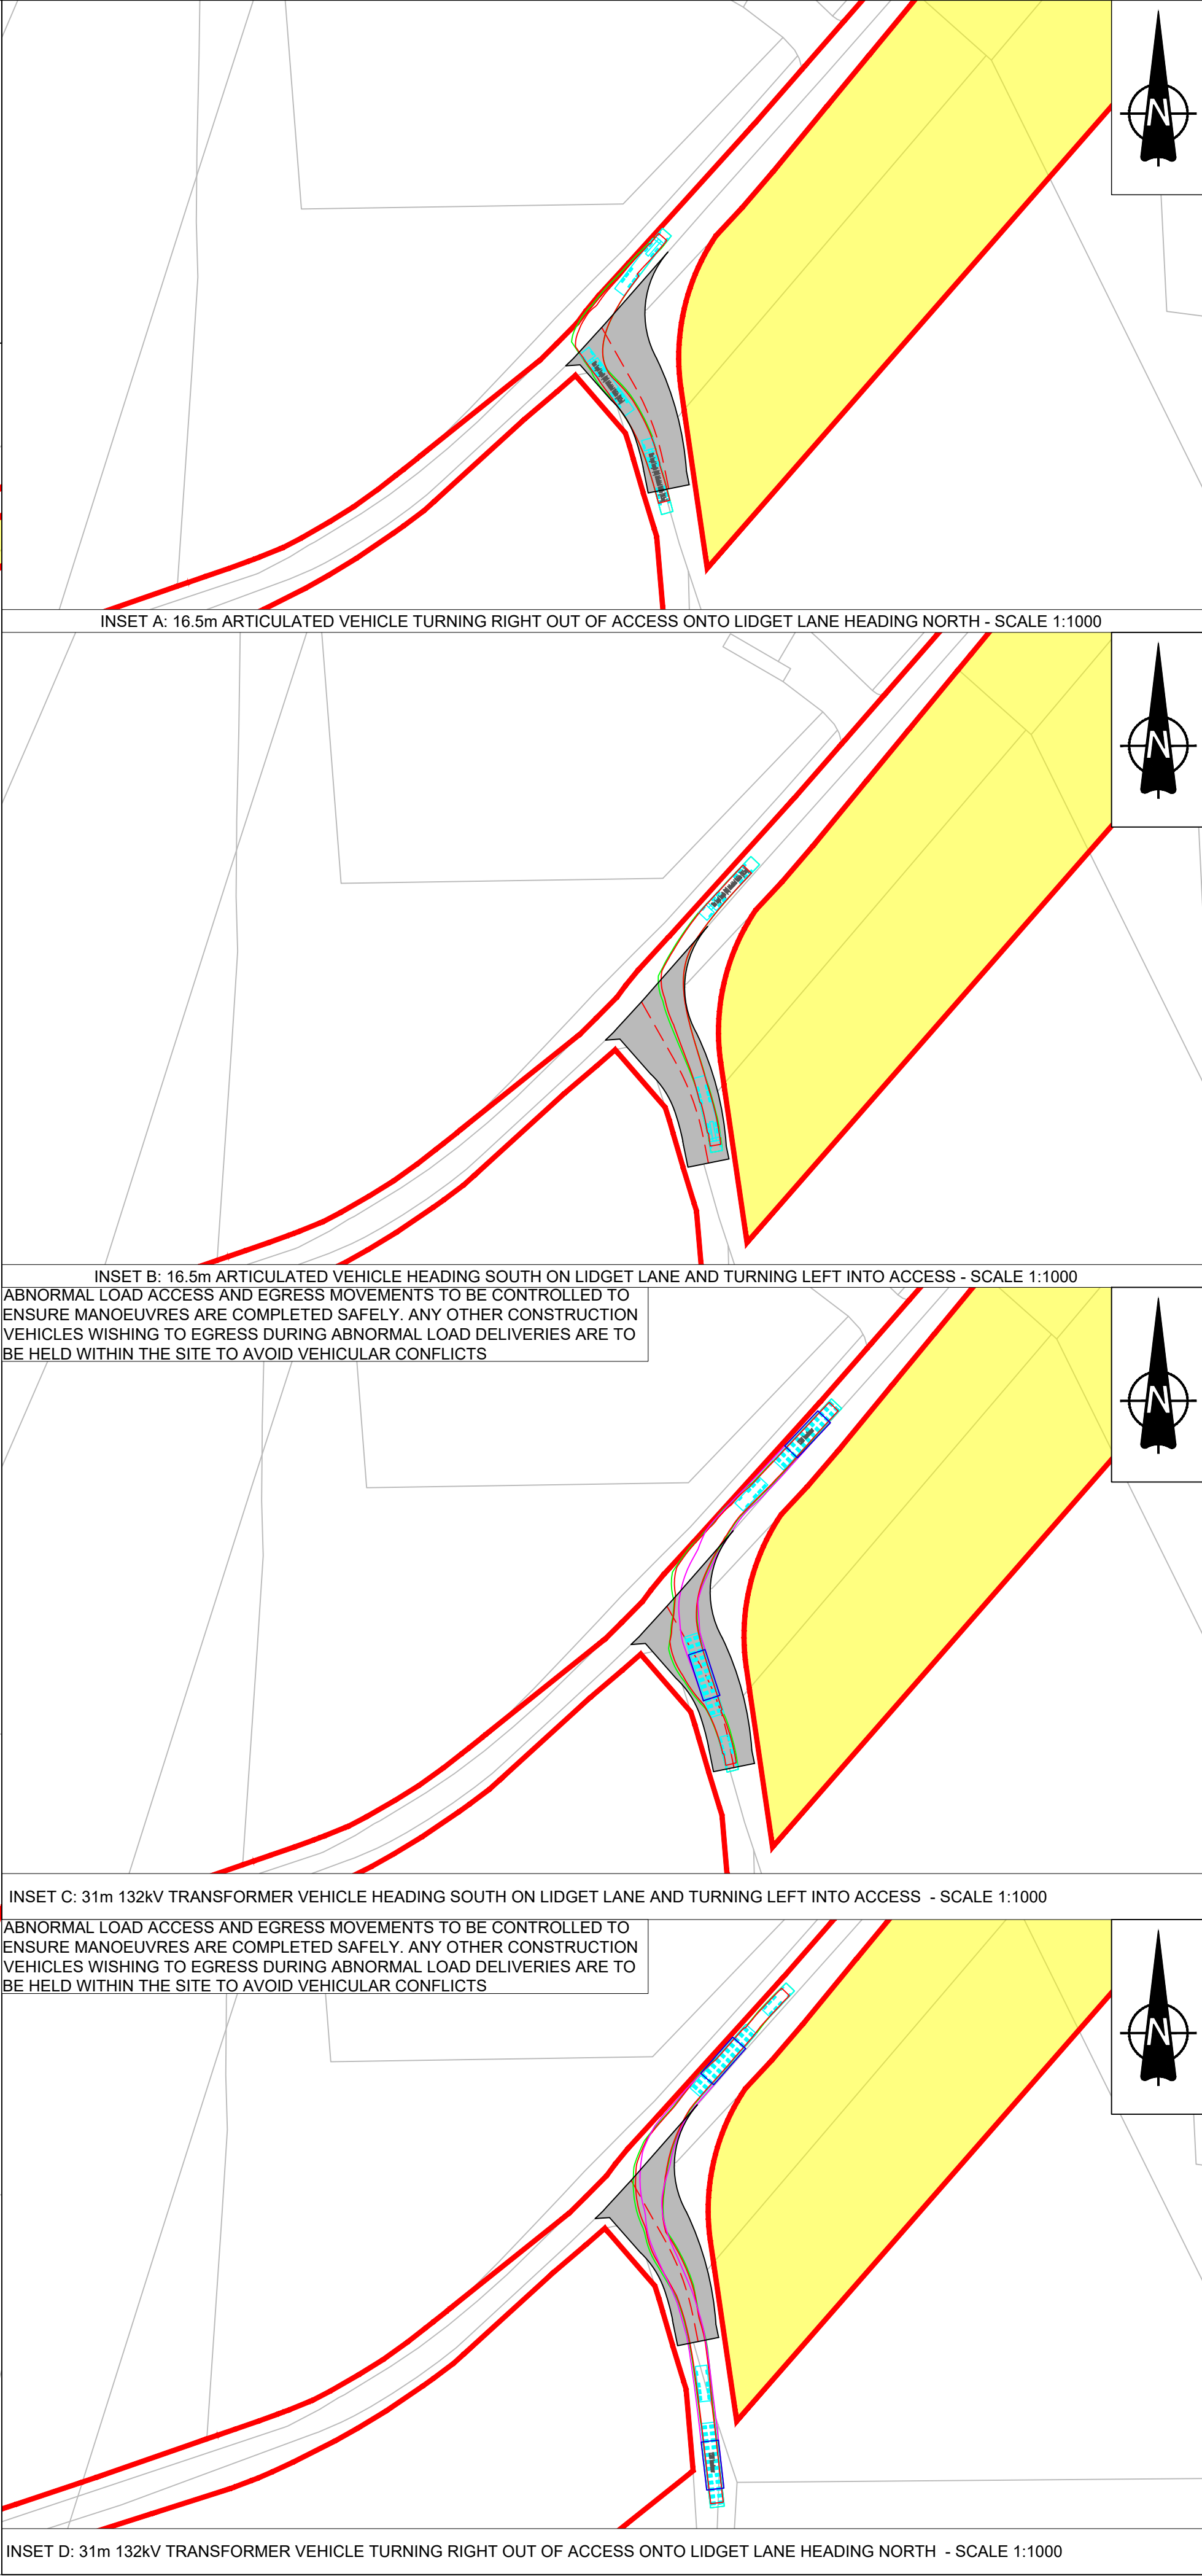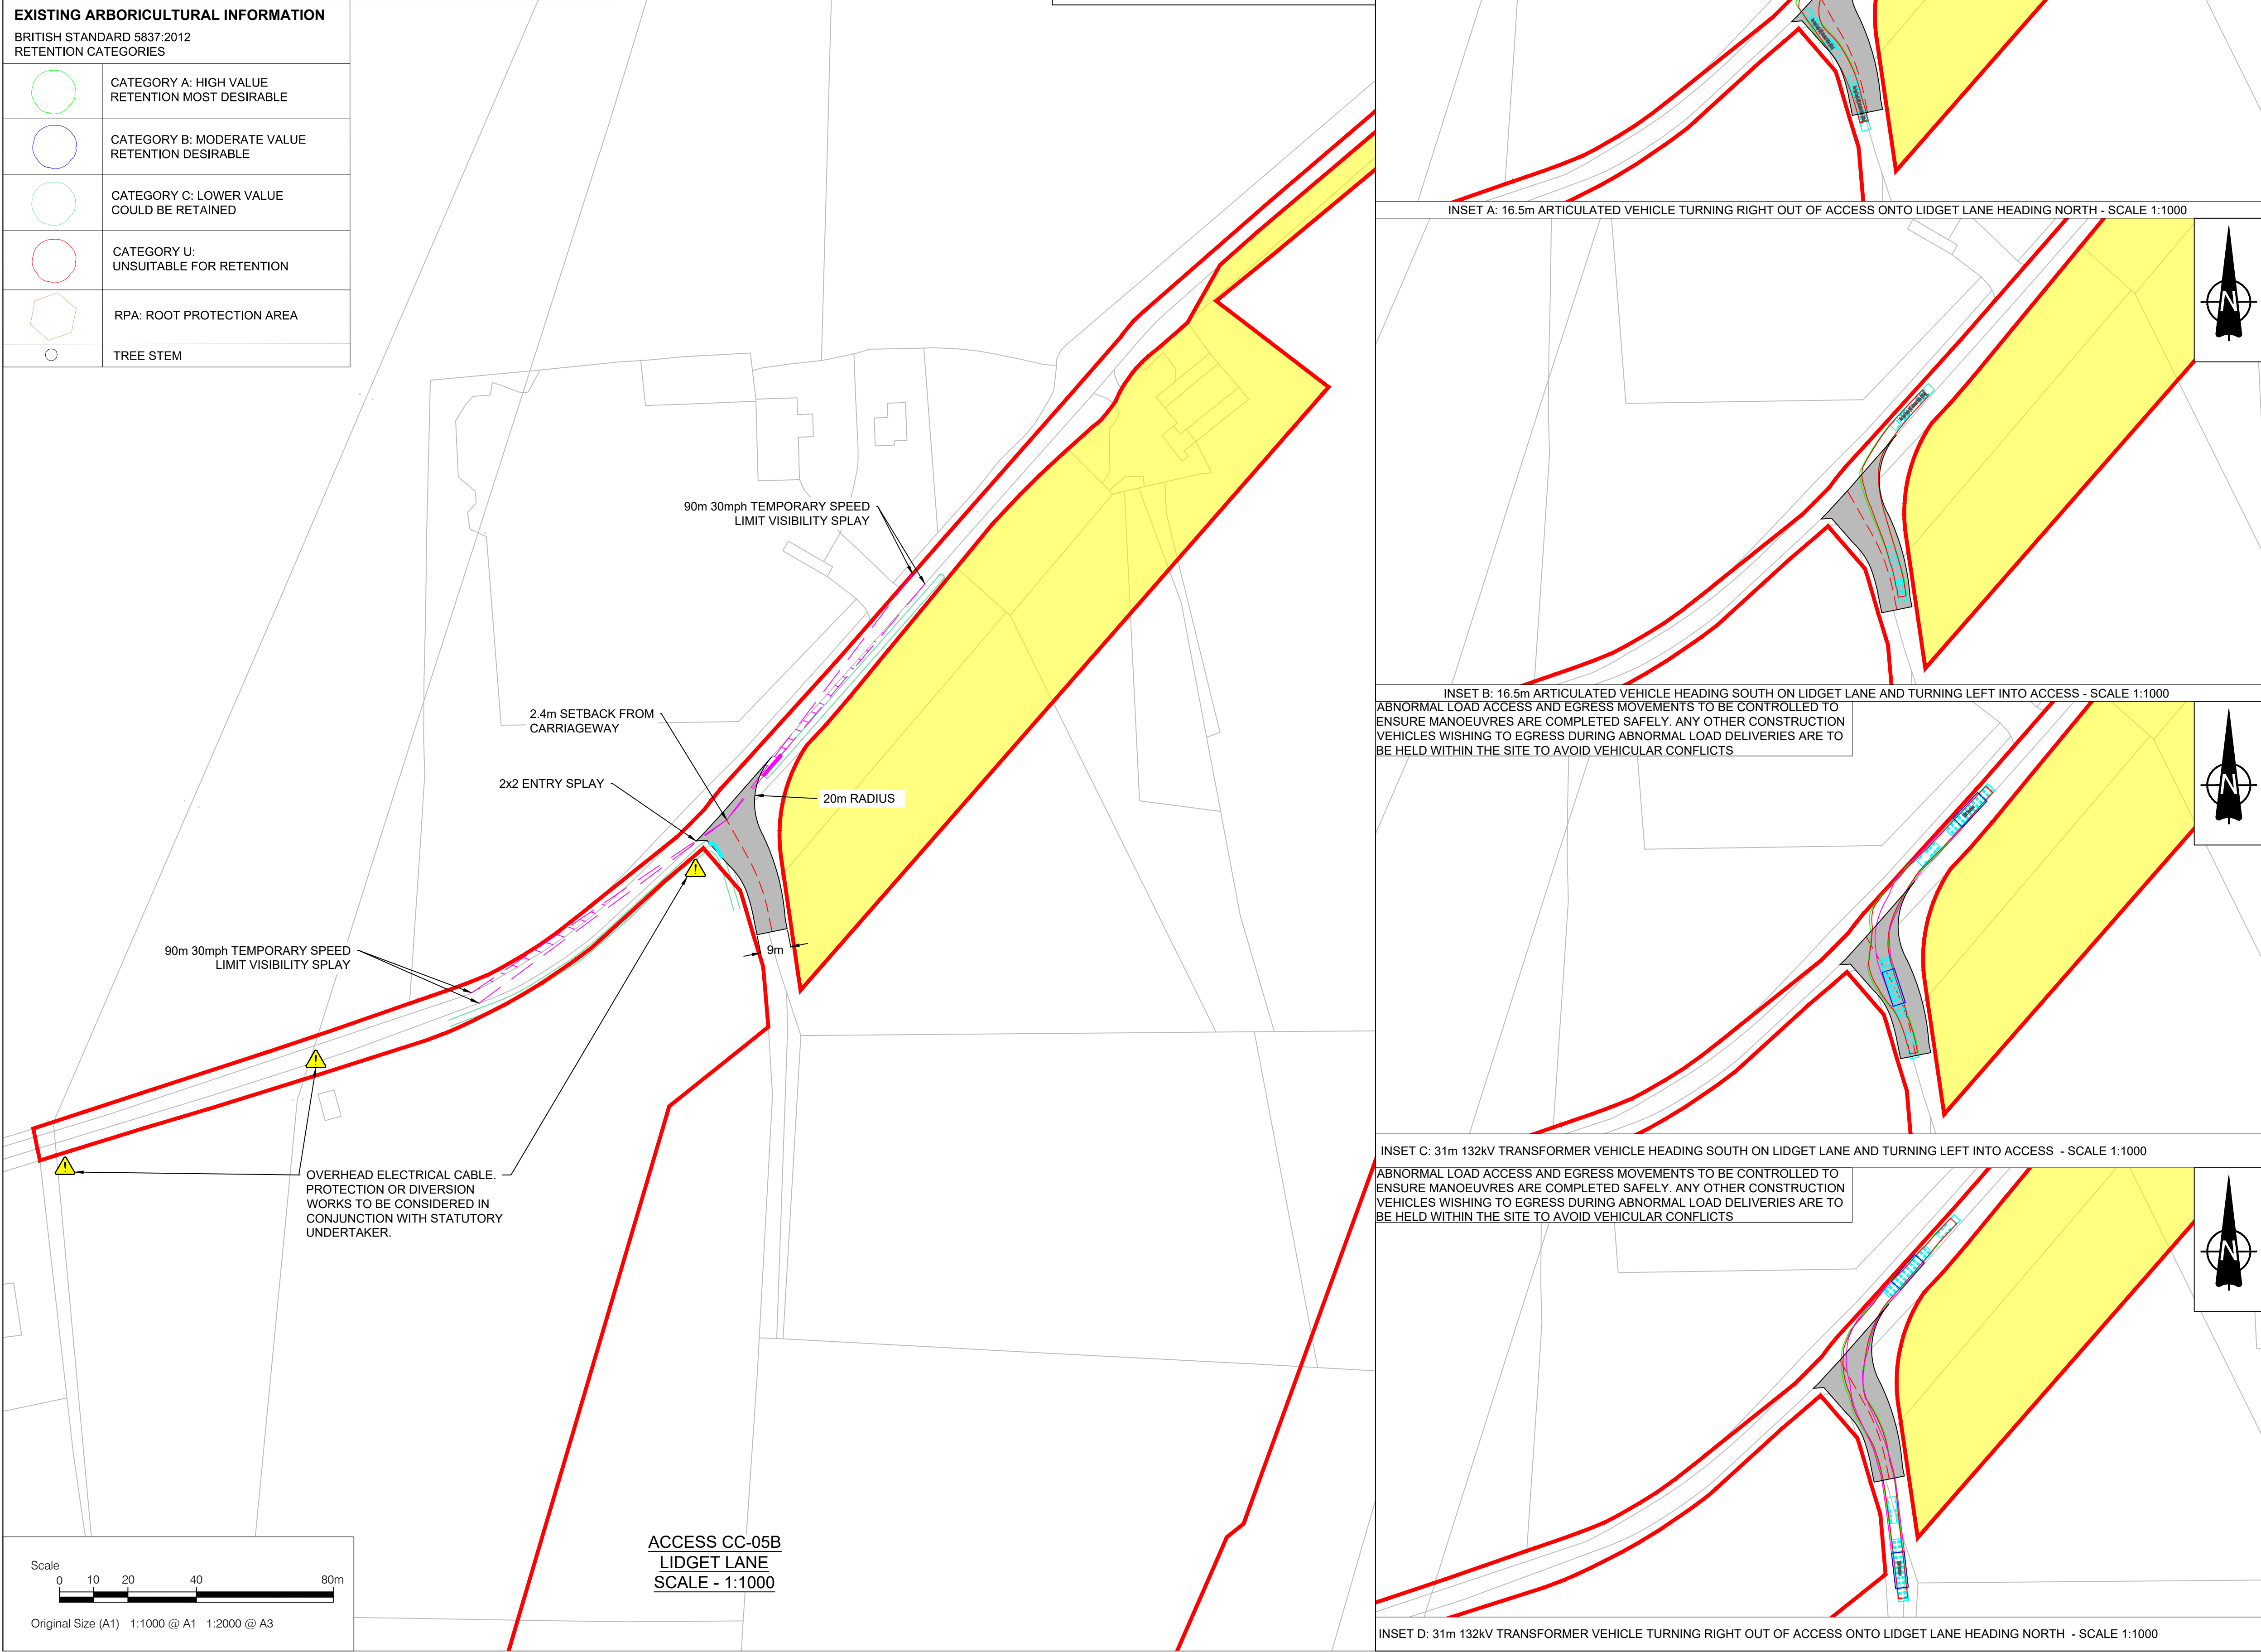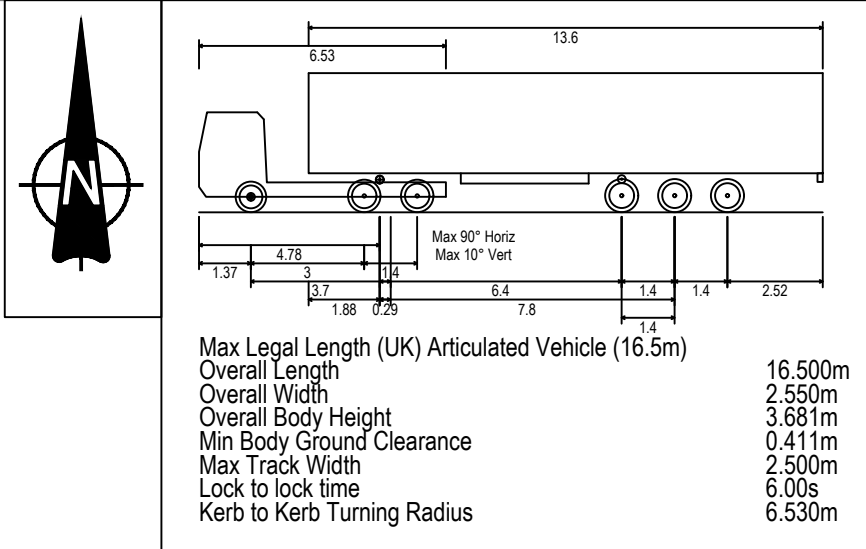

NOTES

- This drawing is to be read in conjunction with all other relevant documentation.
- Do not scale from this drawing, use only printed dimensions.
- All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
- This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
- Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
- The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
- Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
- Junction visibility for the access is based upon DMRB CD109 Table 2.10 on the basis of a 30mph temporary speed limit being enforced.

LEGEND

- Extent of Access Footprint
- Order Limits
- Land Excluded from Order Limits
- Vehicle Body
- Vehicle Body Path
- Vehicle Load
- Vehicle Load Path
- Vehicle Wheels Path
- Edge of Road
- Access Centreline
- Junction Visibility 30mph Temporary Speed Limit
- Vegetation to be Removed 30mph Temporary Speed Limit Vis Splay
- Indicative Hedgerow Removal 30mph Temporary Speed Limit
- Indicative Hedgerow Removal for Bellmouth Access
- Health and Safety Risk Identifier
- Existing Public Right of Way

SHEET PLAN

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:

Cable Corridor Area Access CC-05B

Appendix 3 - Sheet 34 of 53

Whitestone Solar Farm

Regulation 5(2)(o)


DRAWING DATE: 03/06/2026

SCALE: 1:1000	SHEET: Sheet 34 of 53
SIZE: A1	REVISION: 01







DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020

WHITESTONE
solar farm

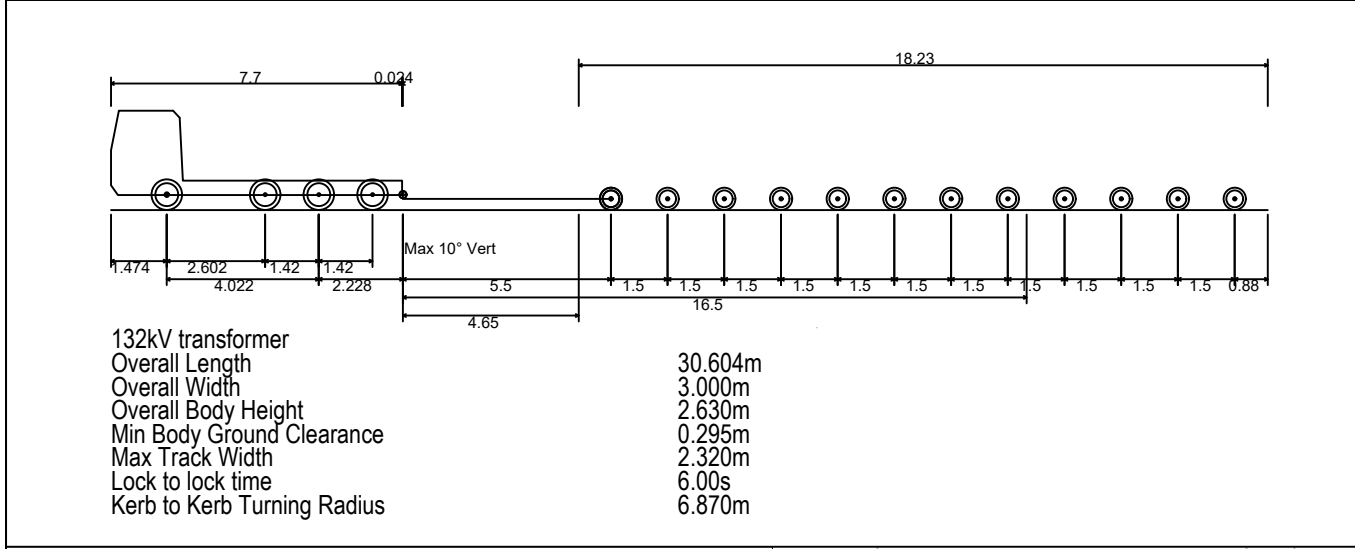


EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012	
RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

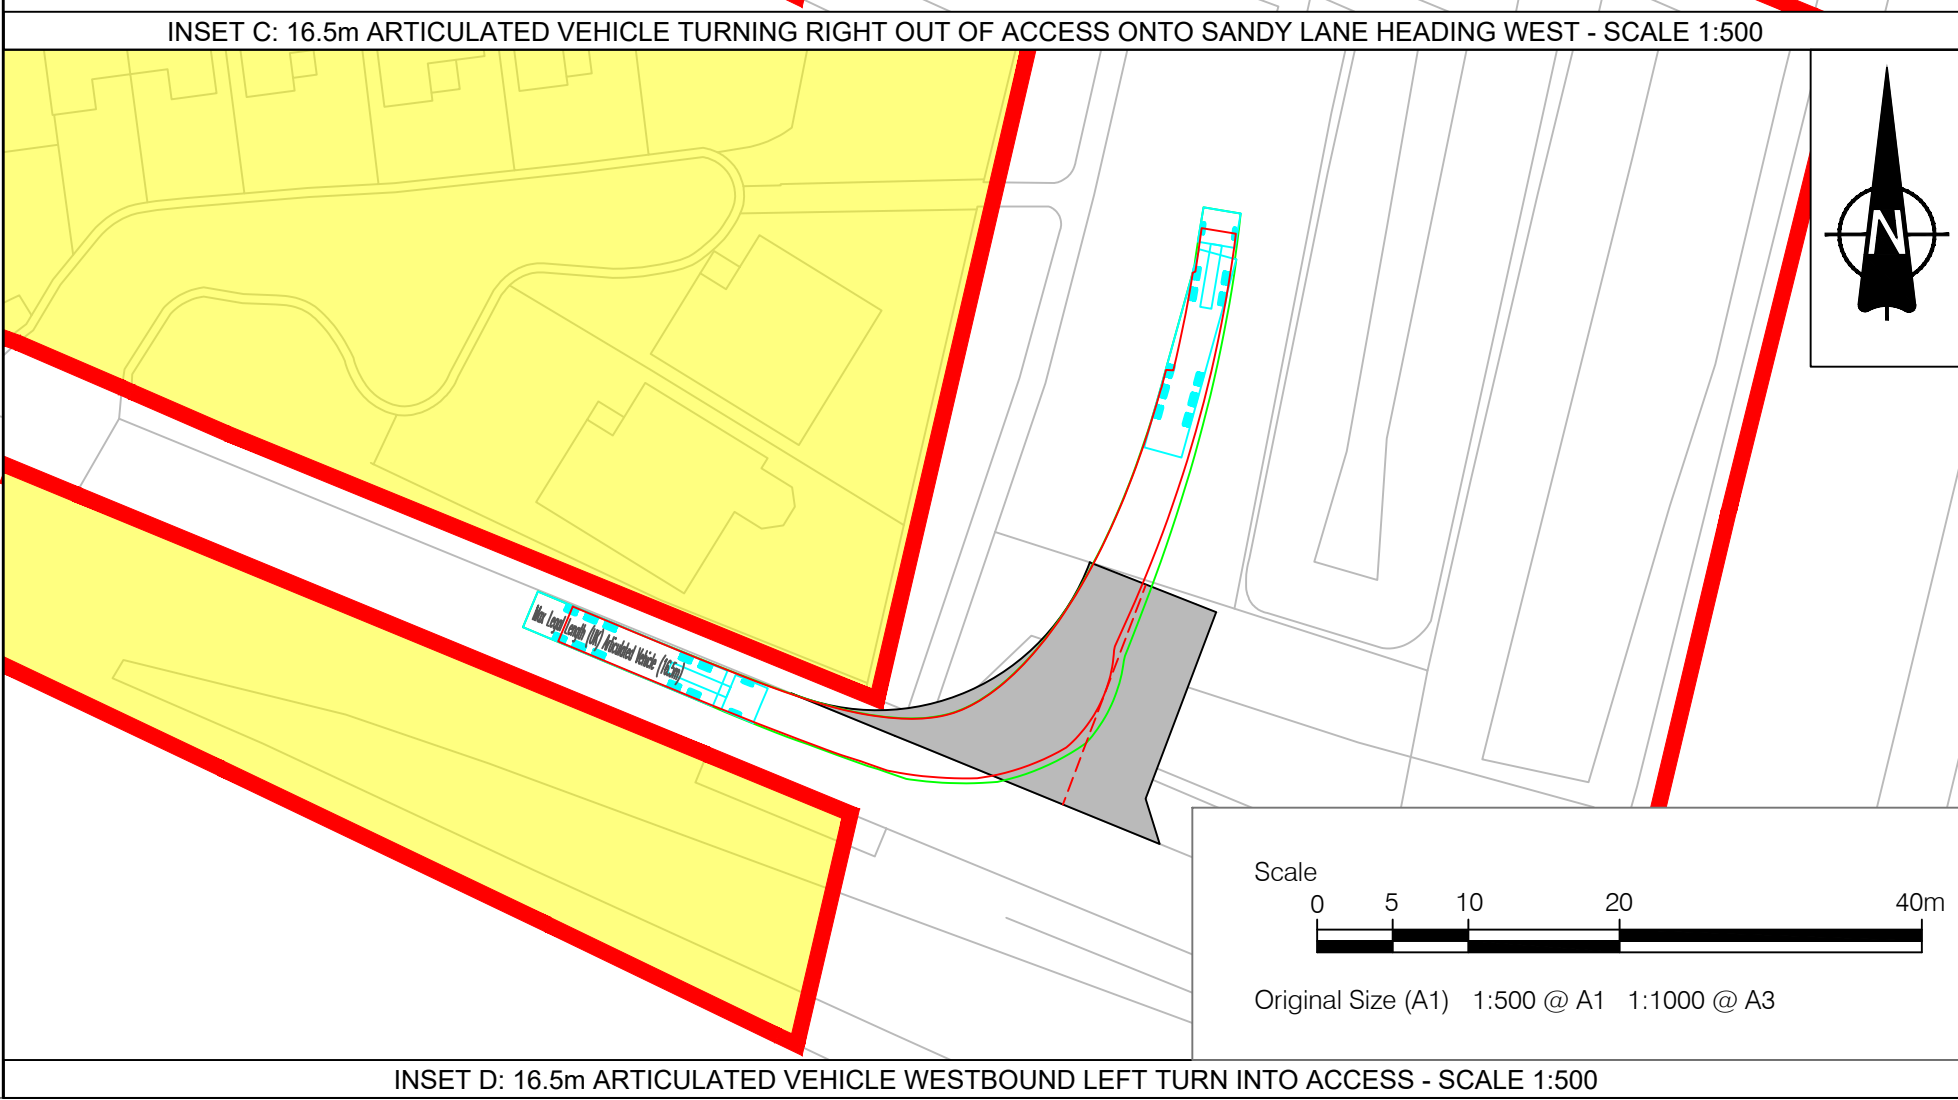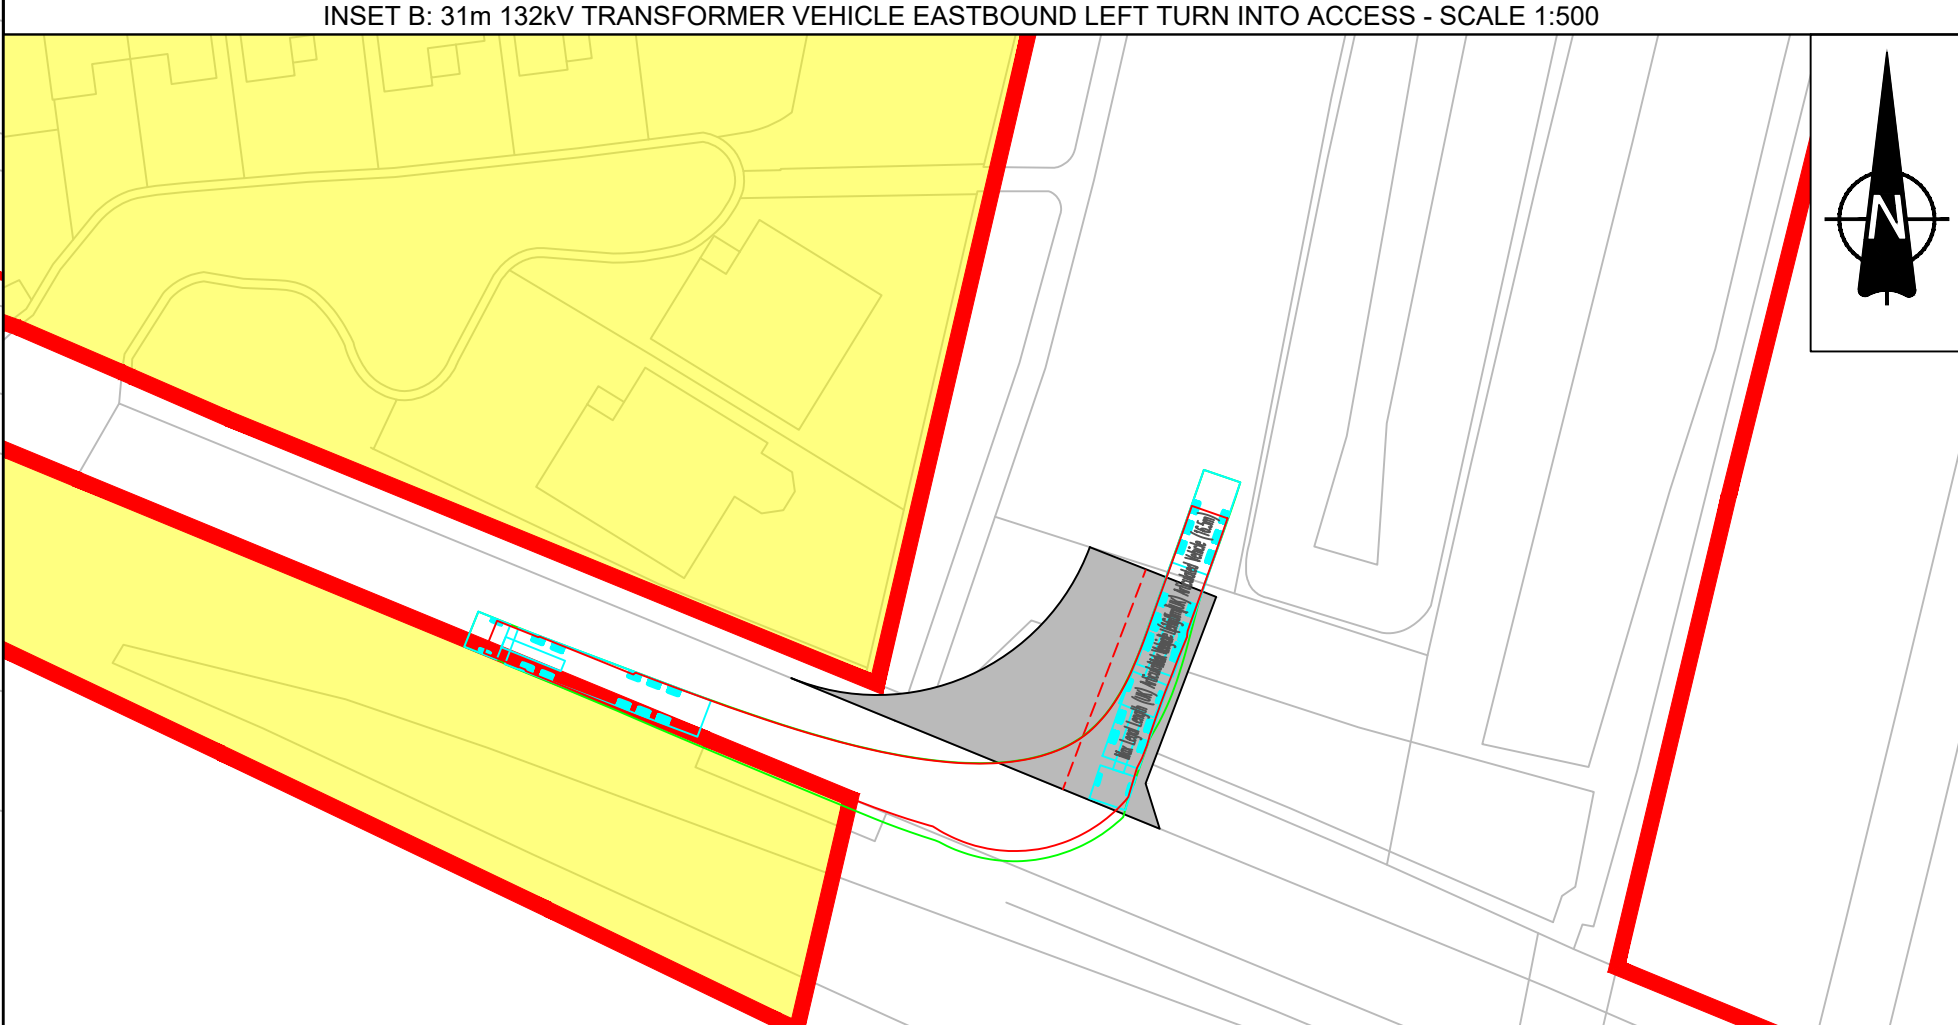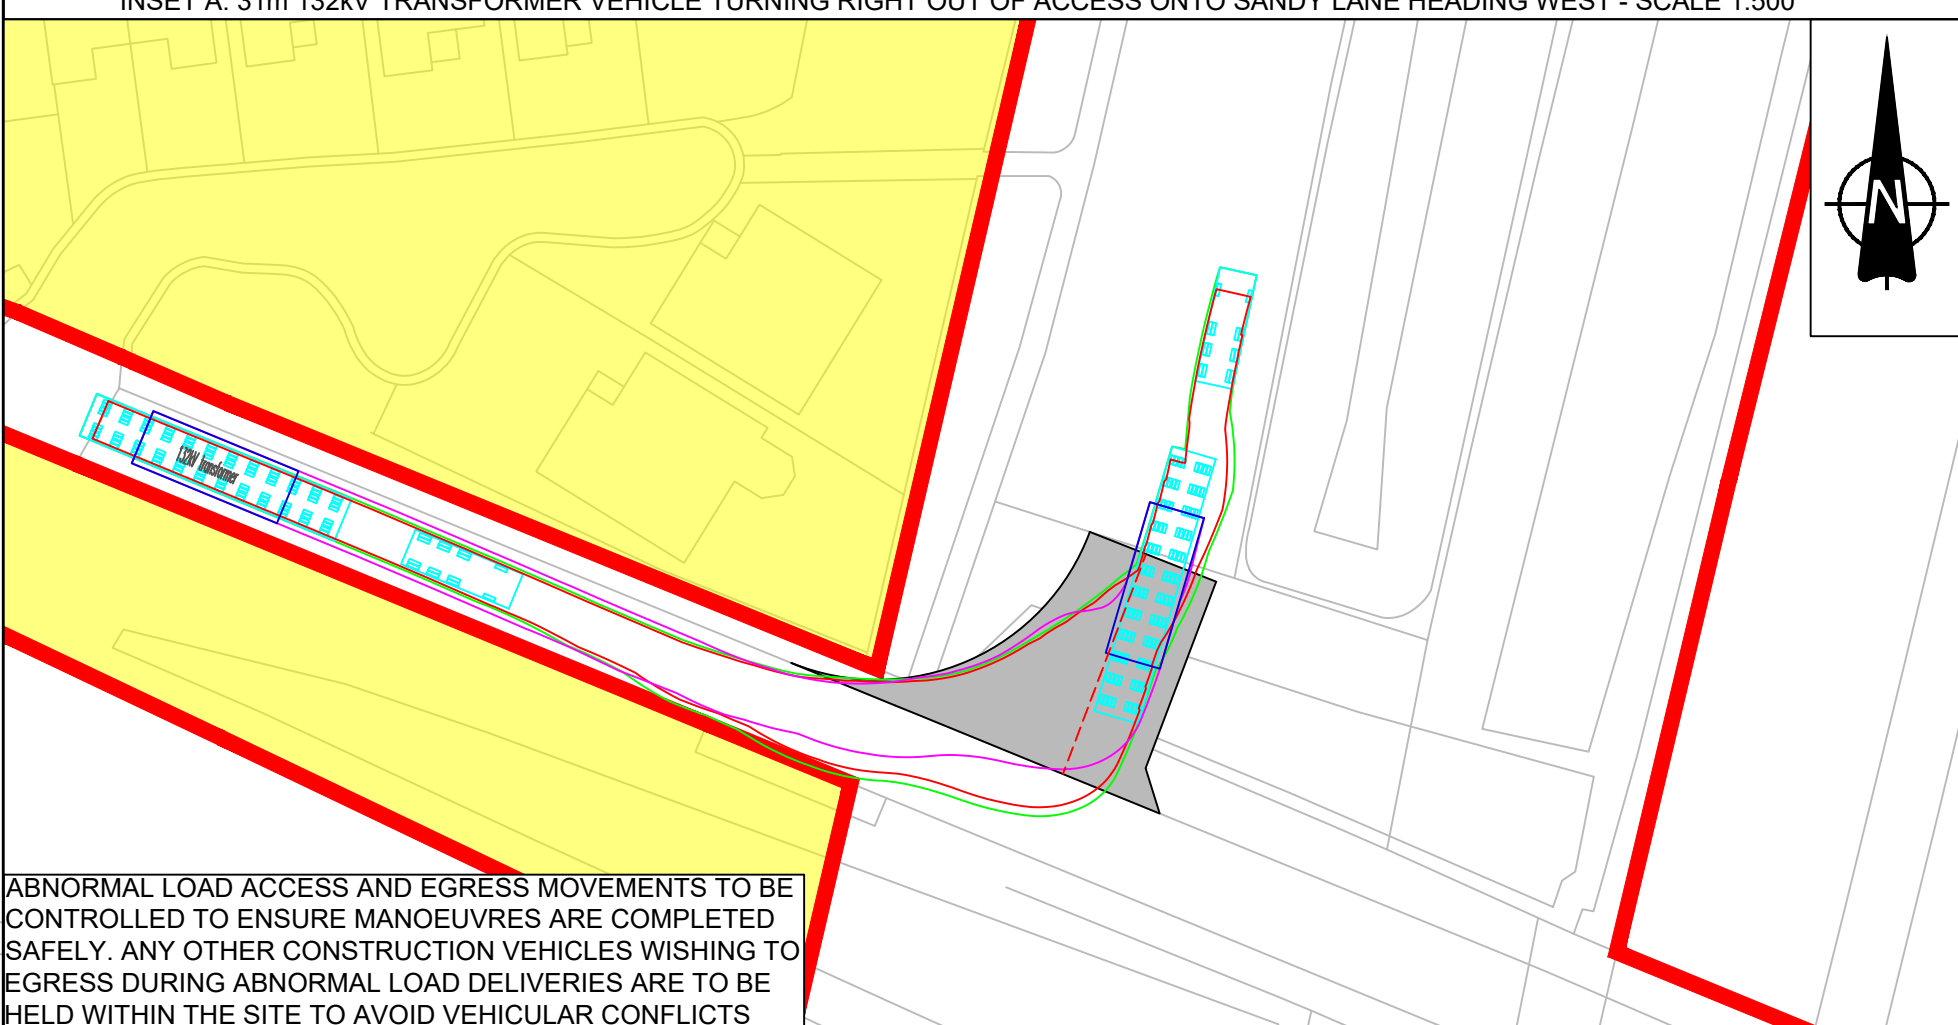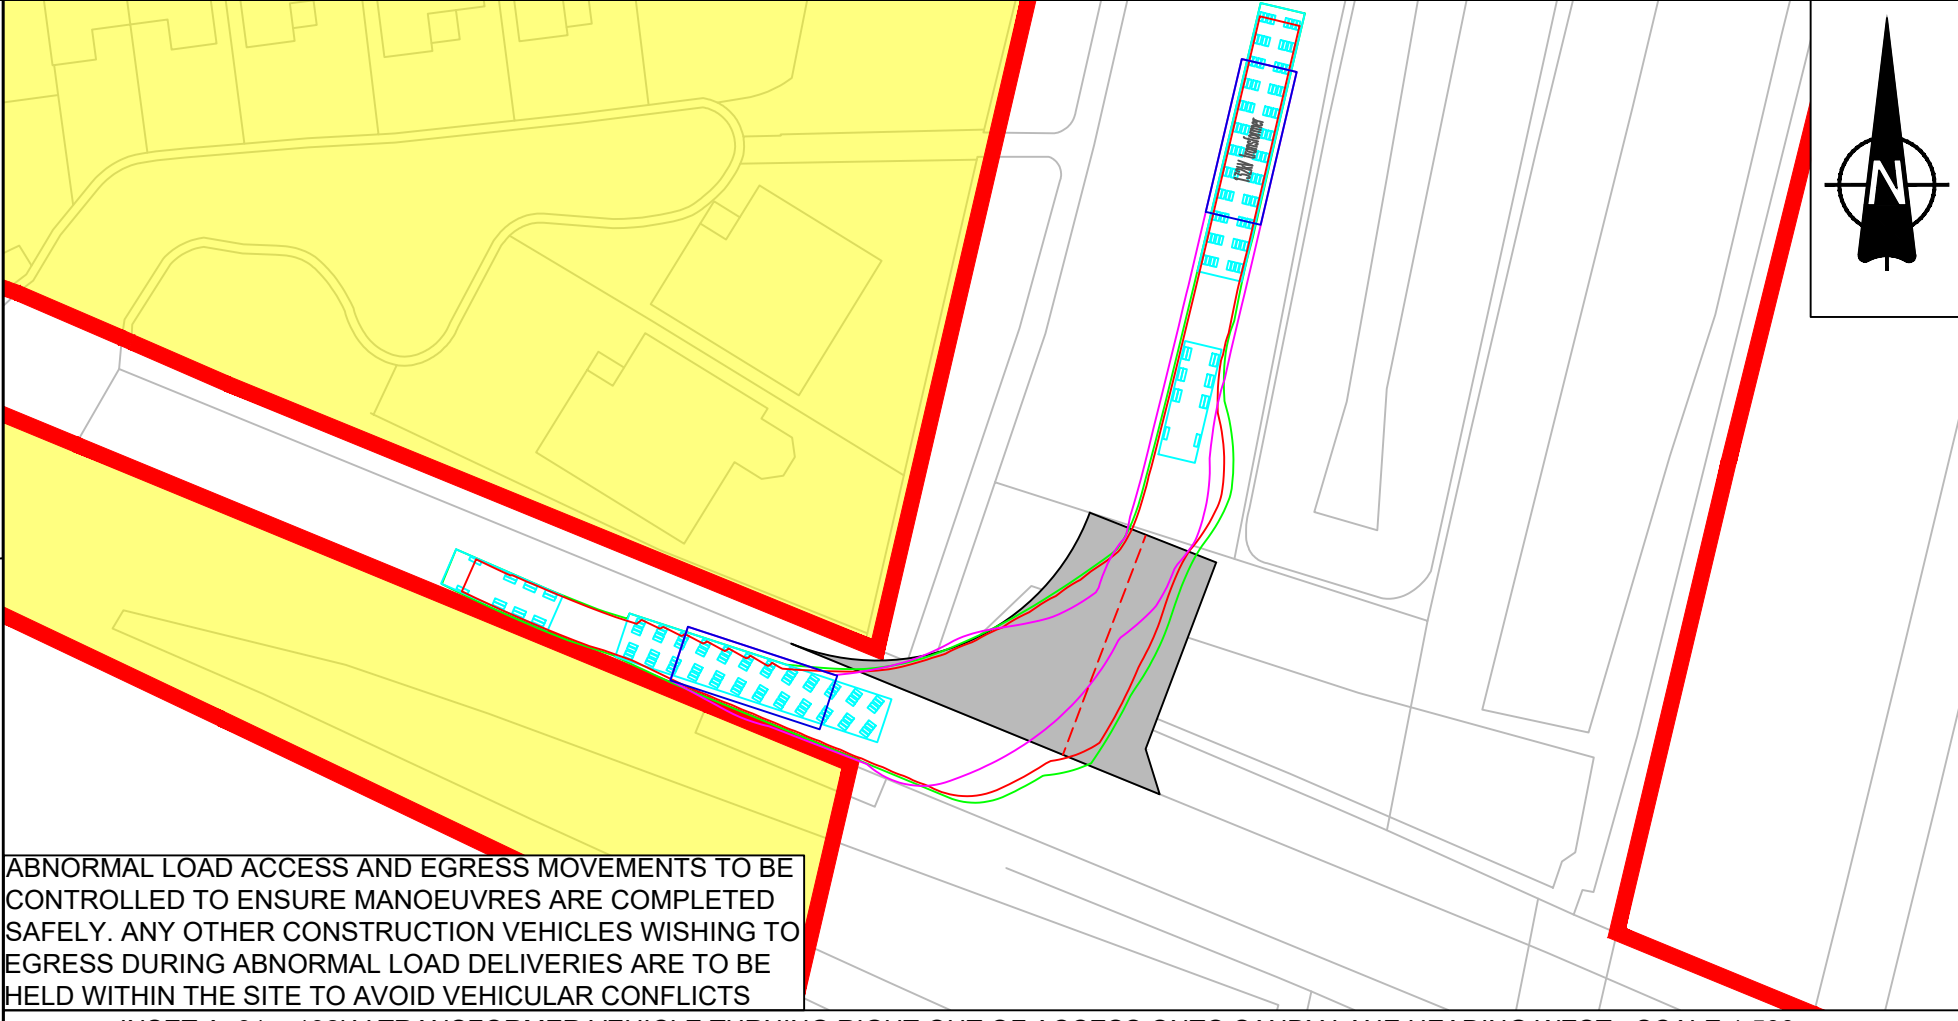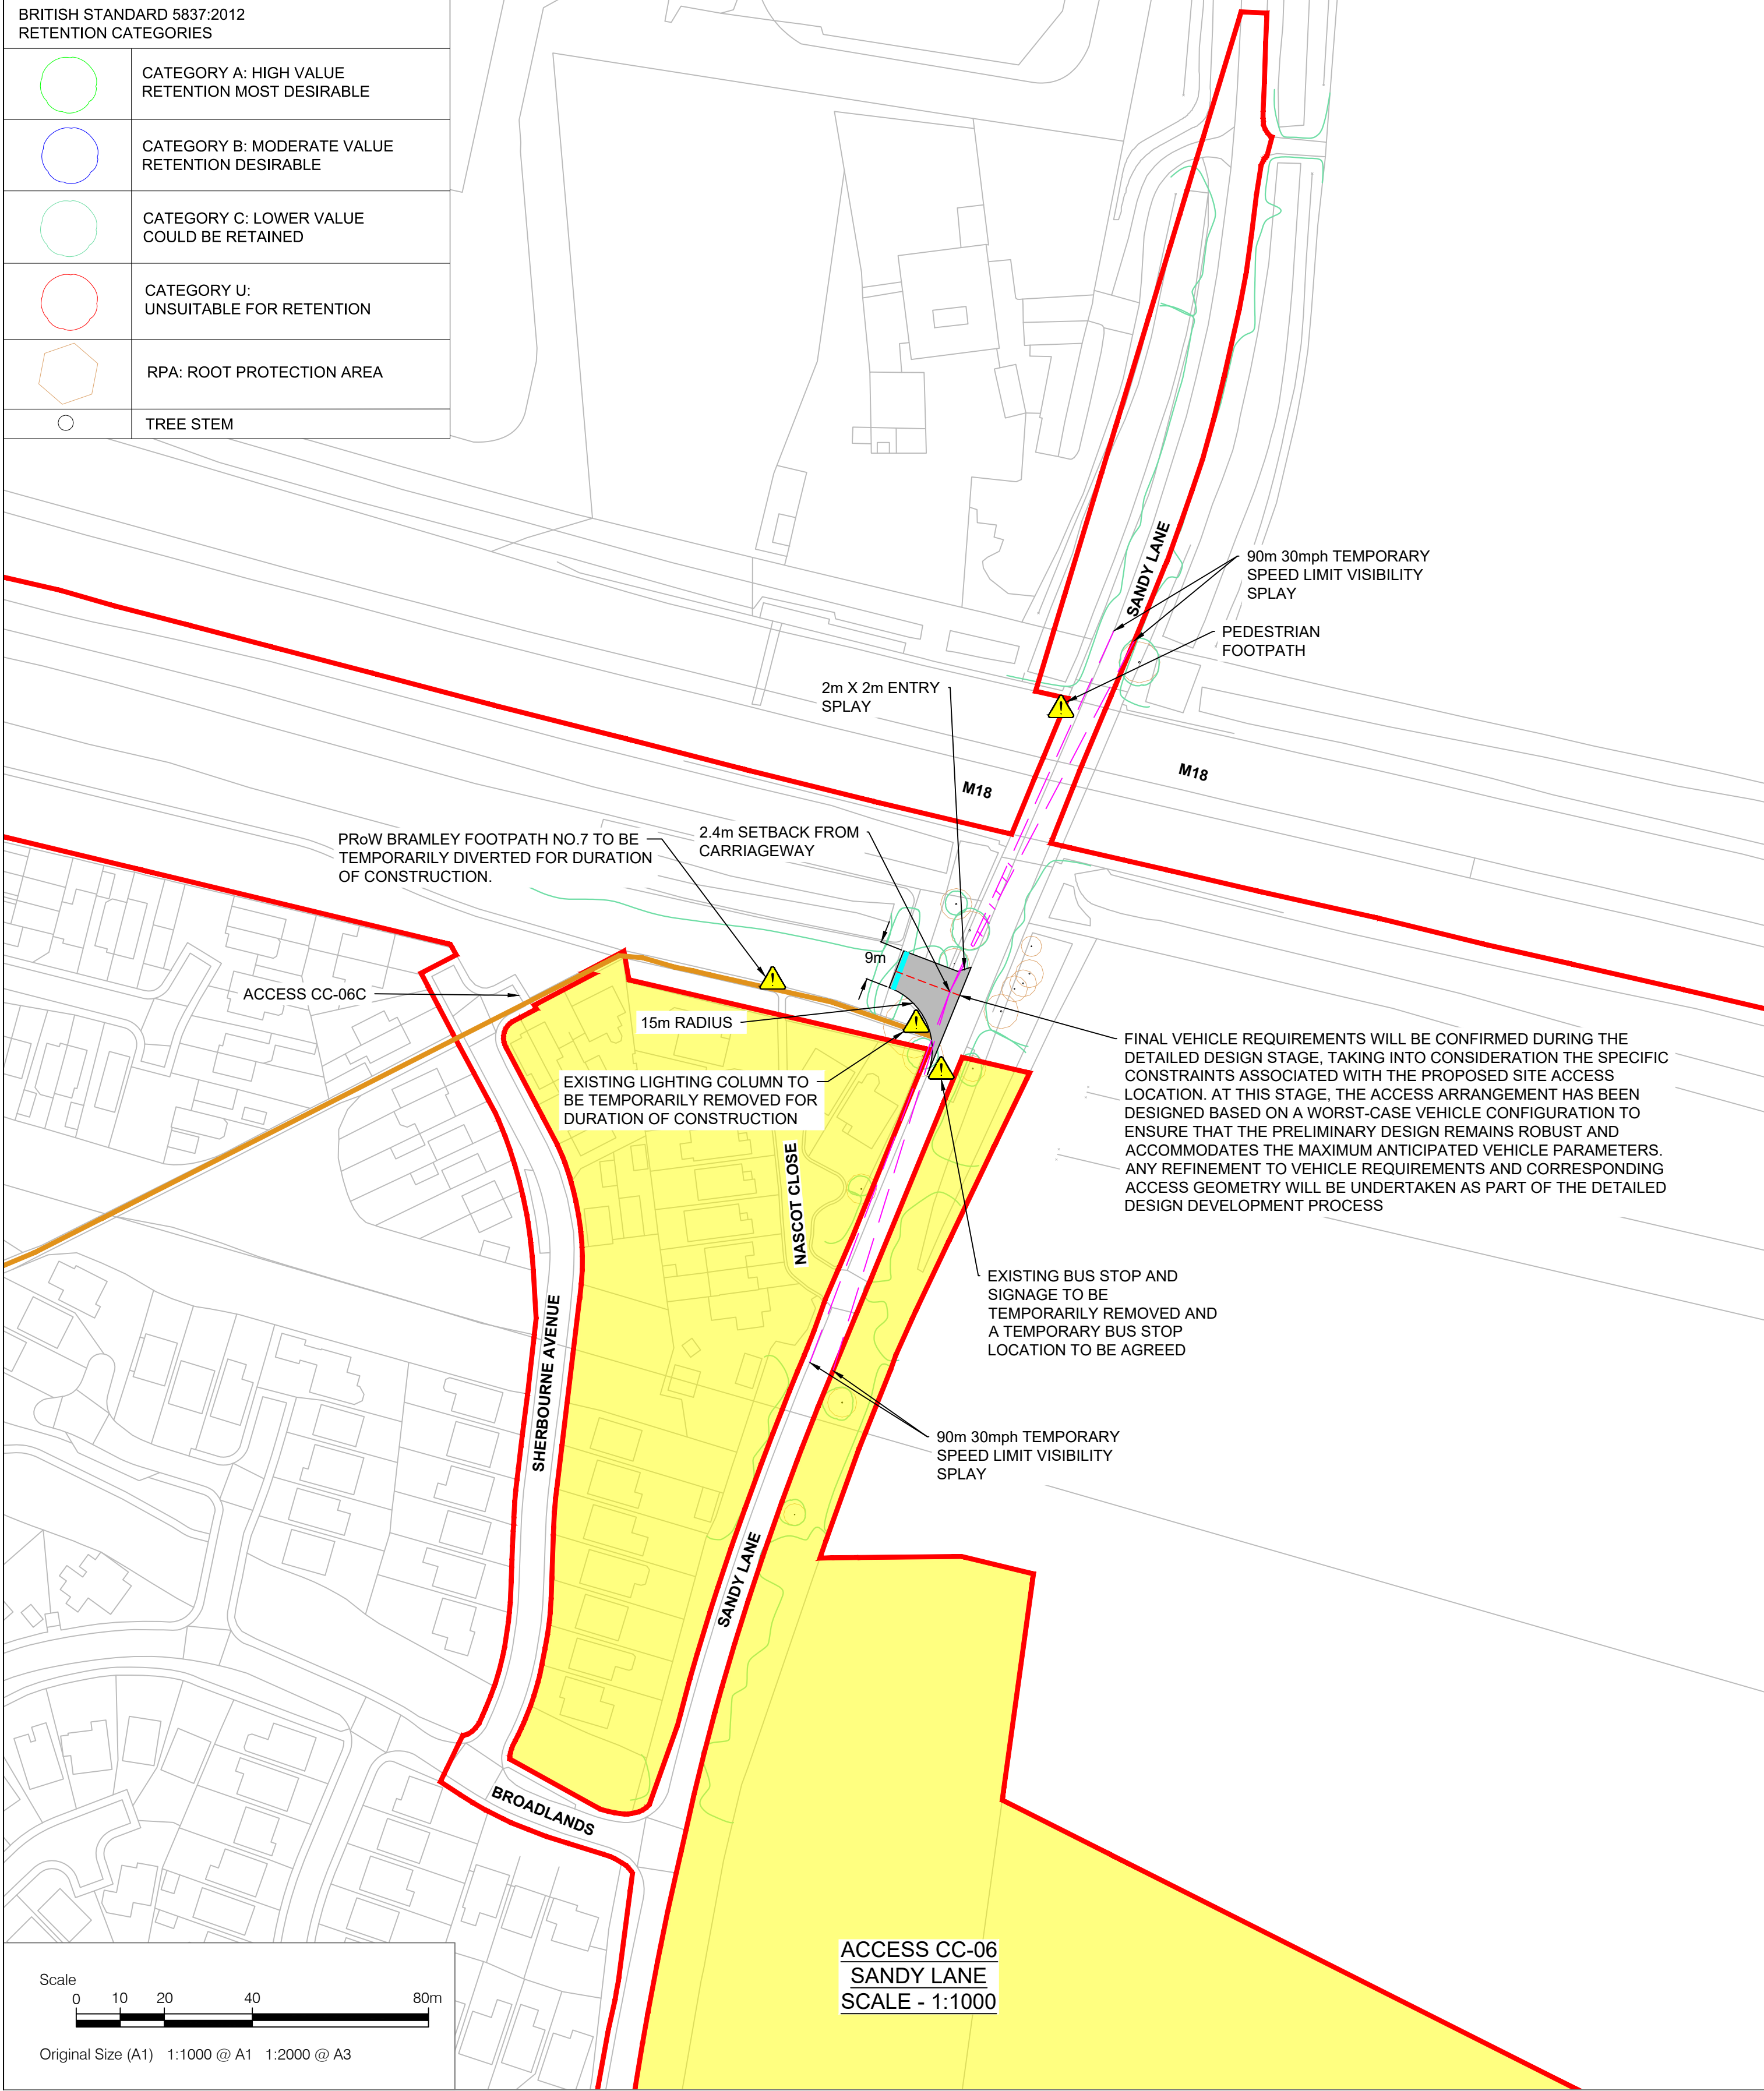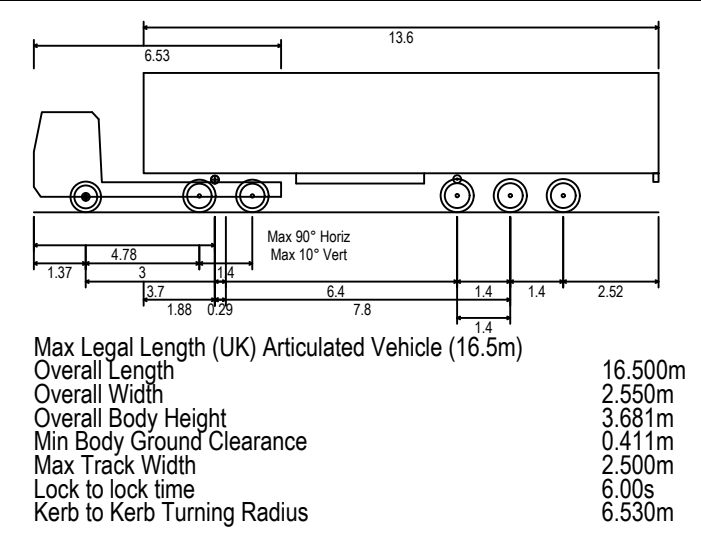

- NOTES**
- This drawing is to be read in conjunction with all other relevant documentation.
 - Do not scale from this drawing, use only printed dimensions.
 - All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
 - This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
 - Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
 - The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
 - Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
 - Junction visibility for the access is based upon DMRB CD109 Table 2.10 on the basis of a 30mph temporary speed limit being enforced.










- LEGEND**
- Extent of Access Footprint
 - Order Limits
 - Land Excluded from Order Limits
 - Vehicle Body
 - Vehicle Body Path
 - Vehicle Load
 - Vehicle Load Path
 - Vehicle Wheels Path
 - Edge of Road
 - Access Centreline
 - Junction Visibility 30mph Temporary Speed Limit
 - Vegetation to be Removed 30mph Temporary Speed Limit Vis Splay
 - Indicative Hedgerow Removal 30mph Temporary Speed Limit
 - Indicative Hedgerow Removal for Bellmouth Access
 - Health and Safety Risk Identifier
 - Existing Public Right of Way

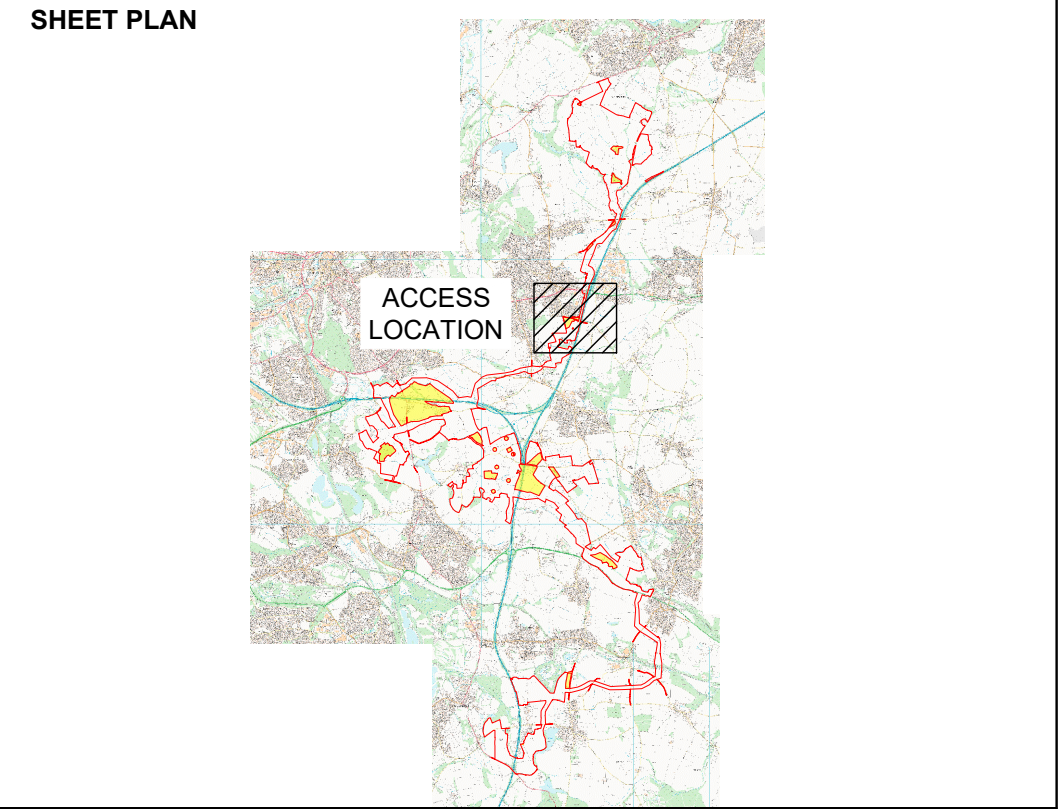

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED
TITLE: Cable Corridor Area Access CC-06 Appendix 3 - Sheet 35 of 53 Whitestone Solar Farm Regulation 5(2)(o)					
DRAWING DATE: 03/06/2026					
SCALE: AS SHOWN			SHEET: Sheet 35 of 53		
SIZE: A1			REVISION: 01		
DOCUMENT REFERENCE: EN0110020/APP/5.12					
APPLICATION NUMBER: EN0110020					




EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012 RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

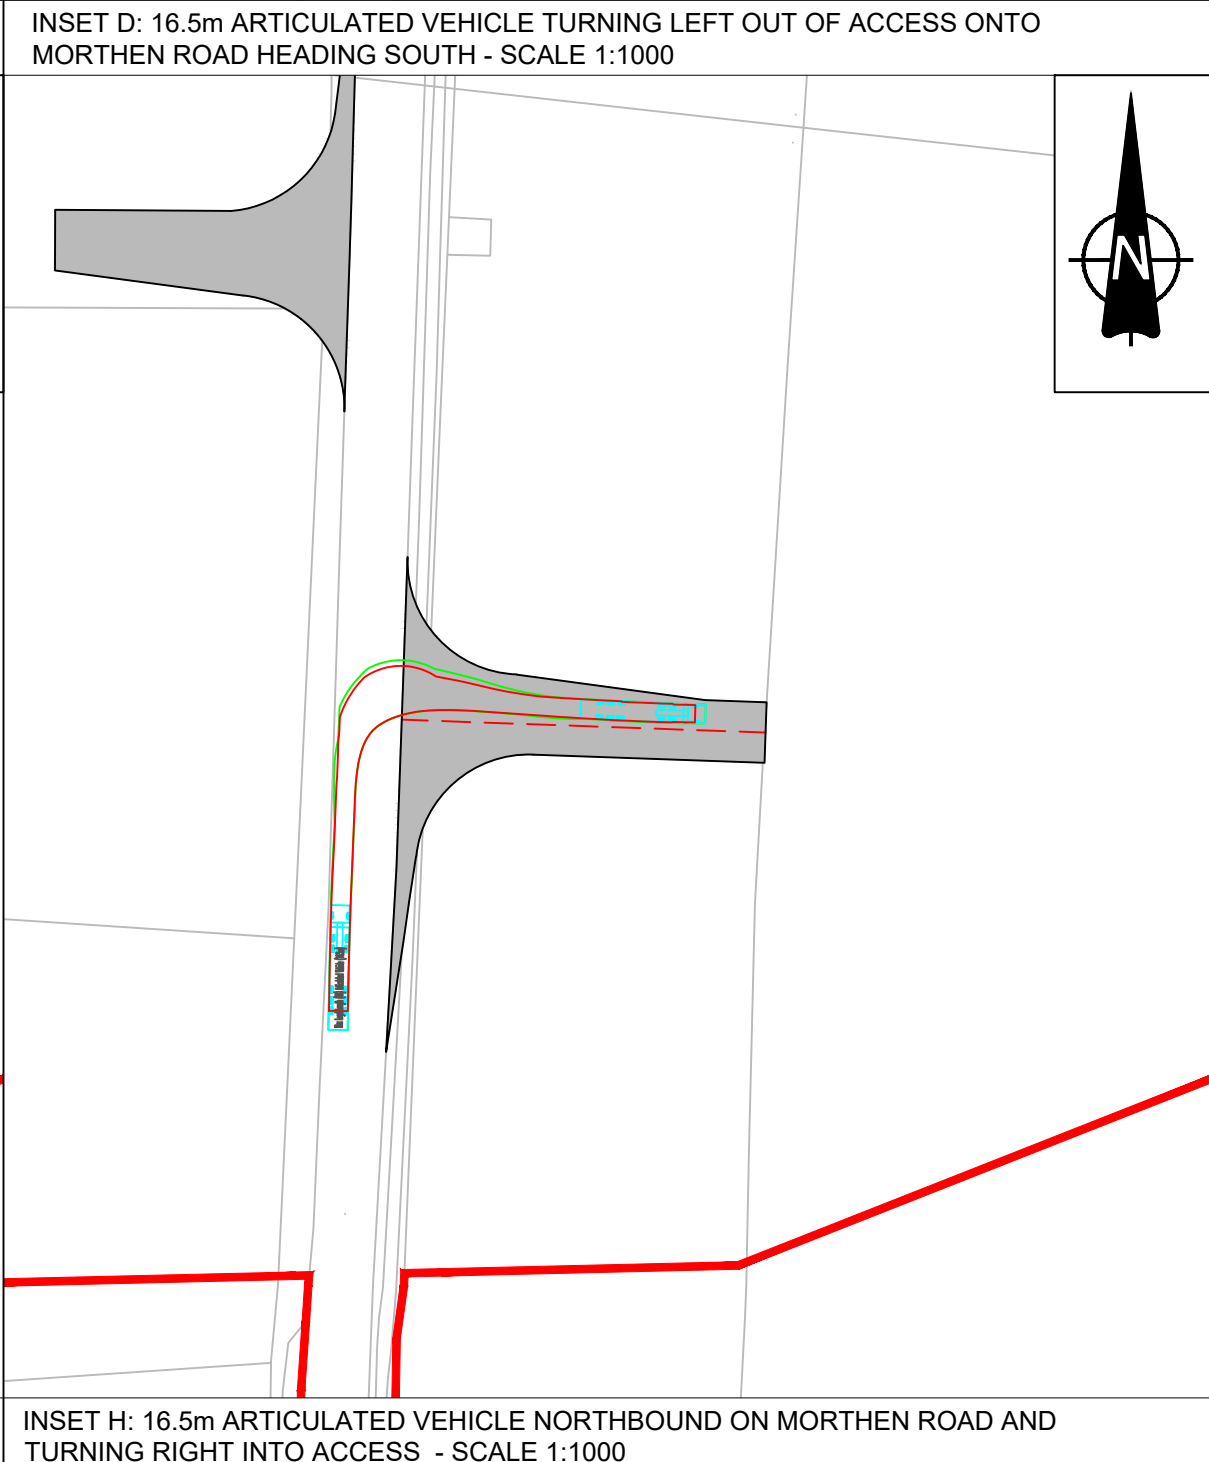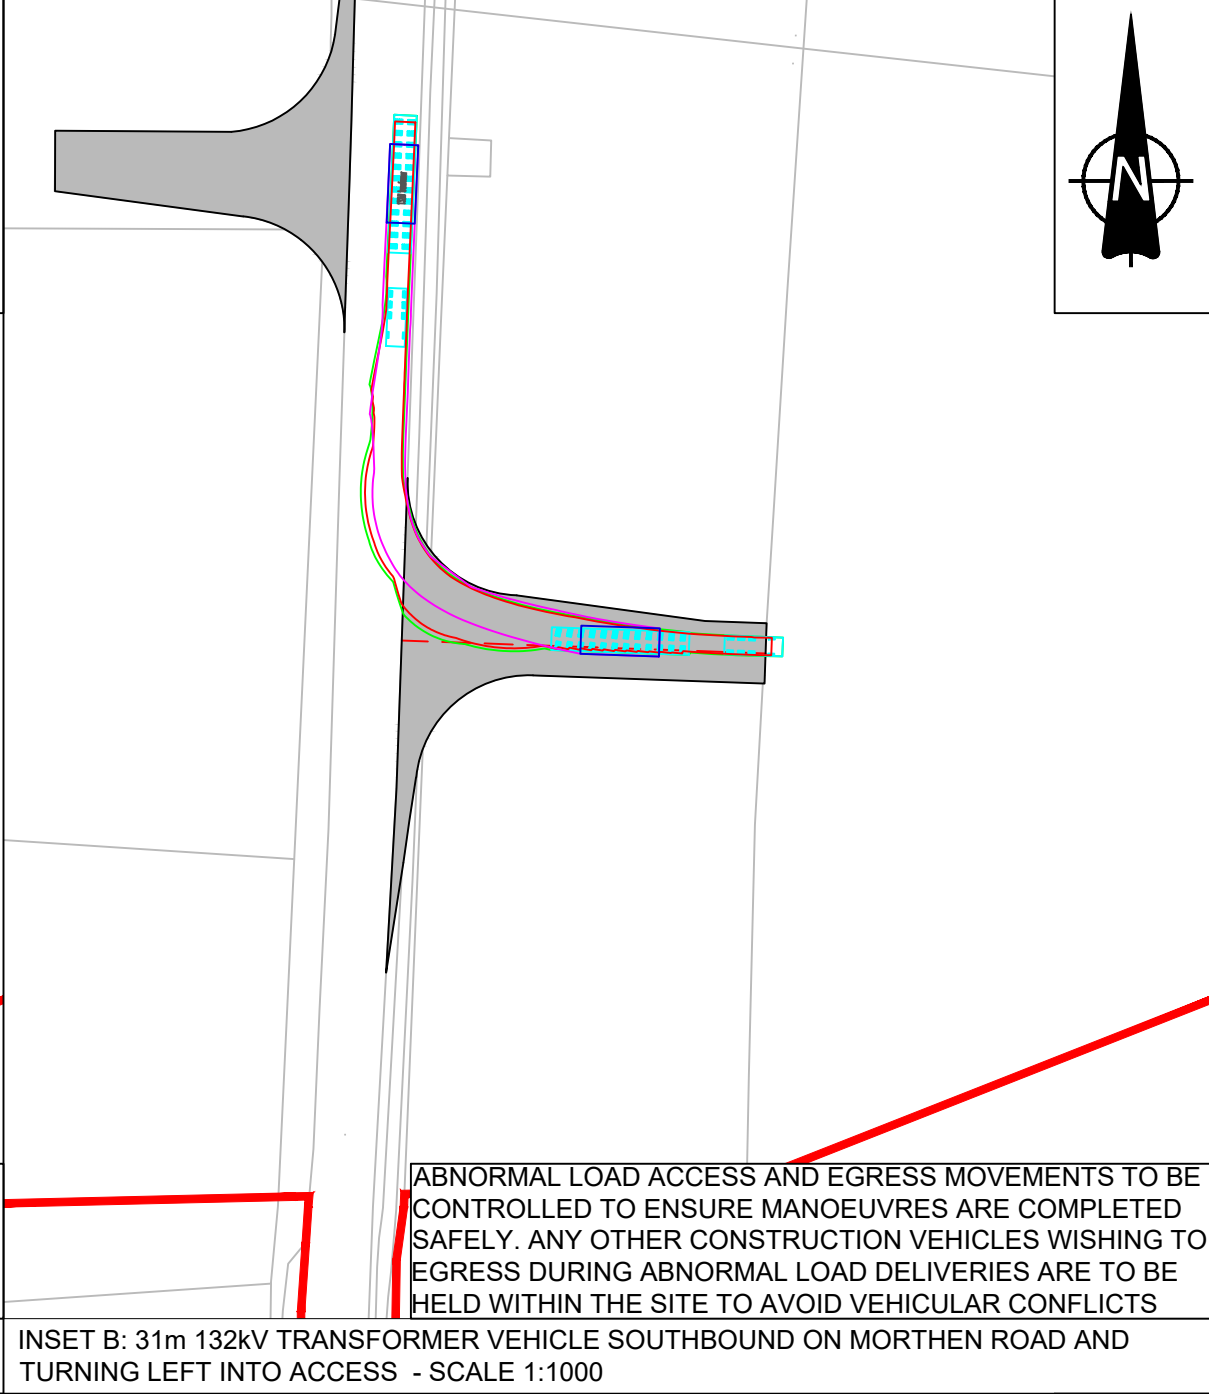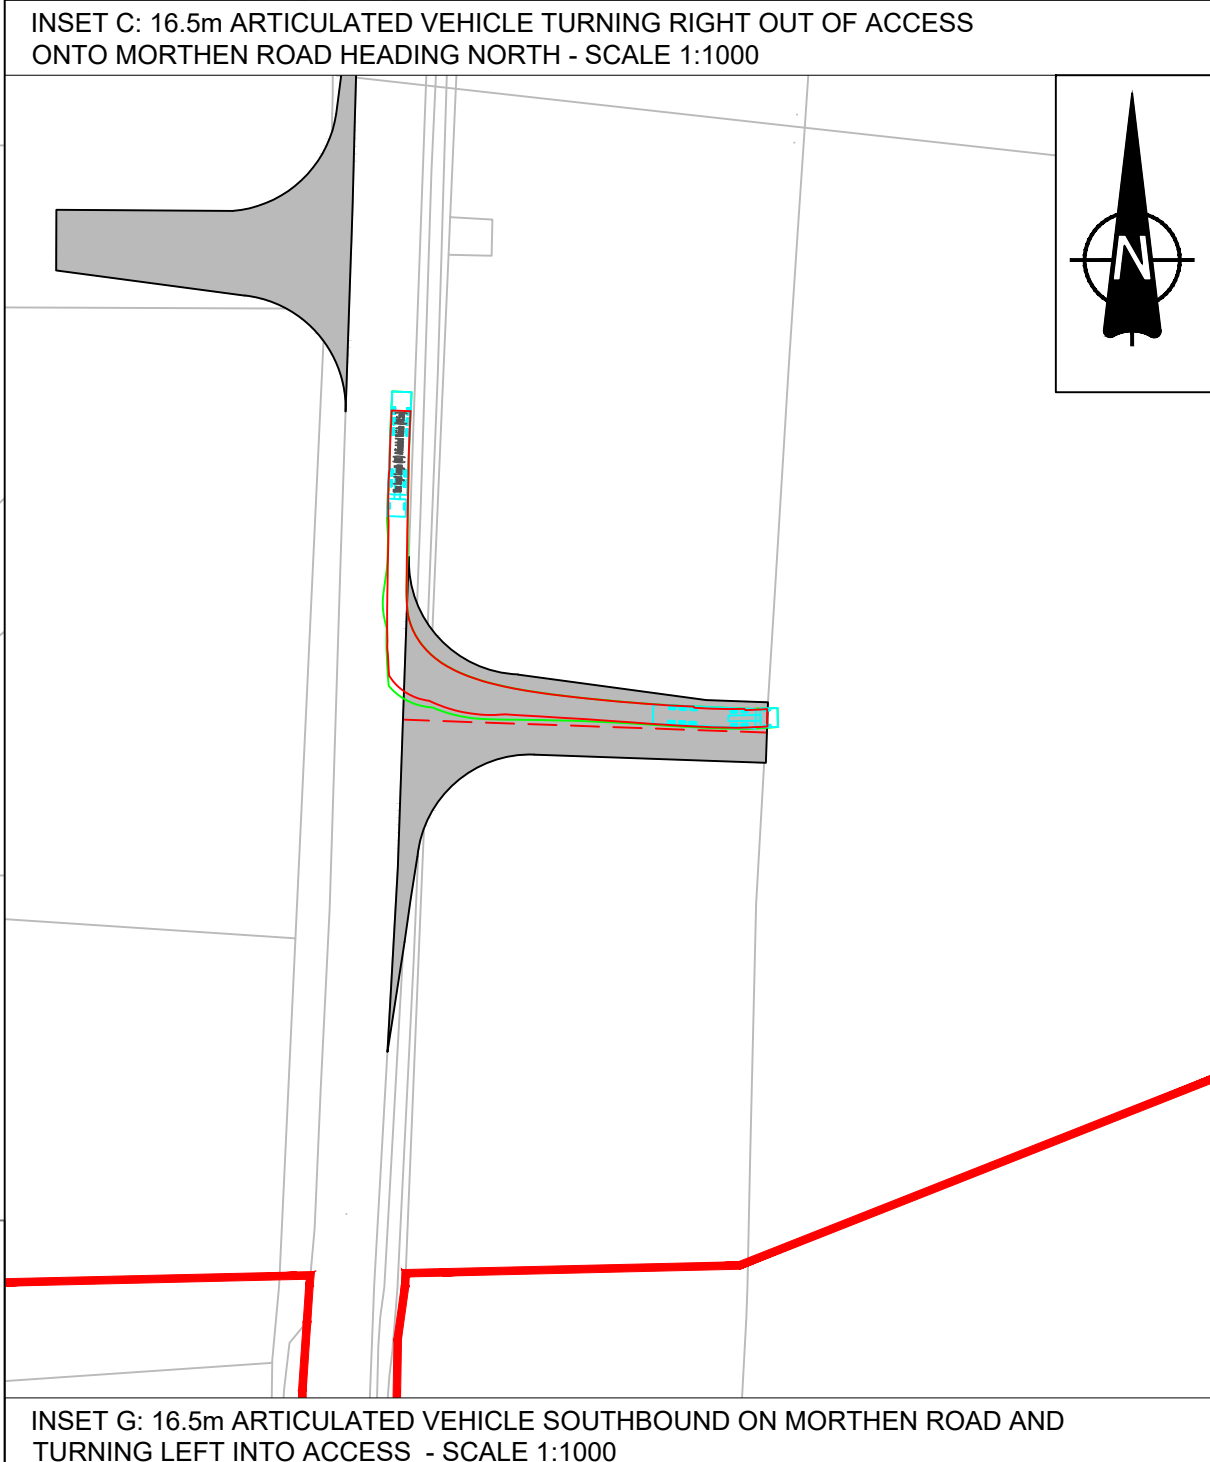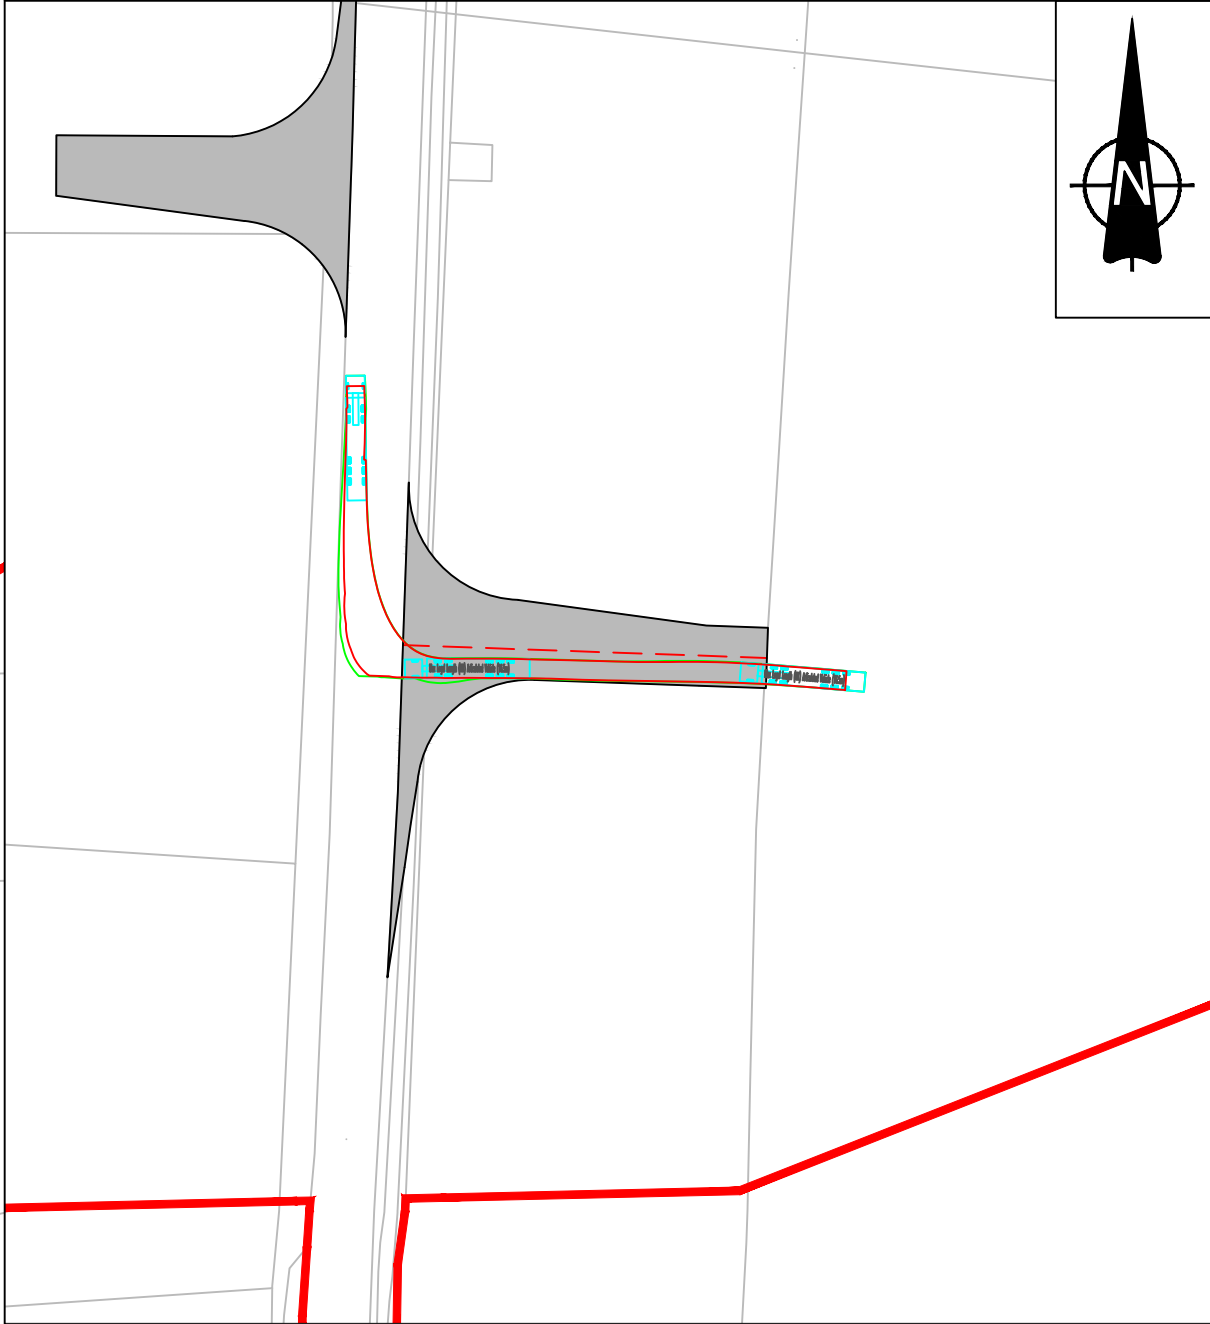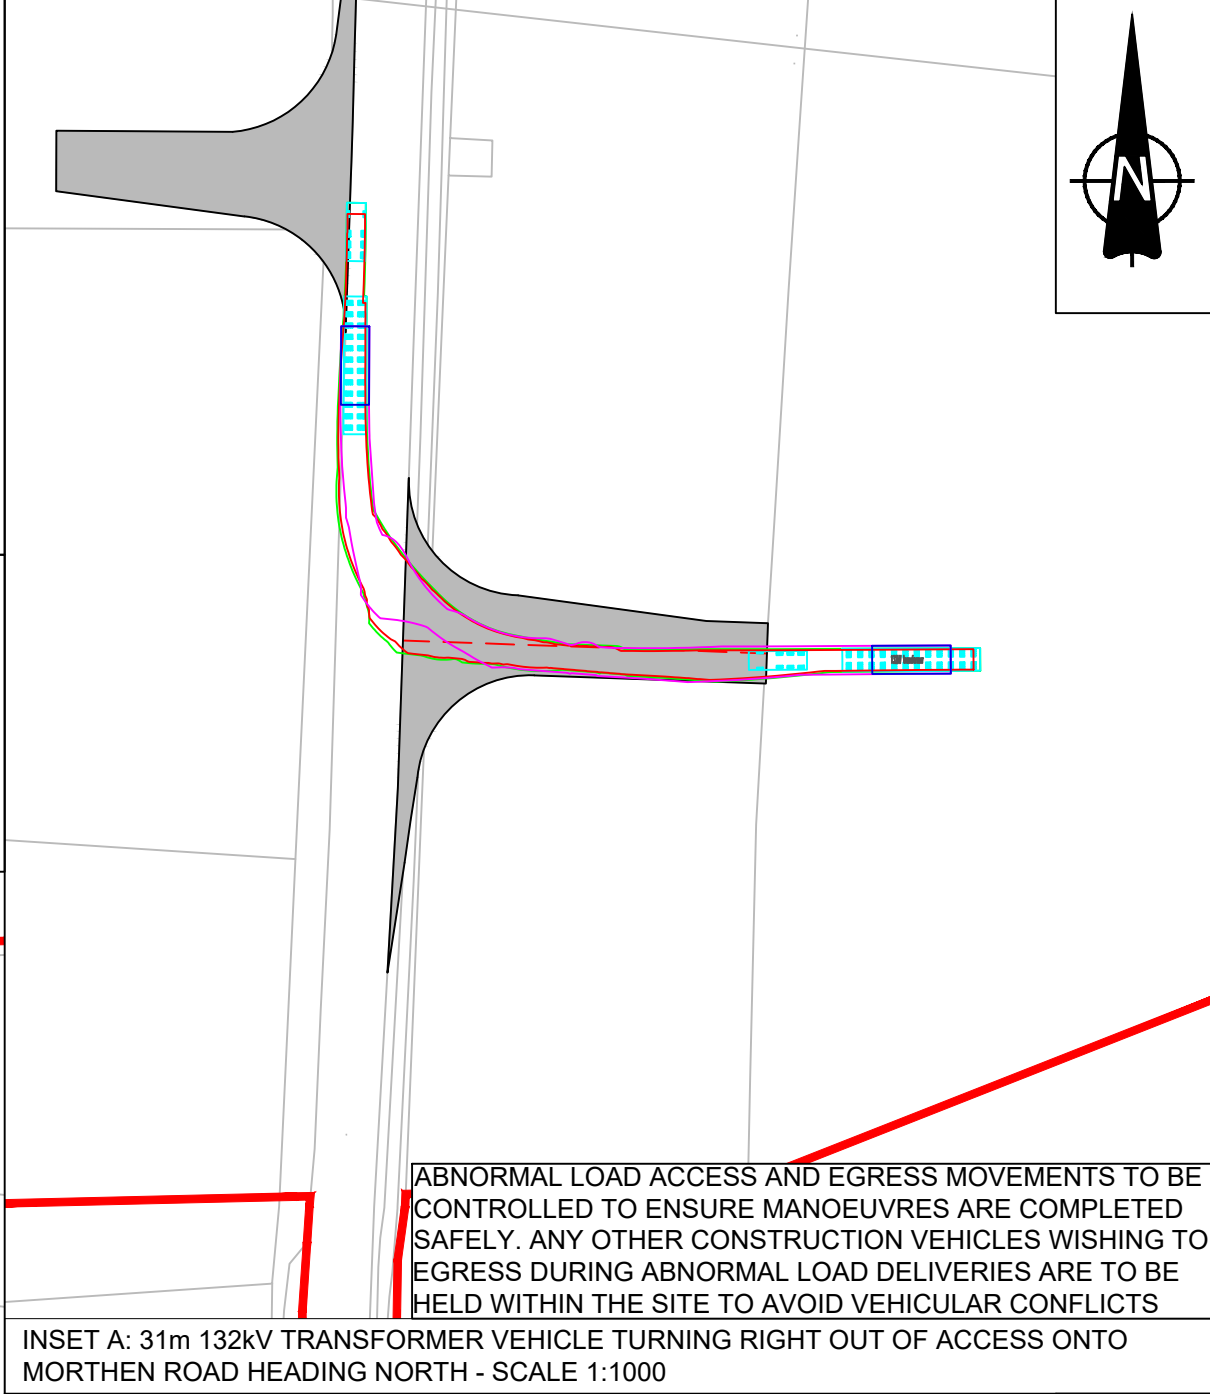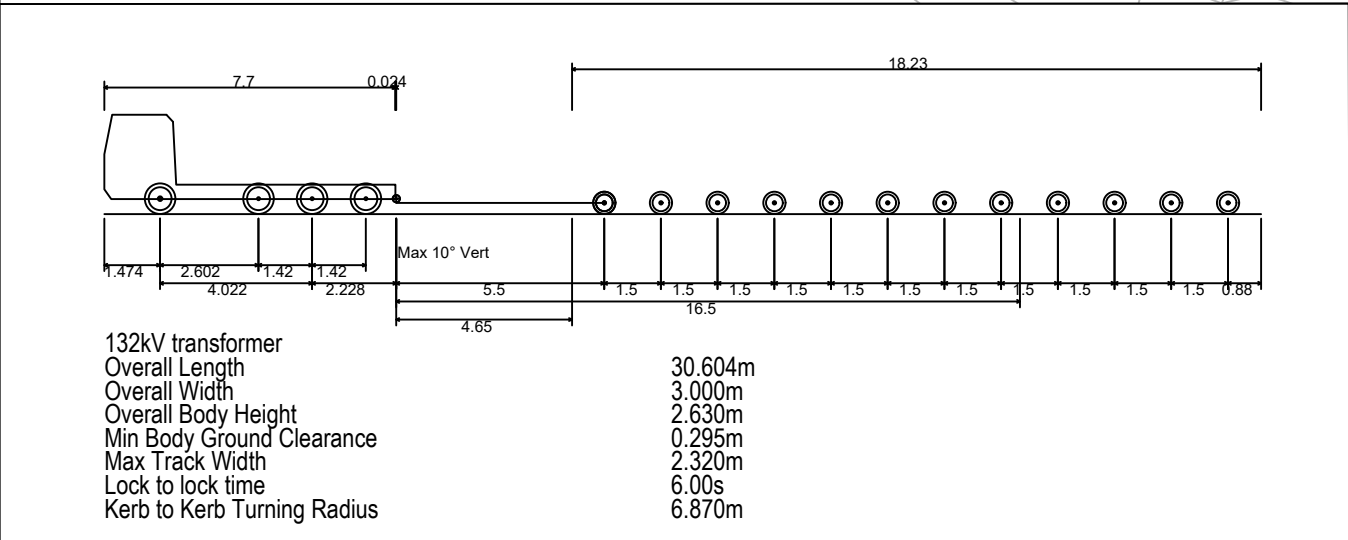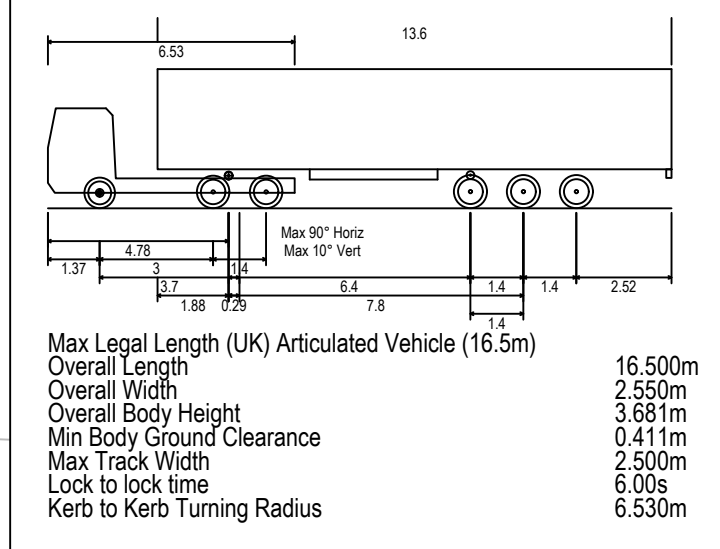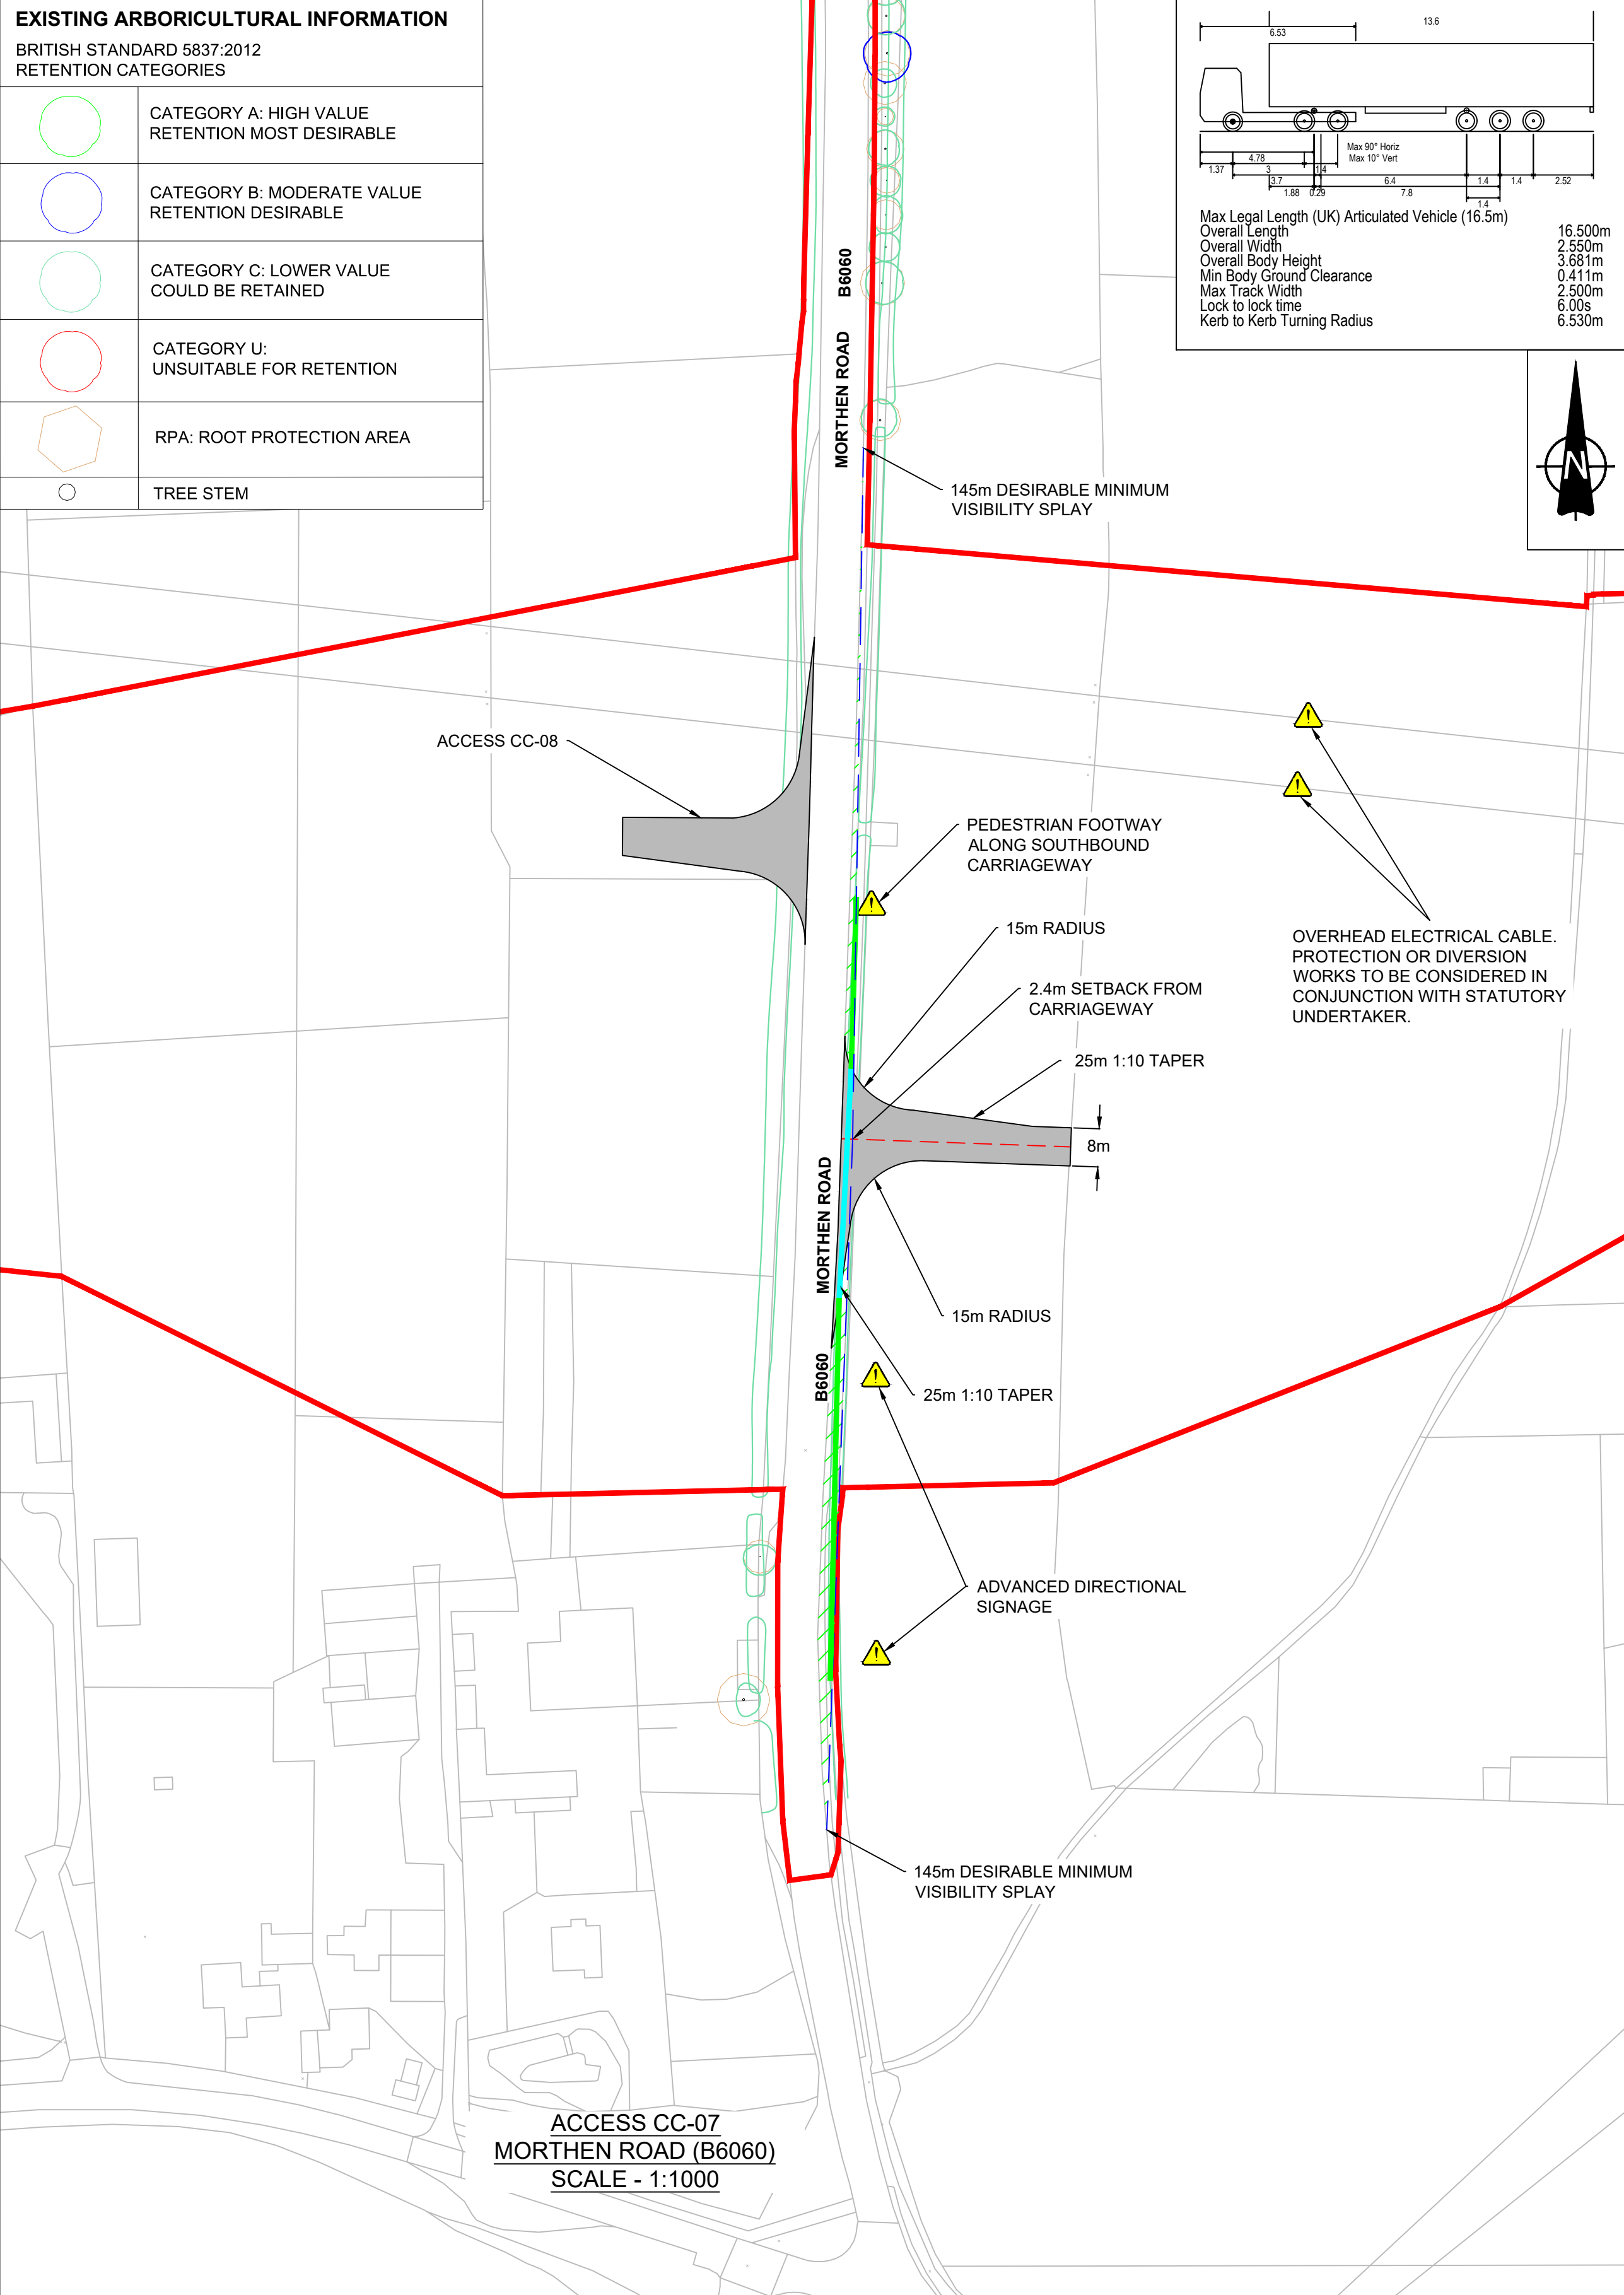








- NOTES**
- This drawing is to be read in conjunction with all other relevant documentation.
 - Do not scale from this drawing, use only printed dimensions.
 - All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
 - This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
 - Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
 - The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
 - Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
 - Junction visibility for the access is based upon visibility parameters derived using the 85th percentile speed survey conducted between the 4th June 2025 to the 10th June 2025.

- LEGEND**
- Extent of Access Footprint
 - Order Limits
 - Land Excluded from Order Limits
 - Vehicle Body
 - Vehicle Body Path
 - Vehicle Load
 - Vehicle Load Path
 - Vehicle Wheels Path
 - Edge of Road
 - Access Centreline
 - Junction Visibility
 - Vegetation to be Removed for Vis Splay
 - Indicative Hedgerow Removal Vis Splay
 - Indicative Hedgerow Removal for Bellmouth Access
 - Health and Safety Risk Identifier
 - Existing Public Right of Way

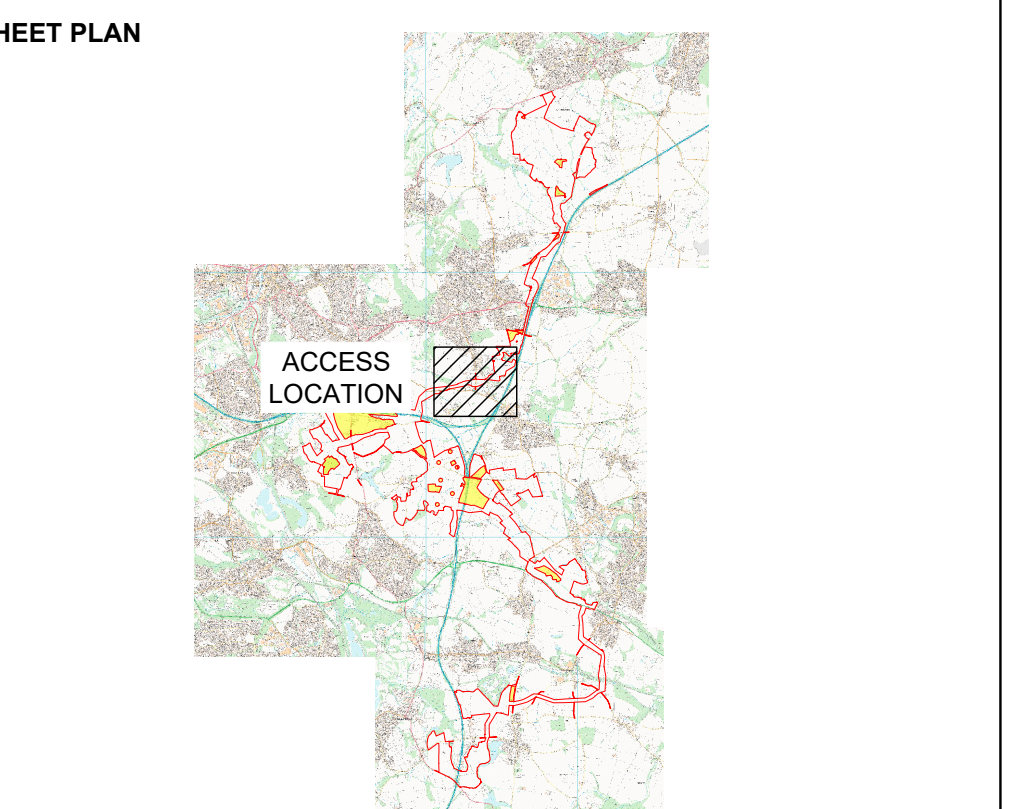


01	03/06/2026	DCO Submission	GH	MEK	JH
SUE	DATE	REMARKS	DRAWN	CHECK	APPROVED
FILE: Cable Corridor Area Access CC-07 Appendix 3 - Sheet 36 of 53 Whitestone Solar Farm Regulation 5(2)(o)					
DRAWING DATE: 03/06/2026					
SCALE: 1:1000			SHEET: Sheet 36 of 53		
SIZE: A1			REVISION: 01		
DOCUMENT REFERENCE: EN0110020/APP/5.12					
APPLICATION NUMBER: EN0110020					
 WHITESTONE solar farm					

EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012 RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

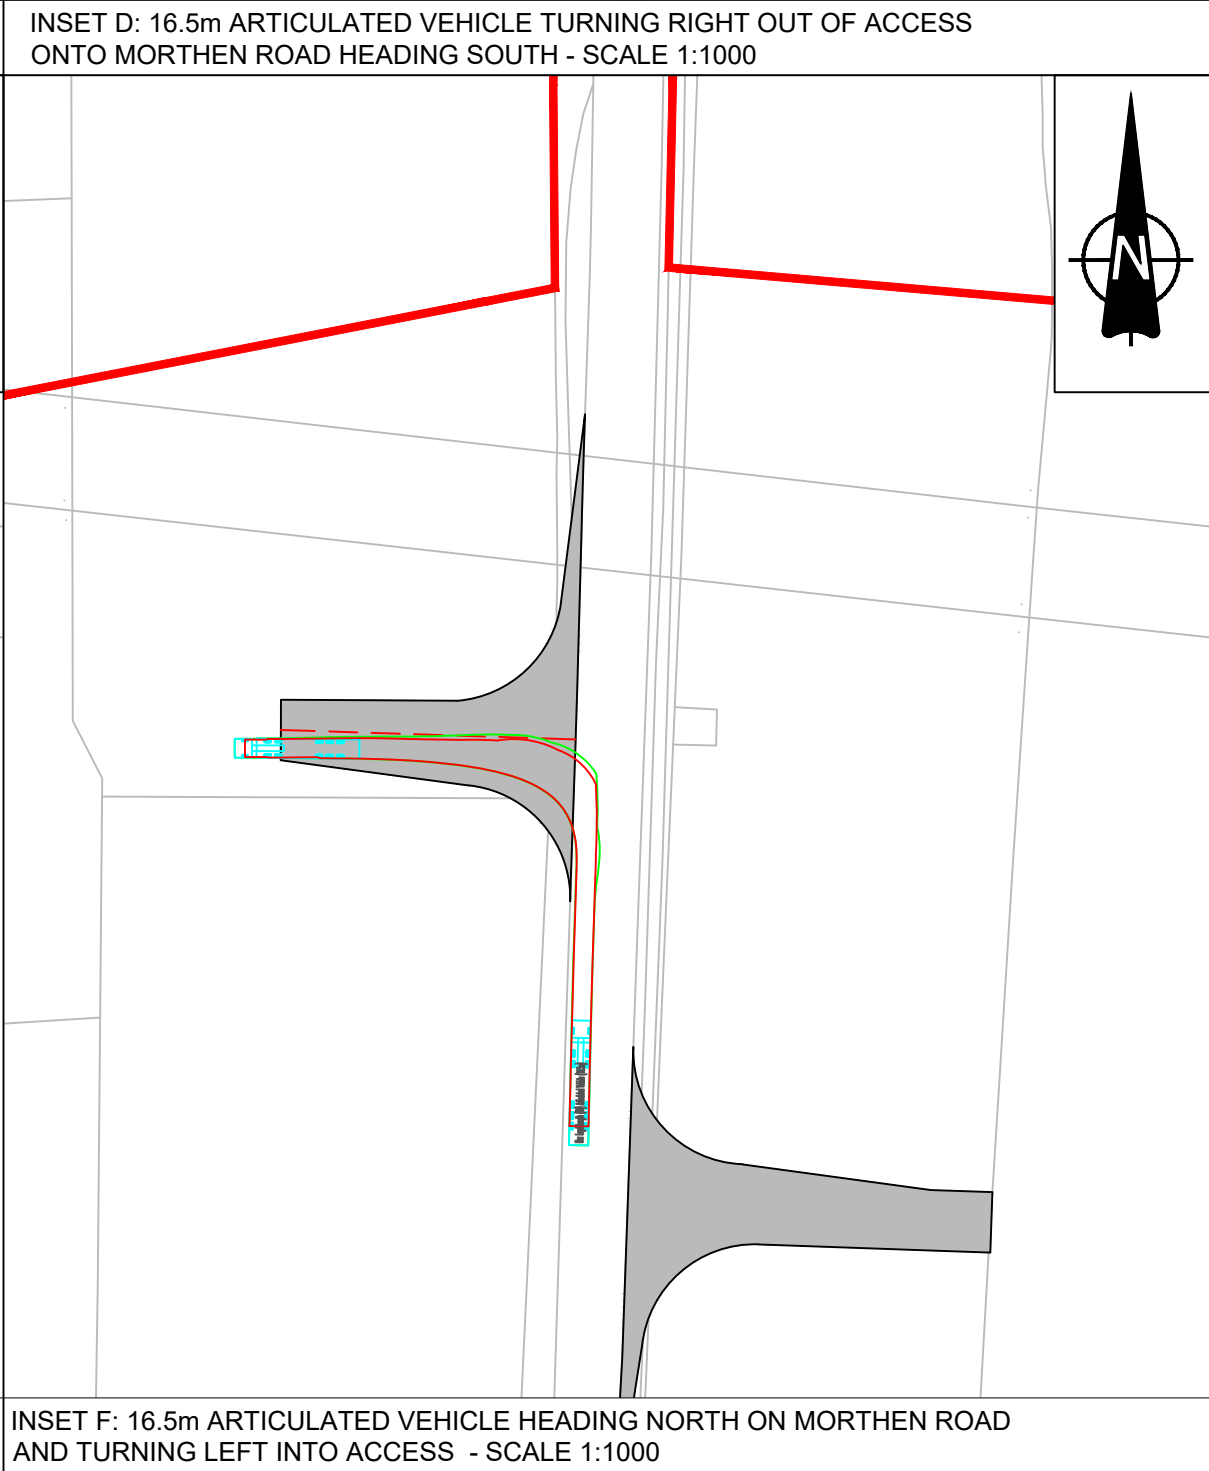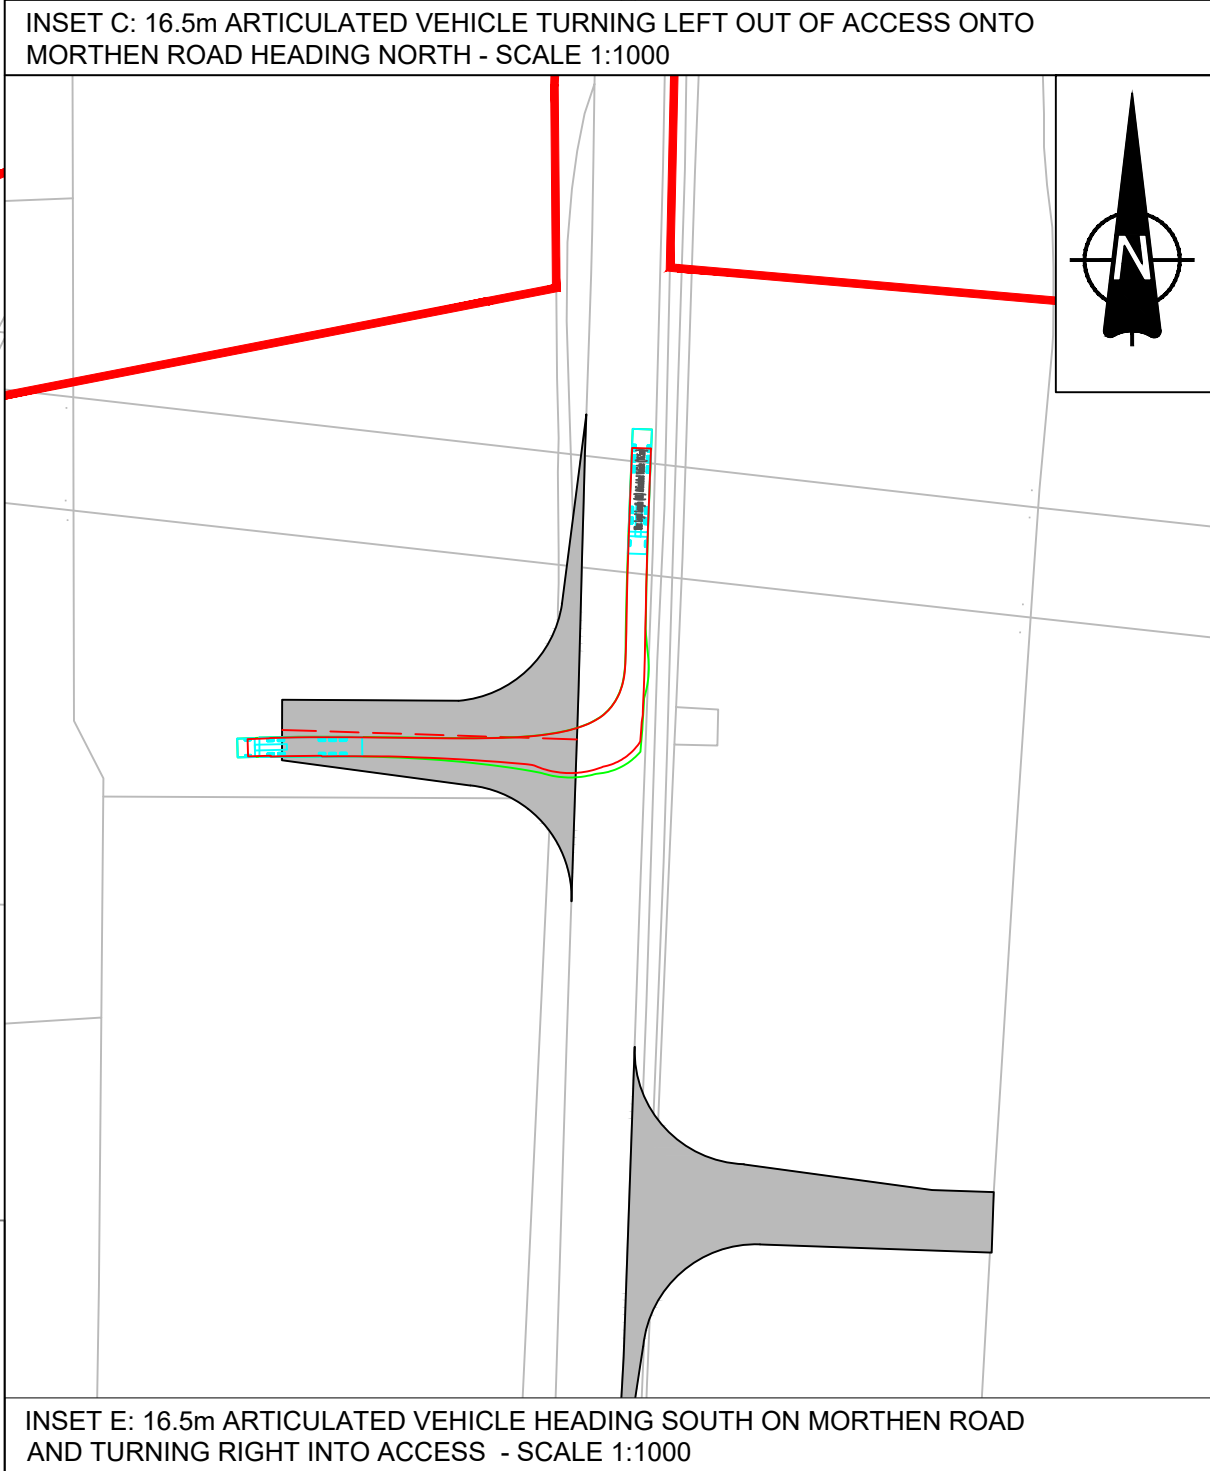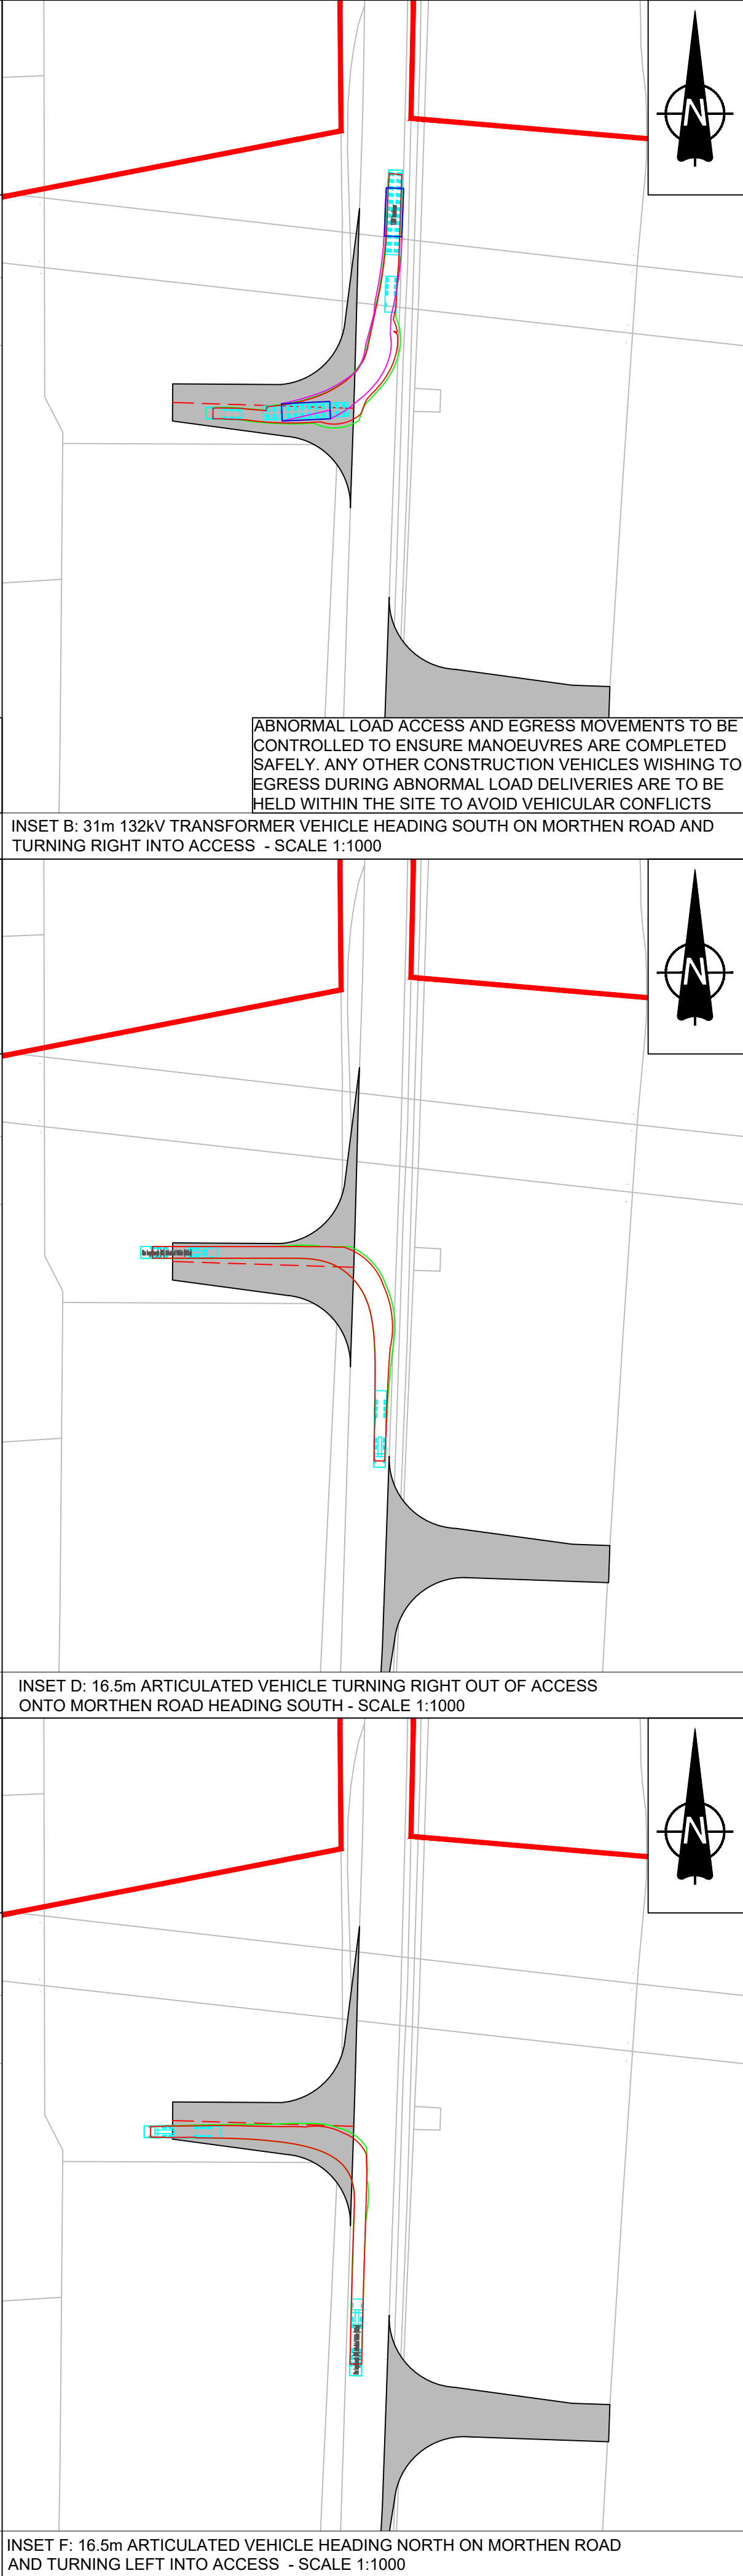
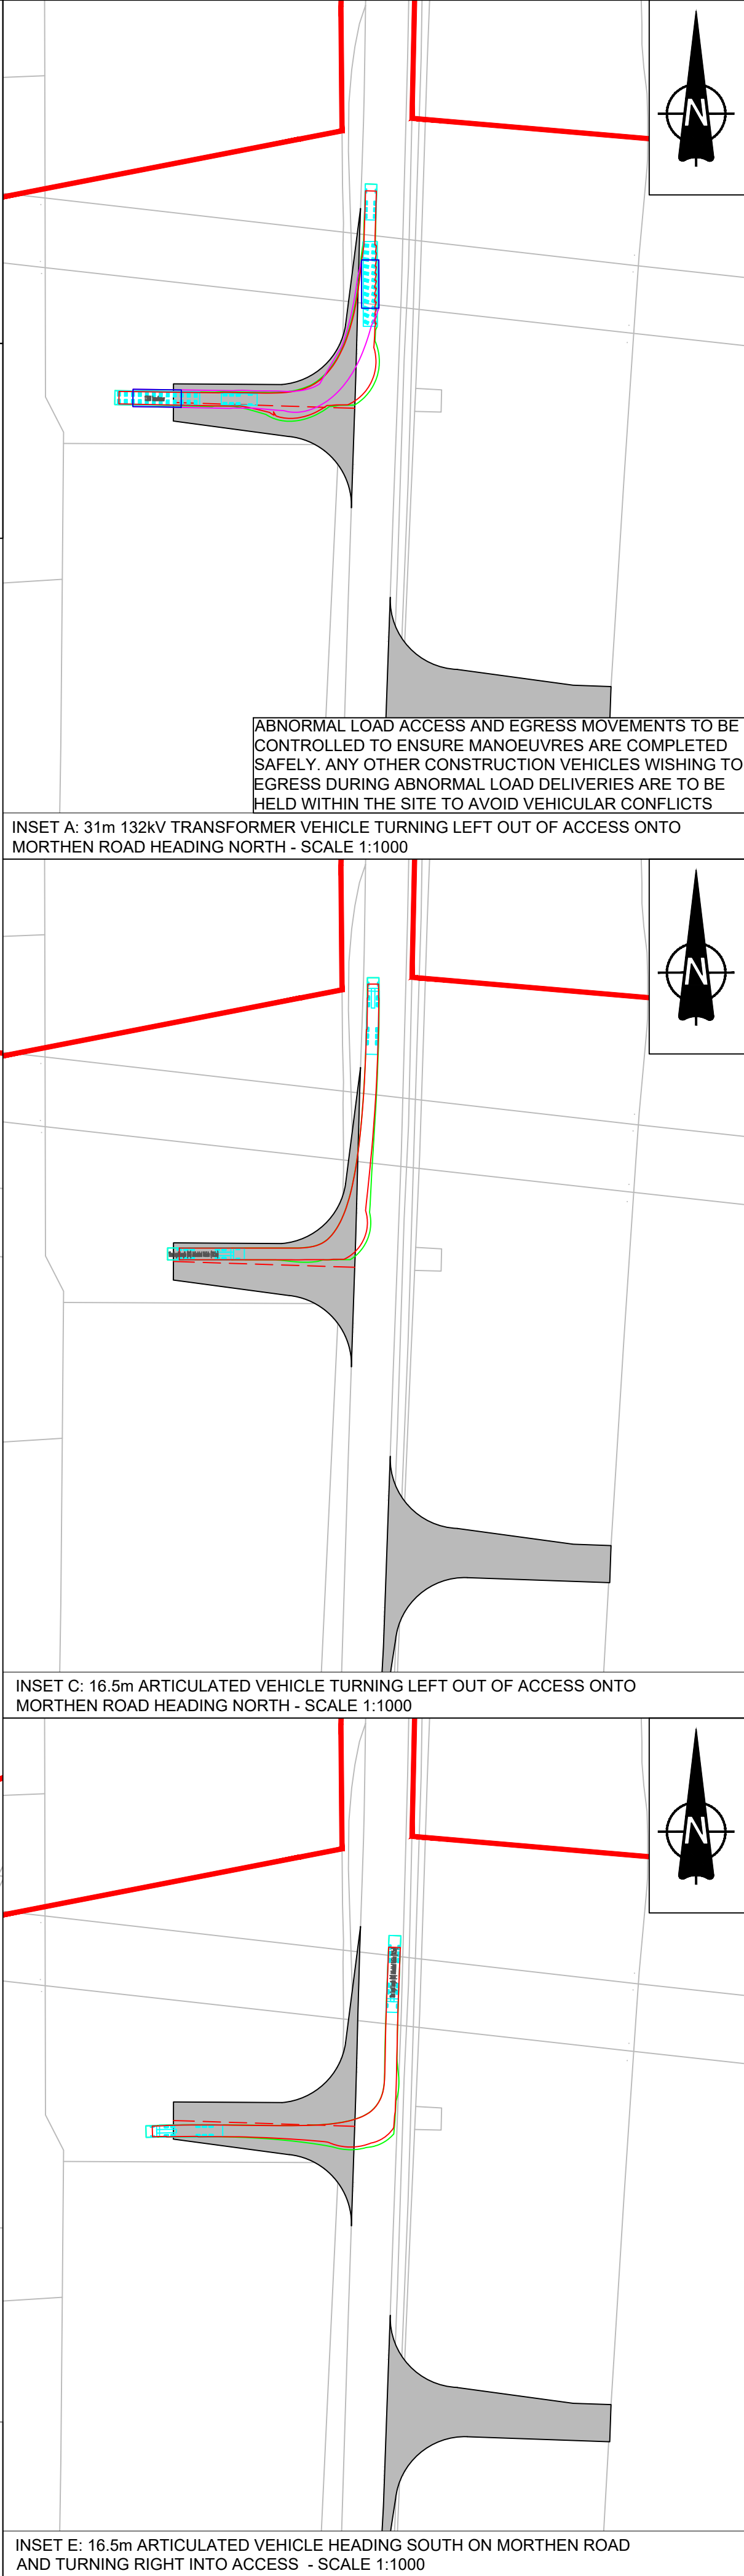
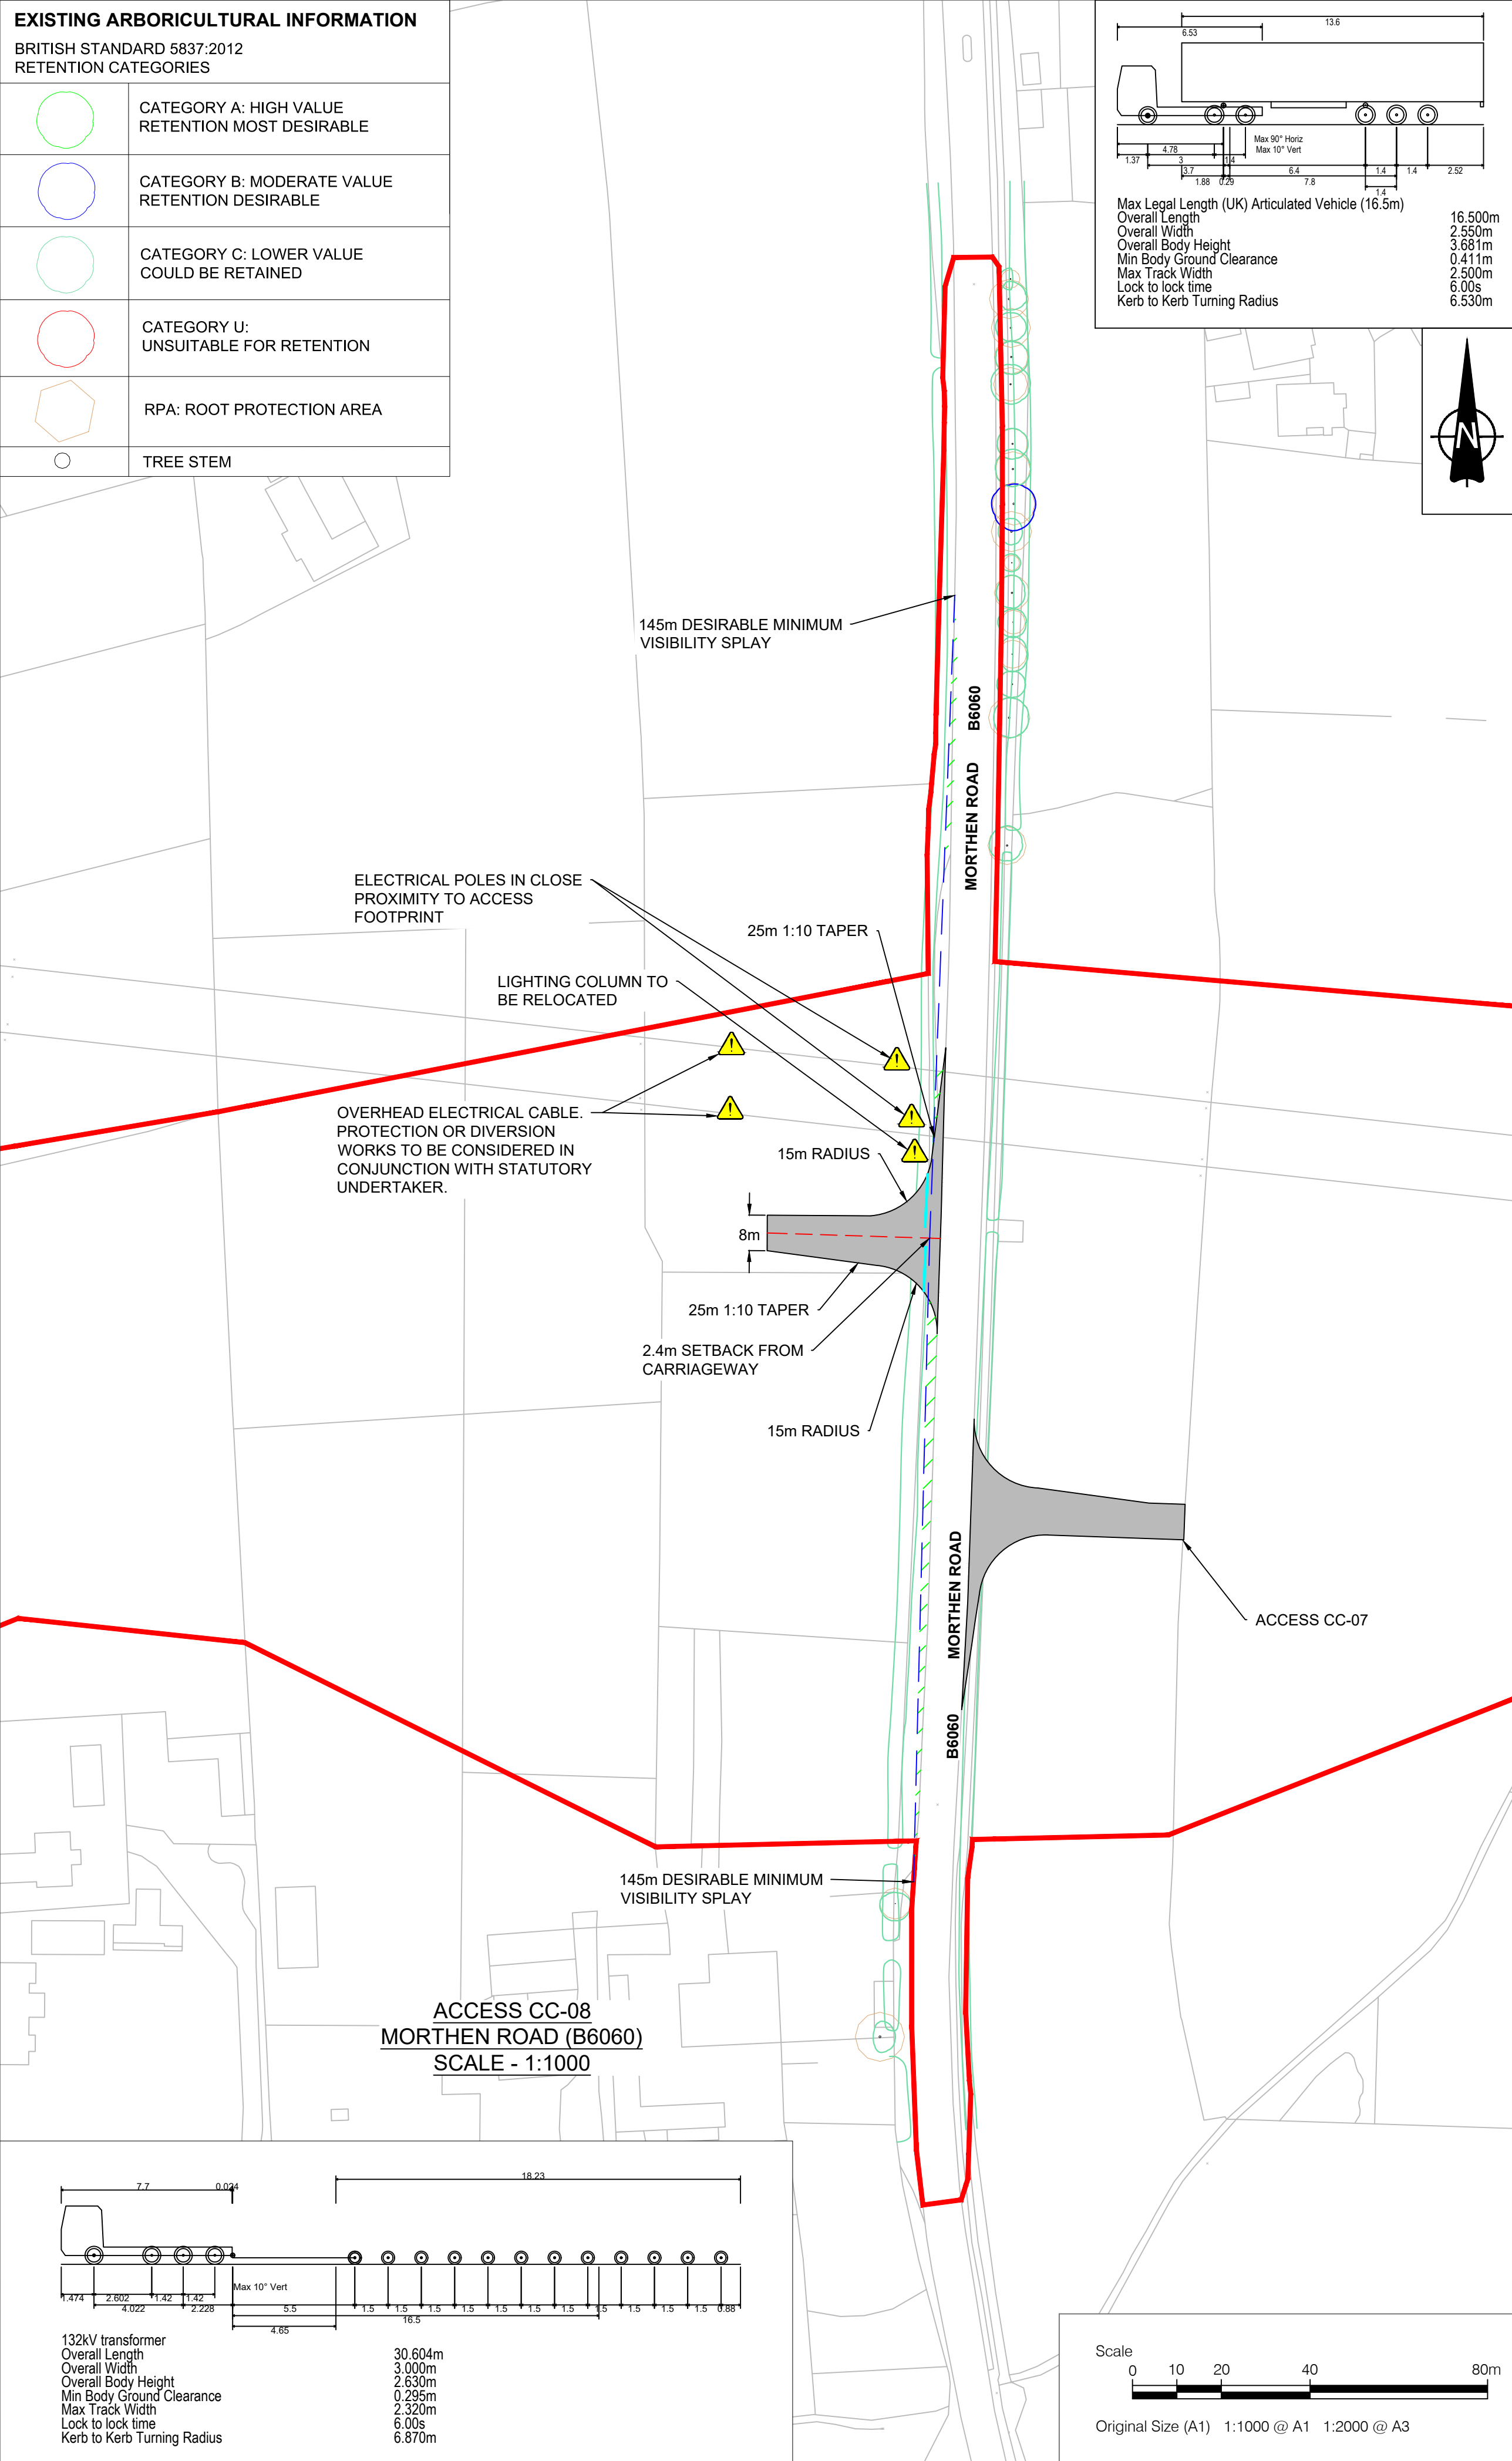


- NOTES**
- This drawing is to be read in conjunction with all other relevant documentation.
 - Do not scale from this drawing, use only printed dimensions.
 - All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
 - This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
 - Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
 - The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
 - Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
 - Junction visibility for the access is based upon visibility parameters derived using the 85th percentile speed survey conducted between the 4th June 2025 to the 10th June 2025.

- LEGEND**
- Extent of Access Footprint
 - Order Limits
 - Land Excluded from Order Limits
 - Vehicle Body
 - Vehicle Body Path
 - Vehicle Load
 - Vehicle Load Path
 - Vehicle Wheels Path
 - Edge of Road
 - Access Centreline
 - Junction Visibility
 - Vegetation to be Removed for Vis Splay
 - Indicative Hedgerow Removal Vis Splay
 - Indicative Hedgerow Removal for Bellmouth Access
 - Health and Safety Risk Identifier
 - Existing Public Right of Way

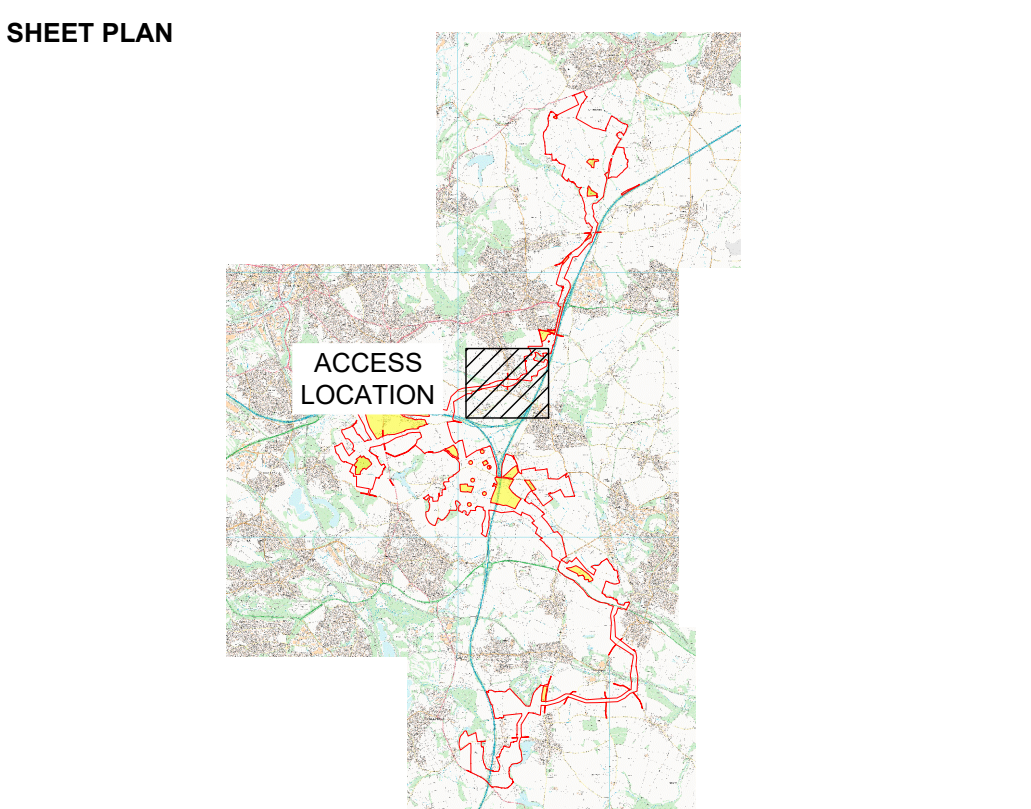

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED
TITLE: Cable Corridor Area Access CC-08 Appendix 3 - Sheet 37 of 53 Whitestone Solar Farm Regulation 5(2)(o)					
DRAWING DATE: 03/06/2026					
SCALE: 1:1000			SHEET: Sheet 37 of 53		
SIZE: A1			REVISION: 01		
DOCUMENT REFERENCE: EN0110020/APP/5.12					
APPLICATION NUMBER: EN0110020					
 WHITESTONE solar farm					

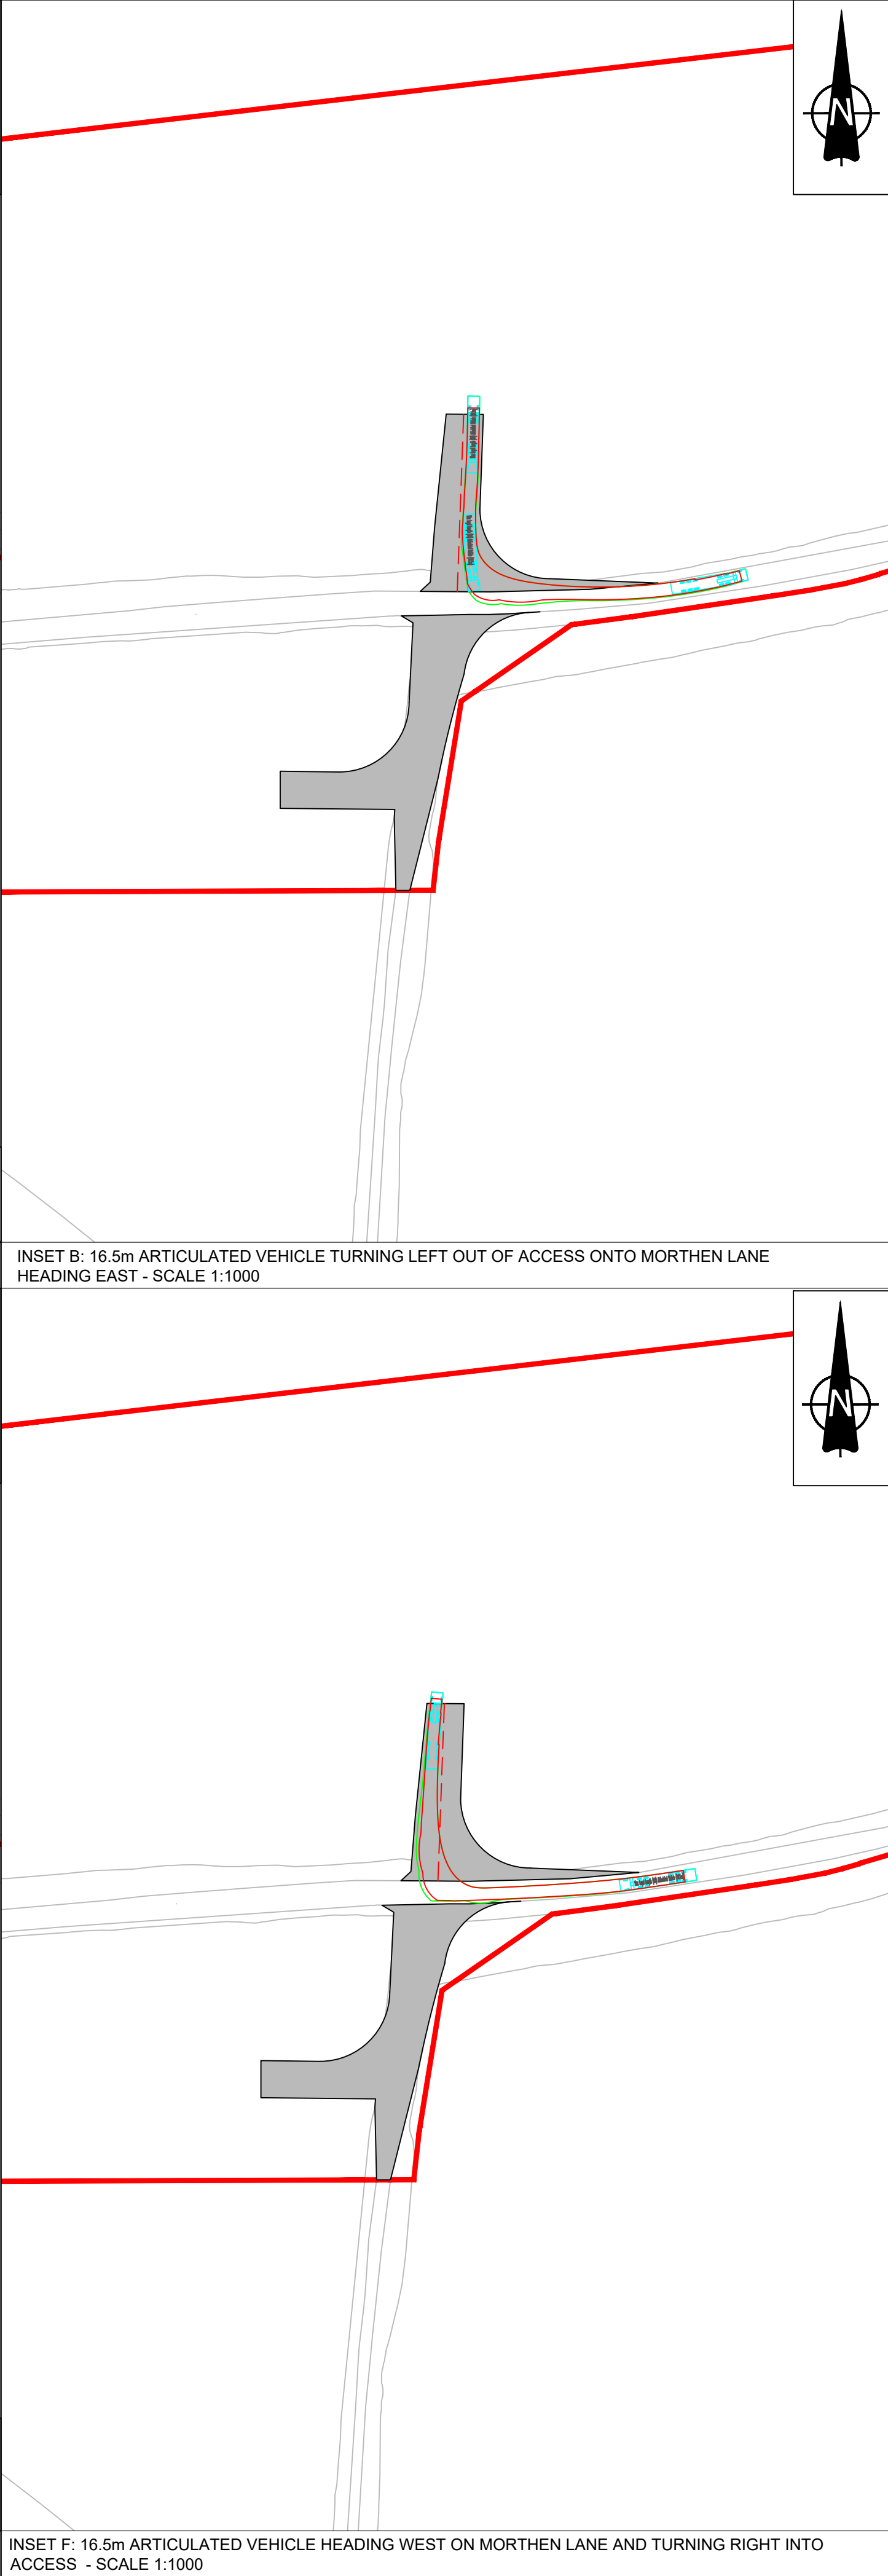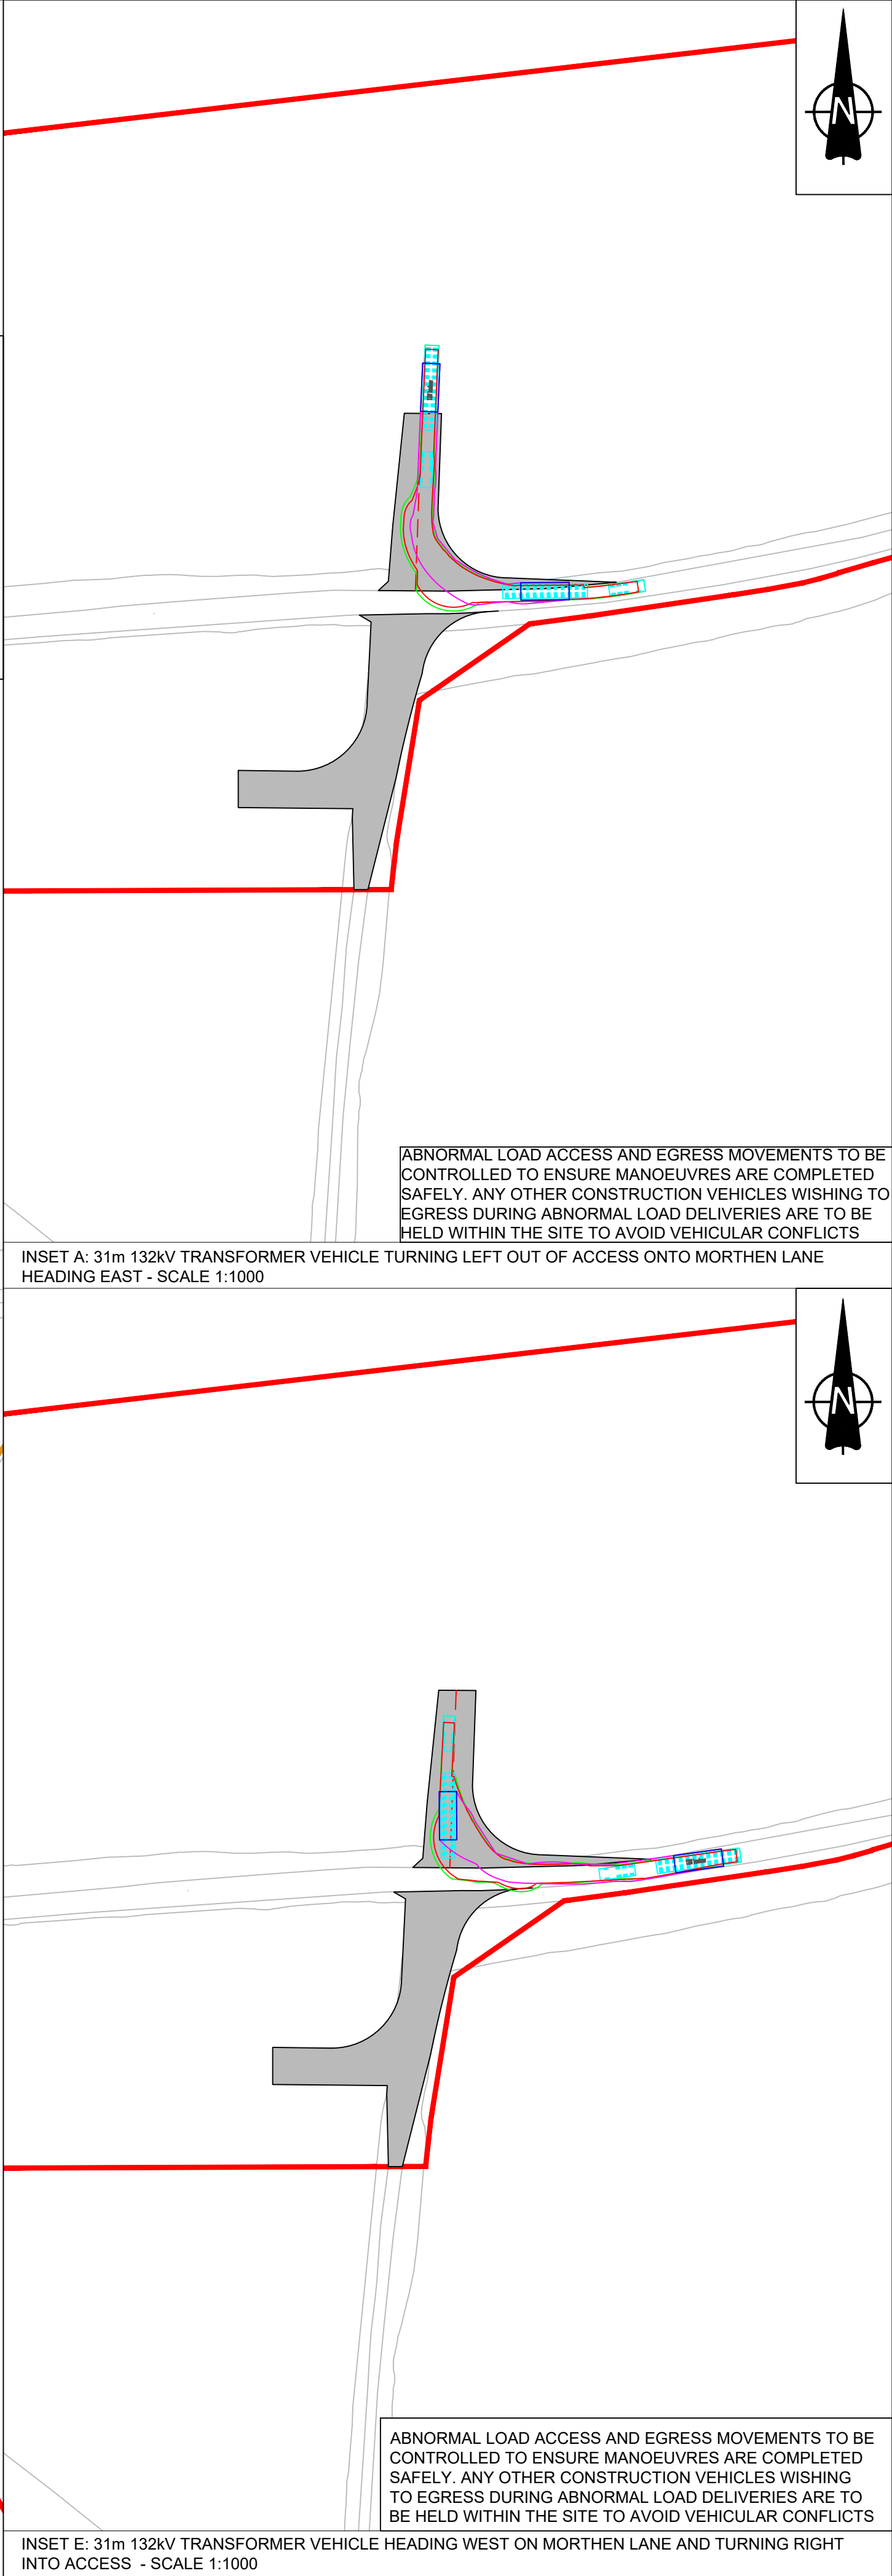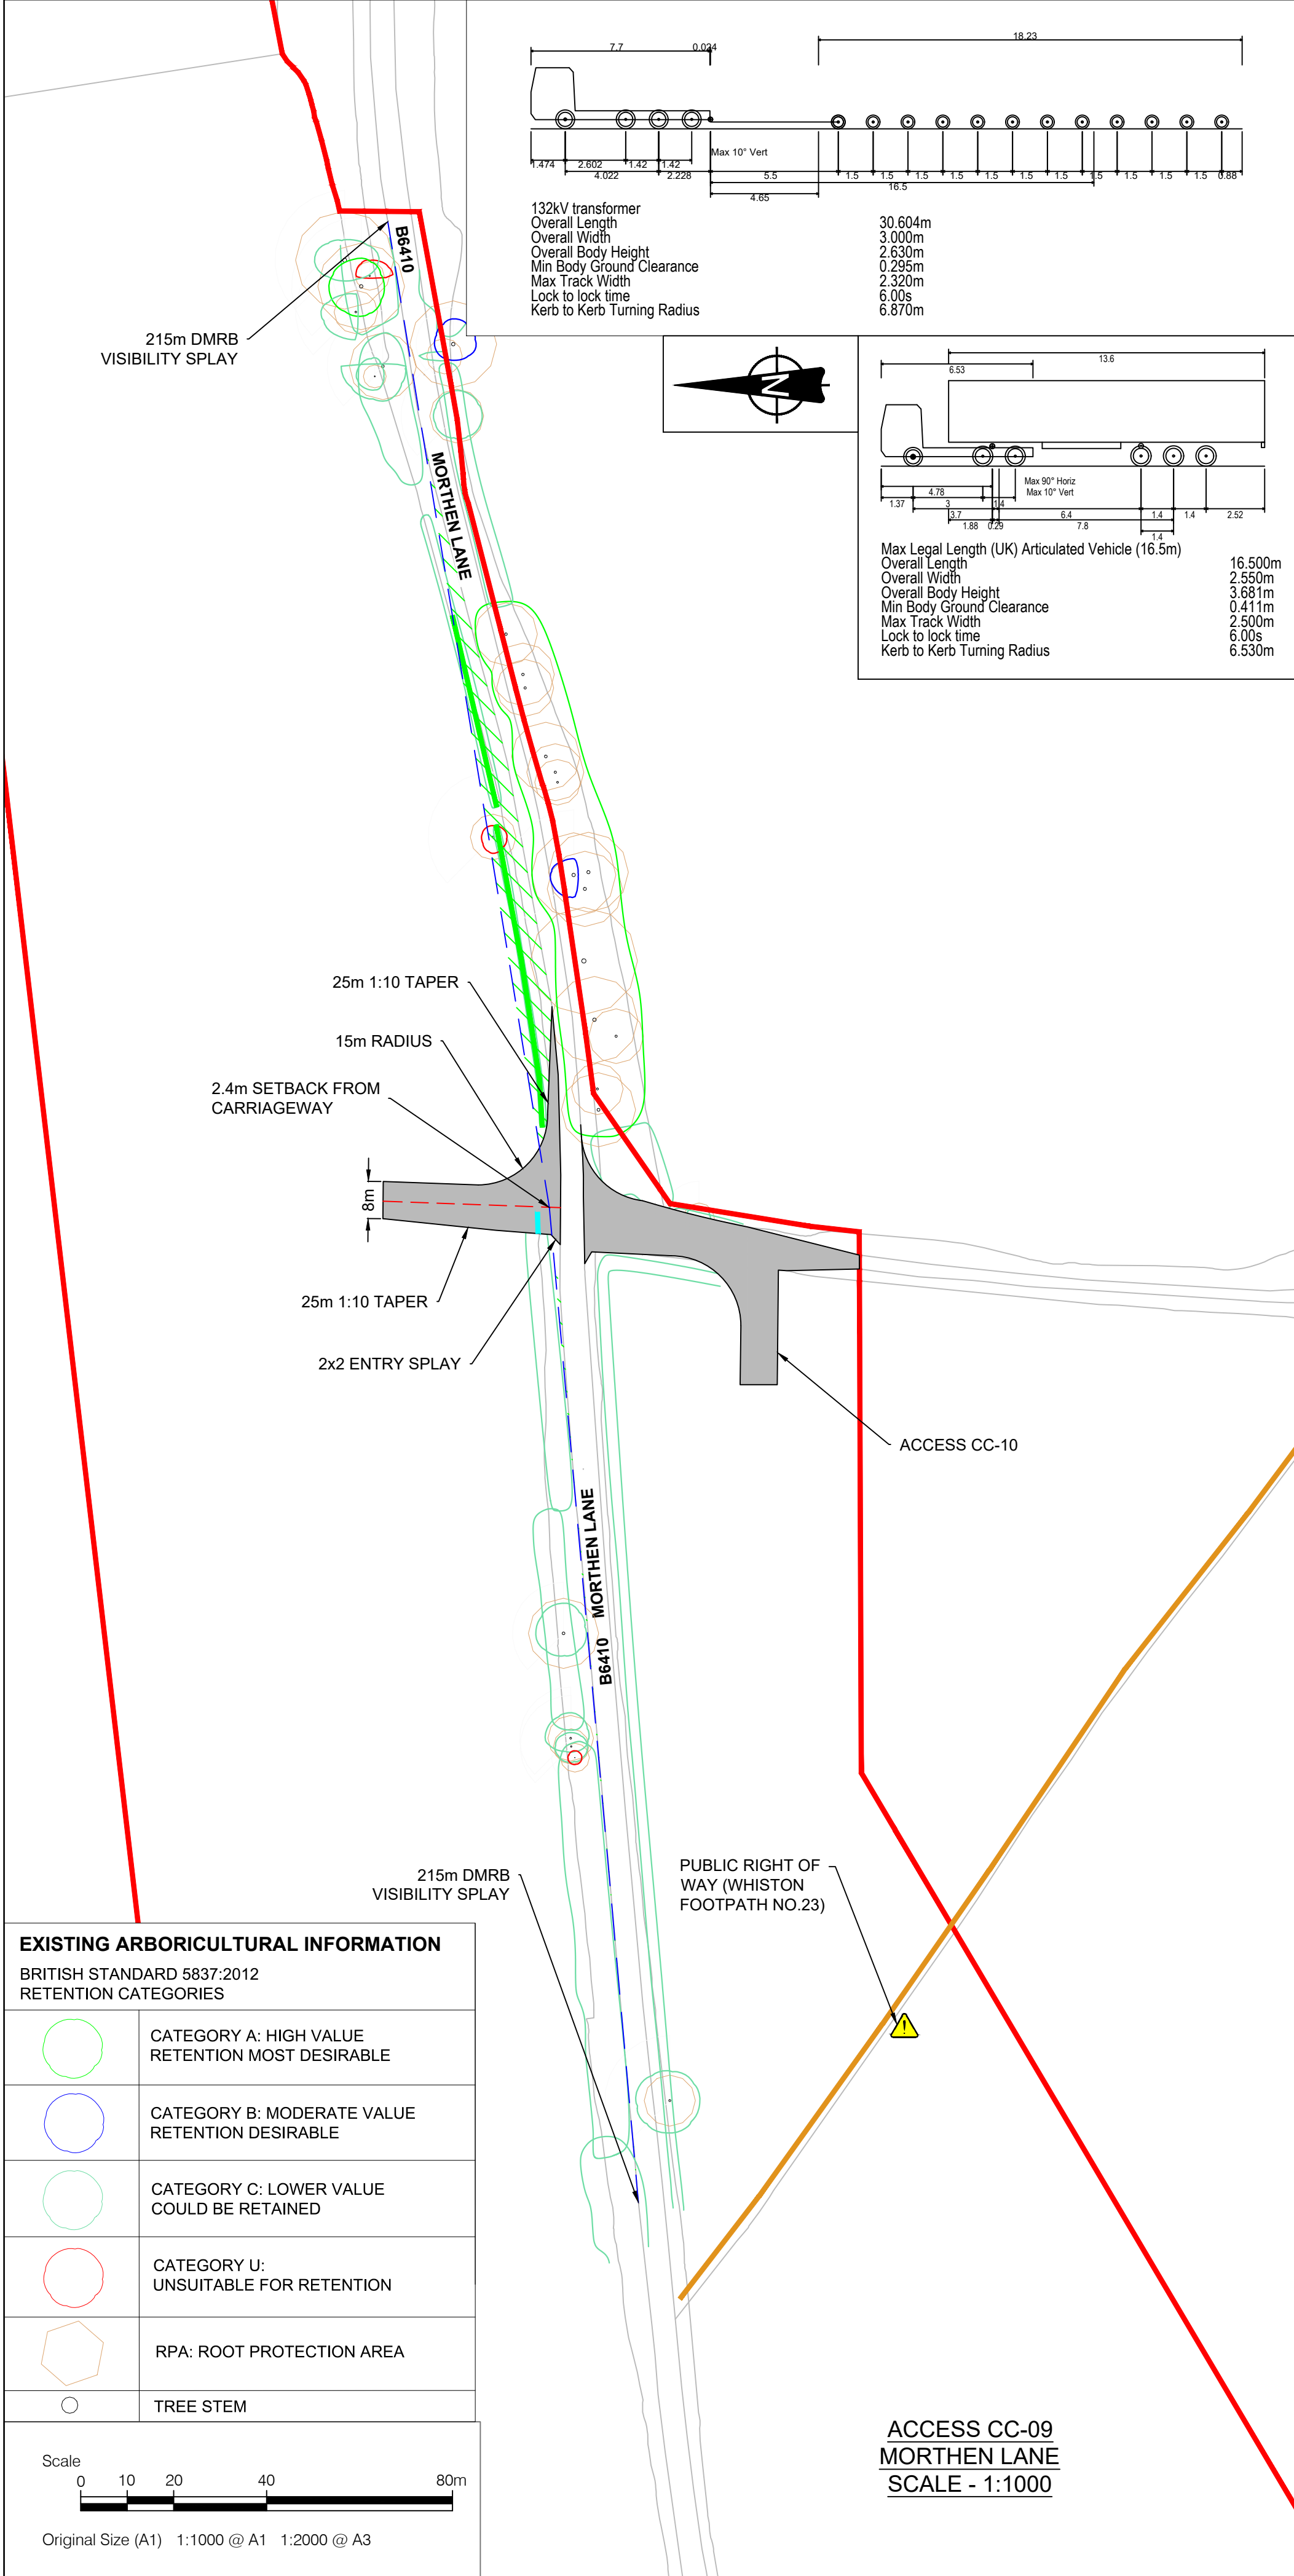

- NOTES
- This drawing is to be read in conjunction with all other relevant documentation.
 - Do not scale from this drawing, use only printed dimensions.
 - All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
 - This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
 - Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
 - The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
 - Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
 - Junction visibility for the access is based upon DMRB CD109 Table 2.10.

- LEGEND
- Extent of Access Footprint
 - Order Limits
 - Land Excluded from Order Limits
 - Vehicle Body
 - Vehicle Body Path
 - Vehicle Load
 - Vehicle Load Path
 - Vehicle Wheels Path
 - Edge of Road
 - Access Centreline
 - Junction Visibility
 - Vegetation to be Removed for Vis Splay
 - Indicative Hedgerow Removal Vis Splay
 - Indicative Hedgerow Removal for Bellmouth Access
 - Health and Safety Risk Identifier
 - Existing Public Right of Way

SHEET PLAN

ACCESS LOCATION

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:

Cable Corridor Area Access CC-09

Appendix 3 - Sheet 38 of 53

Whitestone Solar Farm

Regulation 5(2)(o)

DRAWING DATE: 03/06/2026

SCALE: 1:1000


SIZE: A1

DOCUMENT REFERENCE: EN0110020/APP/5.12


APPLICATION NUMBER: EN0110020

REVISION: 01

WHITESTONE solar farm

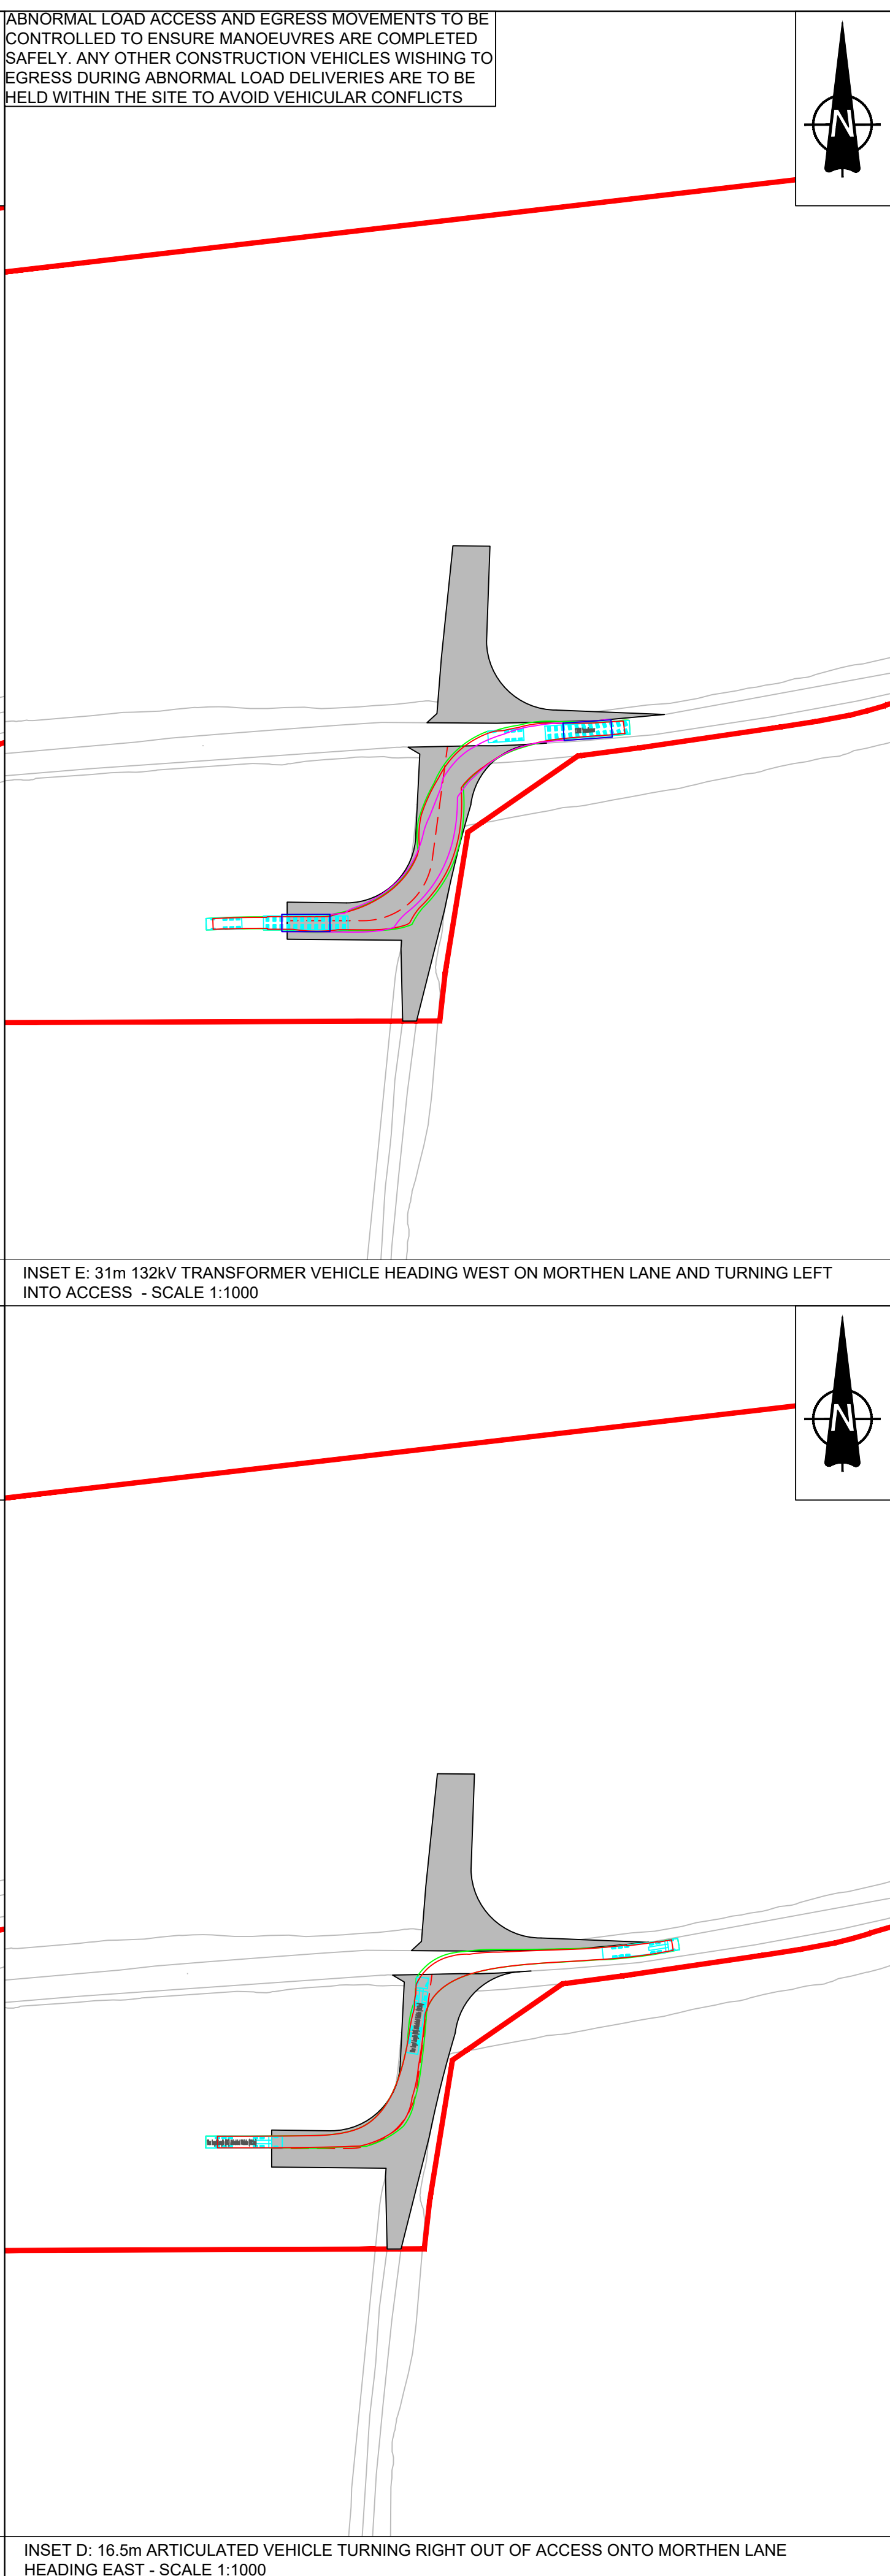

- ## LEGEND
- | | |
|---|--|
|  | Extent of Access Footprint |
|  | Order Limits |
|  | Land Excluded from Order Limits |
|  | Vehicle Body |
|  | Vehicle Body Path |
|  | Vehicle Load |
|  | Vehicle Load Path |
|  | Vehicle Wheels Path |
|  | Edge of Road |
|  | Access Centreline |
|  | Junction Visibility |
|  | Vegetation to be Removed for Vis Splay |
|  | Indicative Hedgerow Removal Vis Splay |
|  | Indicative Hedgerow Removal for Bellmouth Access |
|  | Health and Safety Risk Identifier |
|  | Existing Public Right of Way |

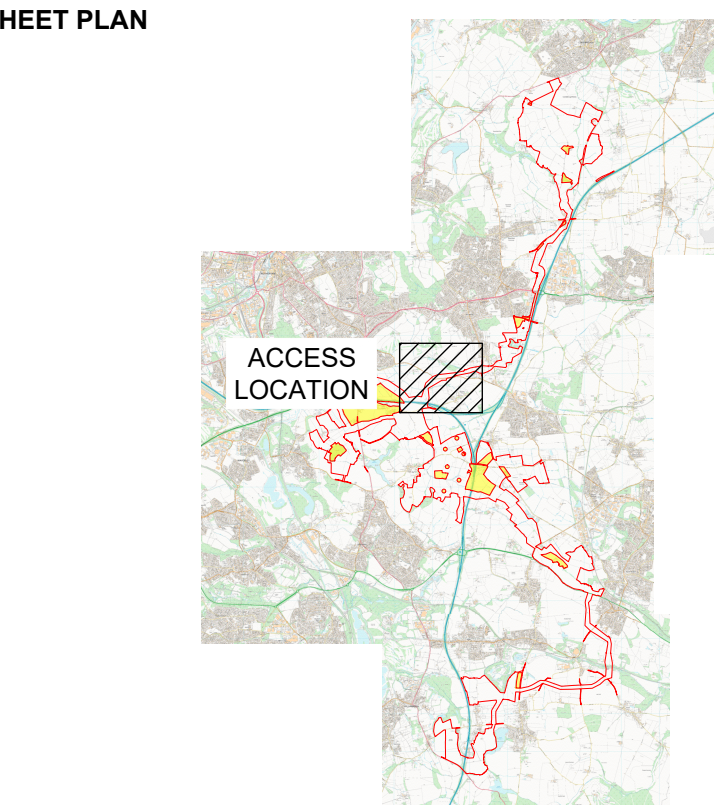

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:
Cable Corridor Area Access CC-10
Appendix 3 - Sheet 39 of 53
Whitestone Solar Farm
Regulation 5(2)(o)

DRAWING DATE: 03/06/2026




SCALE: 1:1000

SHEET: Sheet 39 of 53

SIZE: A1	REVISION
----------	----------

APPLICATION NUMBER: EN0110020



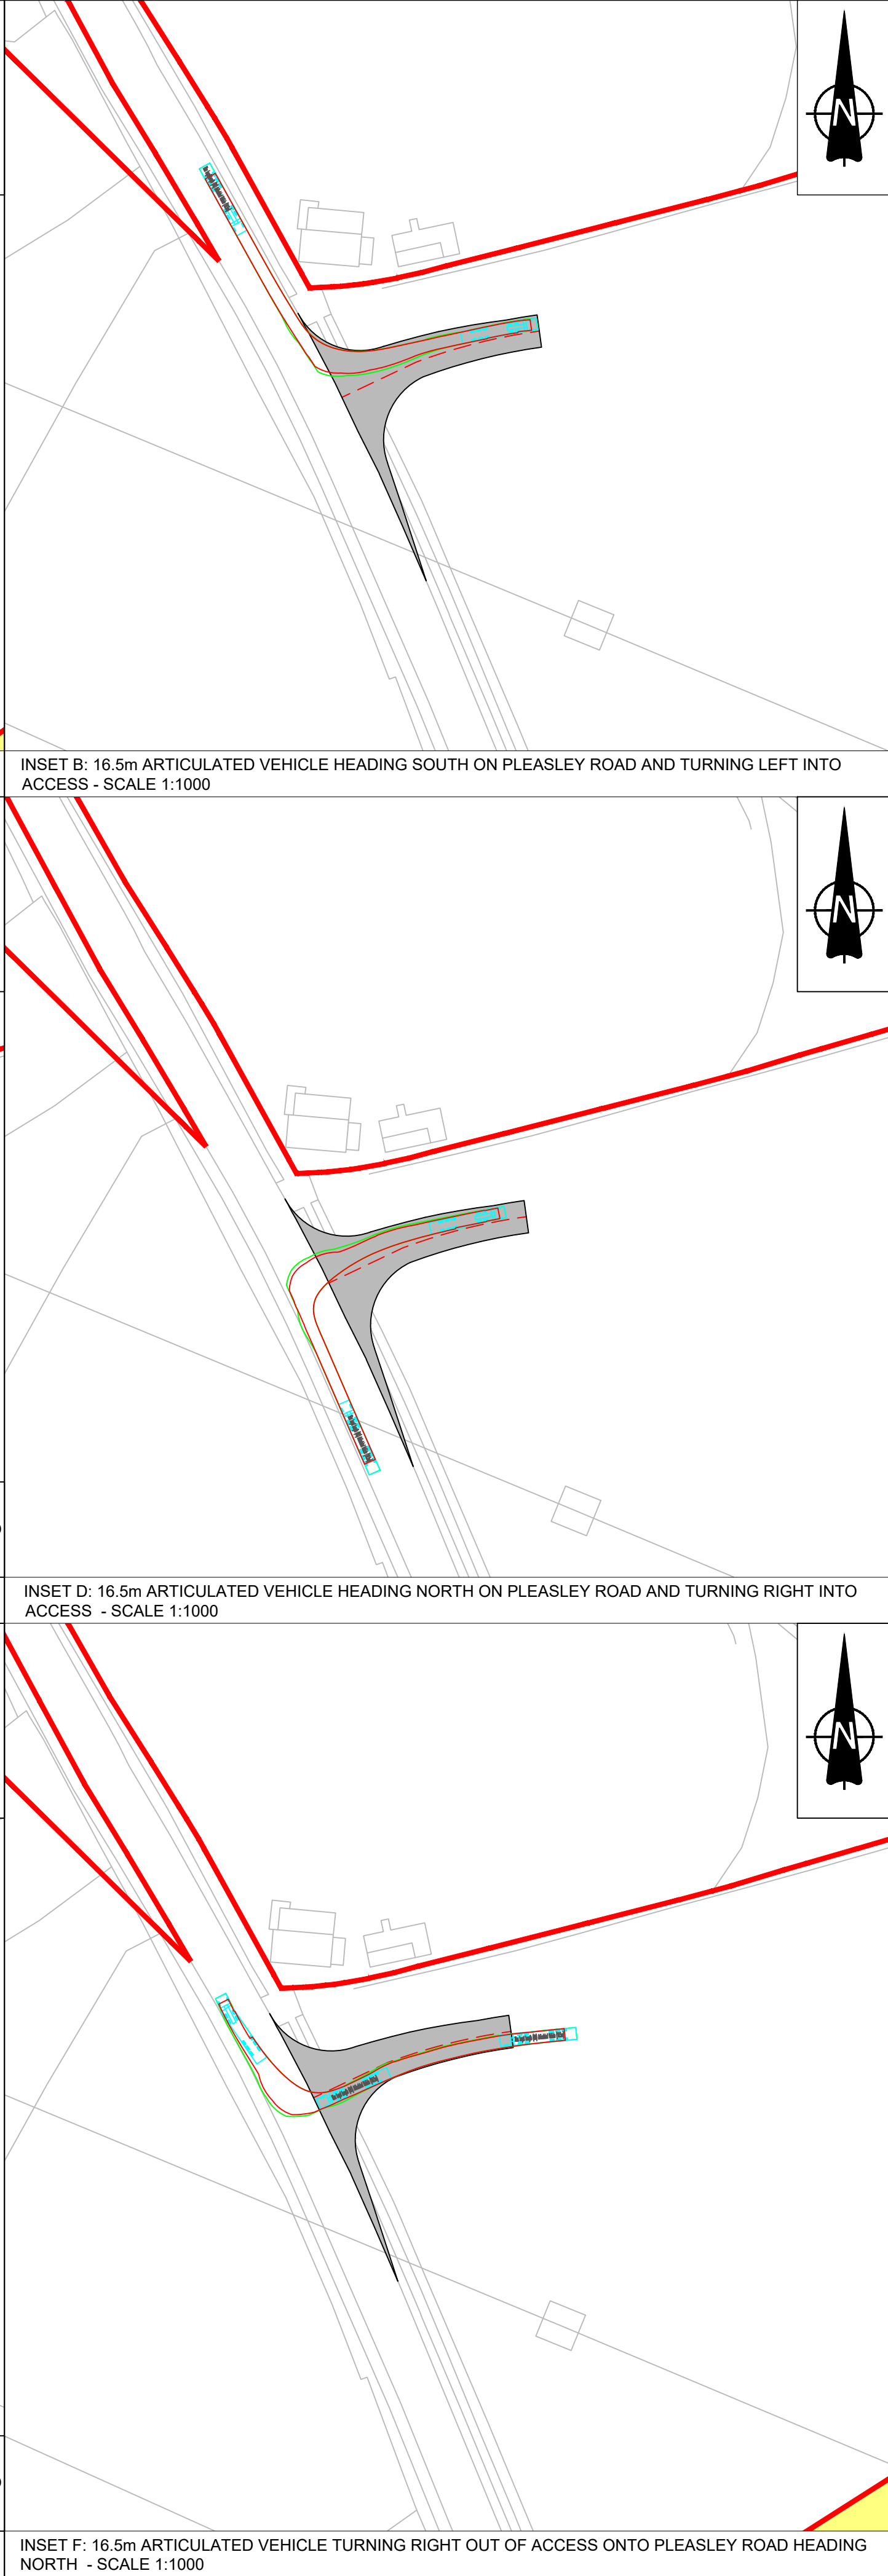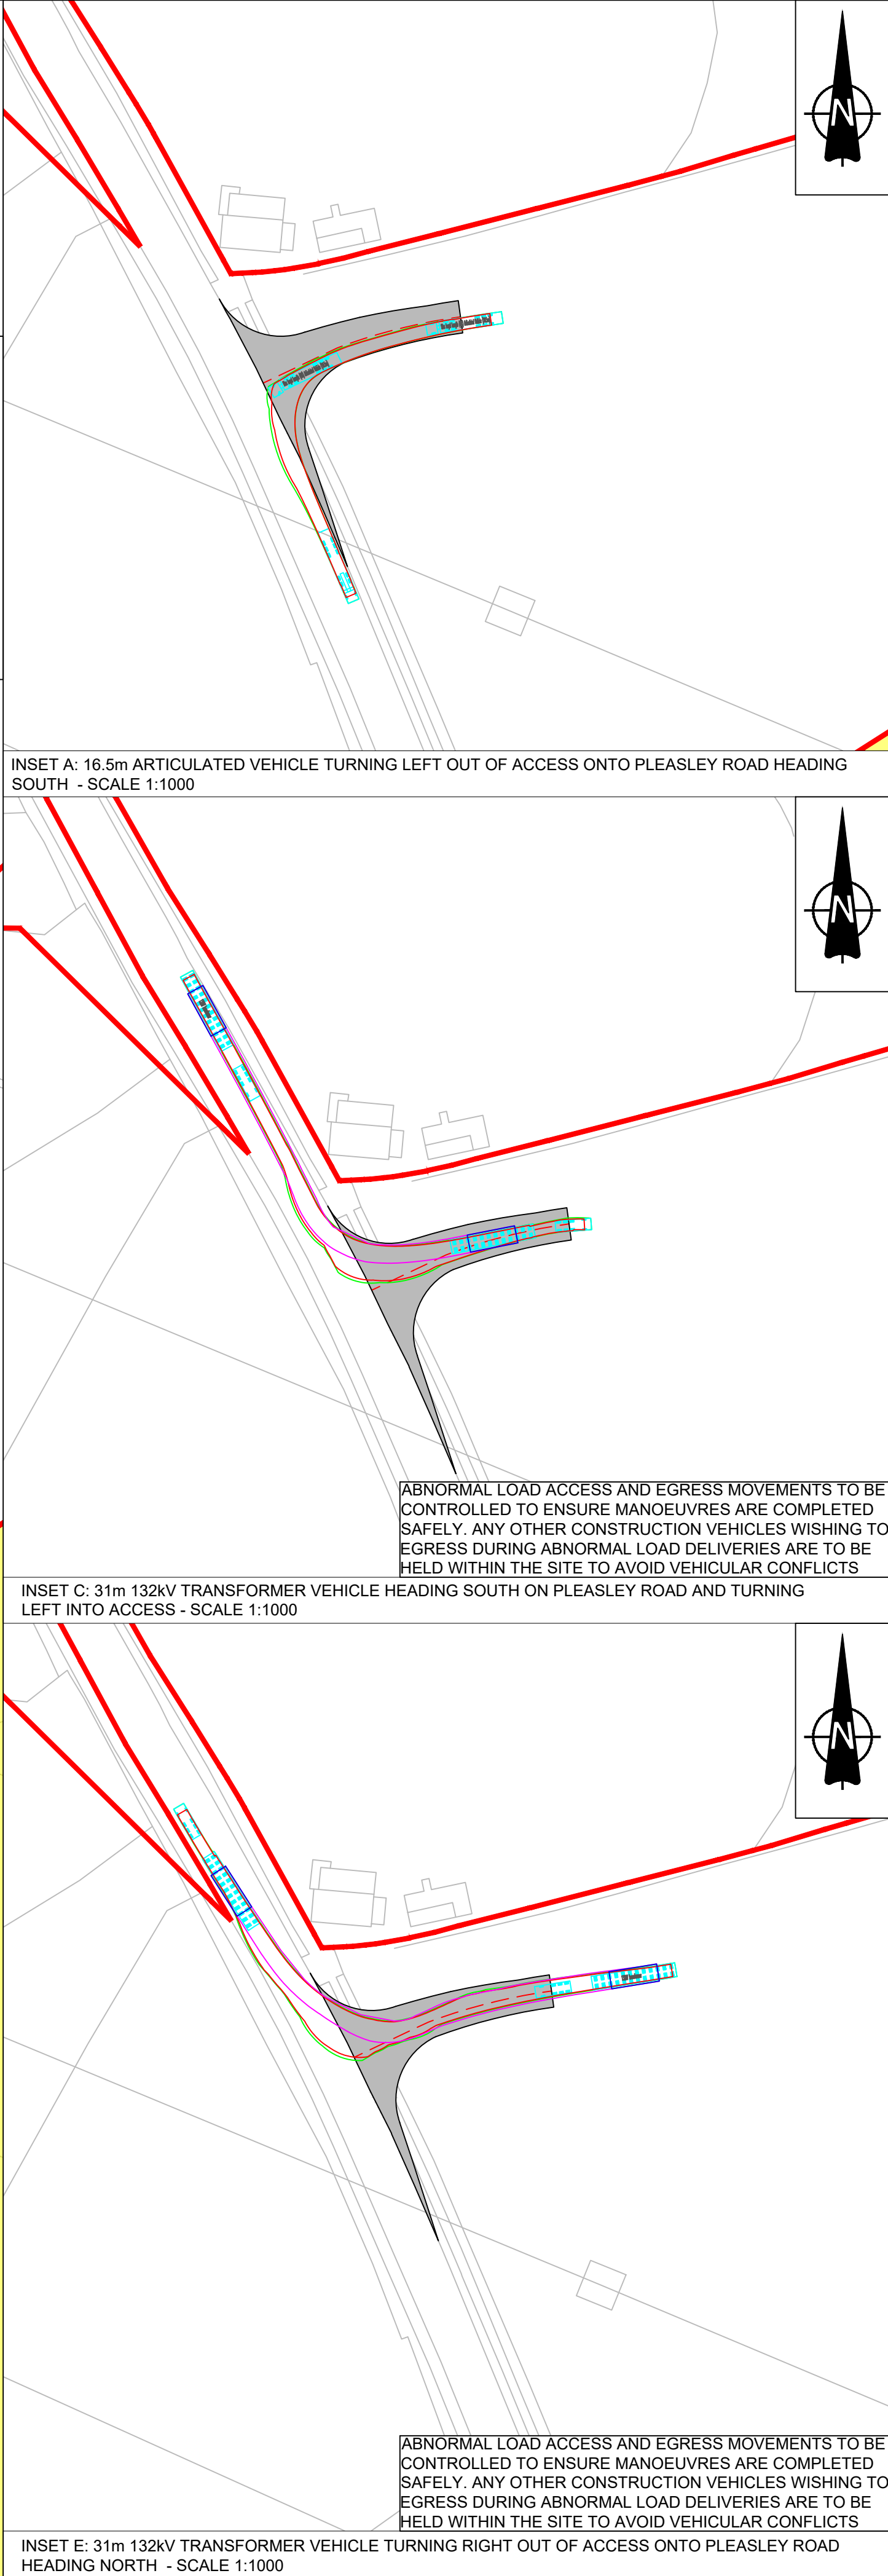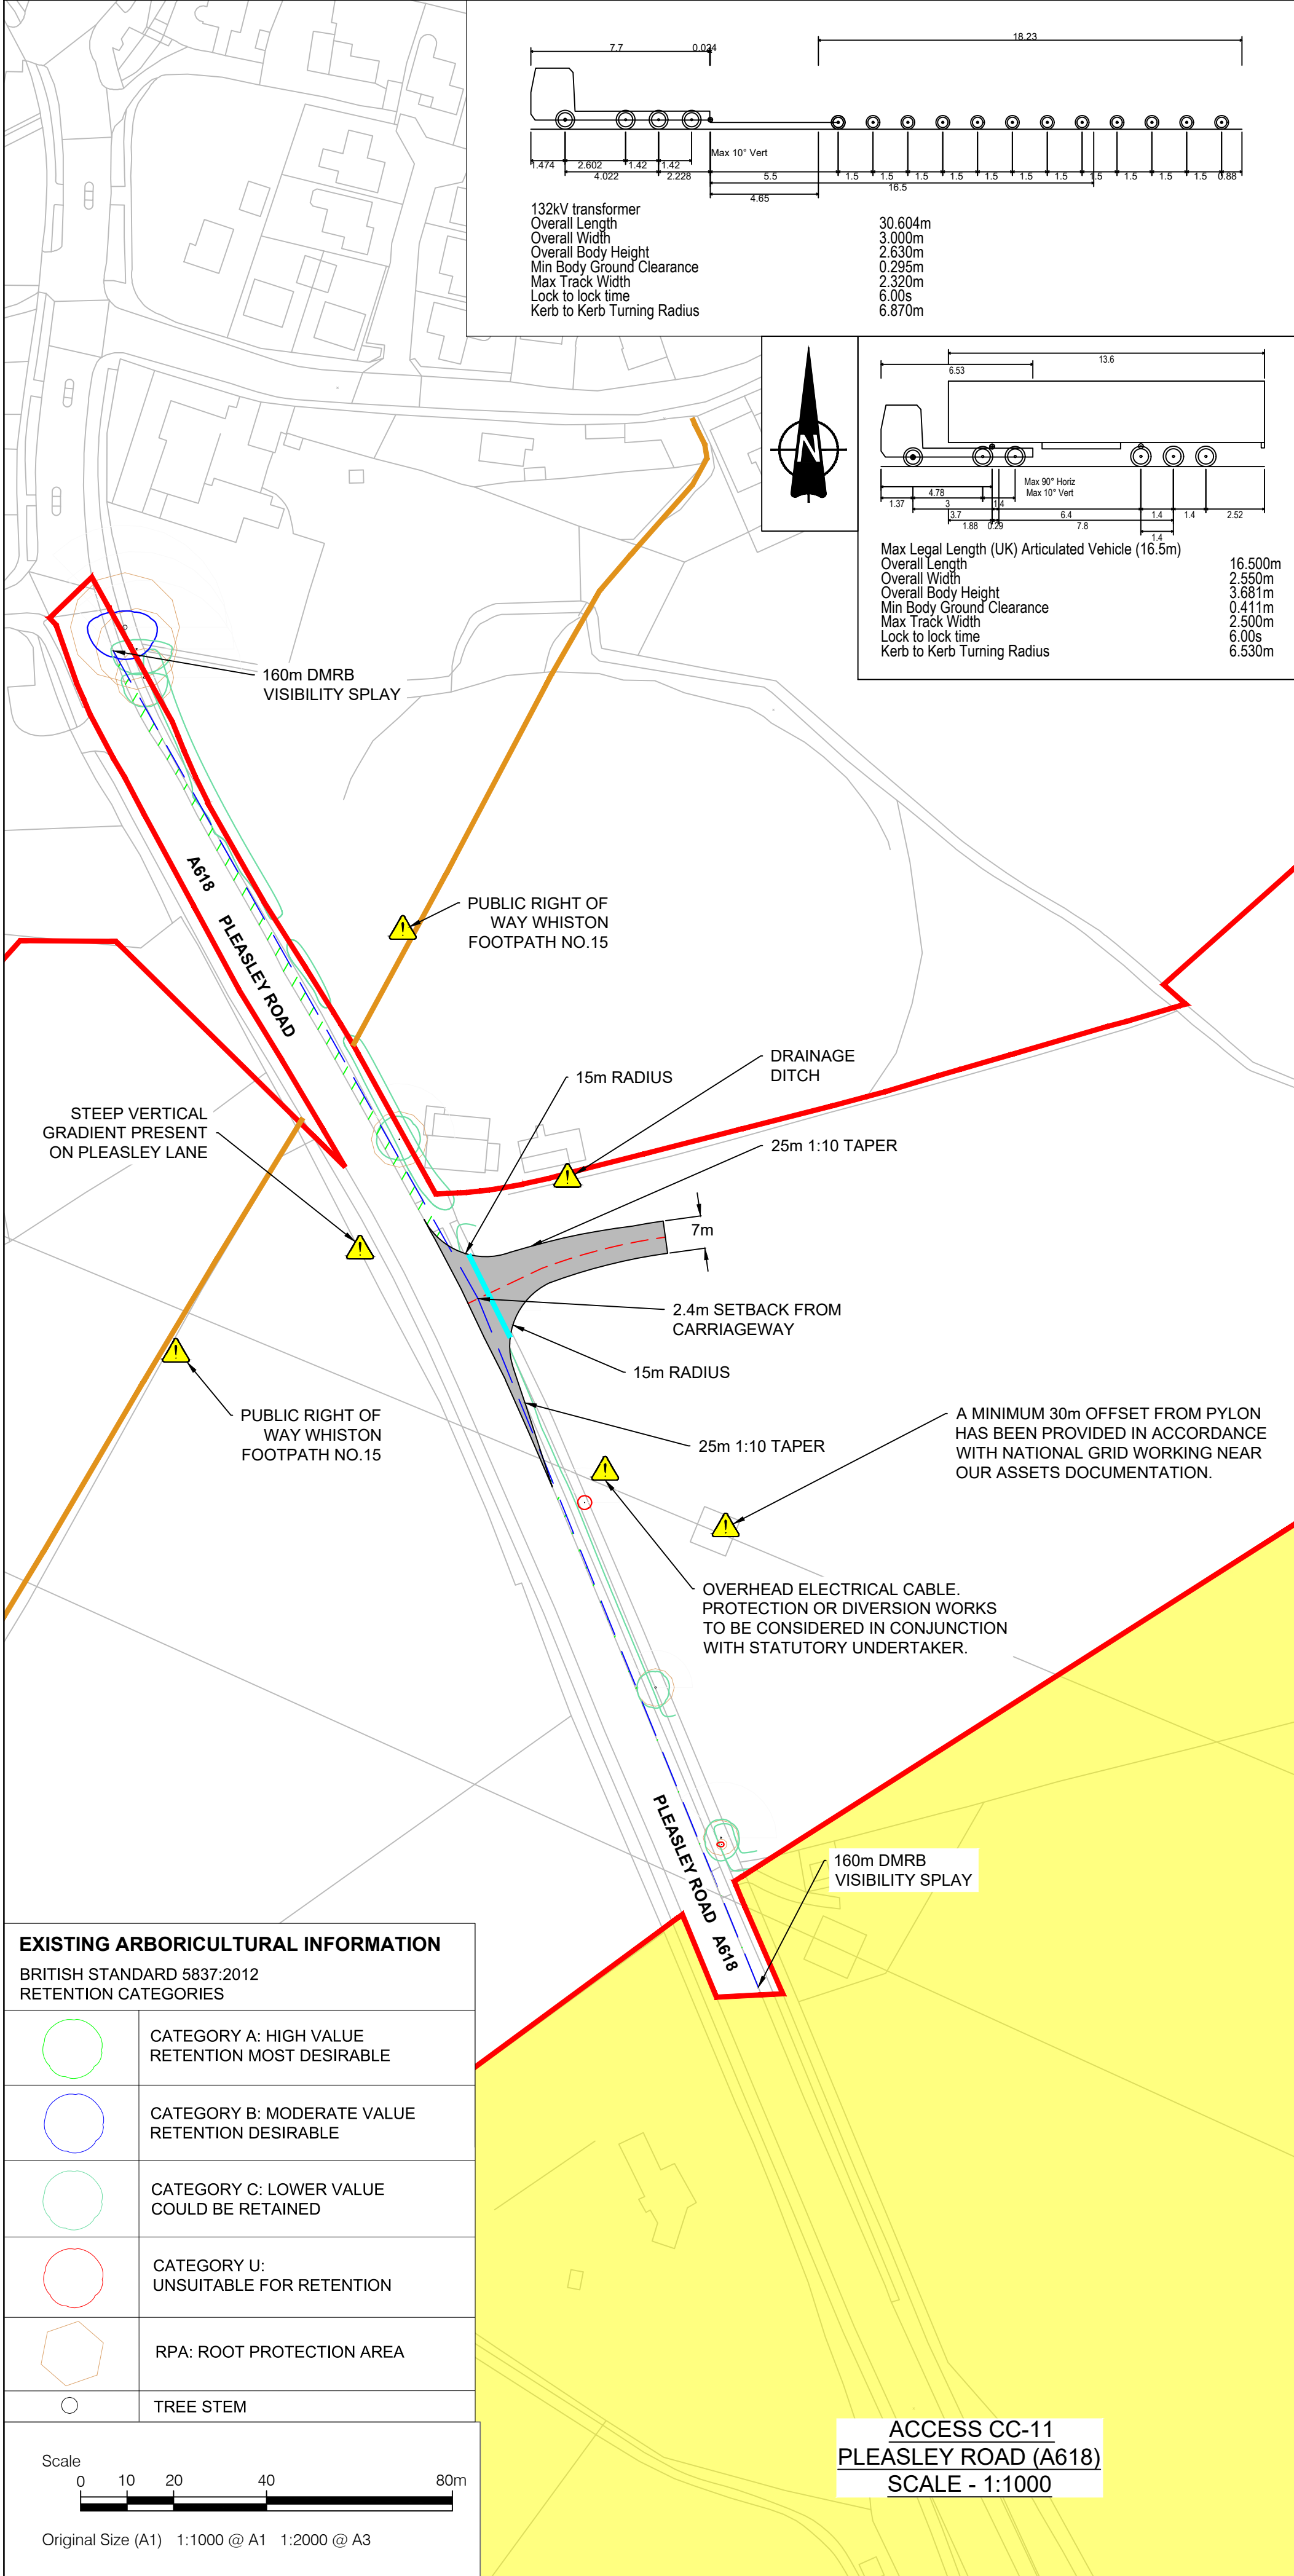


NOTES

1. This drawing is to be read in conjunction with all other relevant documentation.
2. Do not scale from this drawing, use only printed dimensions.
3. All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
4. This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
5. Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
6. The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
7. Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
8. Junction visibility for the access is based upon DMRB CD109 Table 2.10.

LEGEND

- Extent of Access Footprint
- Order Limits
- Land Excluded from Order Limits
- Vehicle Body
- Vehicle Body Path
- Vehicle Load
- Vehicle Load Path
- Vehicle Wheels Path
- Edge of Road
- Access Centreline
- Junction Visibility
- Vegetation to be Removed for Vis Splay
- Indicative Hedgerow Removal Vis Splay
- Indicative Hedgerow Removal for Bellmouth Access
- Health and Safety Risk Identifier
- Existing Public Right of Way

SHEET PLAN

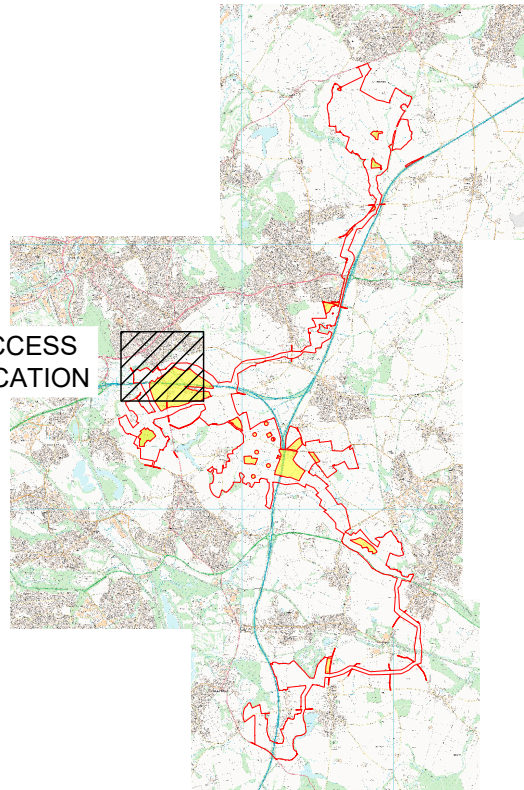

ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED
01	03/06/2026	DCO Submission	GH	MEK	JH

TITLE:
Cable Corridor Area Access CC-11
Appendix 3 - Sheet 40 of 53
Whitestone Solar Farm
Regulation 5(2)(o)




DRAWING DATE: 03/06/2026

SCALE: 1:1000
SIZE: A1
SHEET: Sheet 40 of 53
REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12


APPLICATION NUMBER: EN0110020



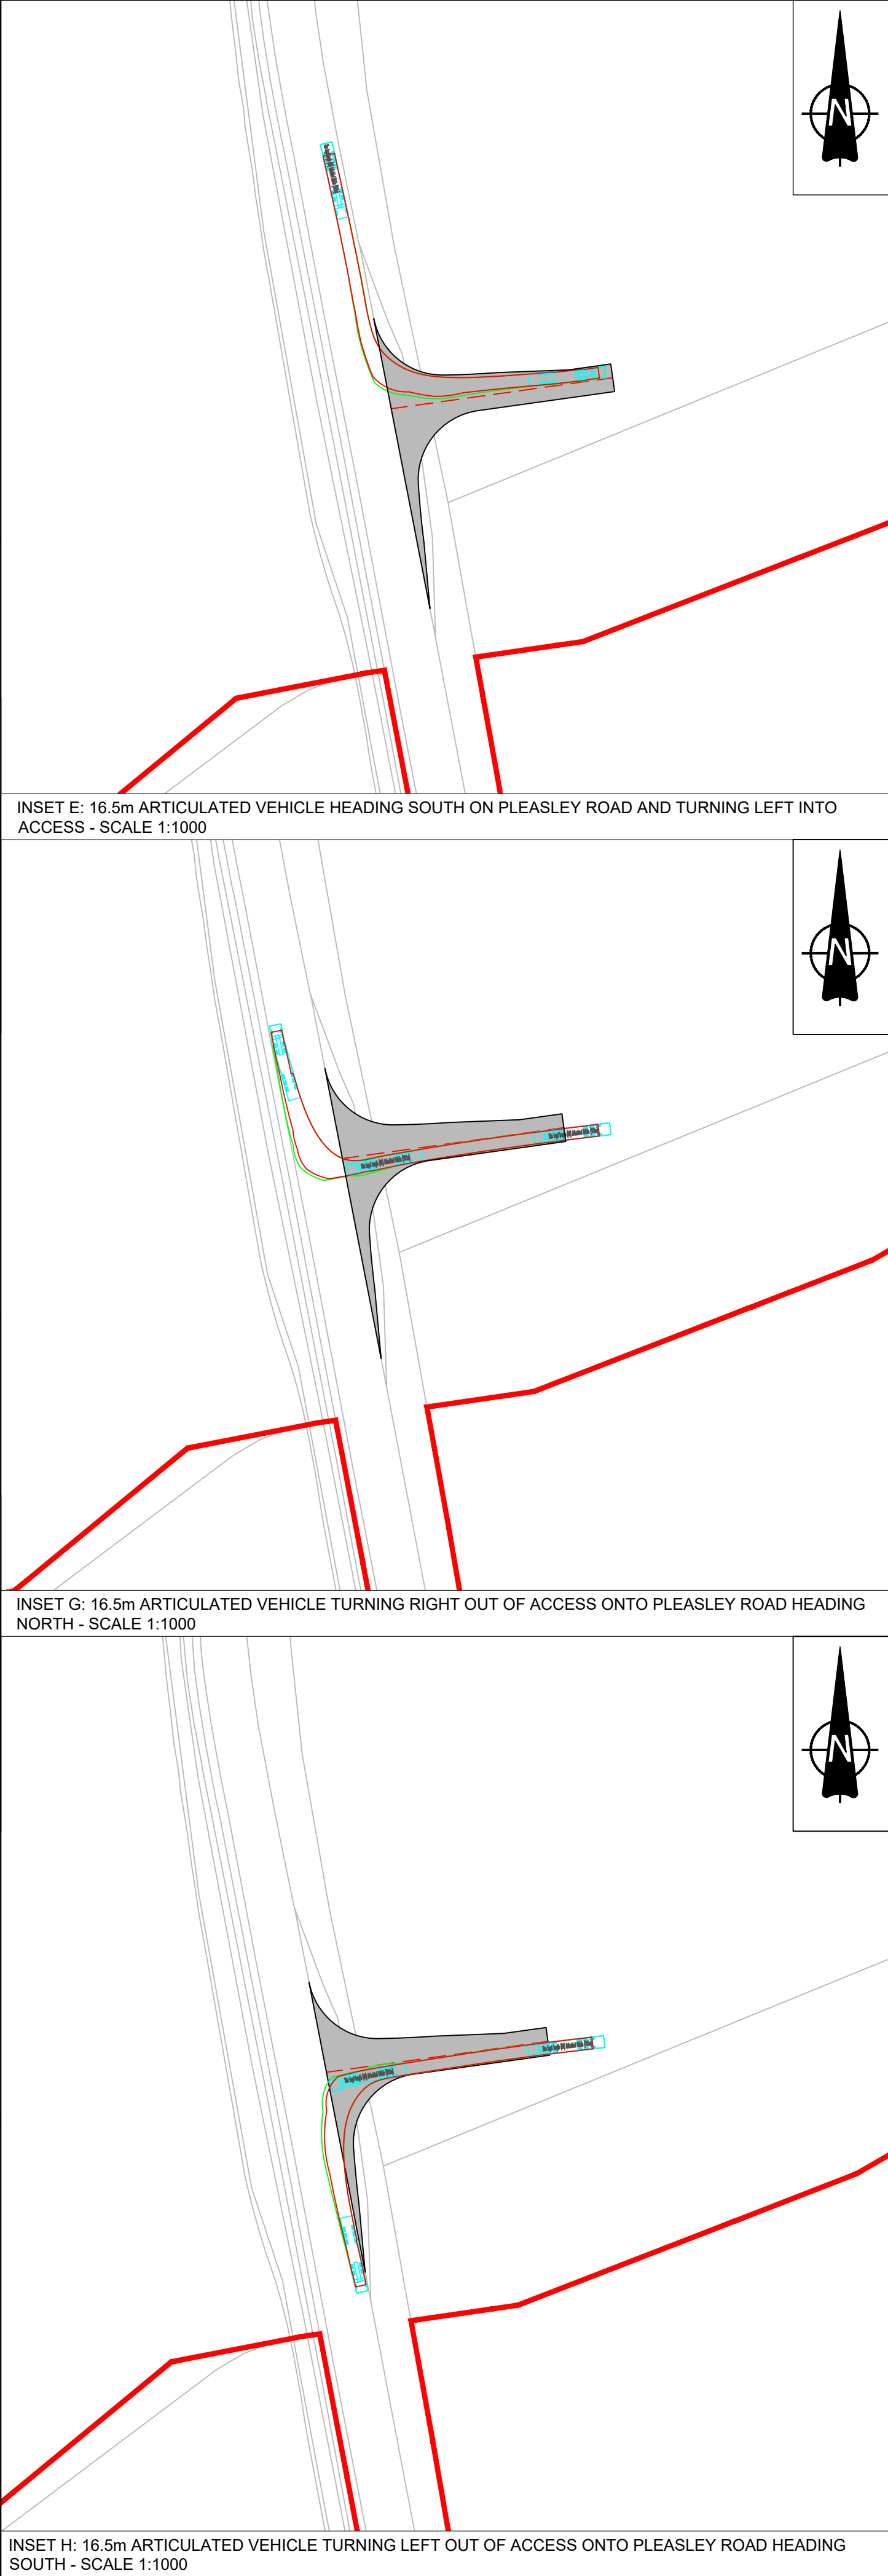
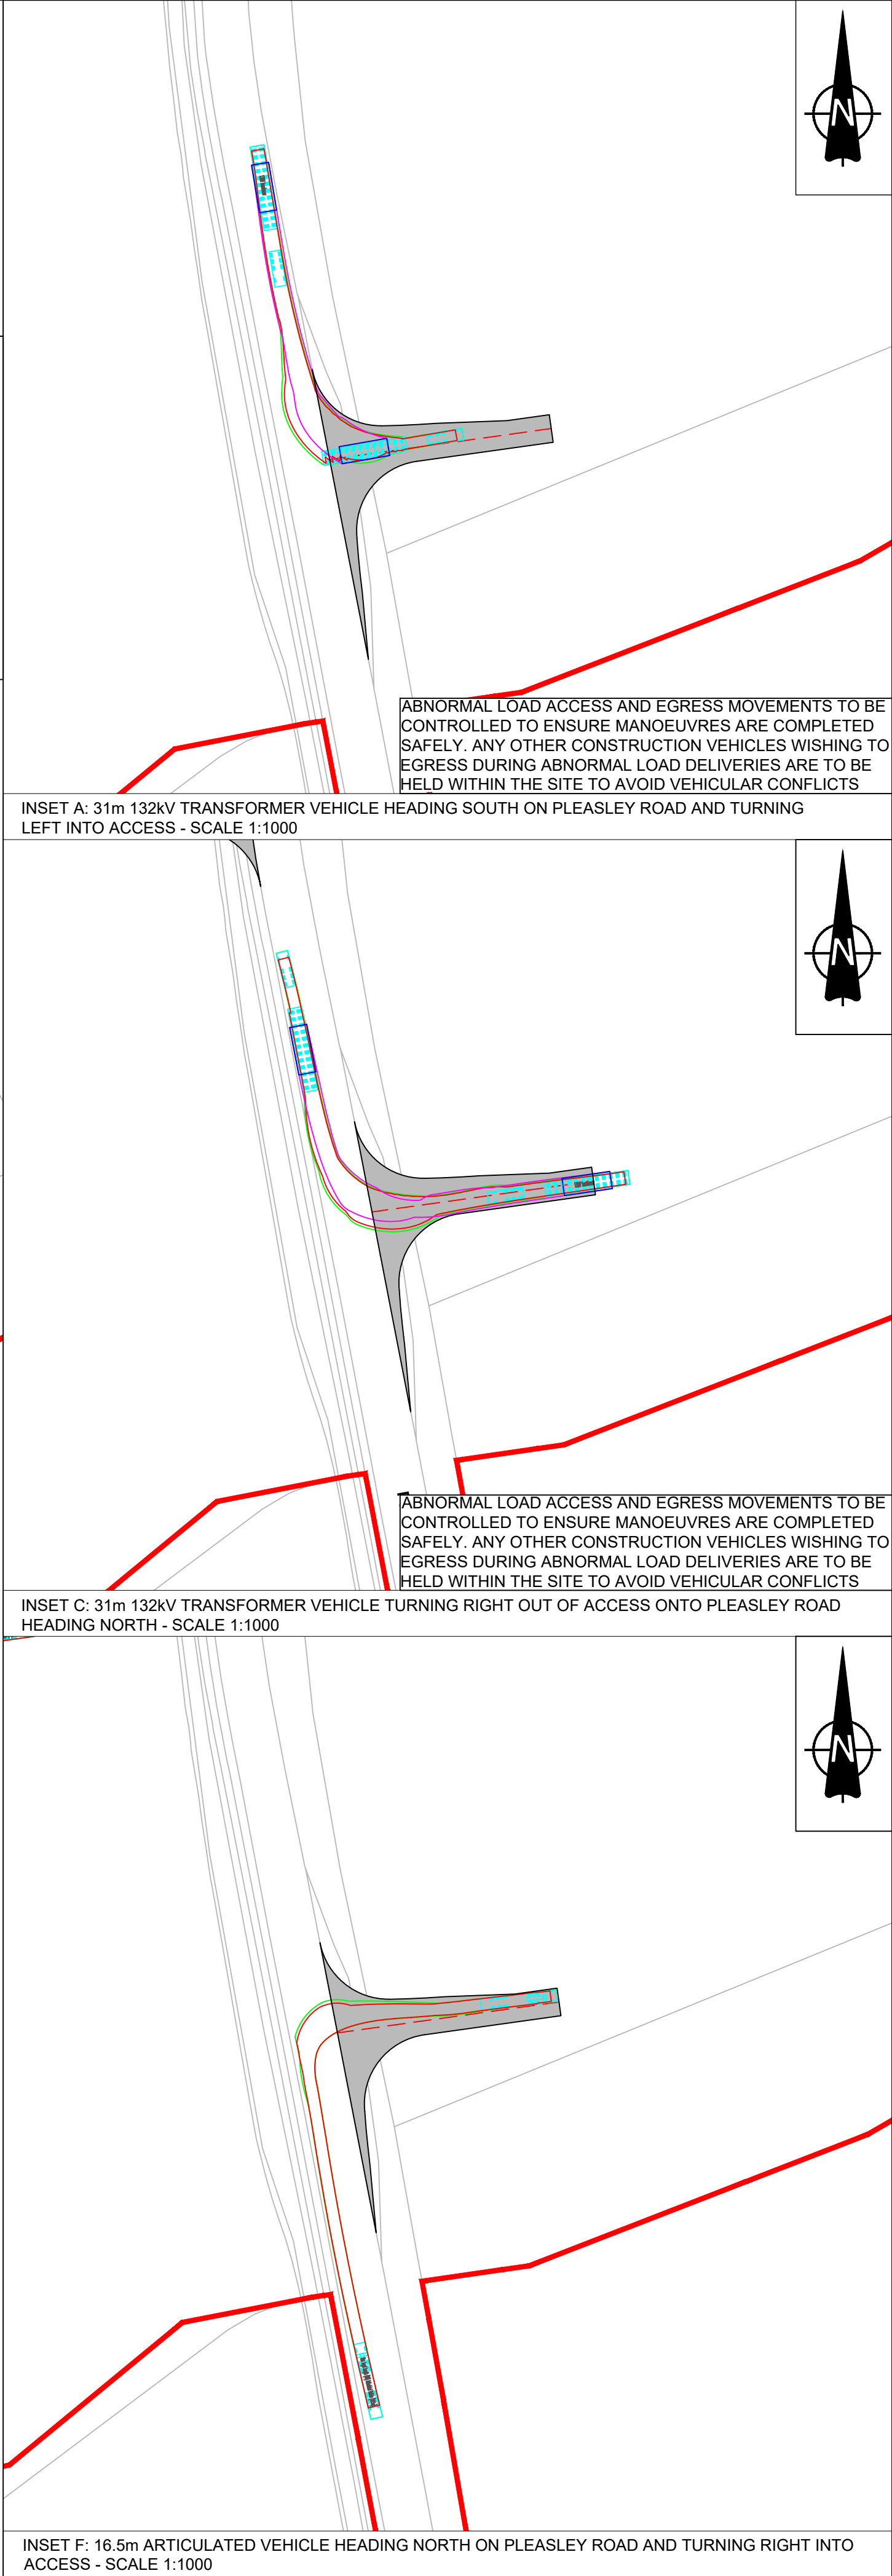
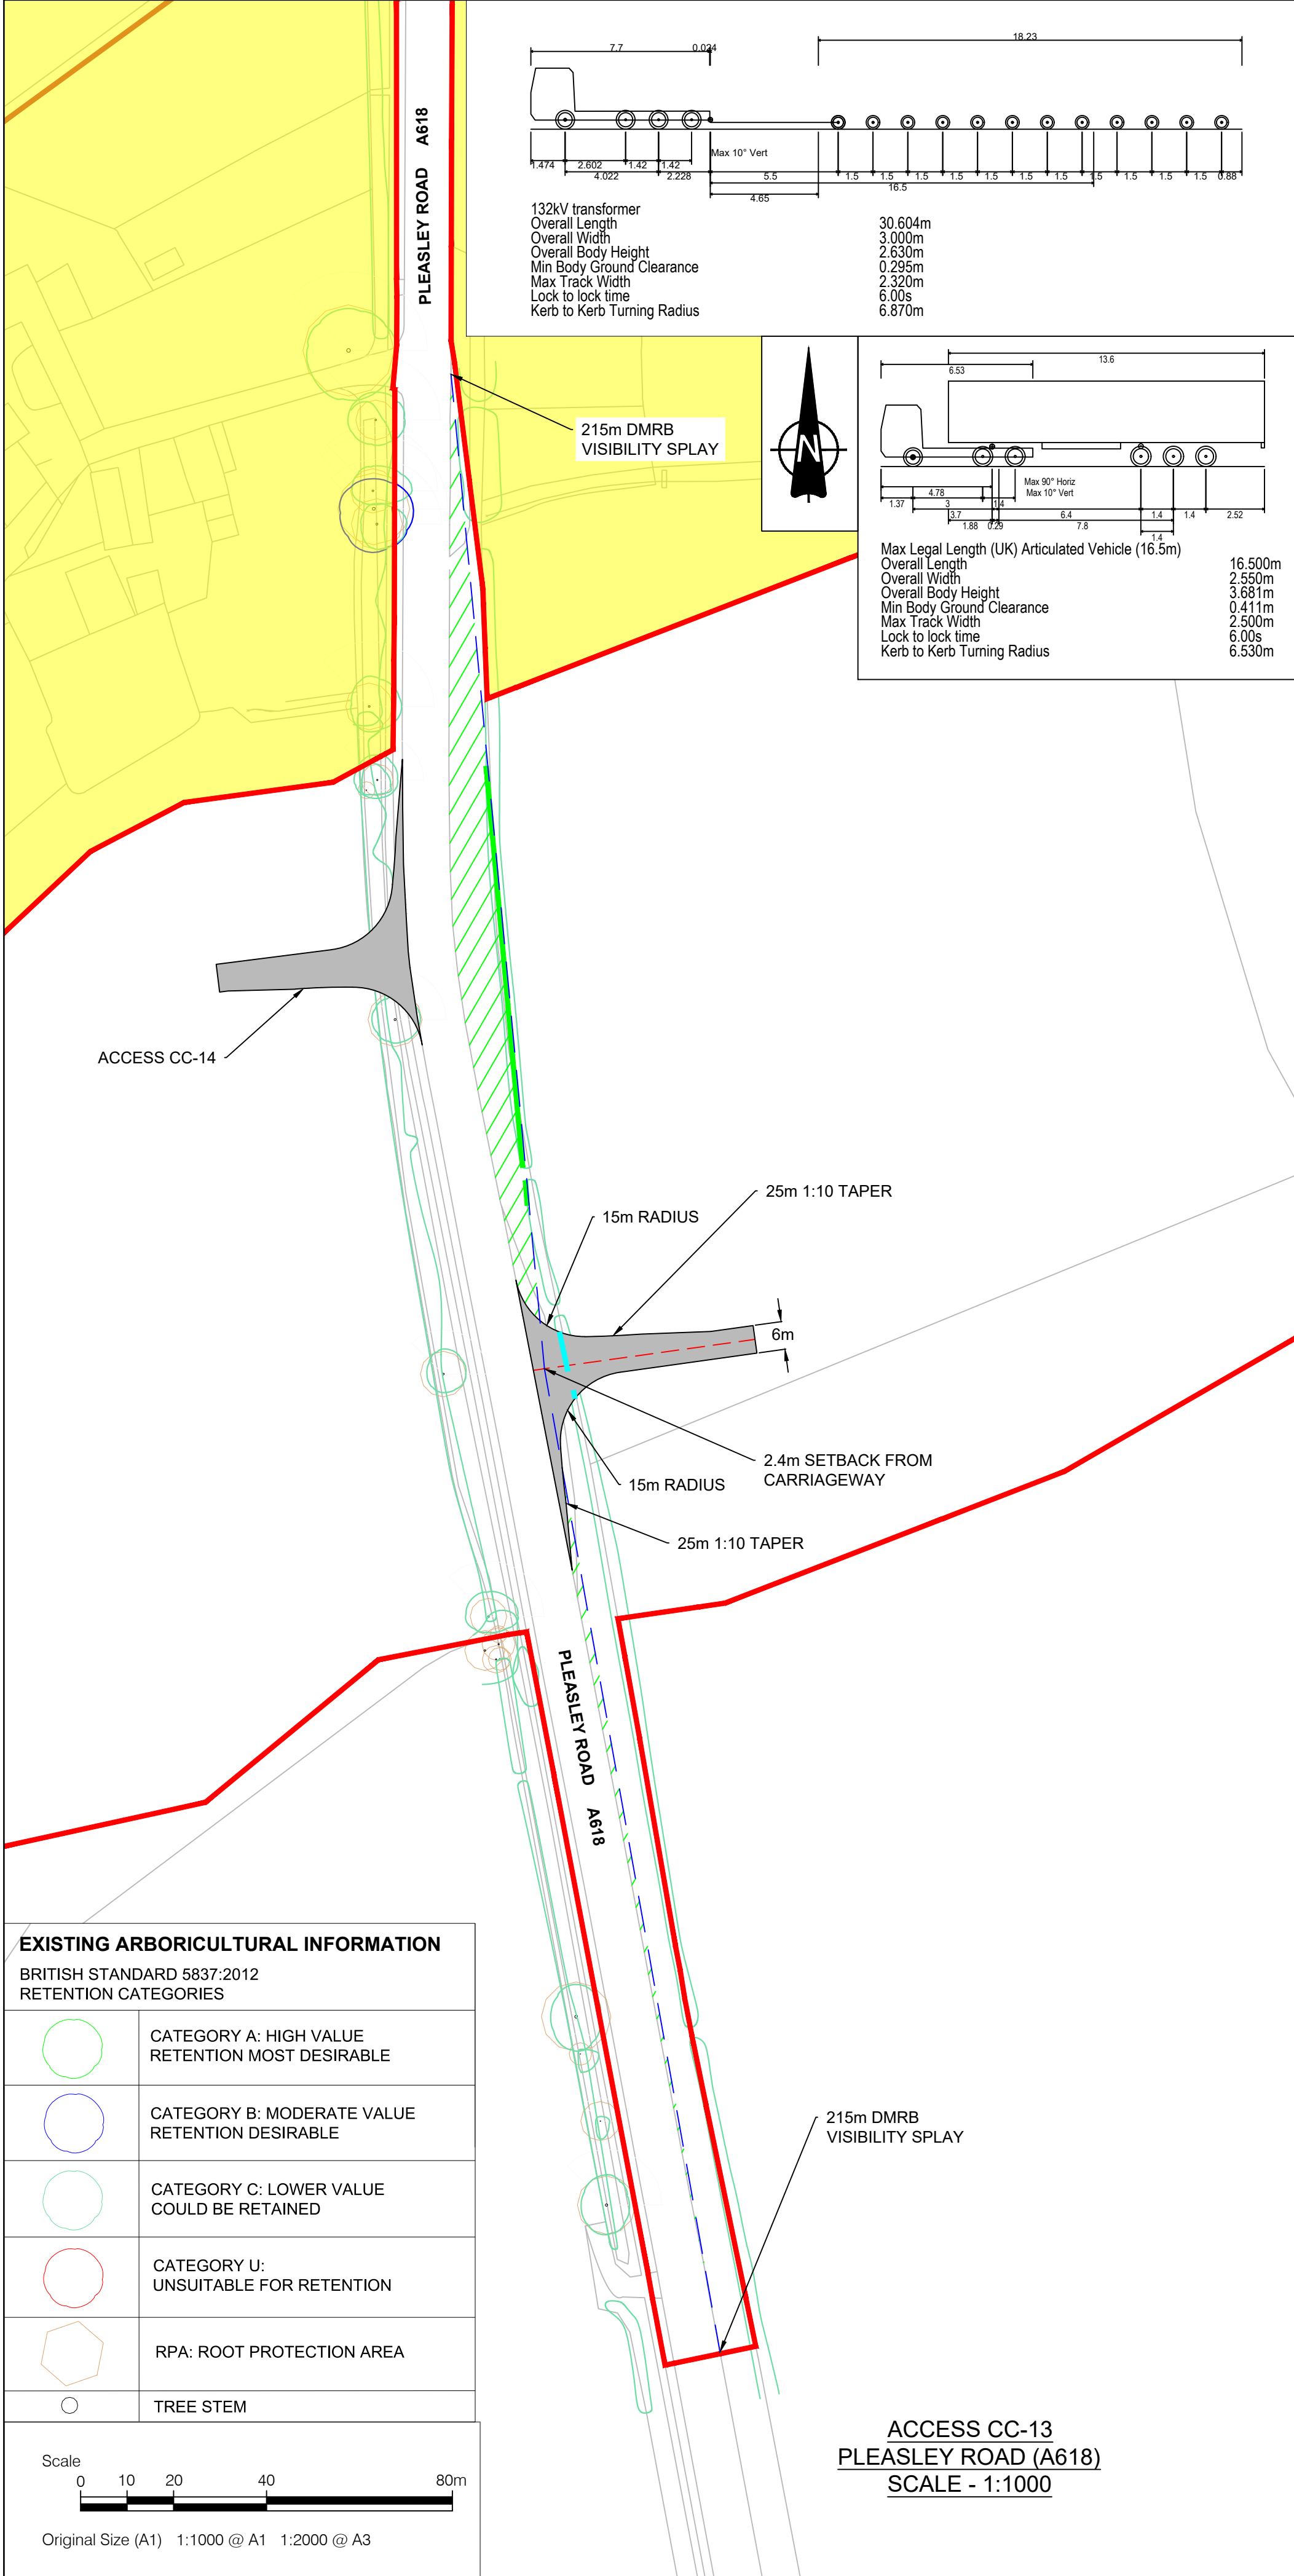


- NOTES
- This drawing is to be read in conjunction with all other relevant documentation.
 - Do not scale from this drawing, use only printed dimensions.
 - All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
 - This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
 - Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
 - The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
 - Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
 - Junction visibility for the access is based upon DMRB CD109 Table 2.10.

- LEGEND
- Extent of Access Footprint
 - Order Limits
 - Land Excluded from Order Limits
 - Vehicle Body
 - Vehicle Body Path
 - Vehicle Load
 - Vehicle Load Path
 - Vehicle Wheels Path
 - Edge of Road
 - Access Centreline
 - Junction Visibility
 - Vegetation to be Removed for Vis Splay
 - Indicative Hedgerow Removal Vis Splay
 - Indicative Hedgerow Removal for Bellmouth Access
 - Health and Safety Risk Identifier
 - Existing Public Right of Way

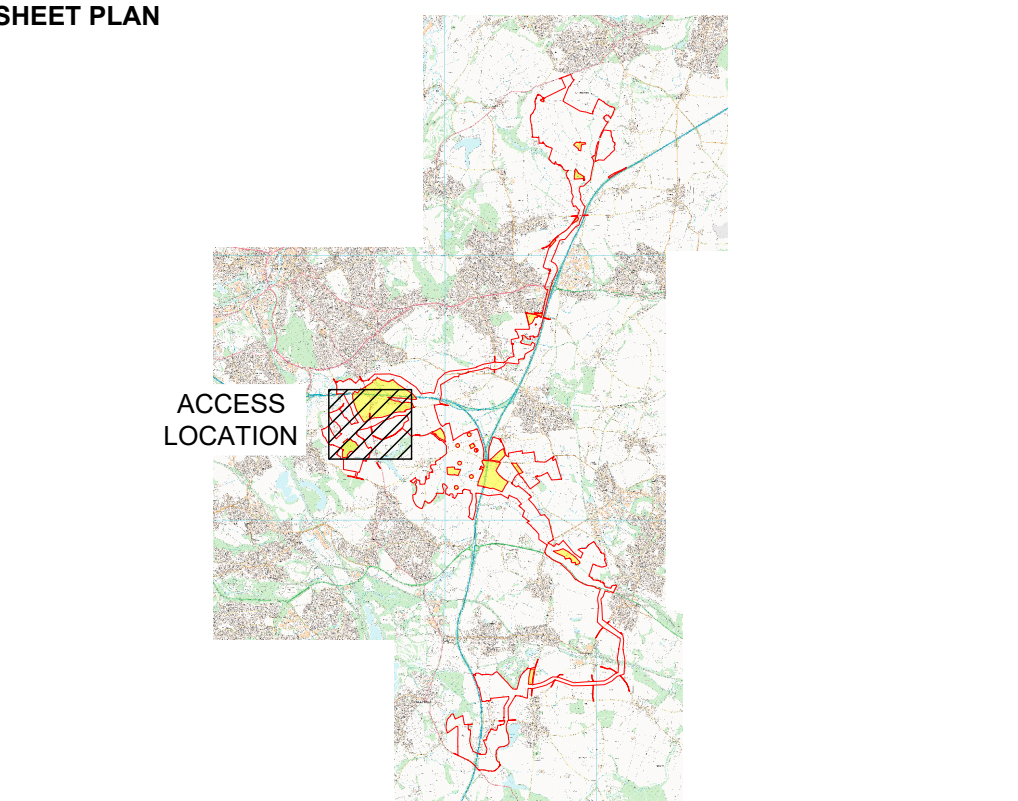

01	03/06/2026	DCO Submission	GH	MEK	JH	
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED	
TITLE:						
Cable Corridor Area Access CC-13						
Appendix 3 - Sheet 41 of 53						
Whitestone Solar Farm						
Regulation 5(2)(o)						
DRAWING DATE: 03/06/2026						
SCALE: 1:1000			SHEET: Sheet 41 of 53			
SIZE: A1			REVISION: 01			
DOCUMENT REFERENCE: EN0110020/APP/5.12						
APPLICATION NUMBER: EN0110020						
 WHITESTONE solar farm						

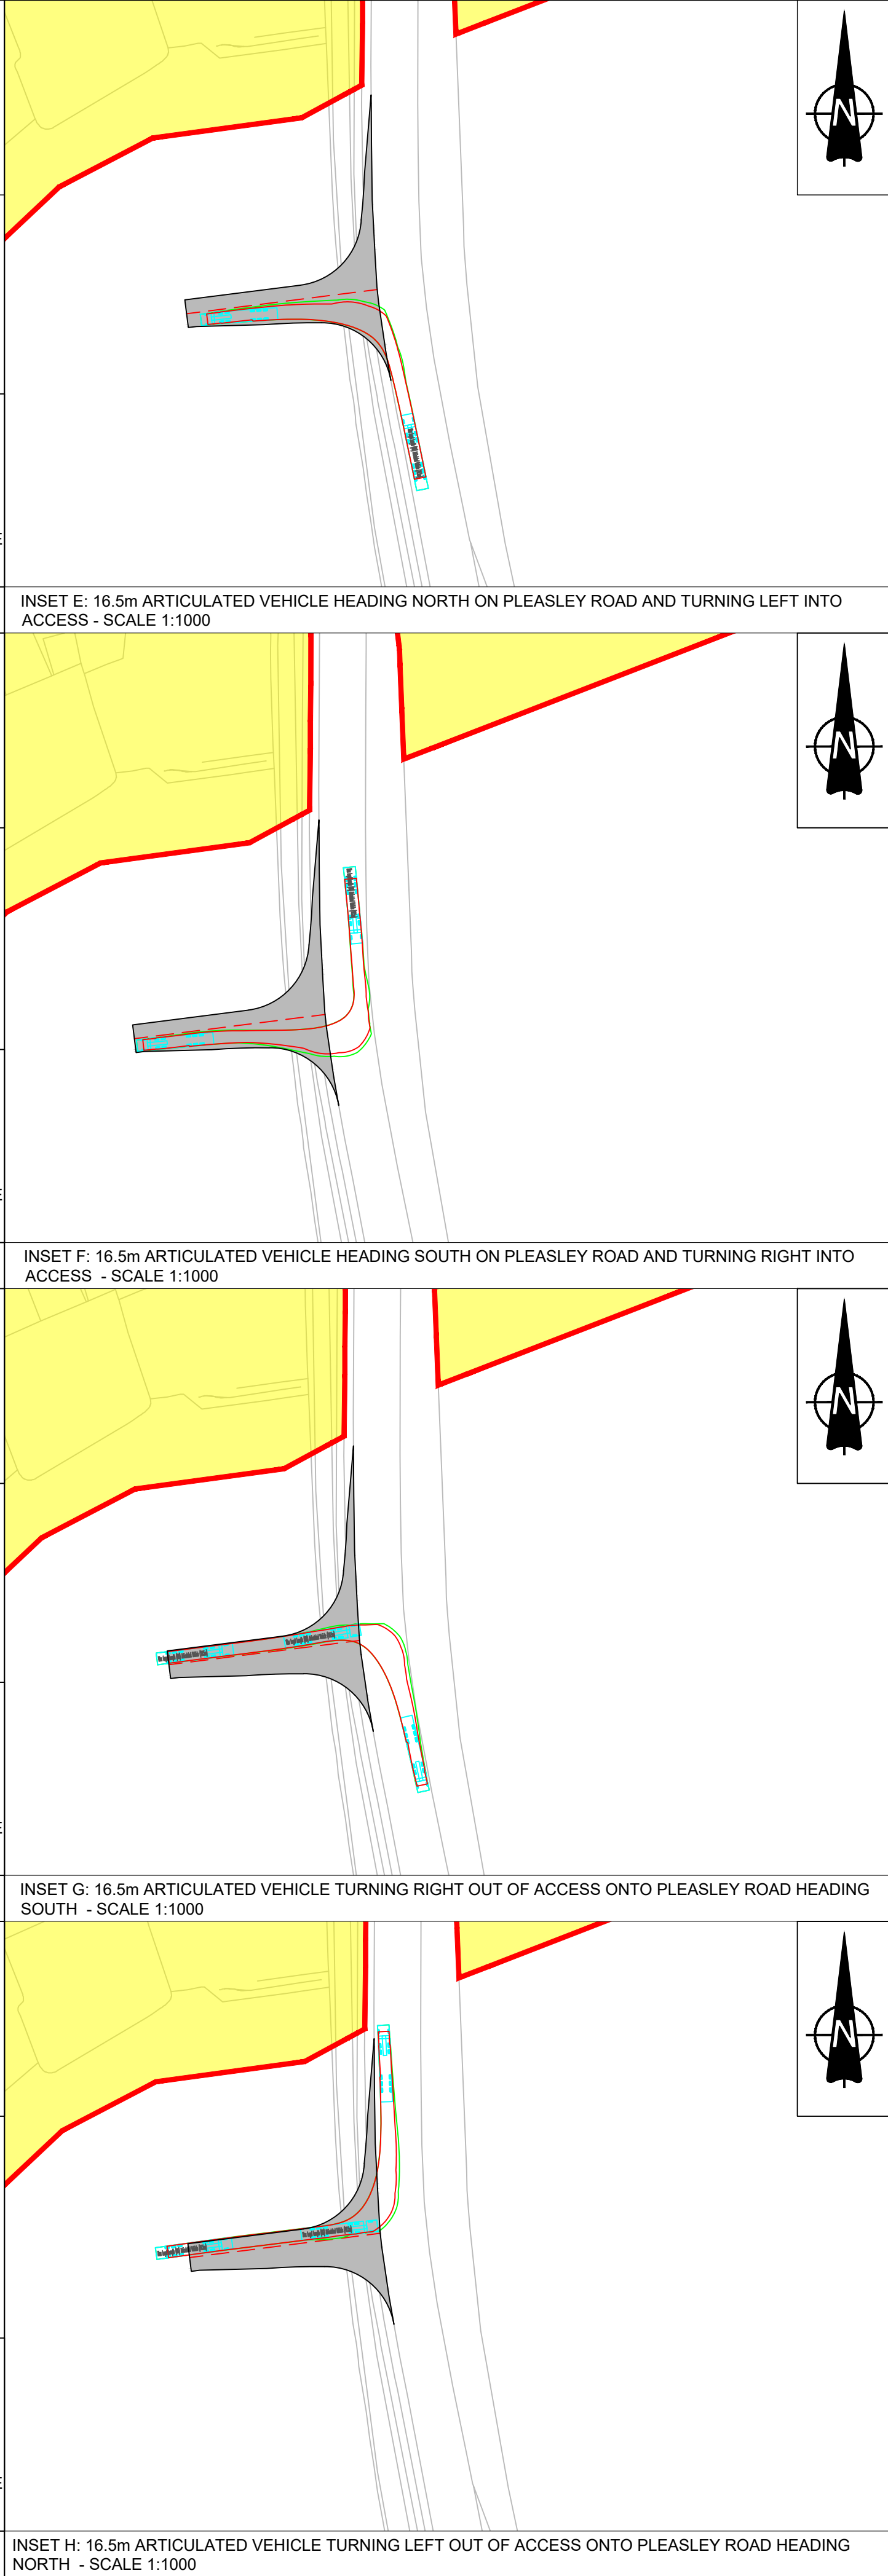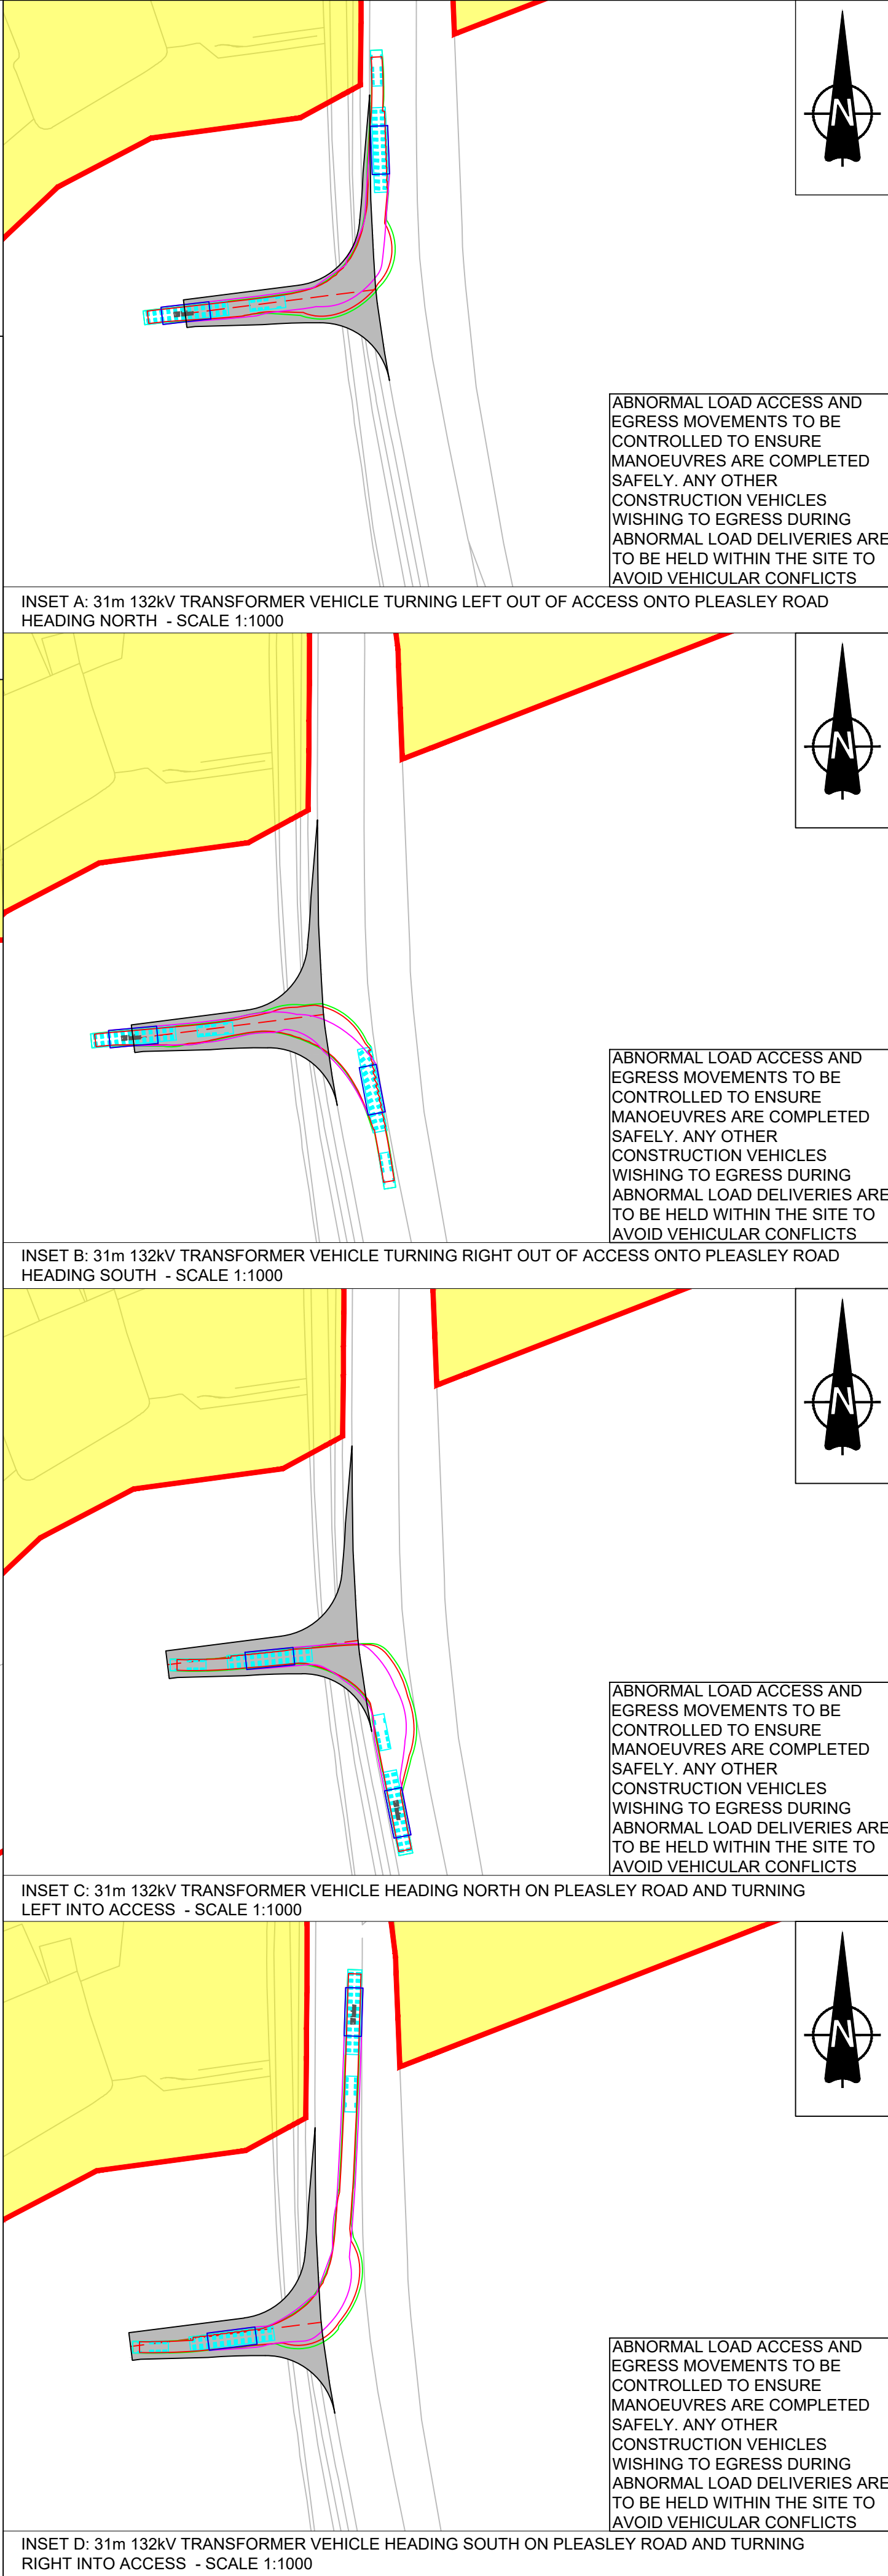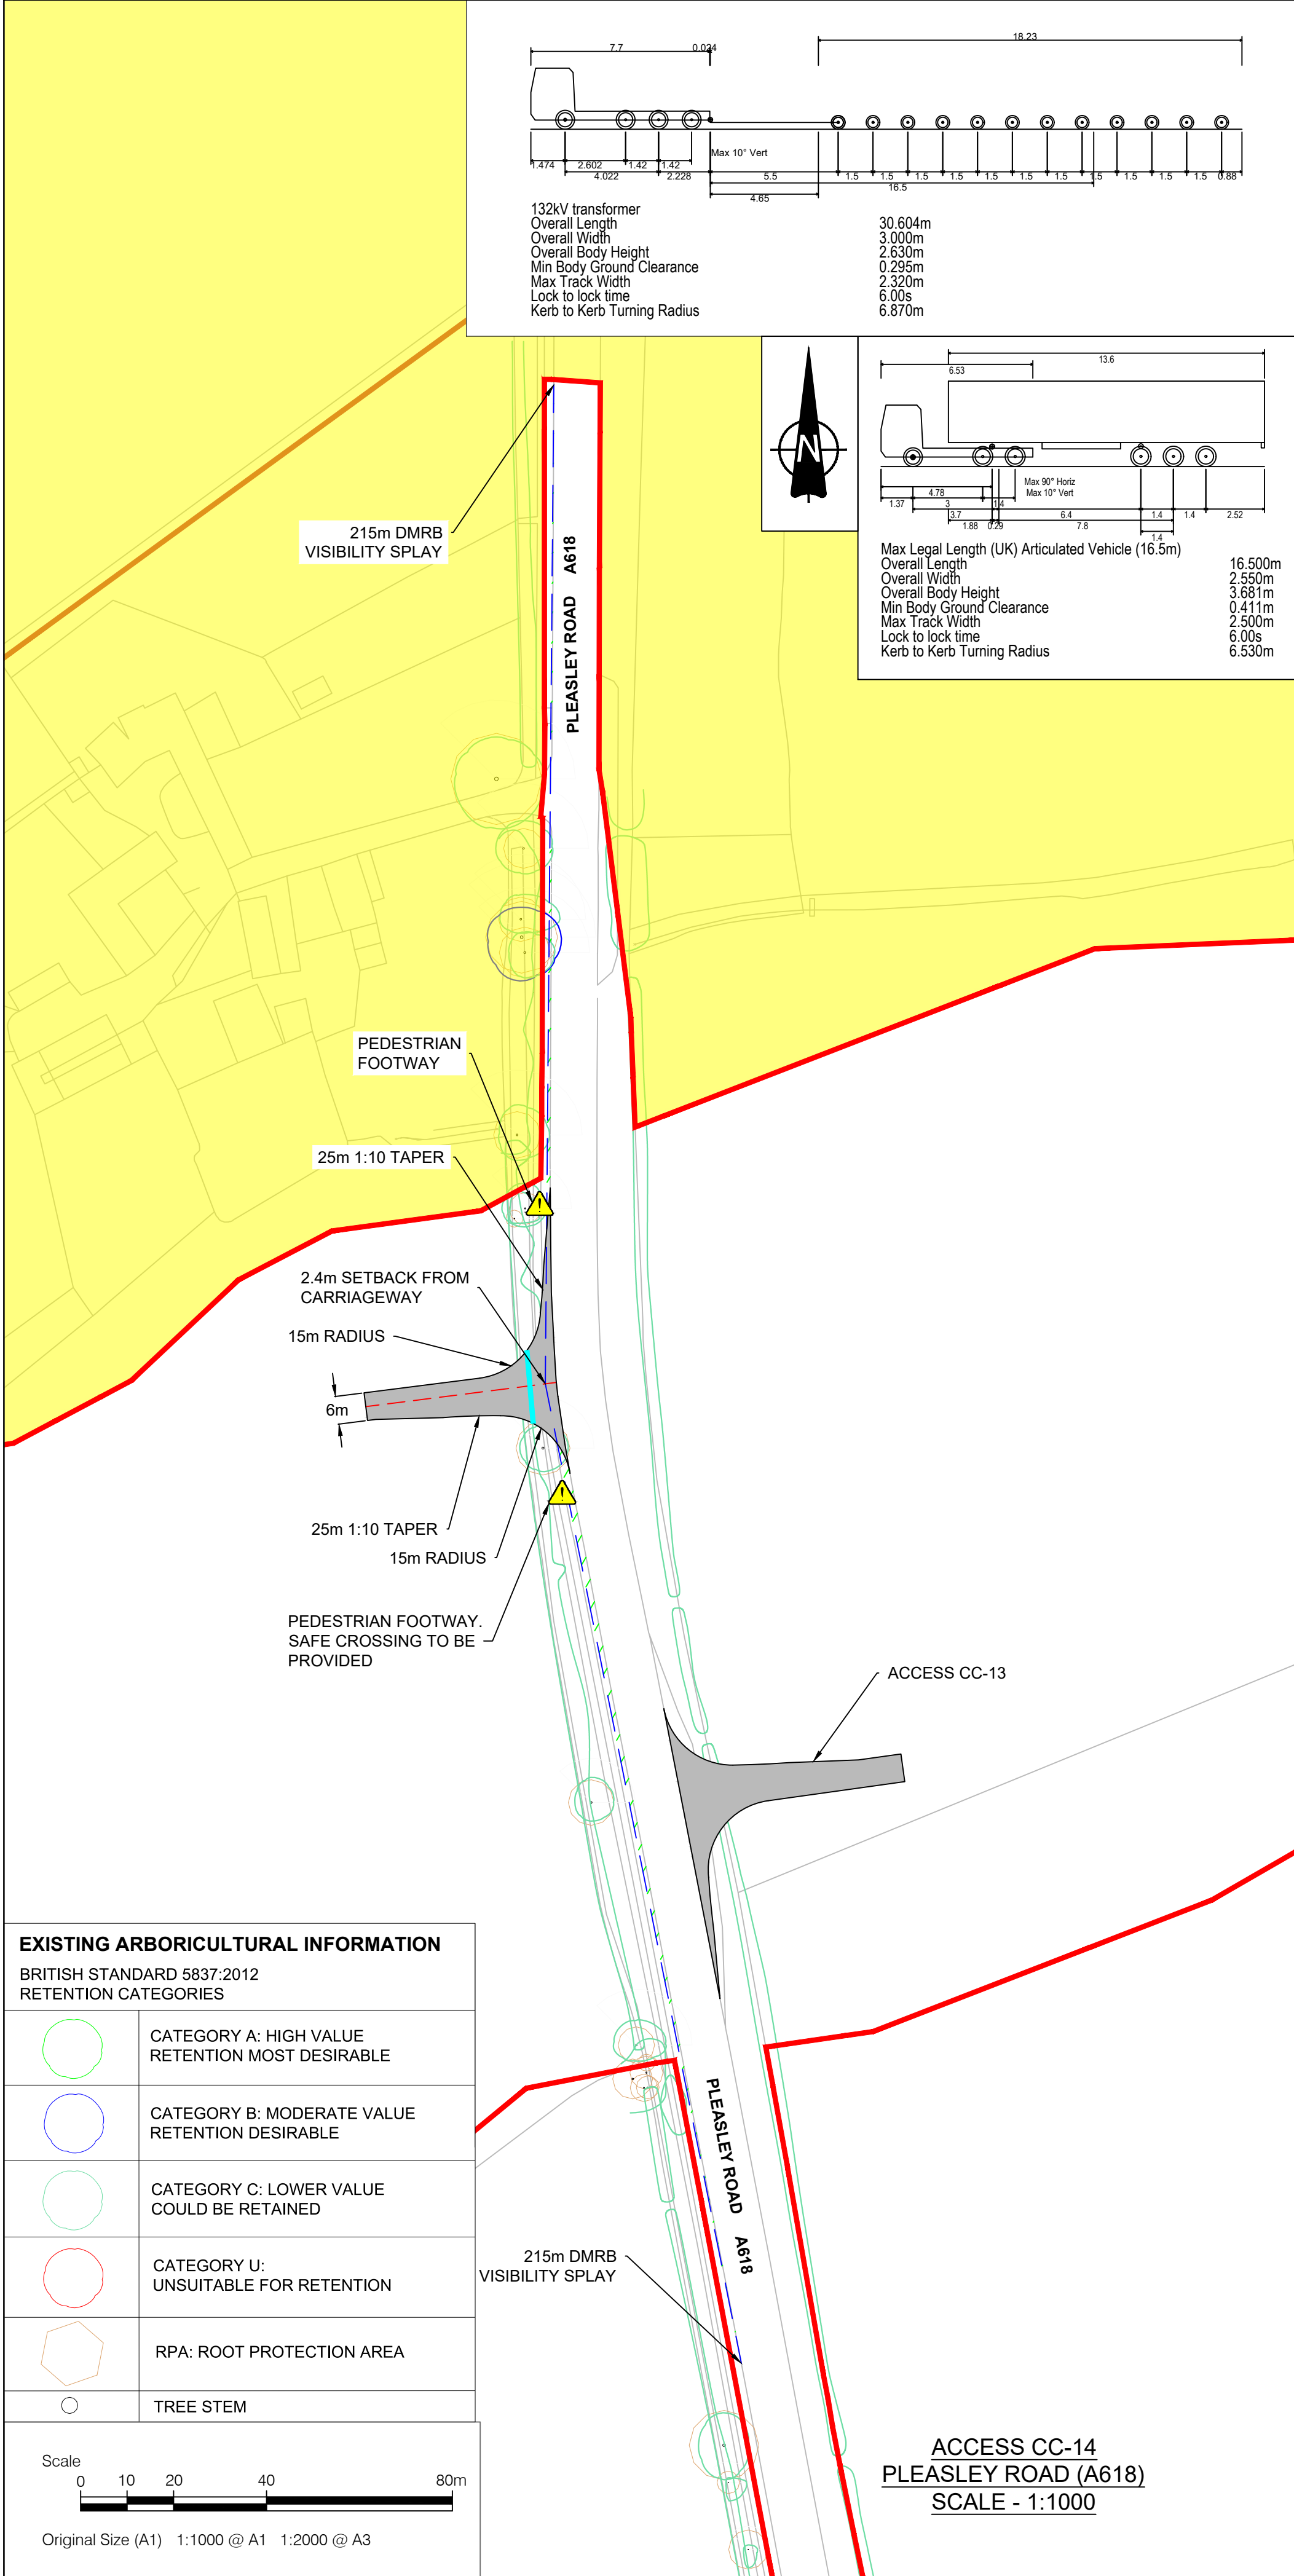


NOTES

- This drawing is to be read in conjunction with all other relevant documentation.
- Do not scale from this drawing, use only printed dimensions.
- All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
- This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
- Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
- The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
- Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
- Junction visibility for the access is based upon DMRB CD109 Table 2.10.

LEGEND

- Extent of Access Footprint
- Order Limits
- Land Excluded from Order Limits
- Vehicle Body
- Vehicle Body Path
- Vehicle Load
- Vehicle Load Path
- Vehicle Wheels Path
- Edge of Road
- Access Centreline
- Junction Visibility
- Vegetation to be Removed for Vis Splay
- Indicative Hedgerow Removal Vis Splay
- Indicative Hedgerow Removal for Bellmouth Access
- Health and Safety Risk Identifier
- Existing Public Right of Way

SHEET PLAN

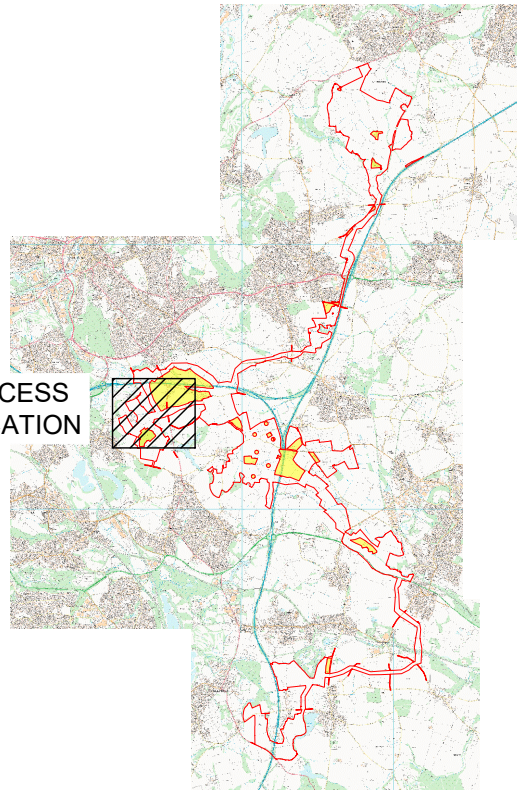

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:

Cable Corridor Area Access CC-14

Appendix 3 - Sheet 42 of 53

Whitestone Solar Farm

Regulation 5(2)(o)

DRAWING DATE: 03/06/2026

SCALE: 1:1000

SIZE: A1


SHEET: Sheet 42 of 53

REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020




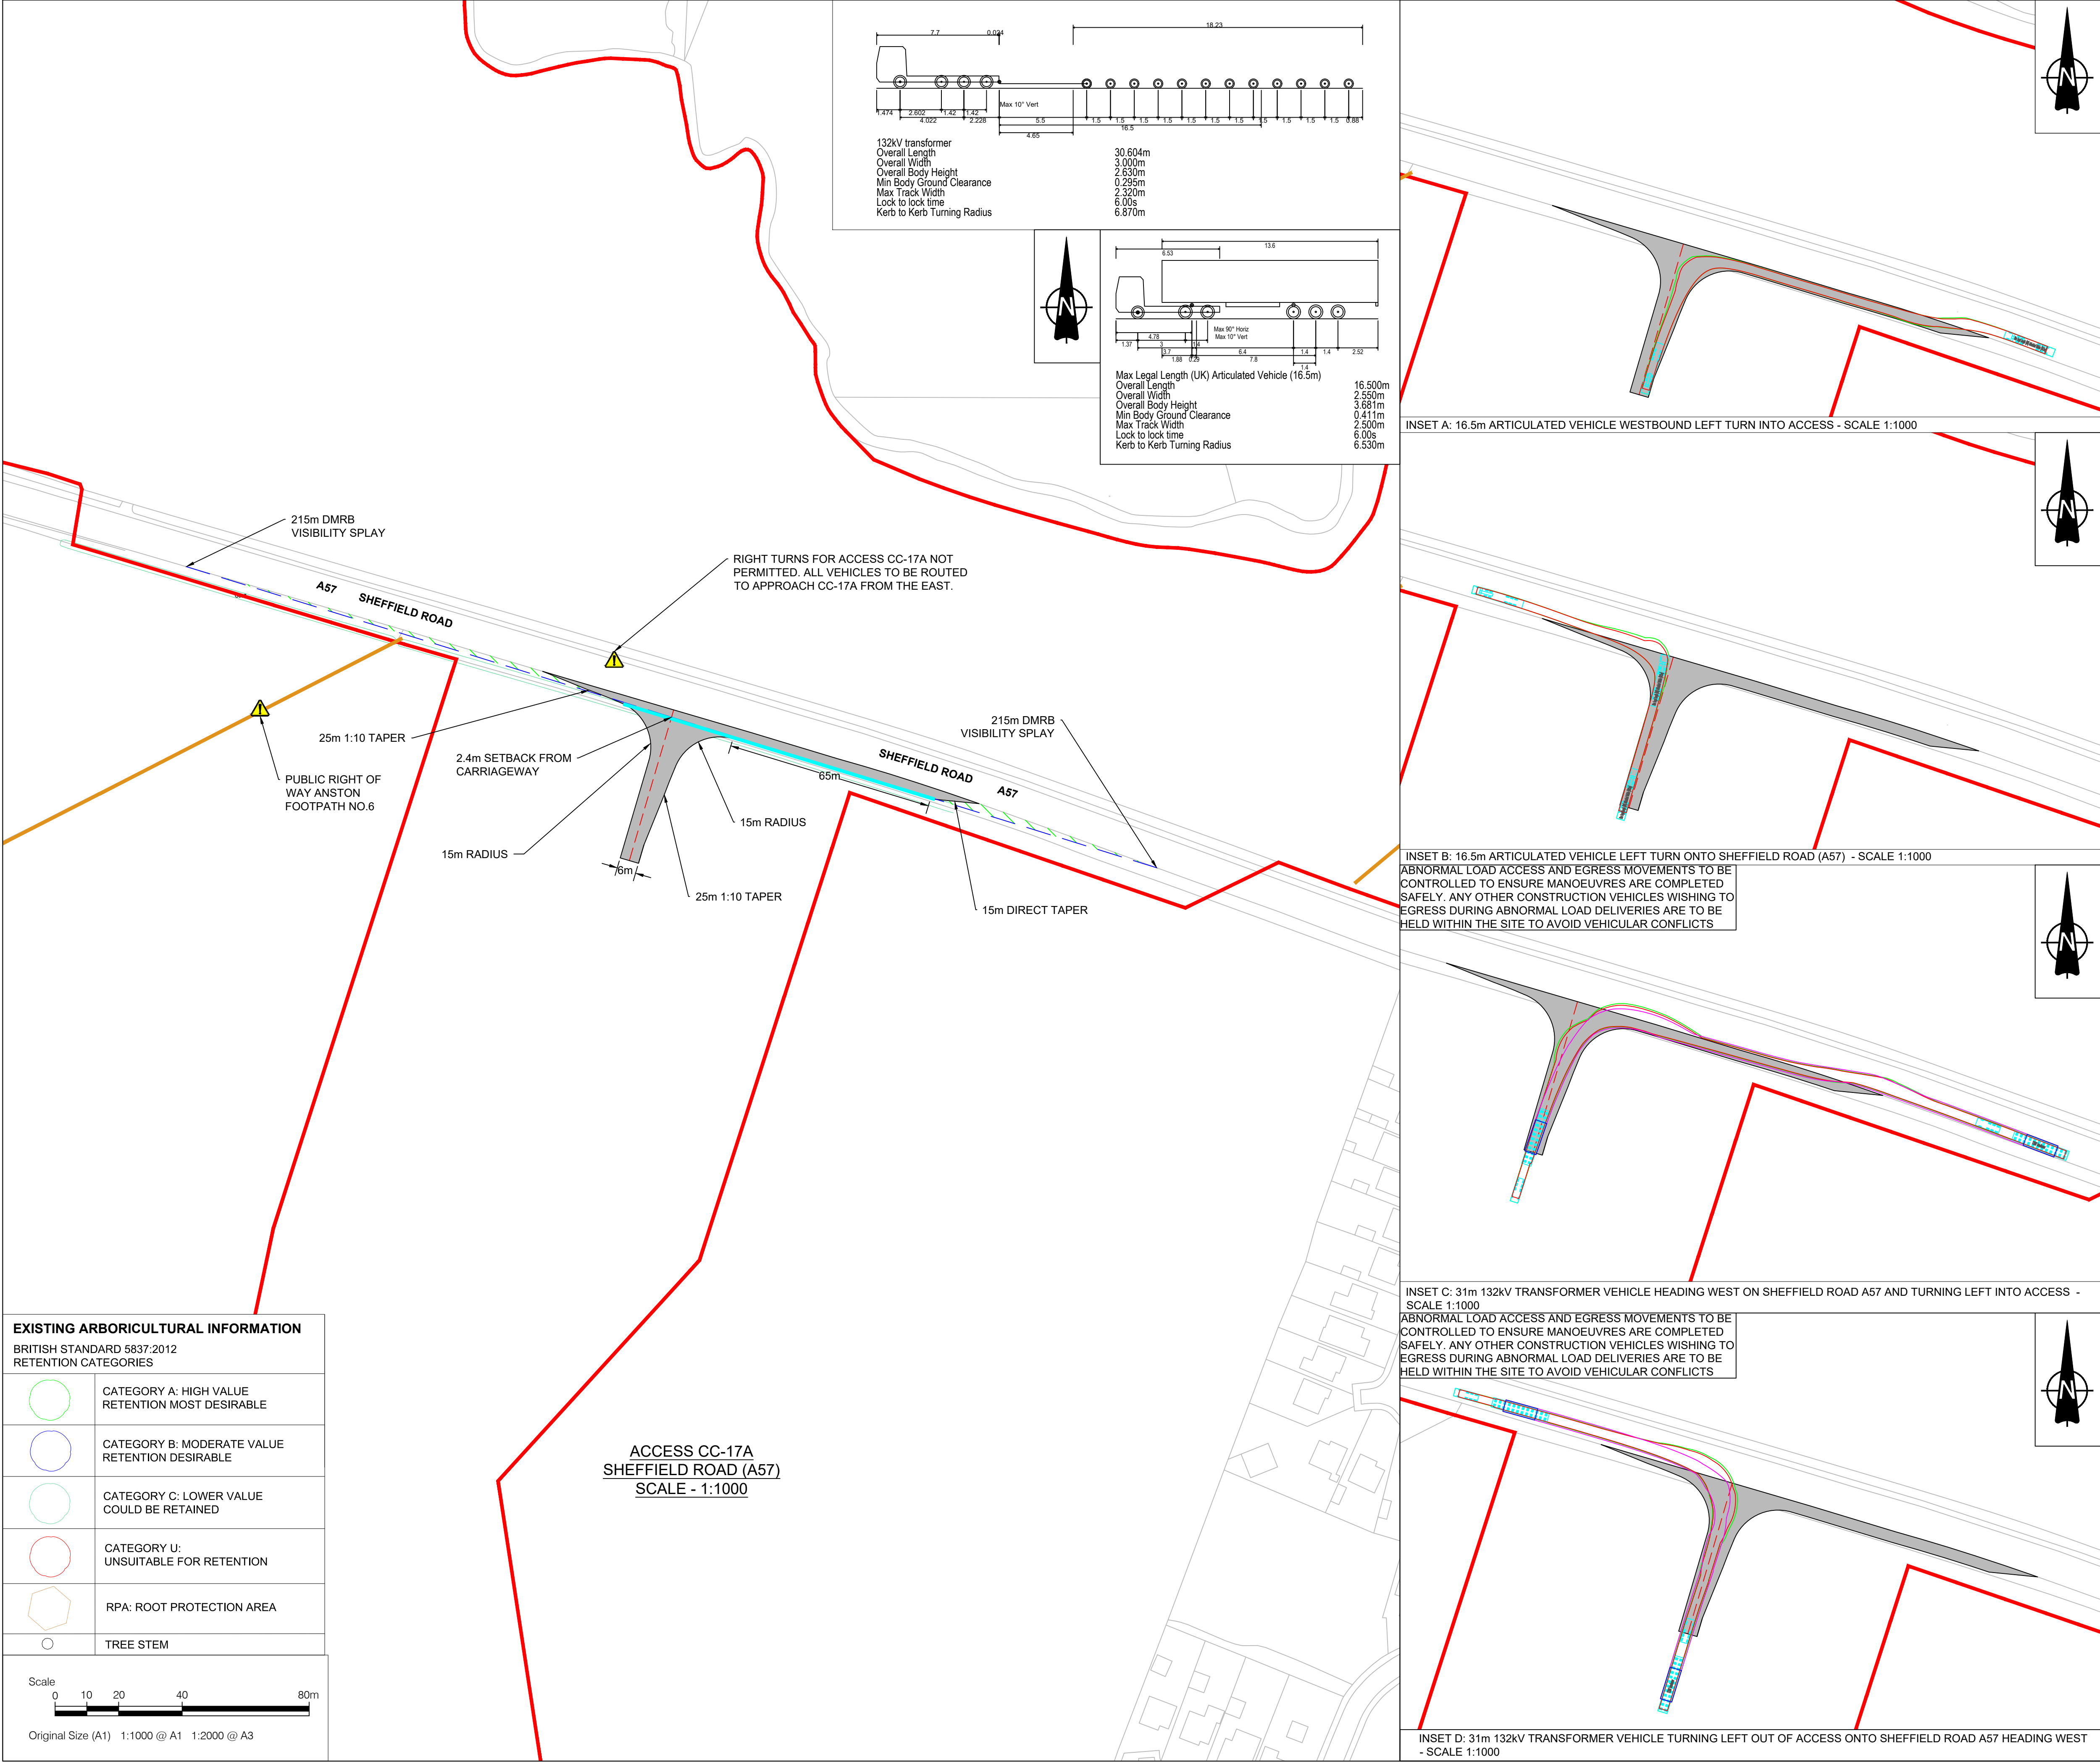


- NOTES**
1. This drawing is to be read in conjunction with all other relevant documentation.
 2. Do not scale from this drawing, use only printed dimensions.
 3. All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
 4. This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
 5. Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
 6. The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
 7. Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
 8. Junction visibility for the access is based upon DMRB CD109 Table 2.10.

- LEGEND**
- Extent of Access Footprint
 - Order Limits
 - Land Excluded from Order Limits
 - Vehicle Body
 - Vehicle Body Path
 - Vehicle Load
 - Vehicle Load Path
 - Vehicle Wheels Path
 - Edge of Road
 - Access Centreline
 - Junction Visibility
 - Vegetation to be Removed for Vis Splay
 - Indicative Hedgerow Removal Vis Splay
 - Indicative Hedgerow Removal for Bellmouth Access
 - Health and Safety Risk Identifier
 - Existing Public Right of Way




SHEET PLAN

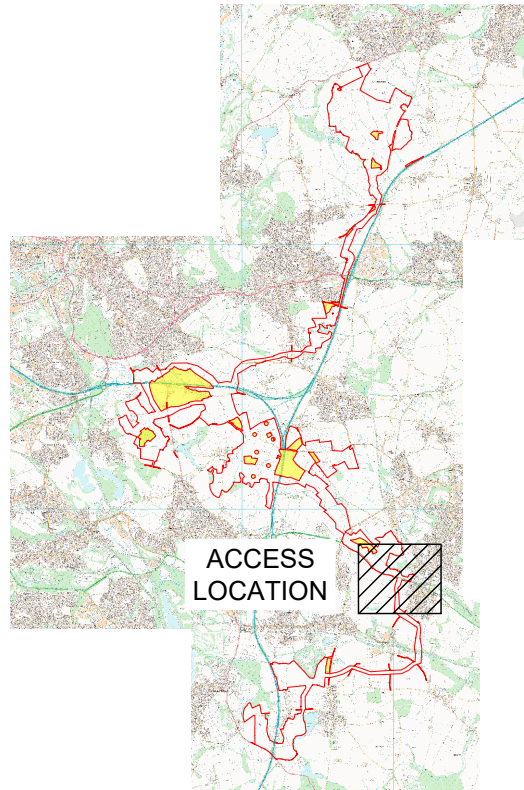

EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012	
RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM



EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012 RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

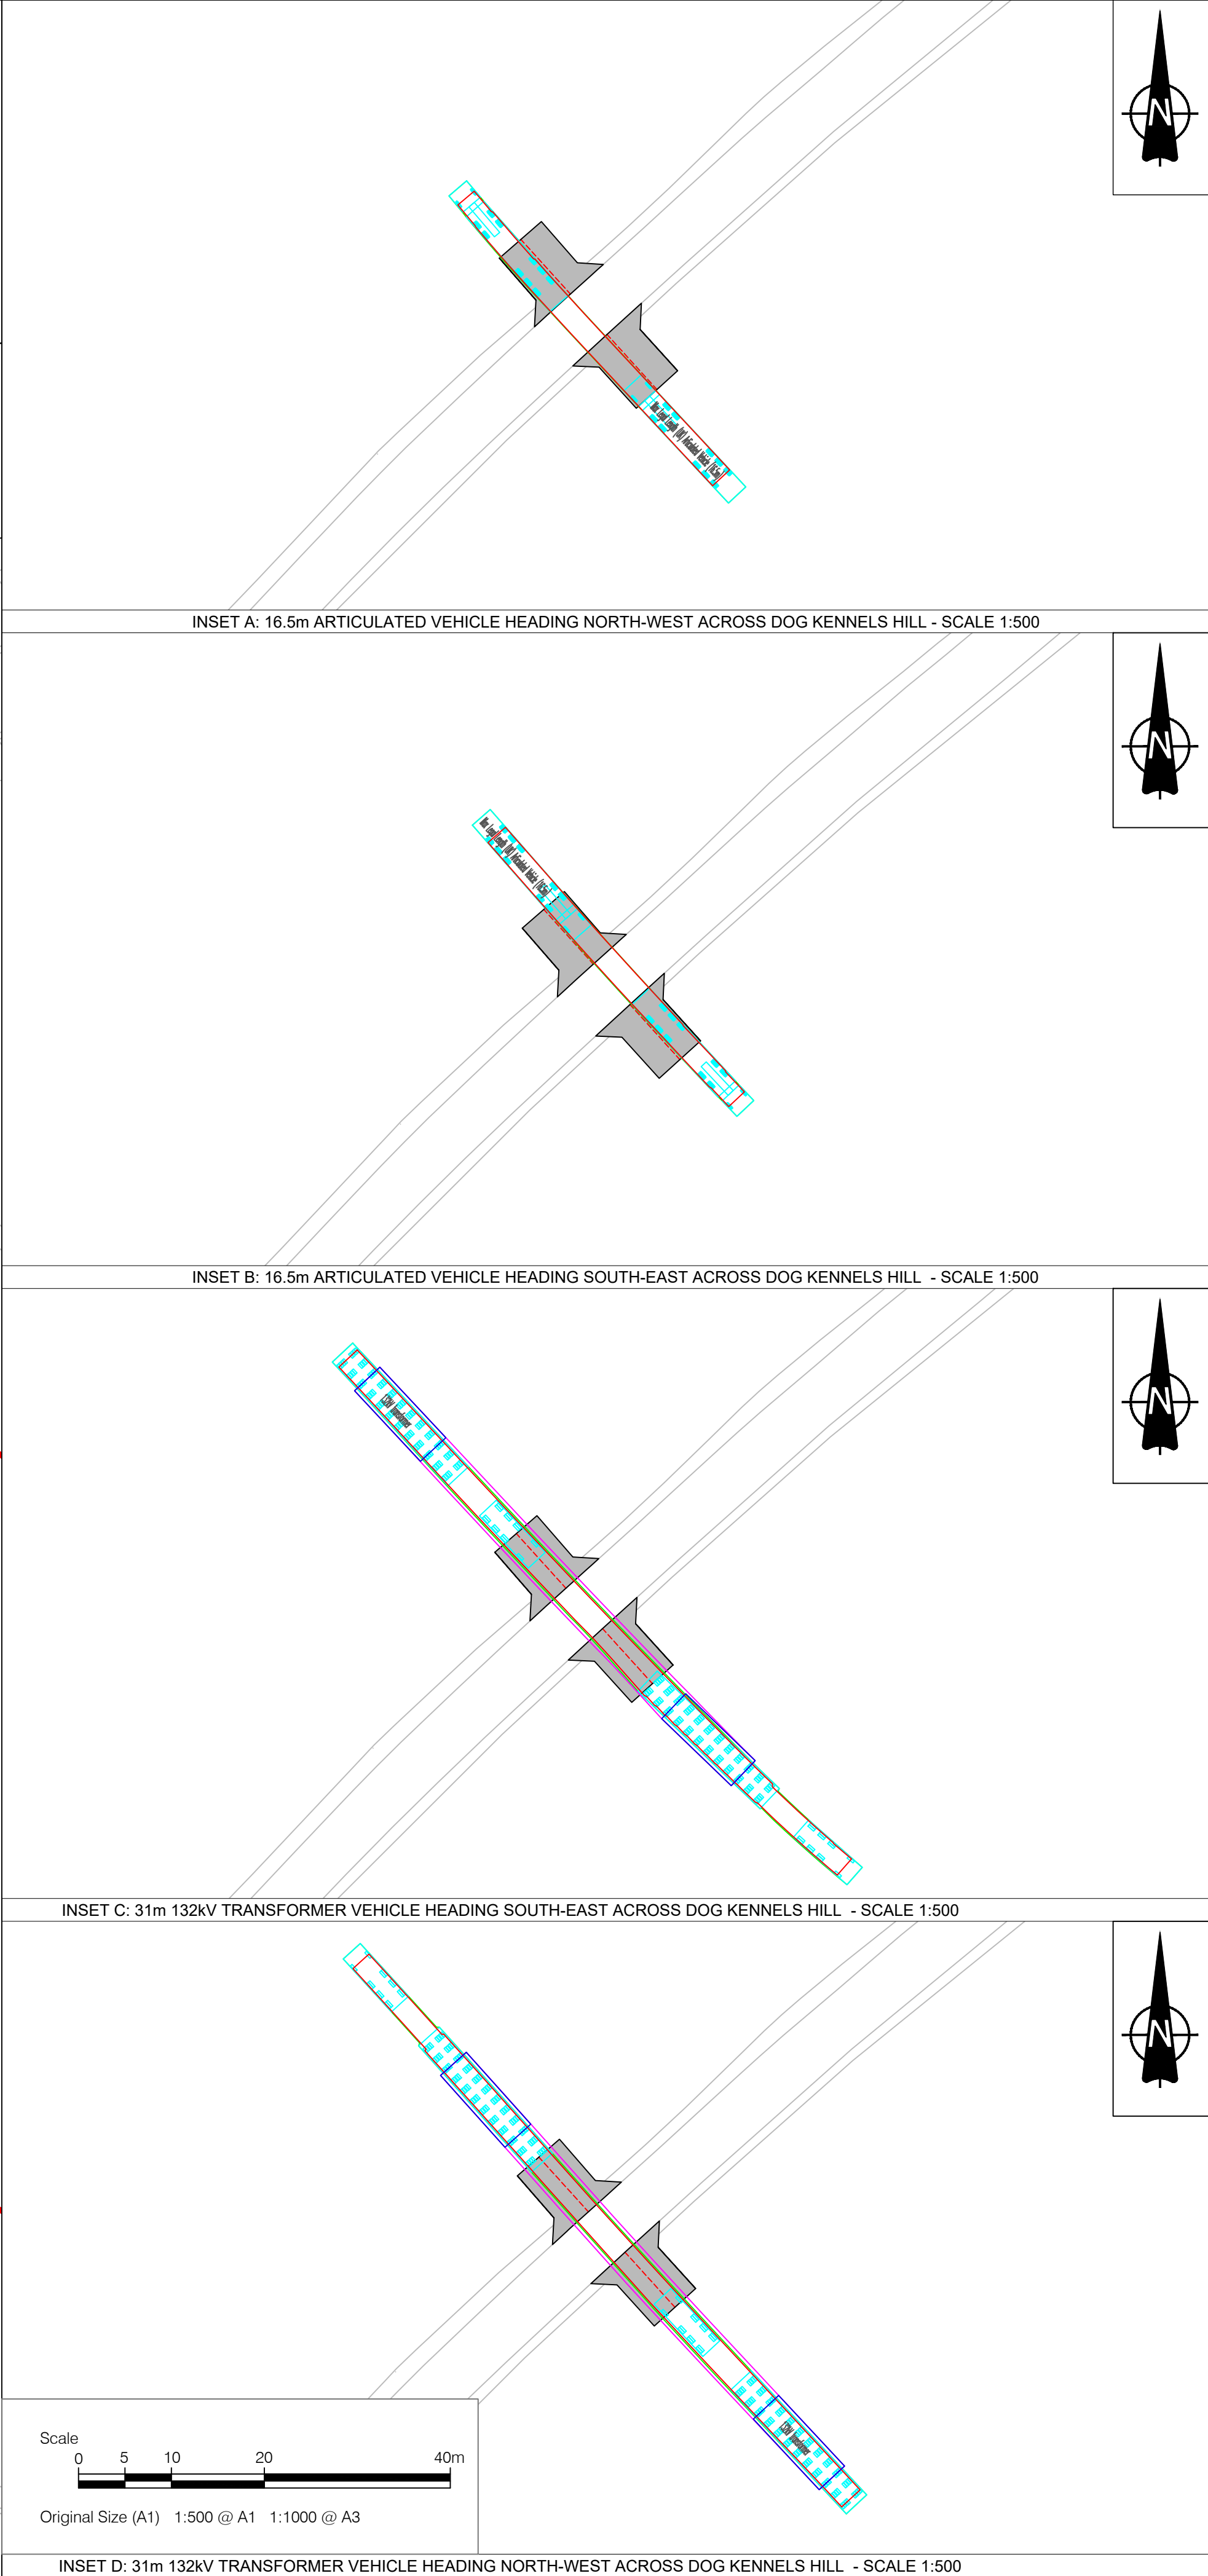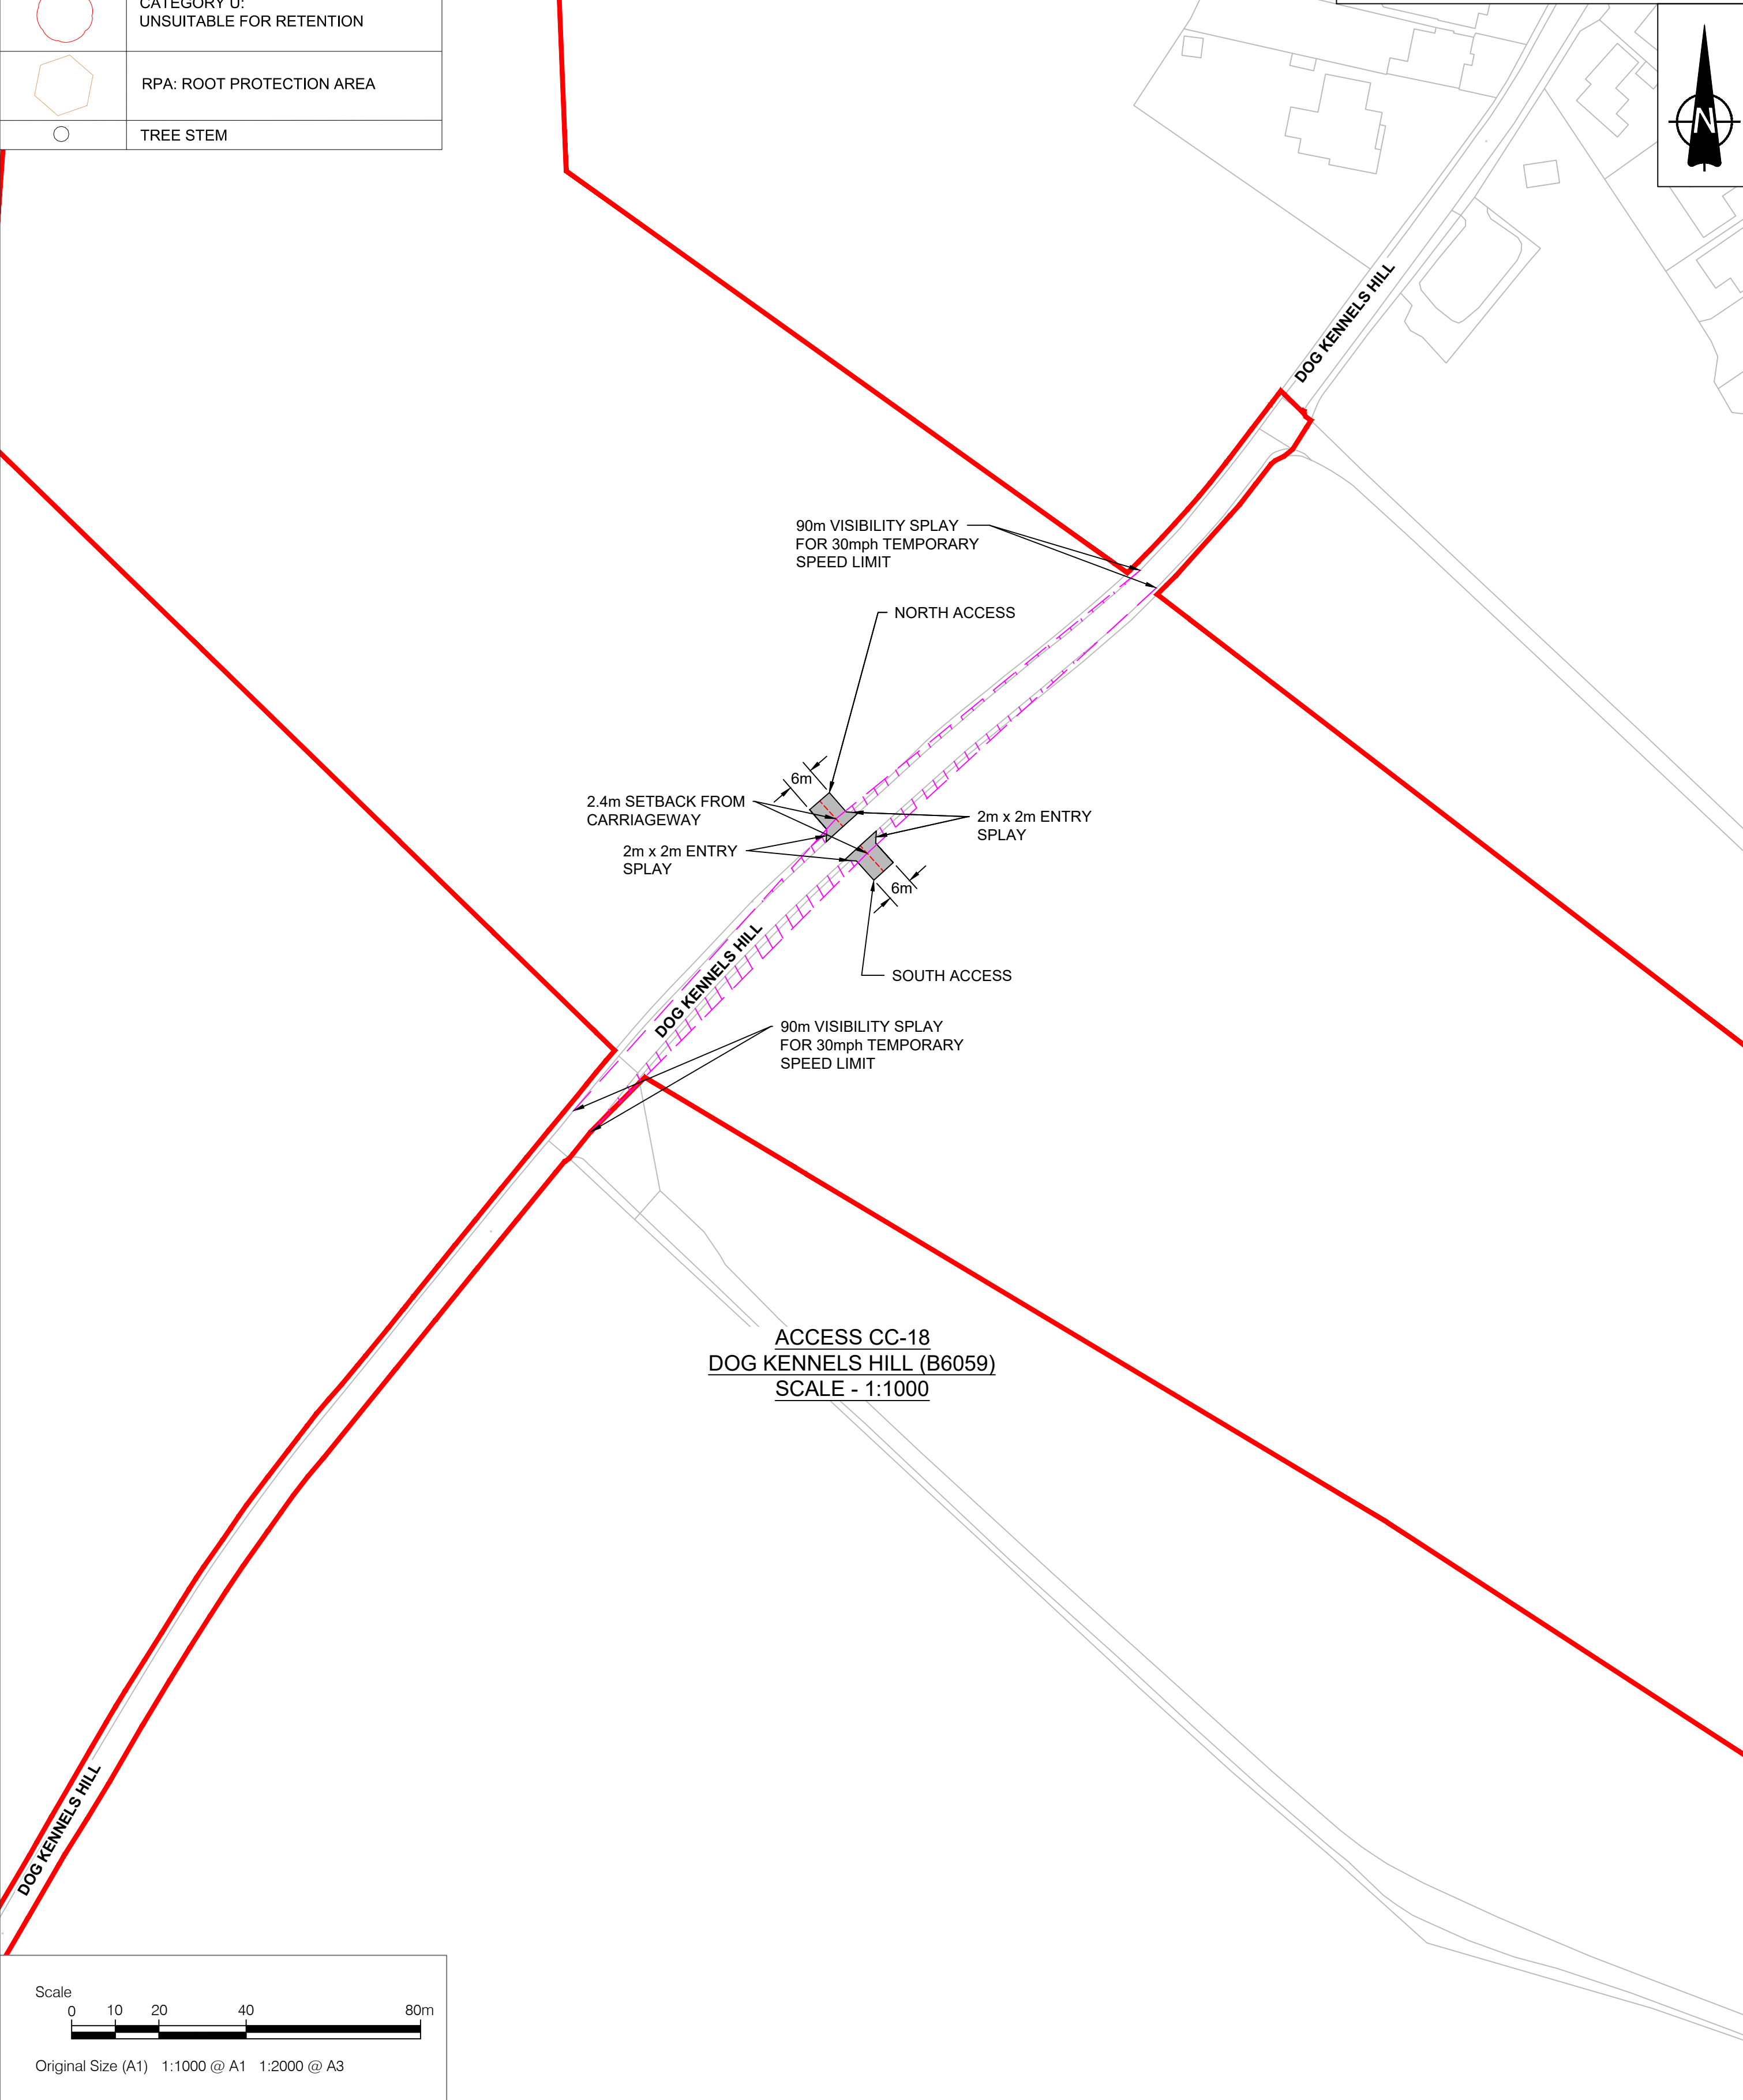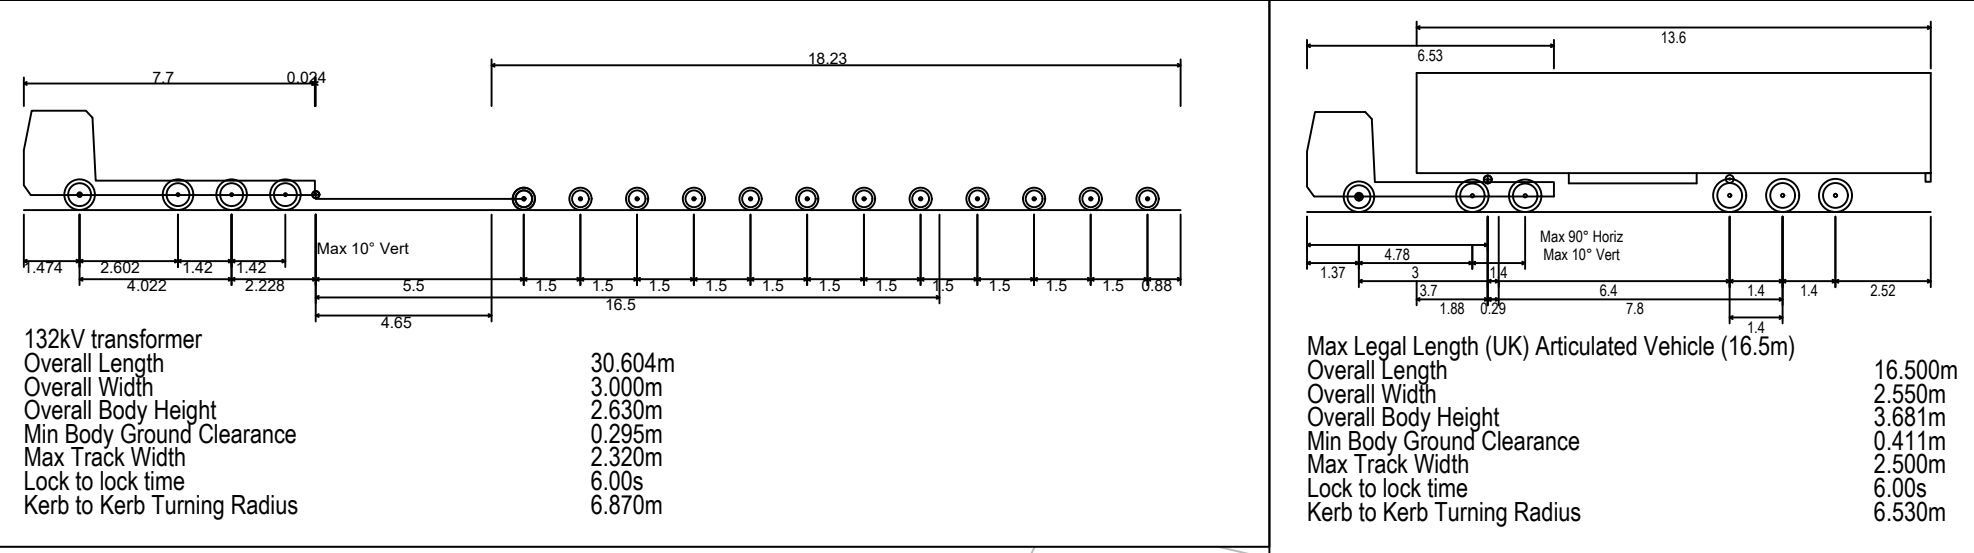

NOTES

- This drawing is to be read in conjunction with all other relevant documentation.
- Do not scale from this drawing, use only printed dimensions.
- All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
- This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
- Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
- The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
- Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
- Junction visibility for the access is based upon DMRB CD109 Table 2.10 on the basis of a 30mph temporary speed limit being enforced.

LEGEND

- Extent of Access Footprint
- Order Limits
- Land Excluded from Order Limits
- Vehicle Body
- Vehicle Body Path
- Vehicle Load
- Vehicle Load Path
- Vehicle Wheels Path
- Edge of Road
- Access Centreline
- Junction Visibility 30mph Temporary Speed Limit
- Vegetation to be Removed 30mph Temporary Speed Limit Vis Splay
- Indicative Hedgerow Removal 30mph Temporary Speed Limit
- Indicative Hedgerow Removal for Bellmouth Access
- Health and Safety Risk Identifier
- Existing Public Right of Way

SHEET PLAN

ACCESS
LOCATION

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:

Cable Corridor Area Access CC-18

Appendix 3 - Sheet 44 of 53

Whitestone Solar Farm

Regulation 5(2)(o)

DRAWING DATE: 03/06/2026




SCALE: AS SHOWN	SHEET: Sheet 44 of 53
SIZE: A1	REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020

WHITESTONE
solar farm

EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012	
RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

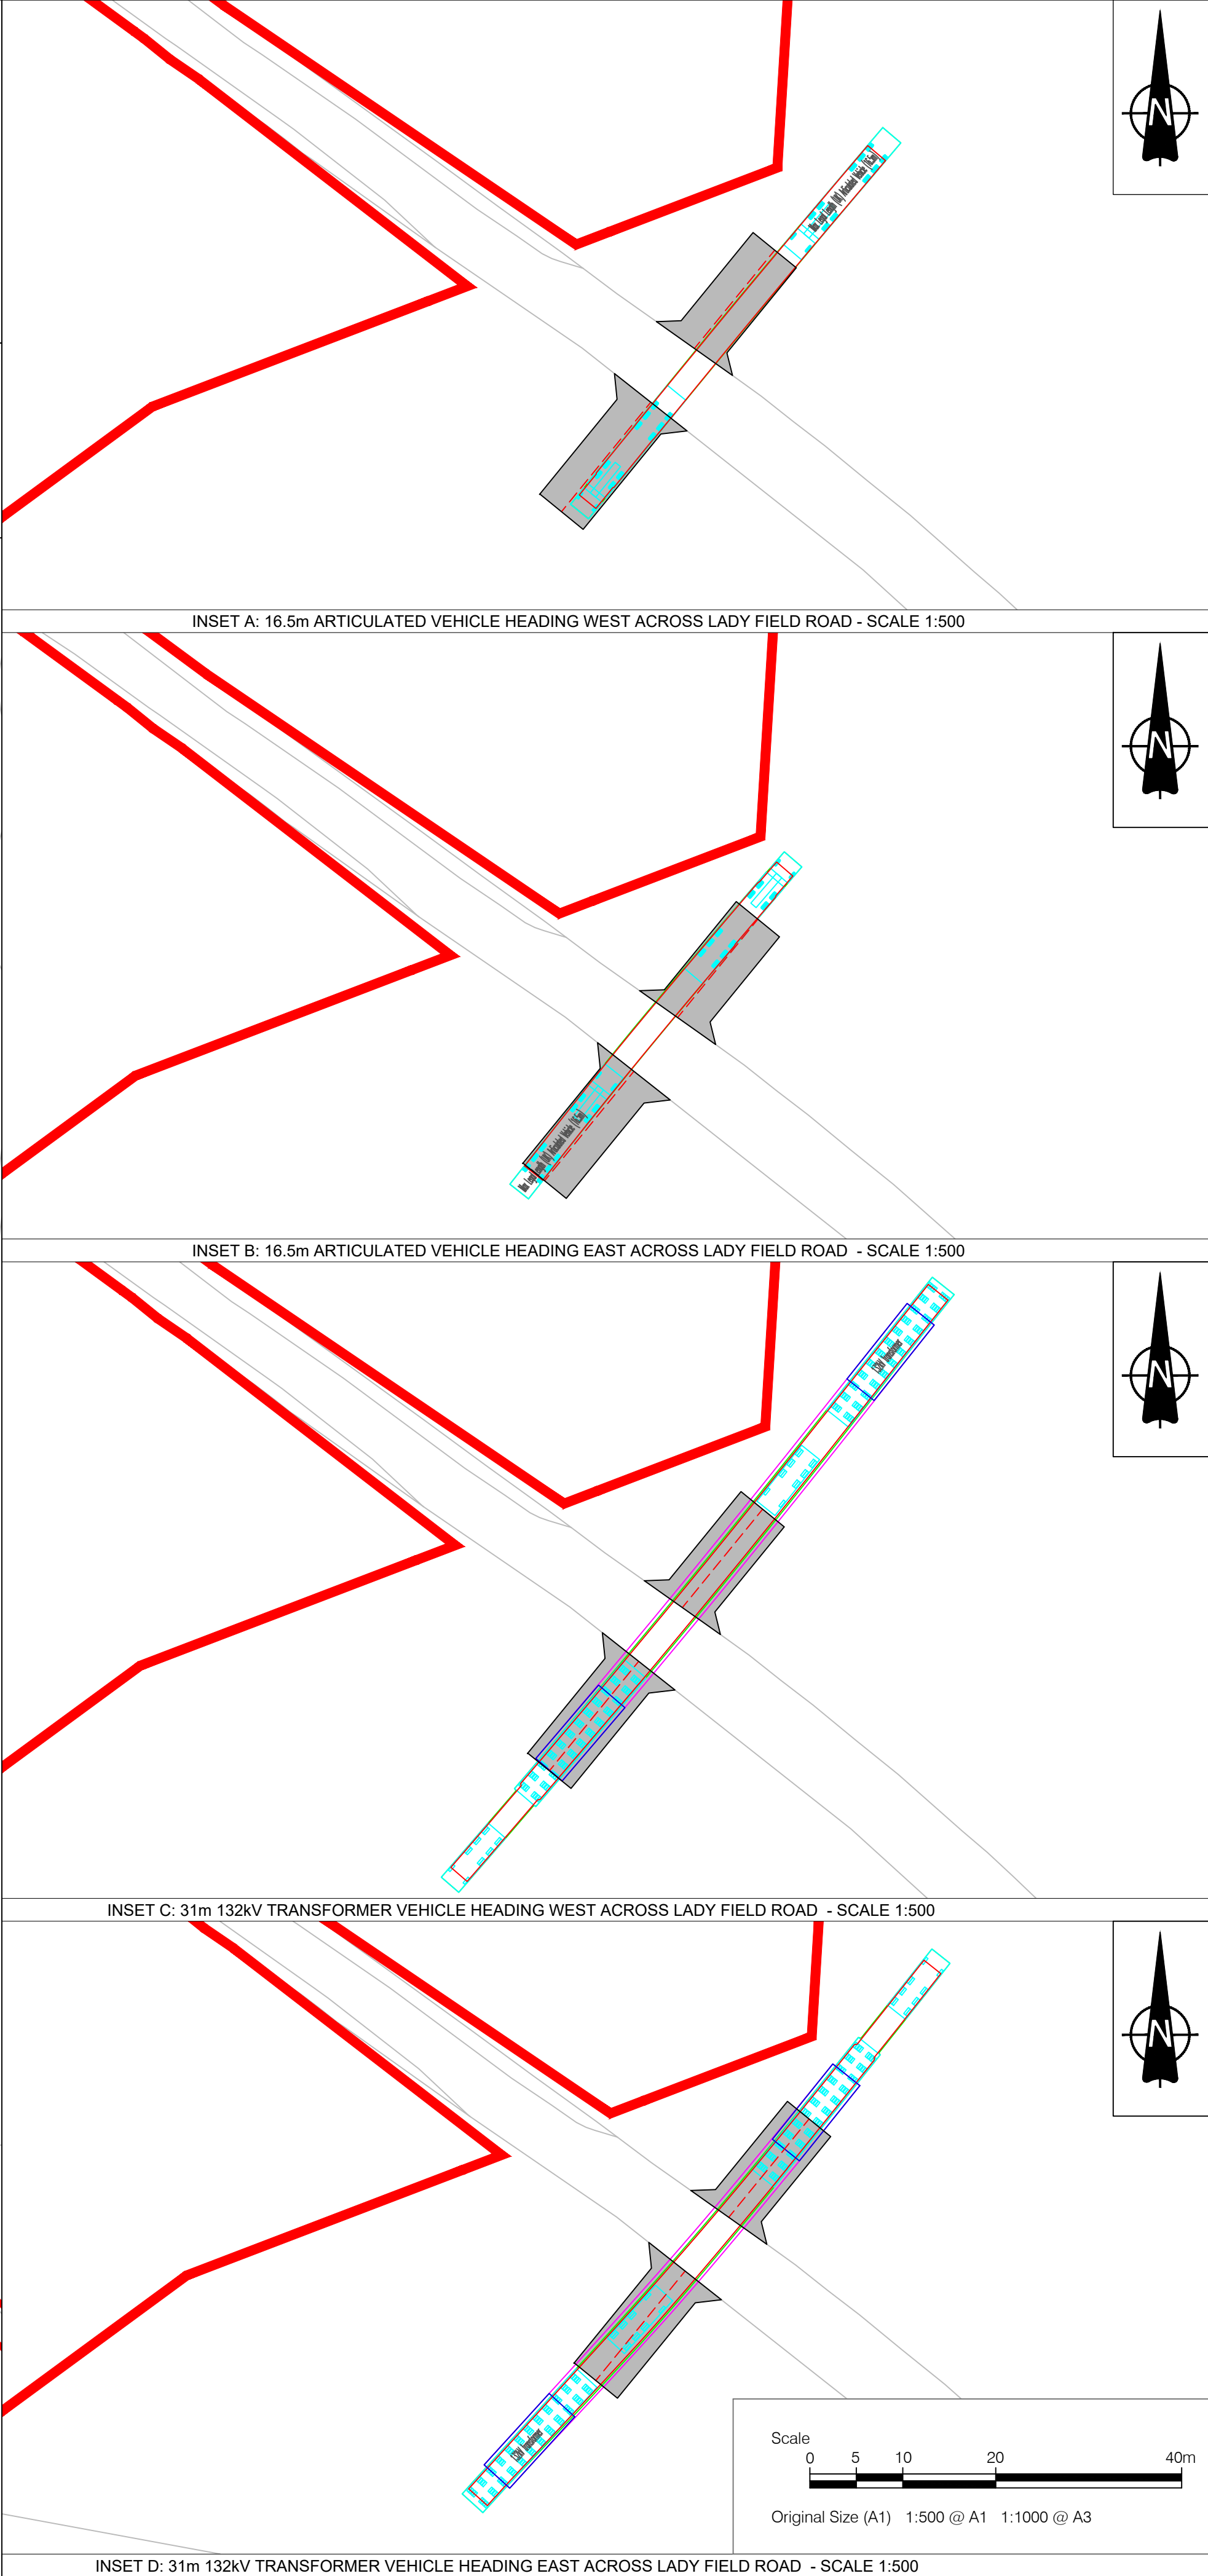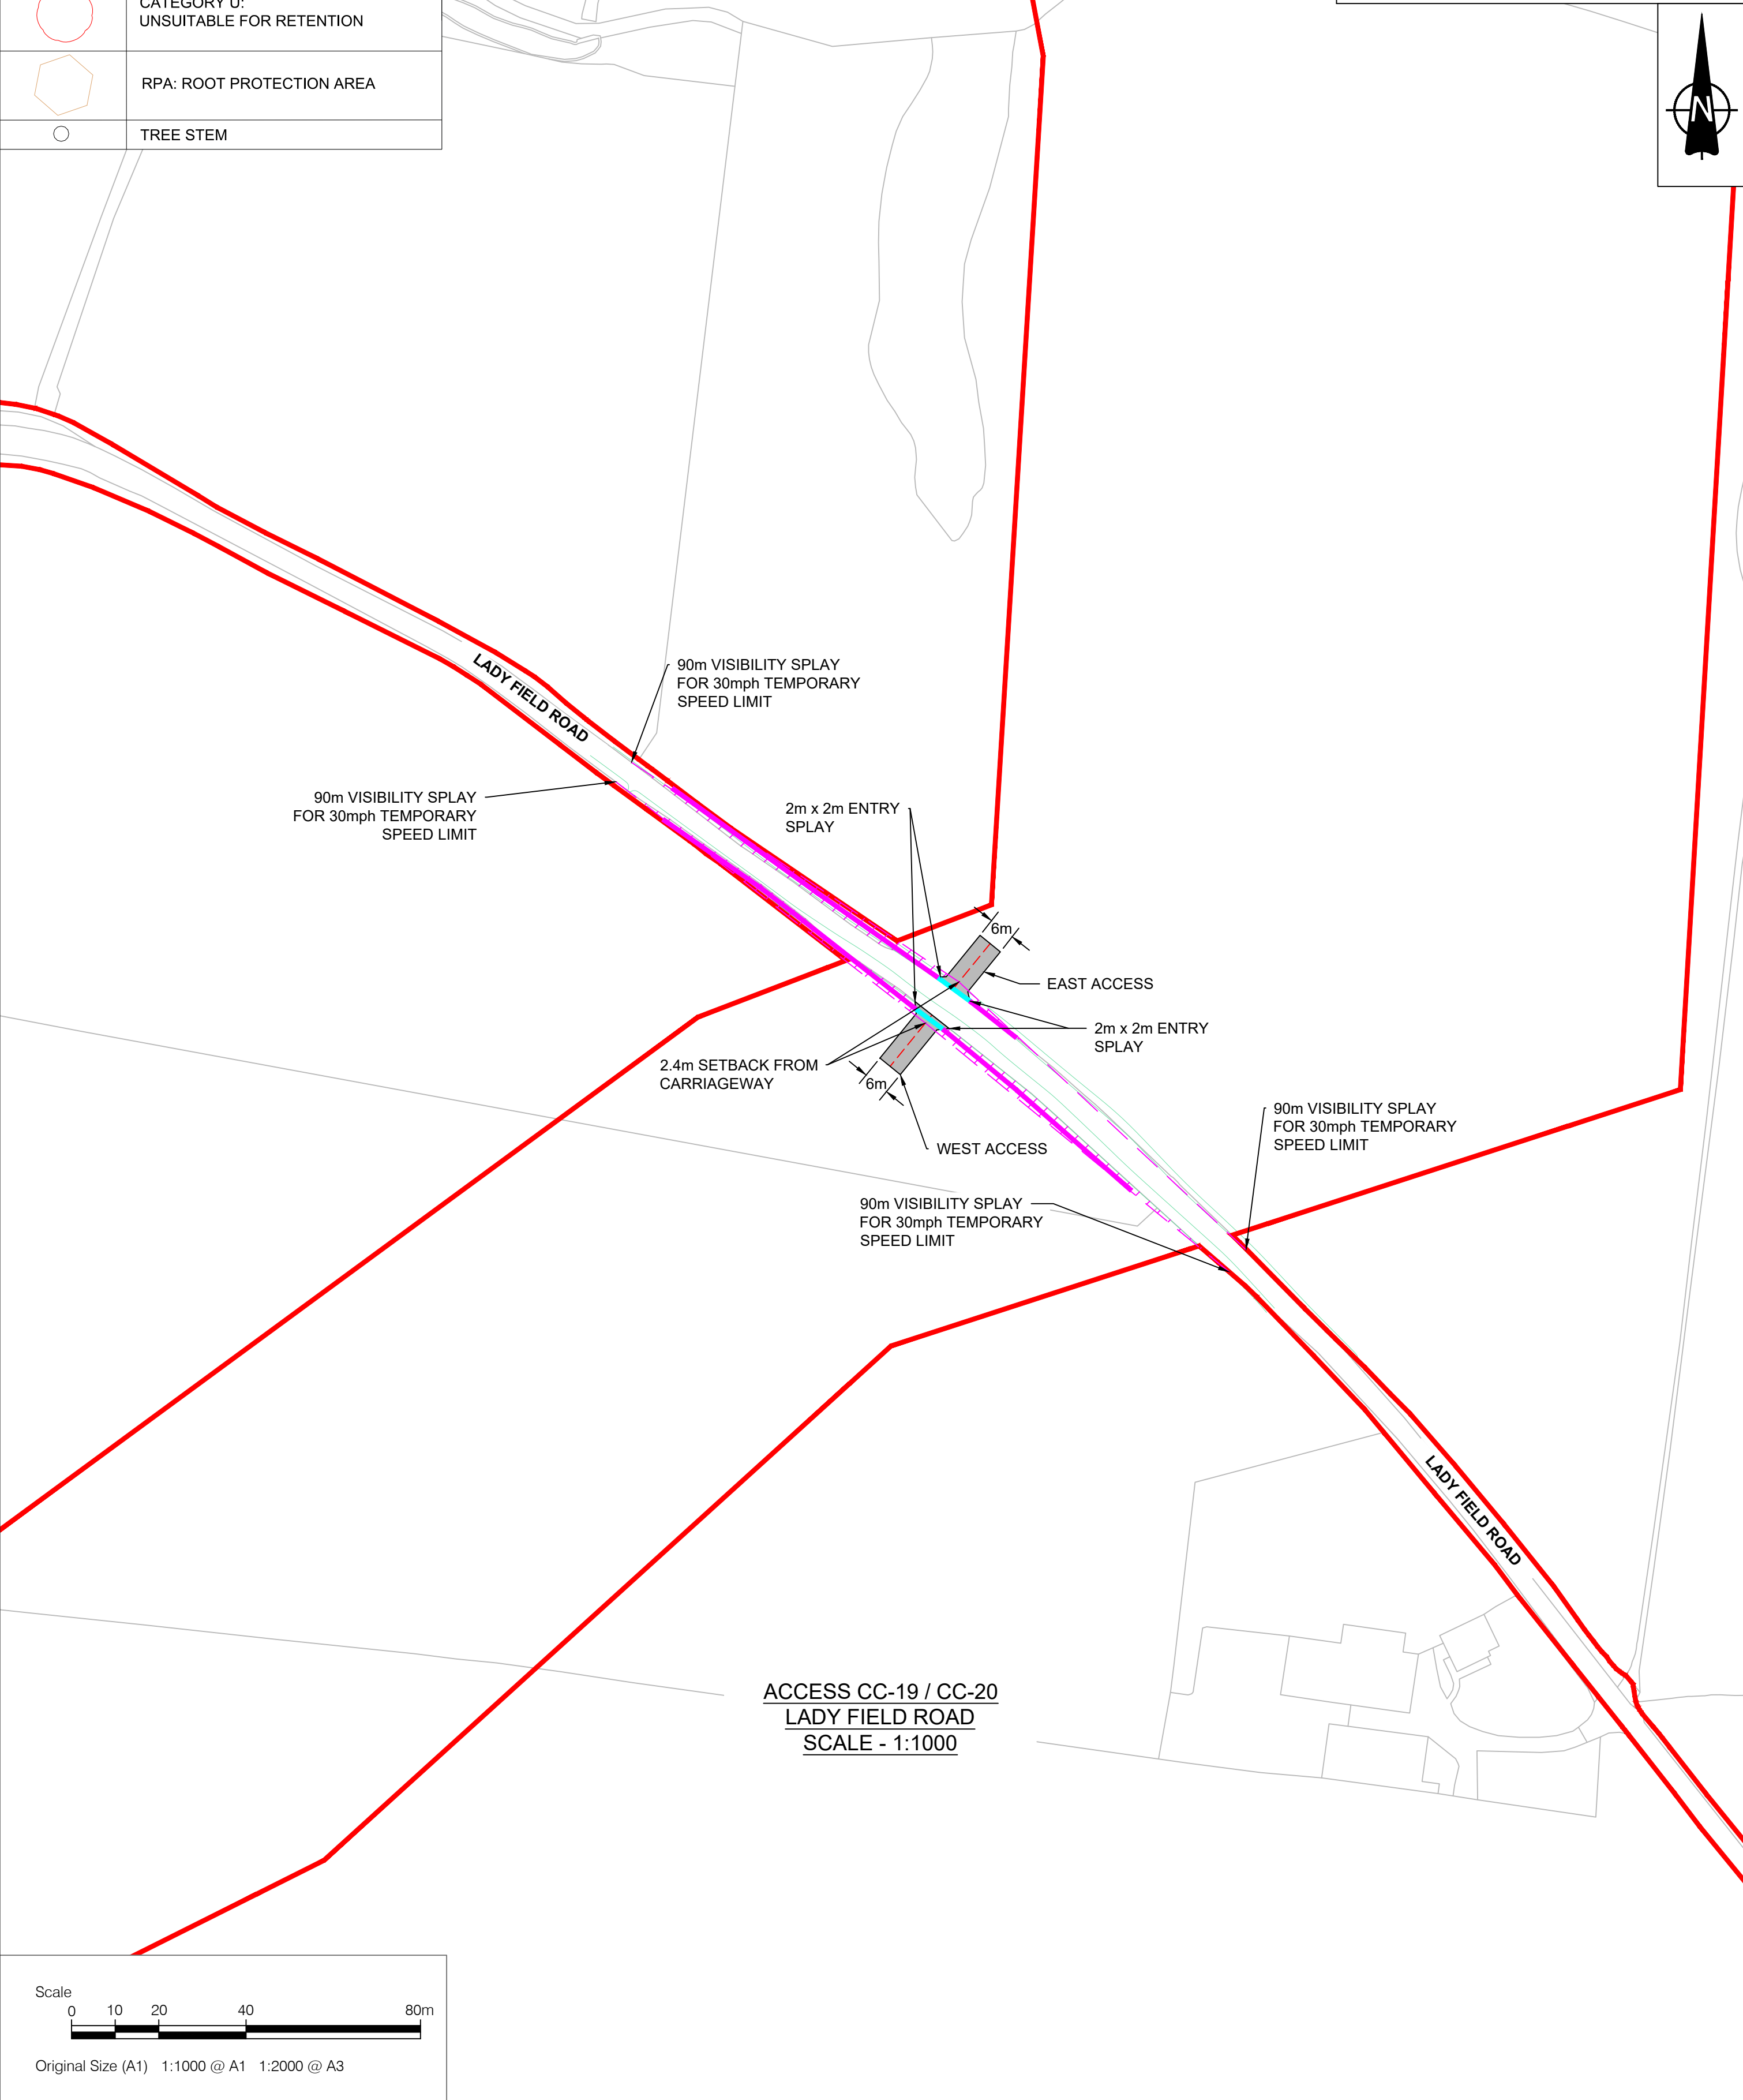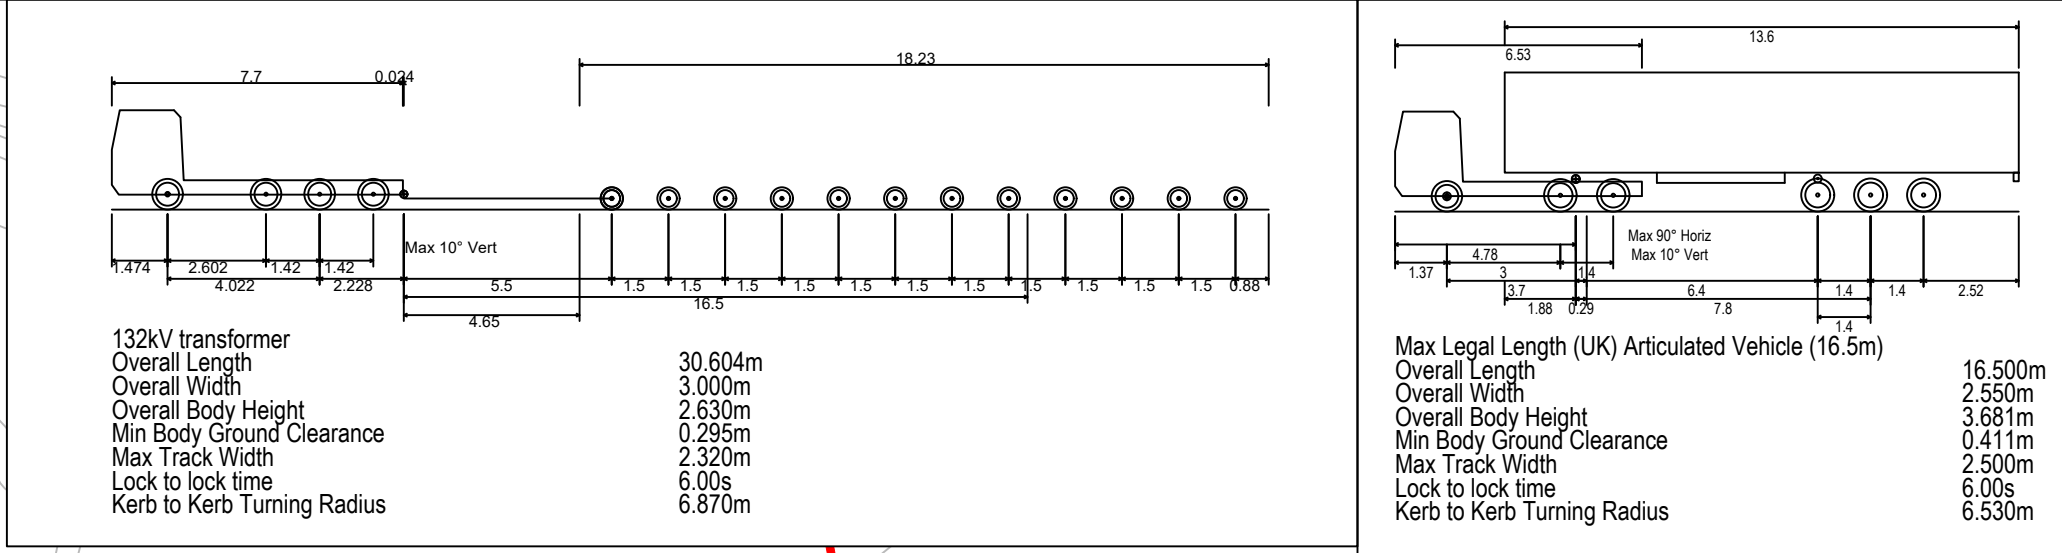

NOTES

- This drawing is to be read in conjunction with all other relevant documentation.
- Do not scale from this drawing, use only printed dimensions.
- All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
- This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
- Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
- The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
- Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
- Junction visibility for the access is based upon DMRB CD109 Table 2.10 on the basis of a 30mph temporary speed limit being enforced.

LEGEND

- Extent of Access Footprint
- Order Limits
- Land Excluded from Order Limits
- Vehicle Body
- Vehicle Body Path
- Vehicle Load
- Vehicle Load Path
- Vehicle Wheels Path
- Edge of Road
- Access Centreline
- Junction Visibility 30mph Temporary Speed Limit
- Vegetation to be Removed 30mph Temporary Speed Limit Vis Splay
- Indicative Hedgerow Removal 30mph Temporary Speed Limit
- Indicative Hedgerow Removal for Bellmouth Access
- Health and Safety Risk Identifier
- Existing Public Right of Way

SHEET PLAN

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:

Cable Corridor Area Access CC-19/20

Appendix 3 - Sheet 45 of 53

Whitestone Solar Farm

Regulation 5(2)(o)





DRAWING DATE: 03/06/2026

SCALE: AS SHOWN	SHEET: Sheet 45 of 53
SIZE: A1	REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020

EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012	
RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

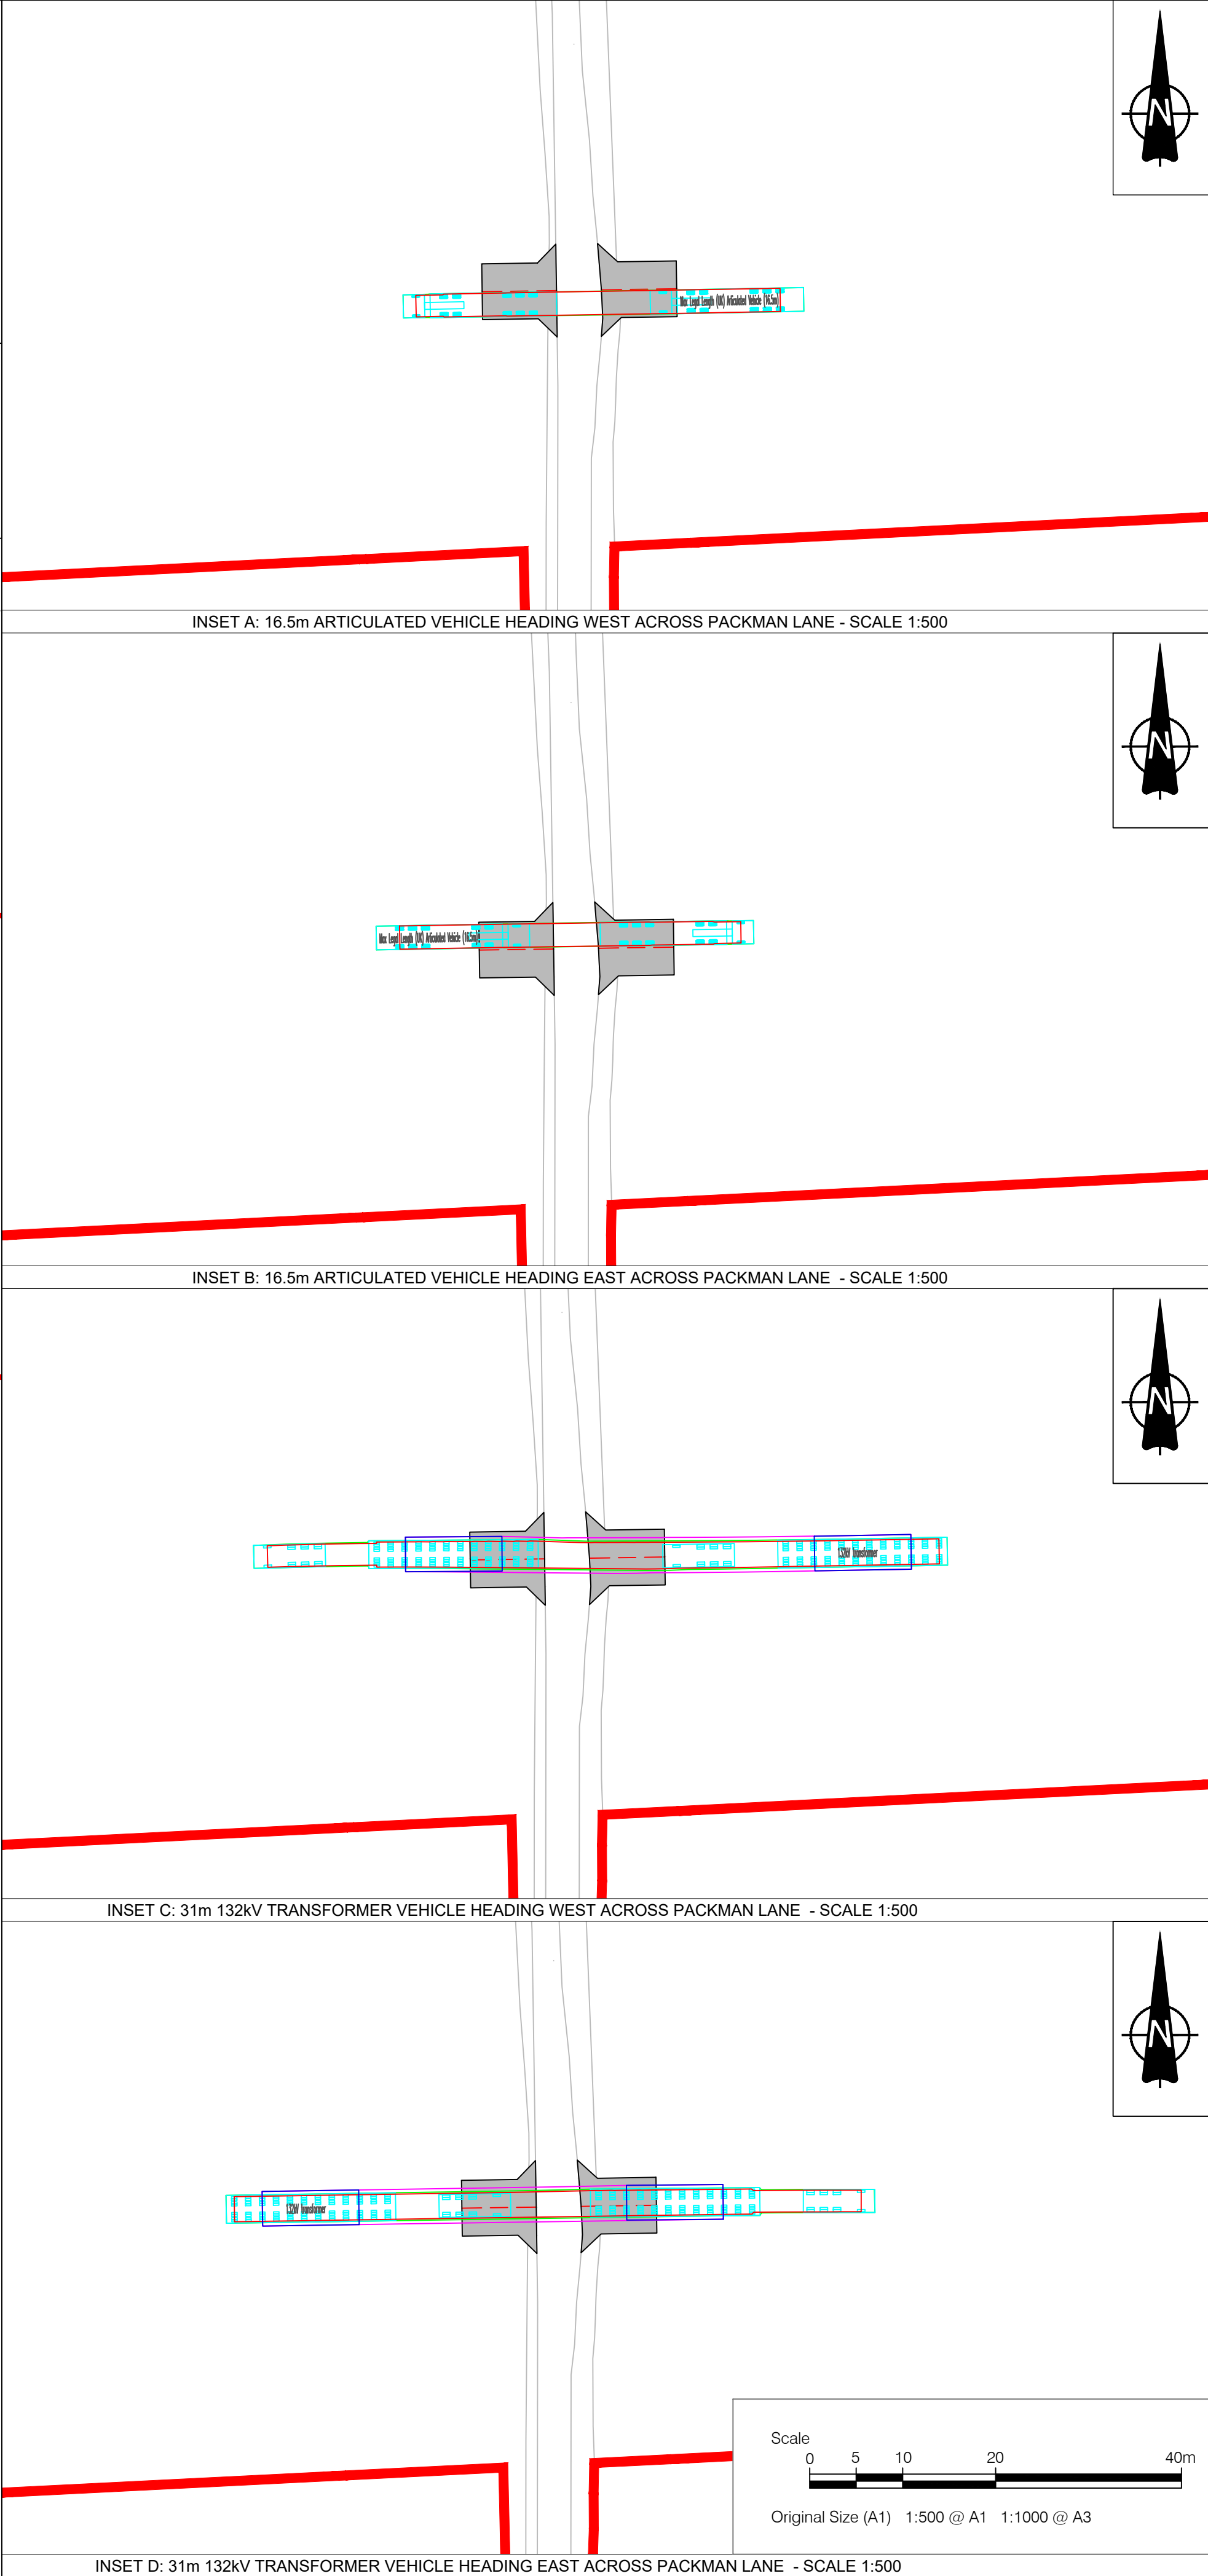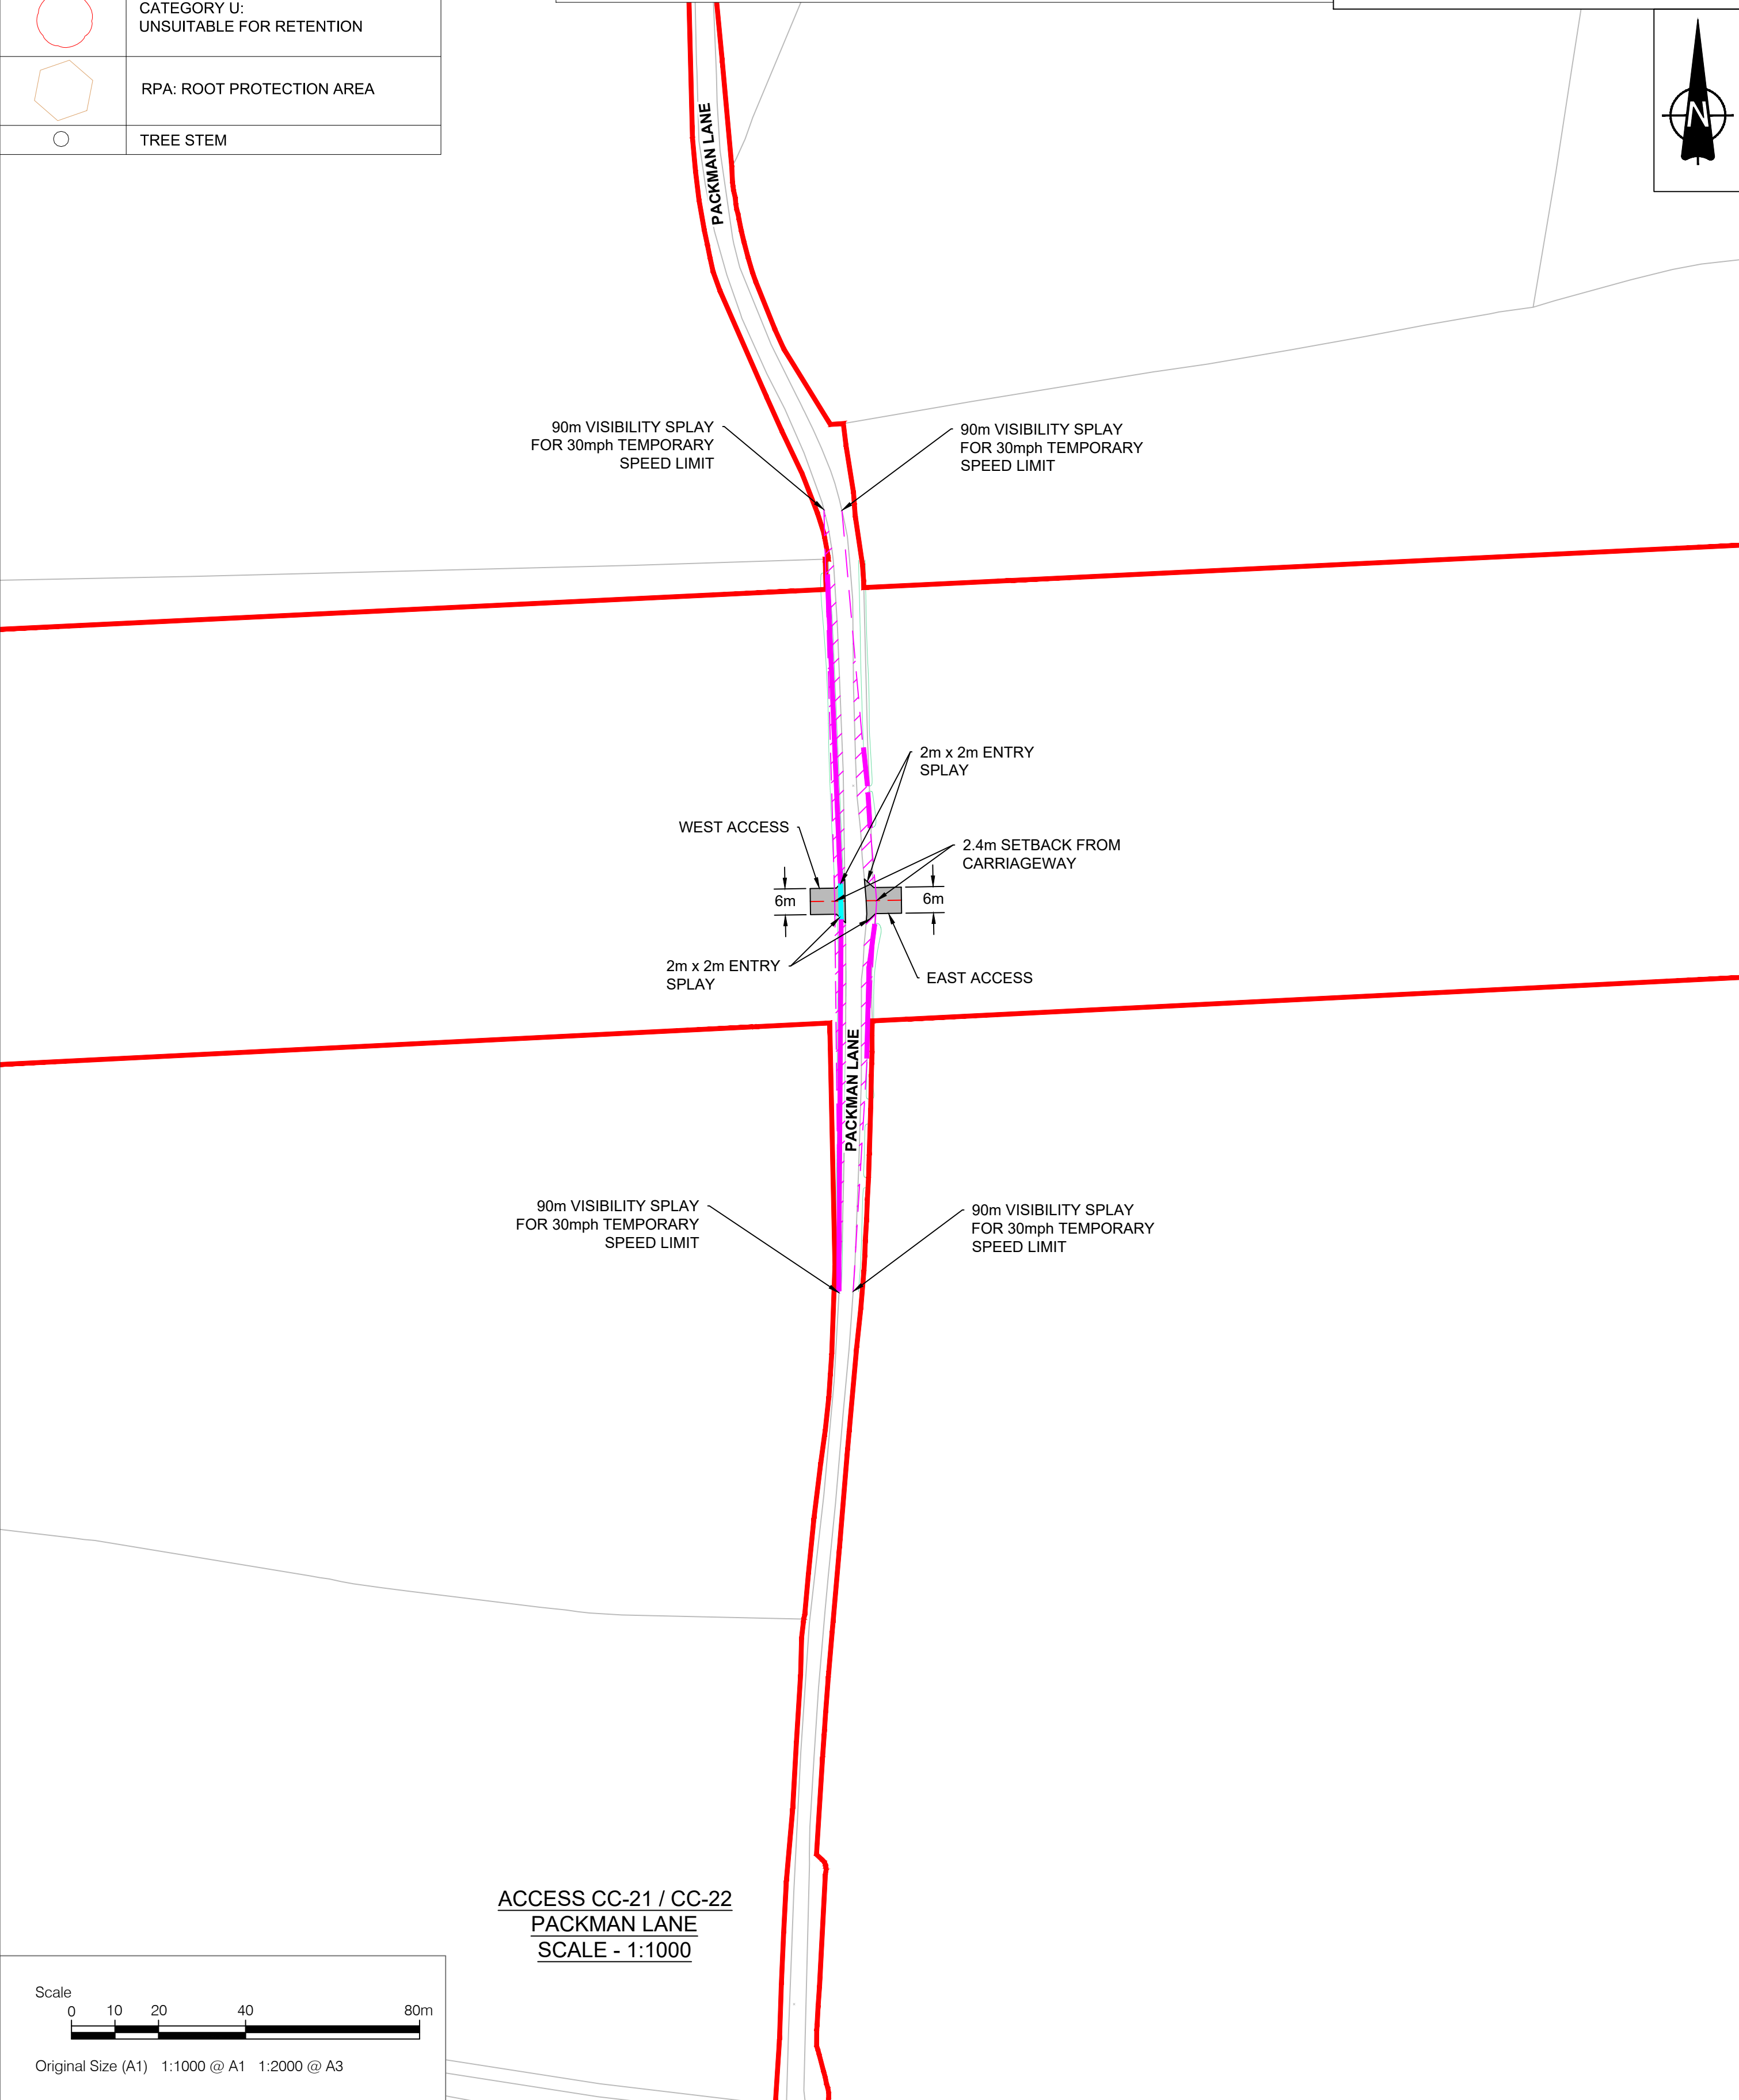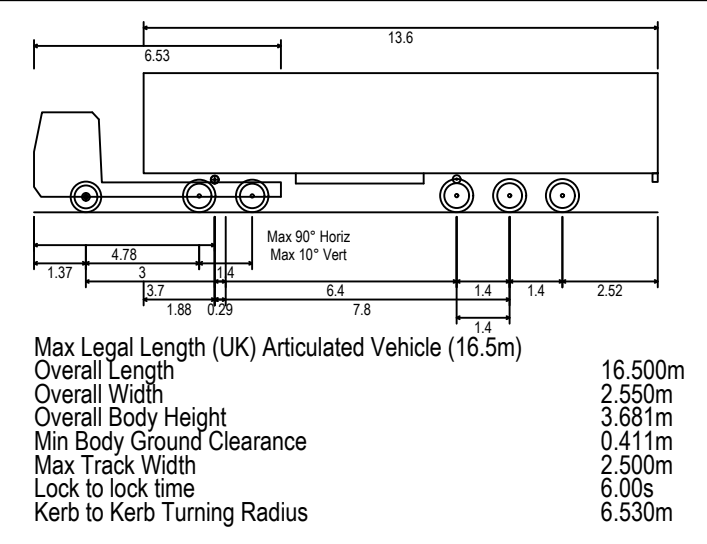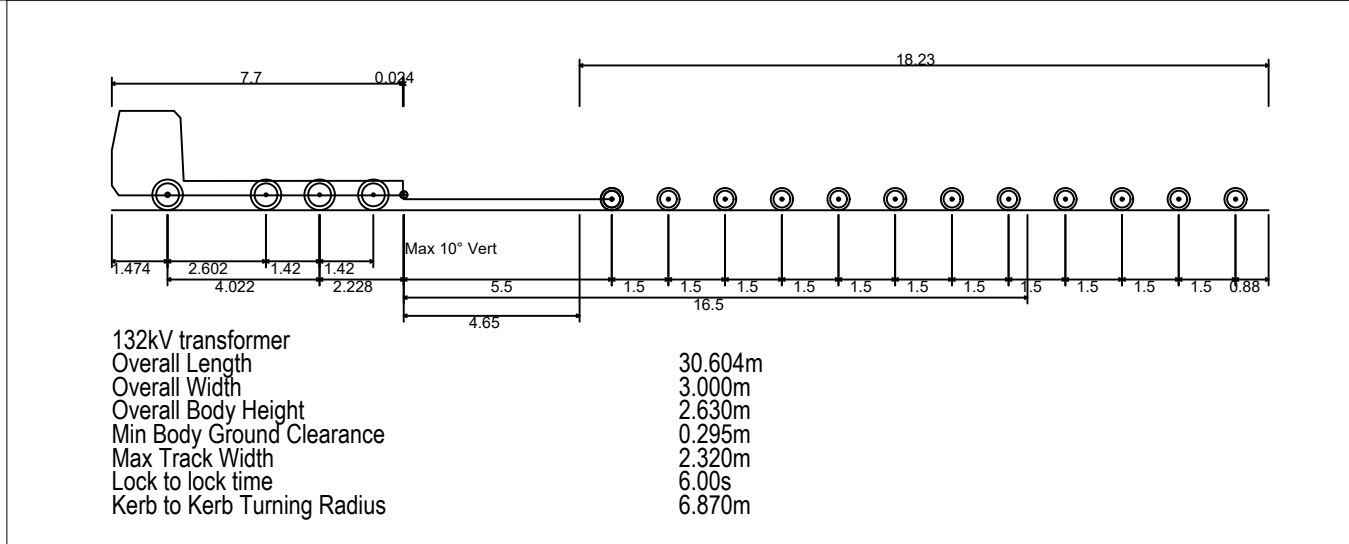

NOTES

- This drawing is to be read in conjunction with all other relevant documentation.
- Do not scale from this drawing, use only printed dimensions.
- All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
- This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
- Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
- The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
- Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
- Junction visibility for the access is based upon DMRB CD109 Table 2.10 on the basis of a 30mph temporary speed limit being enforced.

LEGEND

- Extent of Access Footprint
- Order Limits
- Land Excluded from Order Limits
- Vehicle Body
- Vehicle Body Path
- Vehicle Load
- Vehicle Load Path
- Vehicle Wheels Path
- Edge of Road
- Access Centreline
- Junction Visibility 30mph Temporary Speed Limit
- Vegetation to be Removed 30mph Temporary Speed Limit Vis Splay
- Indicative Hedgerow Removal 30mph Temporary Speed Limit
- Indicative Hedgerow Removal for Bellmouth Access
- Health and Safety Risk Identifier
- Existing Public Right of Way

SHEET PLAN

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:

Cable Corridor Area Access CC-21/22

Appendix 3 - Sheet 46 of 53

Whitestone Solar Farm

Regulation 5(2)(o)





DRAWING DATE: 03/06/2026

SCALE: AS SHOWN	SHEET: Sheet 46 of 53
SIZE: A1	REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12


APPLICATION NUMBER: EN0110020

EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012	
RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

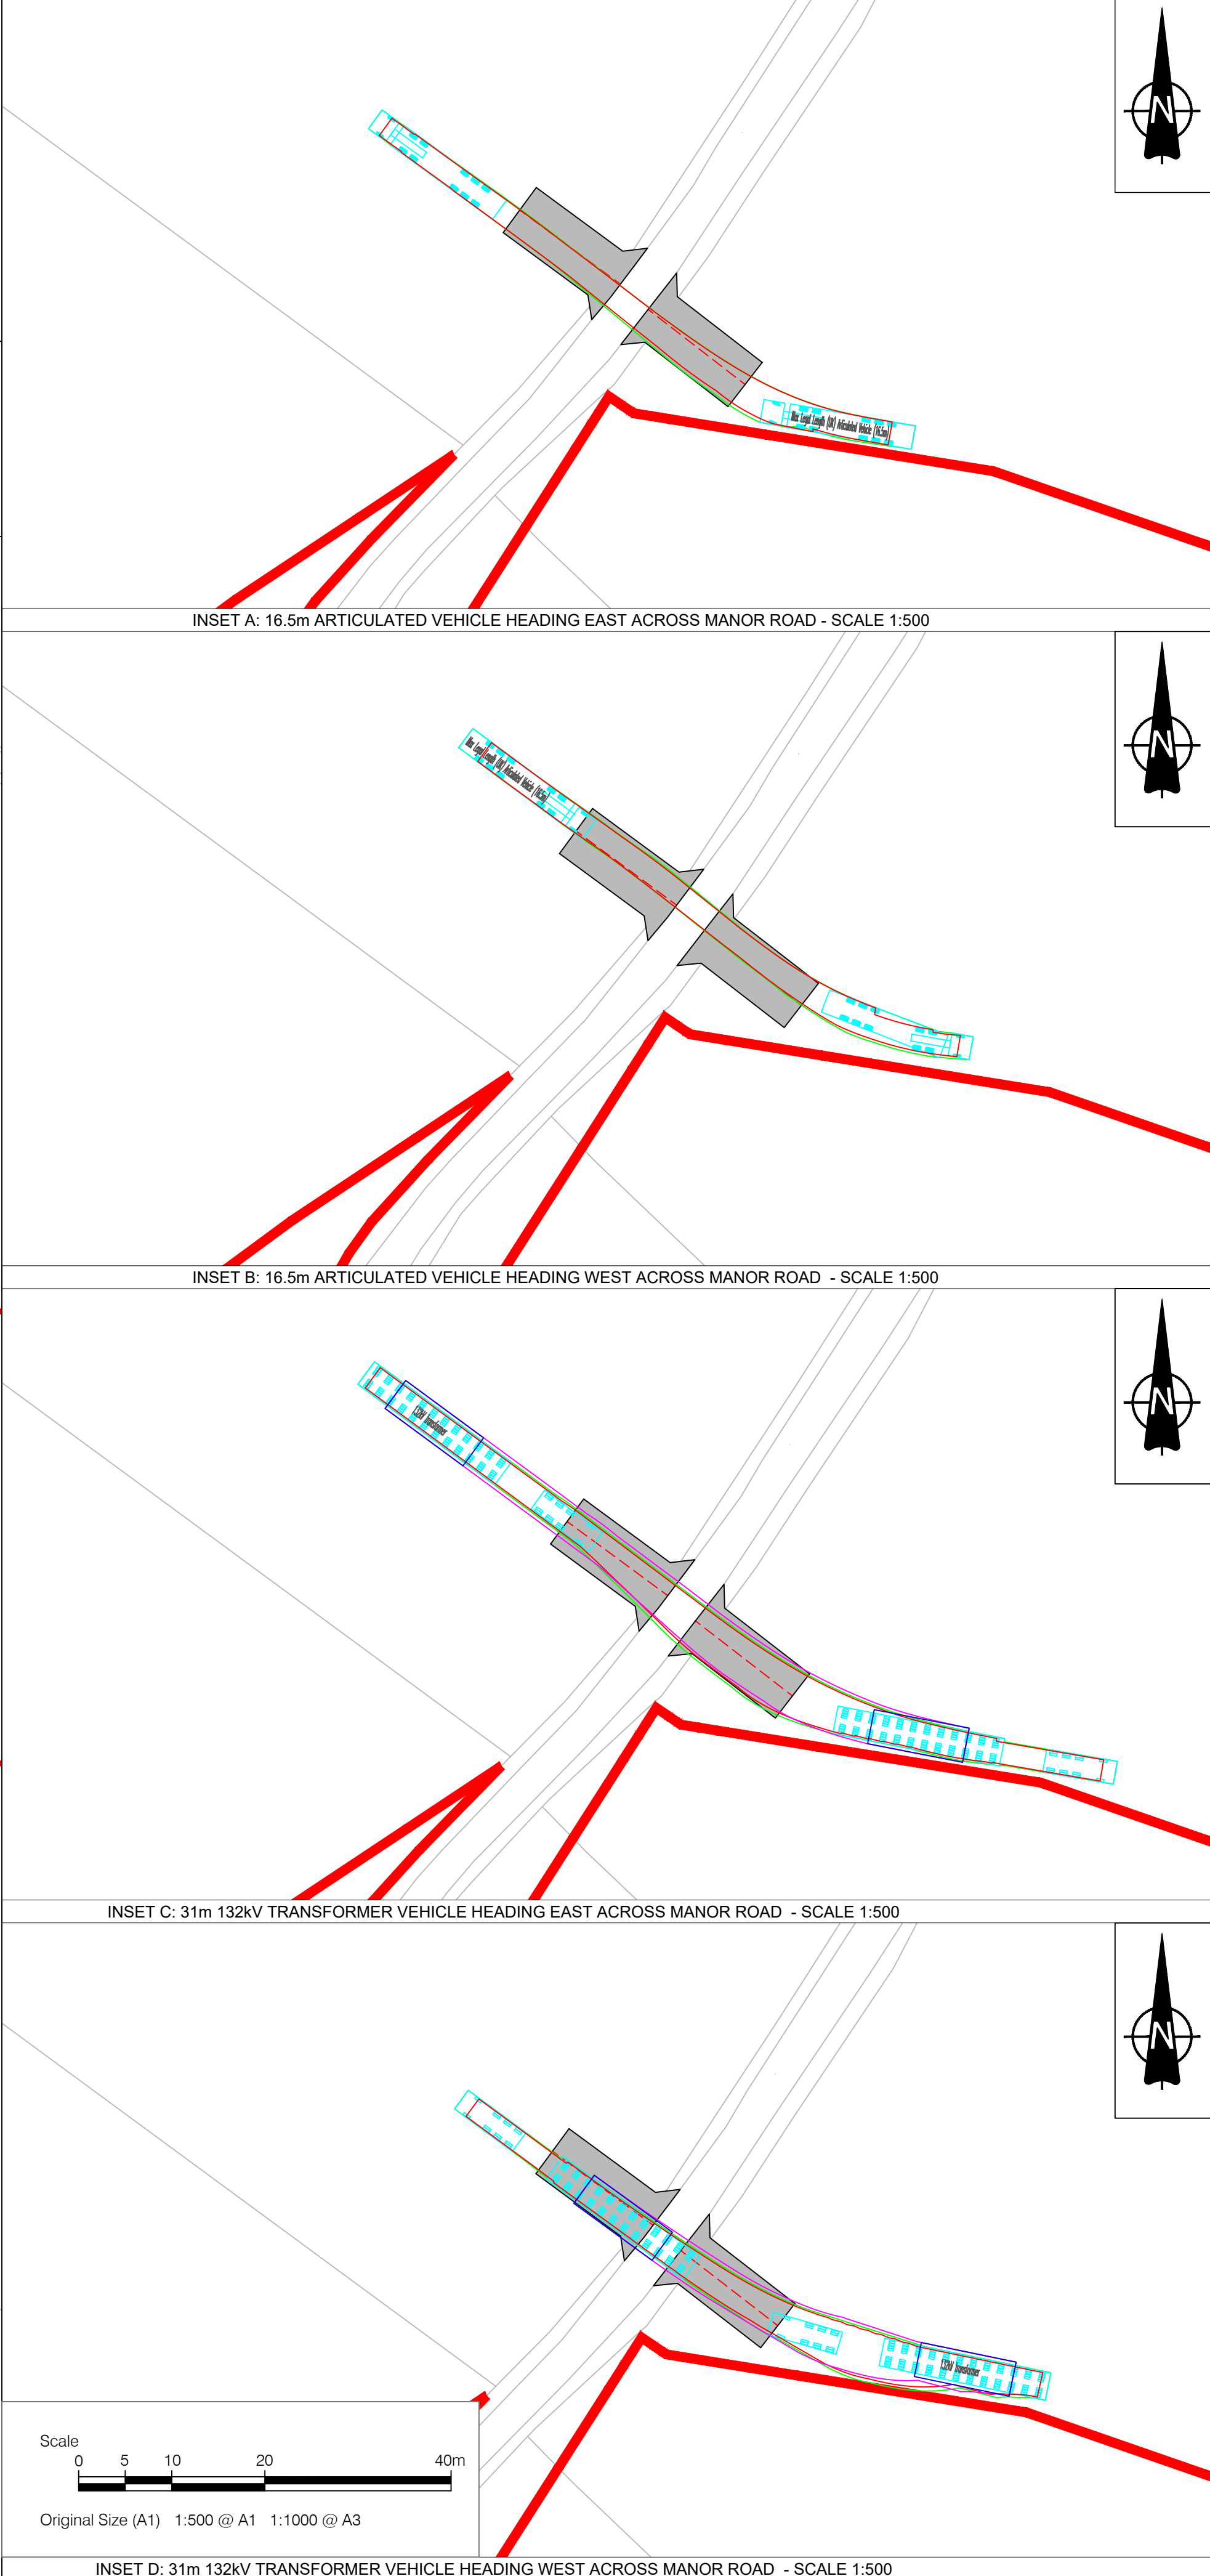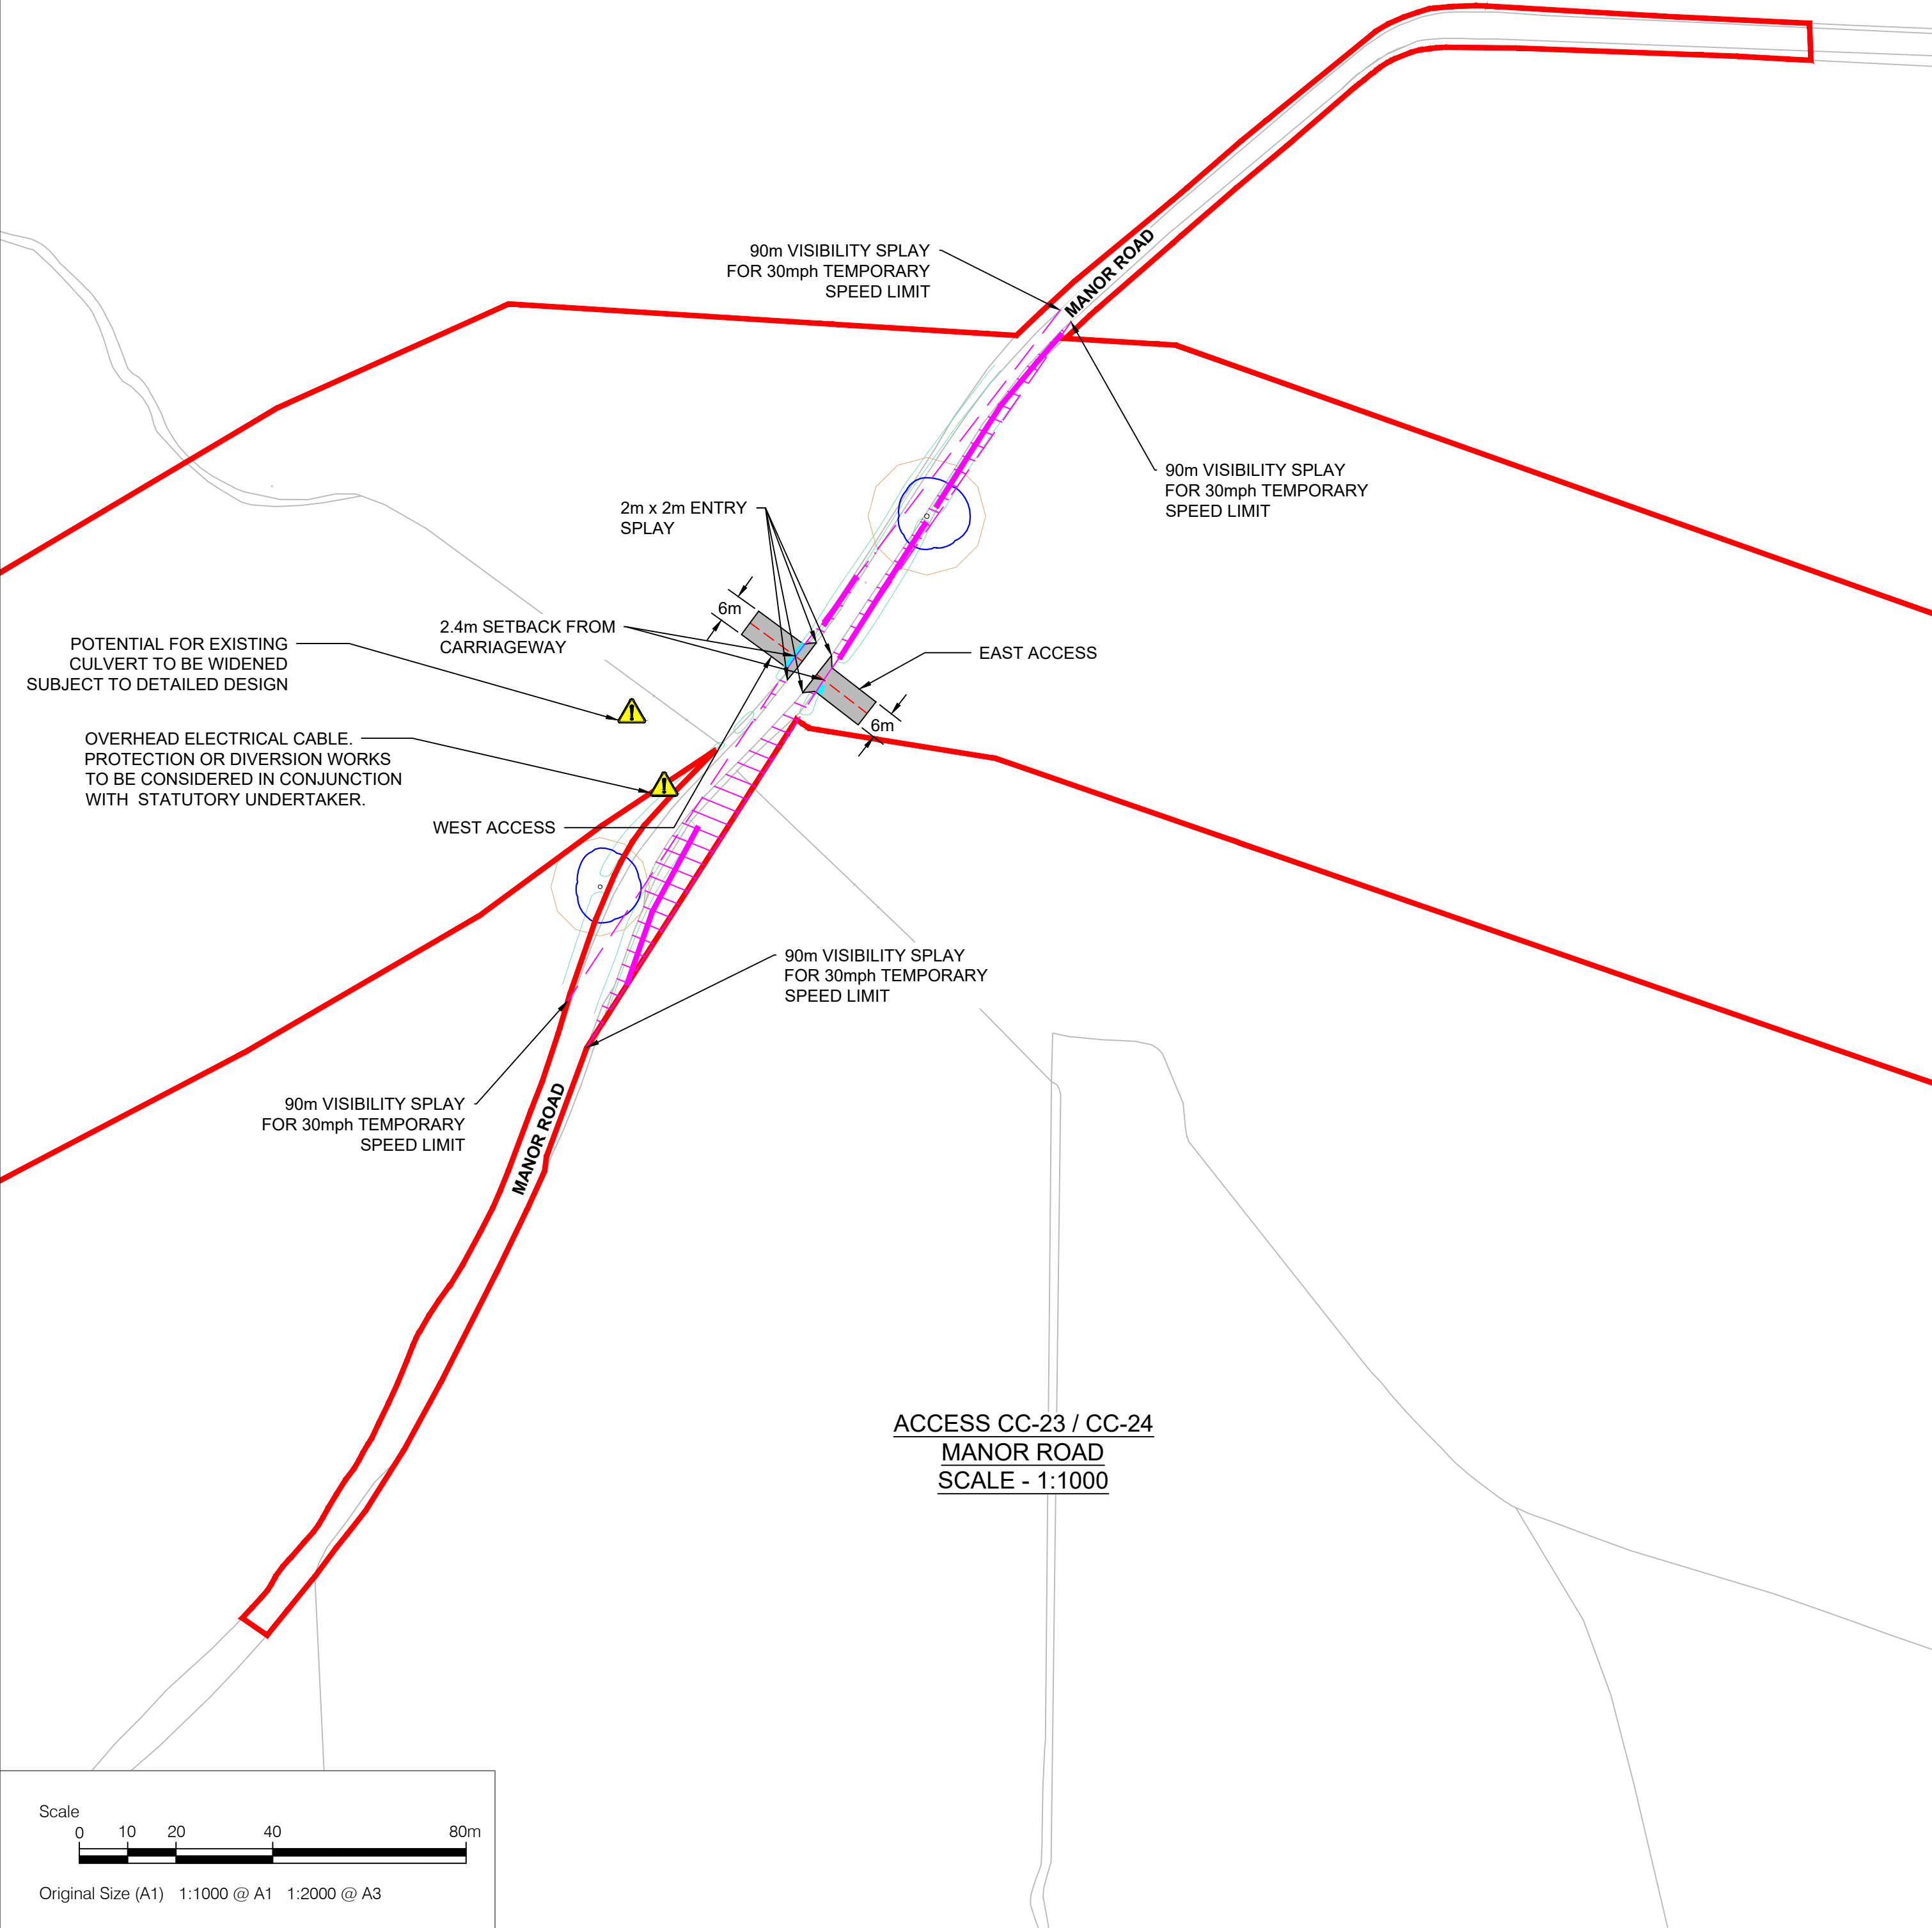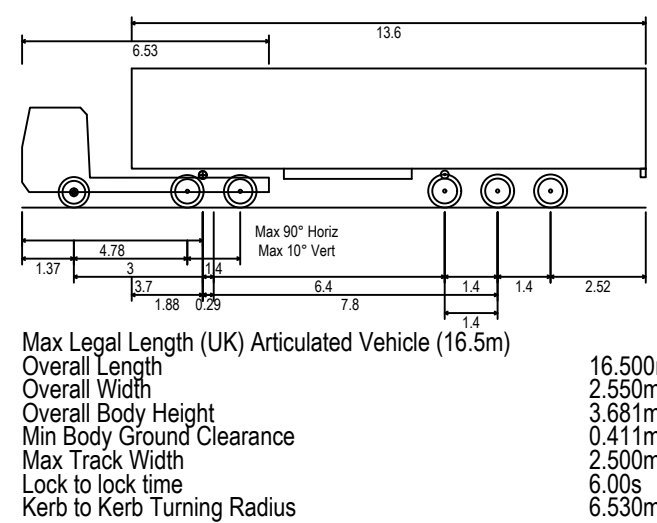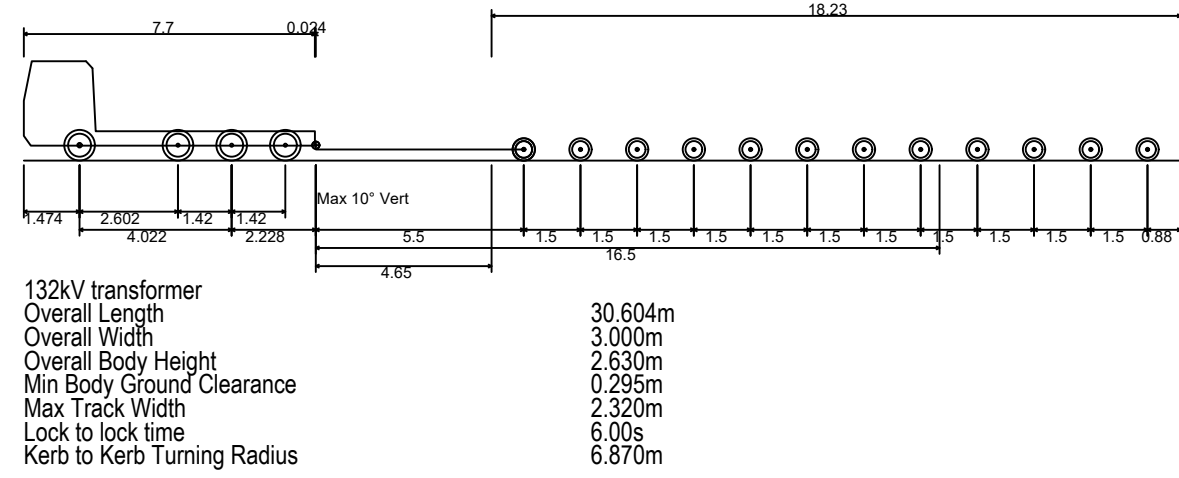

- NOTES**
- This drawing is to be read in conjunction with all other relevant documentation.
 - Do not scale from this drawing, use only printed dimensions.
 - All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
 - This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
 - Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
 - The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
 - Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
 - Junction visibility for the access is based upon DMRB CD109 Table 2.10 on the basis of a 30mph temporary speed limit being enforced.

- LEGEND**
- Extent of Access Footprint
 - Order Limits
 - Land Excluded from Order Limits
 - Vehicle Body
 - Vehicle Body Path
 - Vehicle Load
 - Vehicle Load Path
 - Vehicle Wheels Path
 - Edge of Road
 - Access Centreline
 - Junction Visibility 30mph Temporary Speed Limit
 - Vegetation to be Removed 30mph Temporary Speed Limit Vis Splay
 - Indicative Hedgerow Removal 30mph Temporary Speed Limit
 - Indicative Hedgerow Removal for Bellmouth Access
 - Health and Safety Risk Identifier
 - Existing Public Right of Way

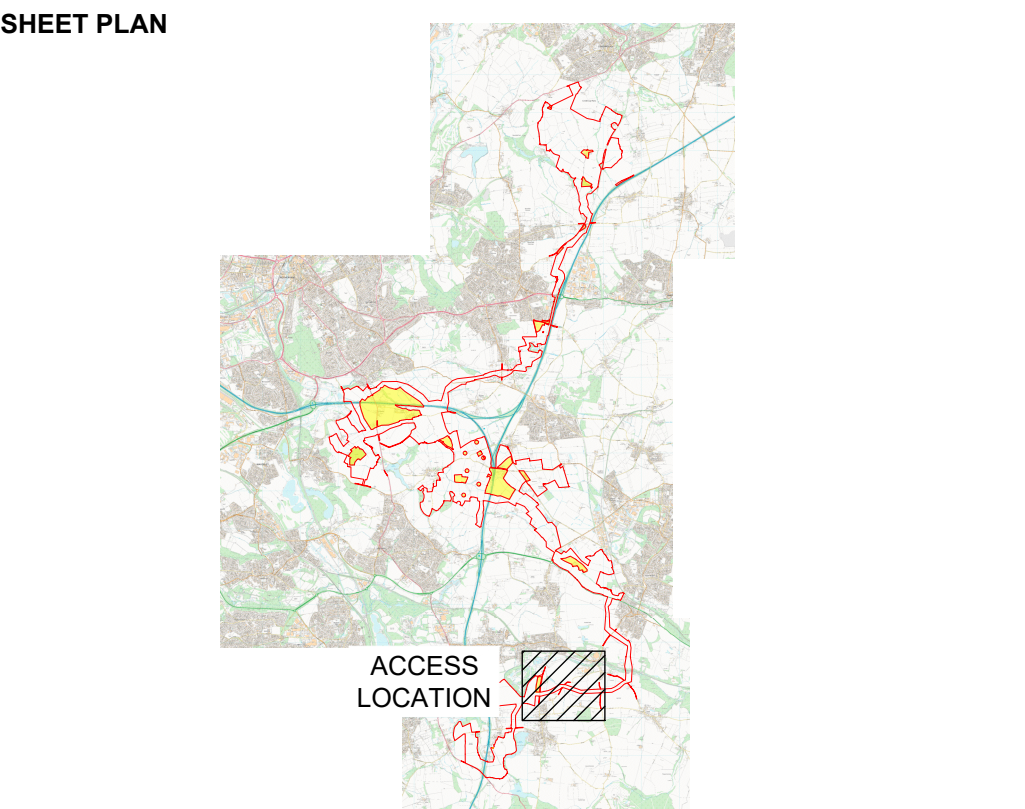

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:

Cable Corridor Area Access CC-23/24
Appendix 3 - Sheet 47 of 53
Whitestone Solar Farm
Regulation 5(2)(o)

DRAWING DATE: 03/06/2026



SCALE: AS SHOWN	SHEET: Sheet 47 of 53
SIZE: A1	REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12


APPLICATION NUMBER: EN0110020


WHITESTONE
solar farm

EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012	
RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

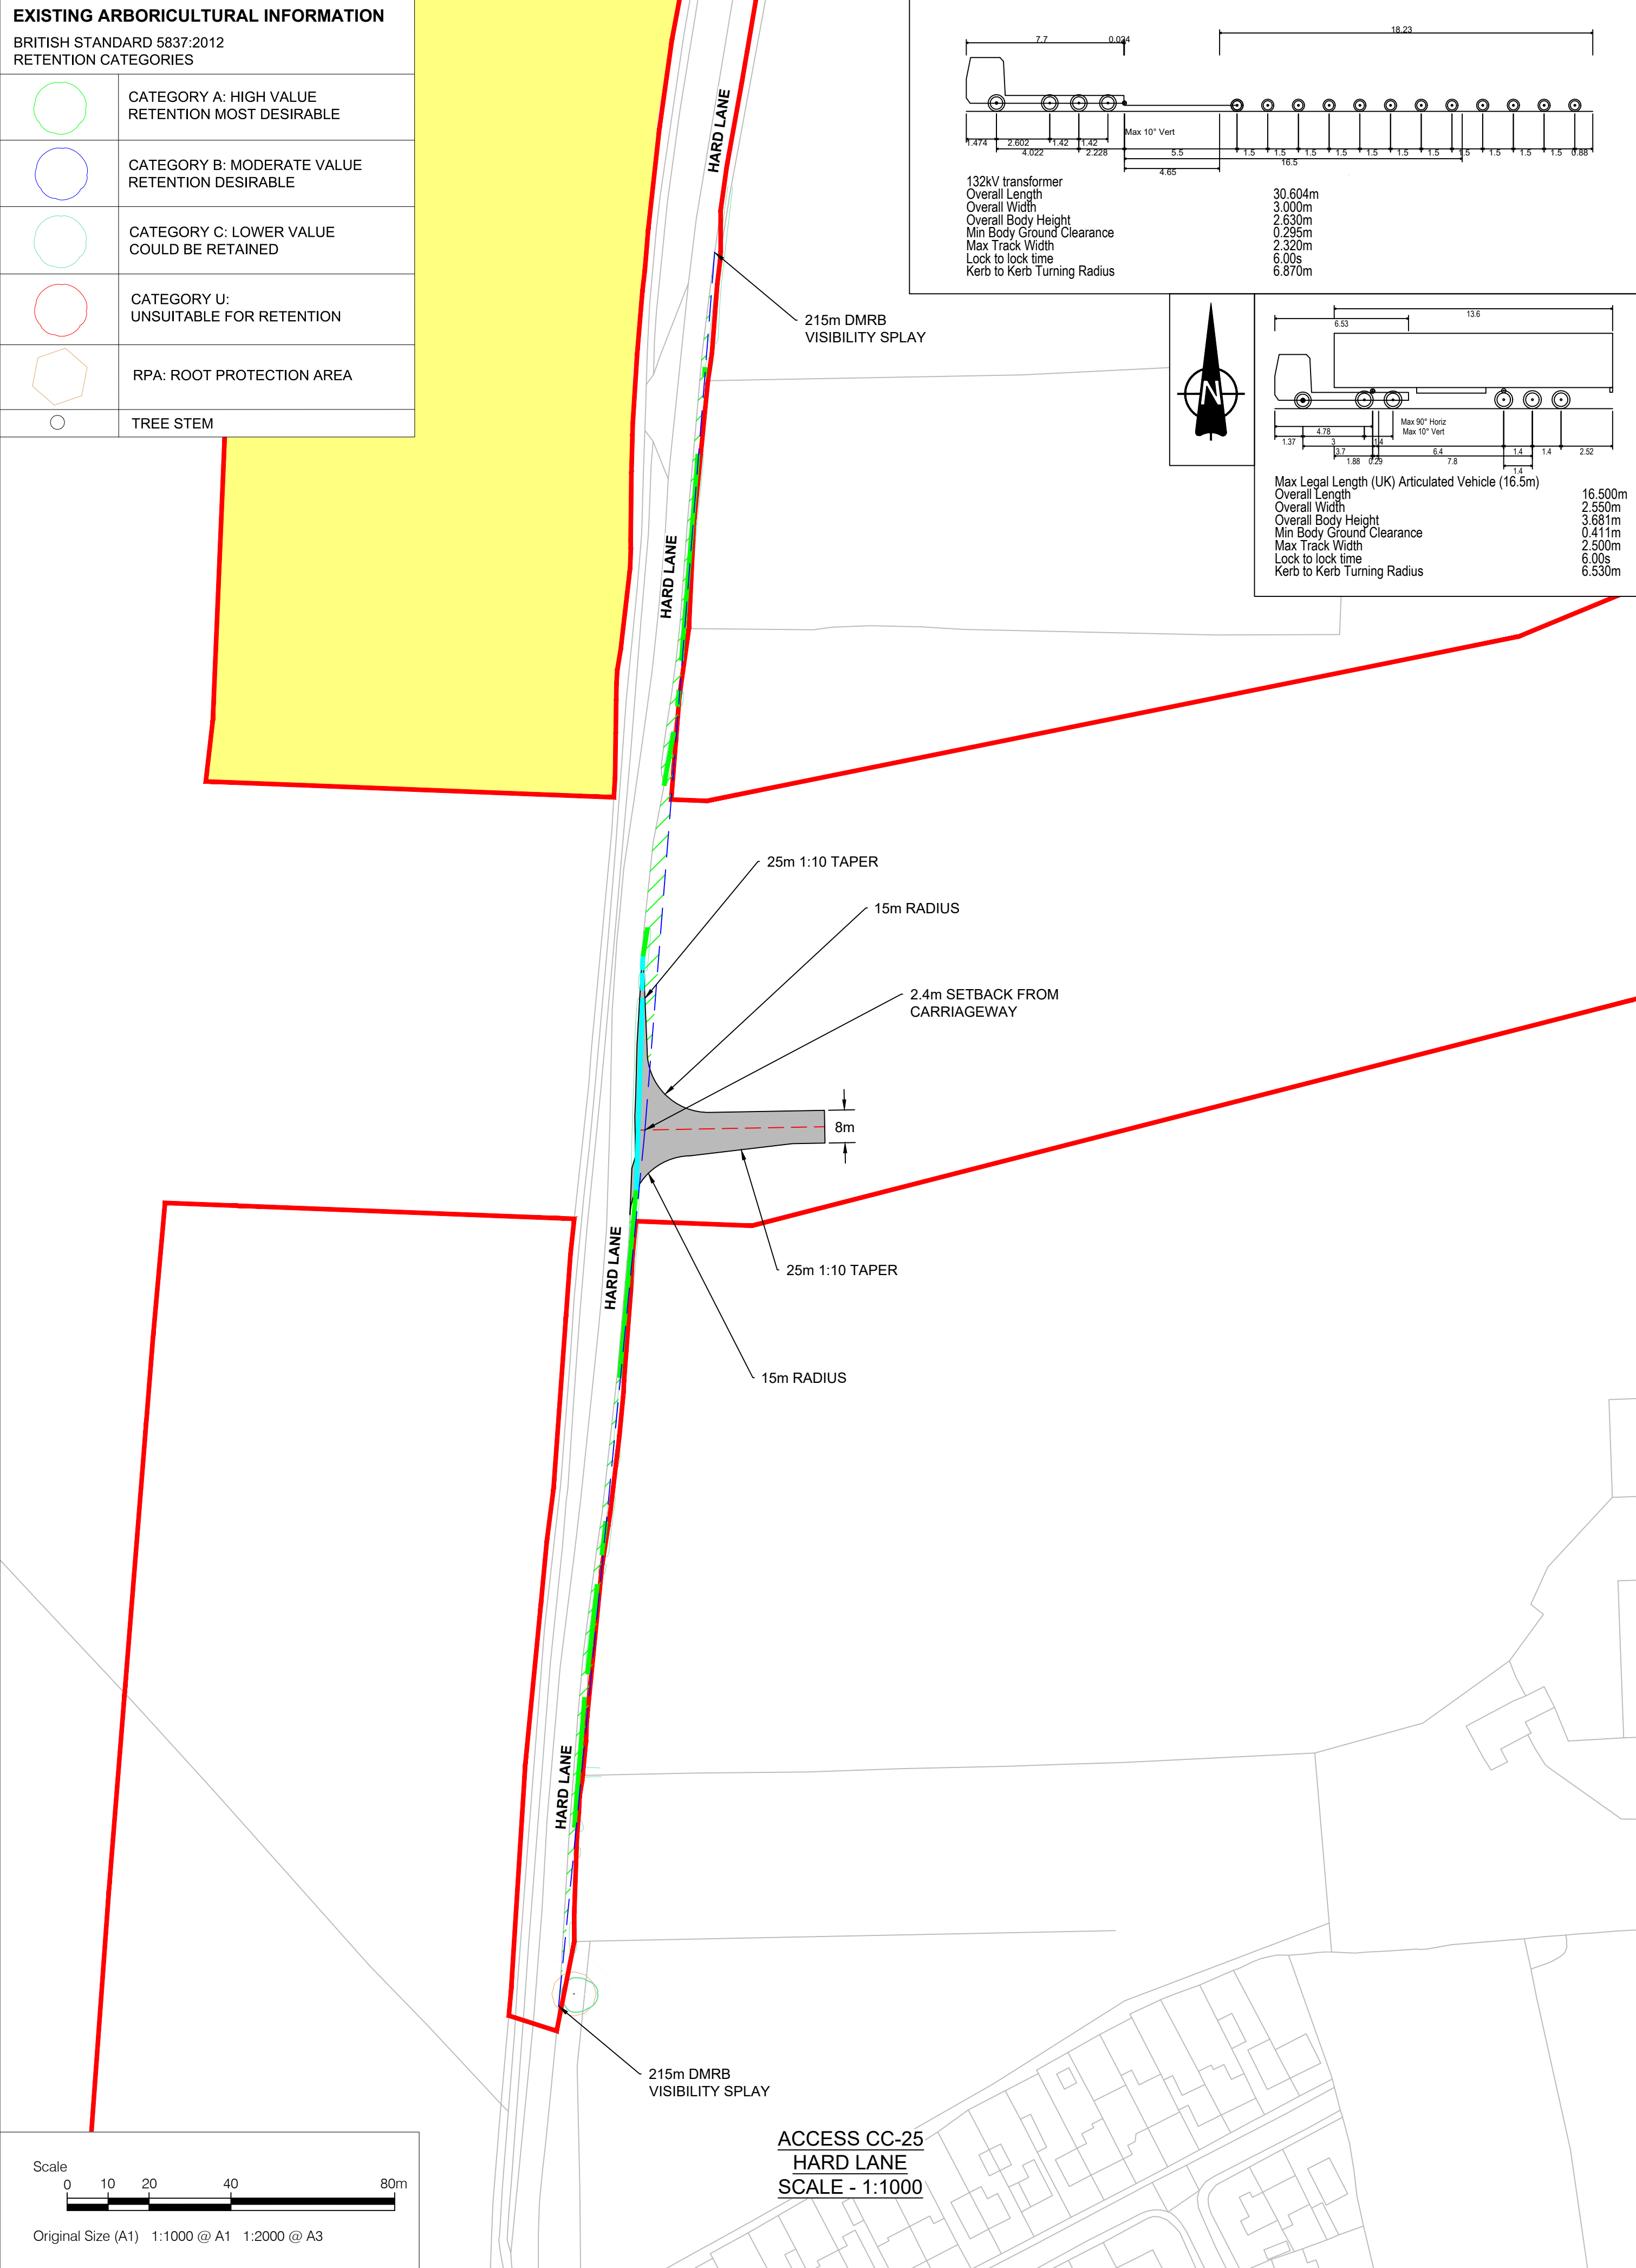


Sources: Esri, TomTom, Garmin, FAO, NOAA, USGS, © OpenStreetMap contributors, and the GIS User Community. Reproduced from Ordnance Survey digital map data © Crown copyright 2026. All rights reserved. License number 0000848182

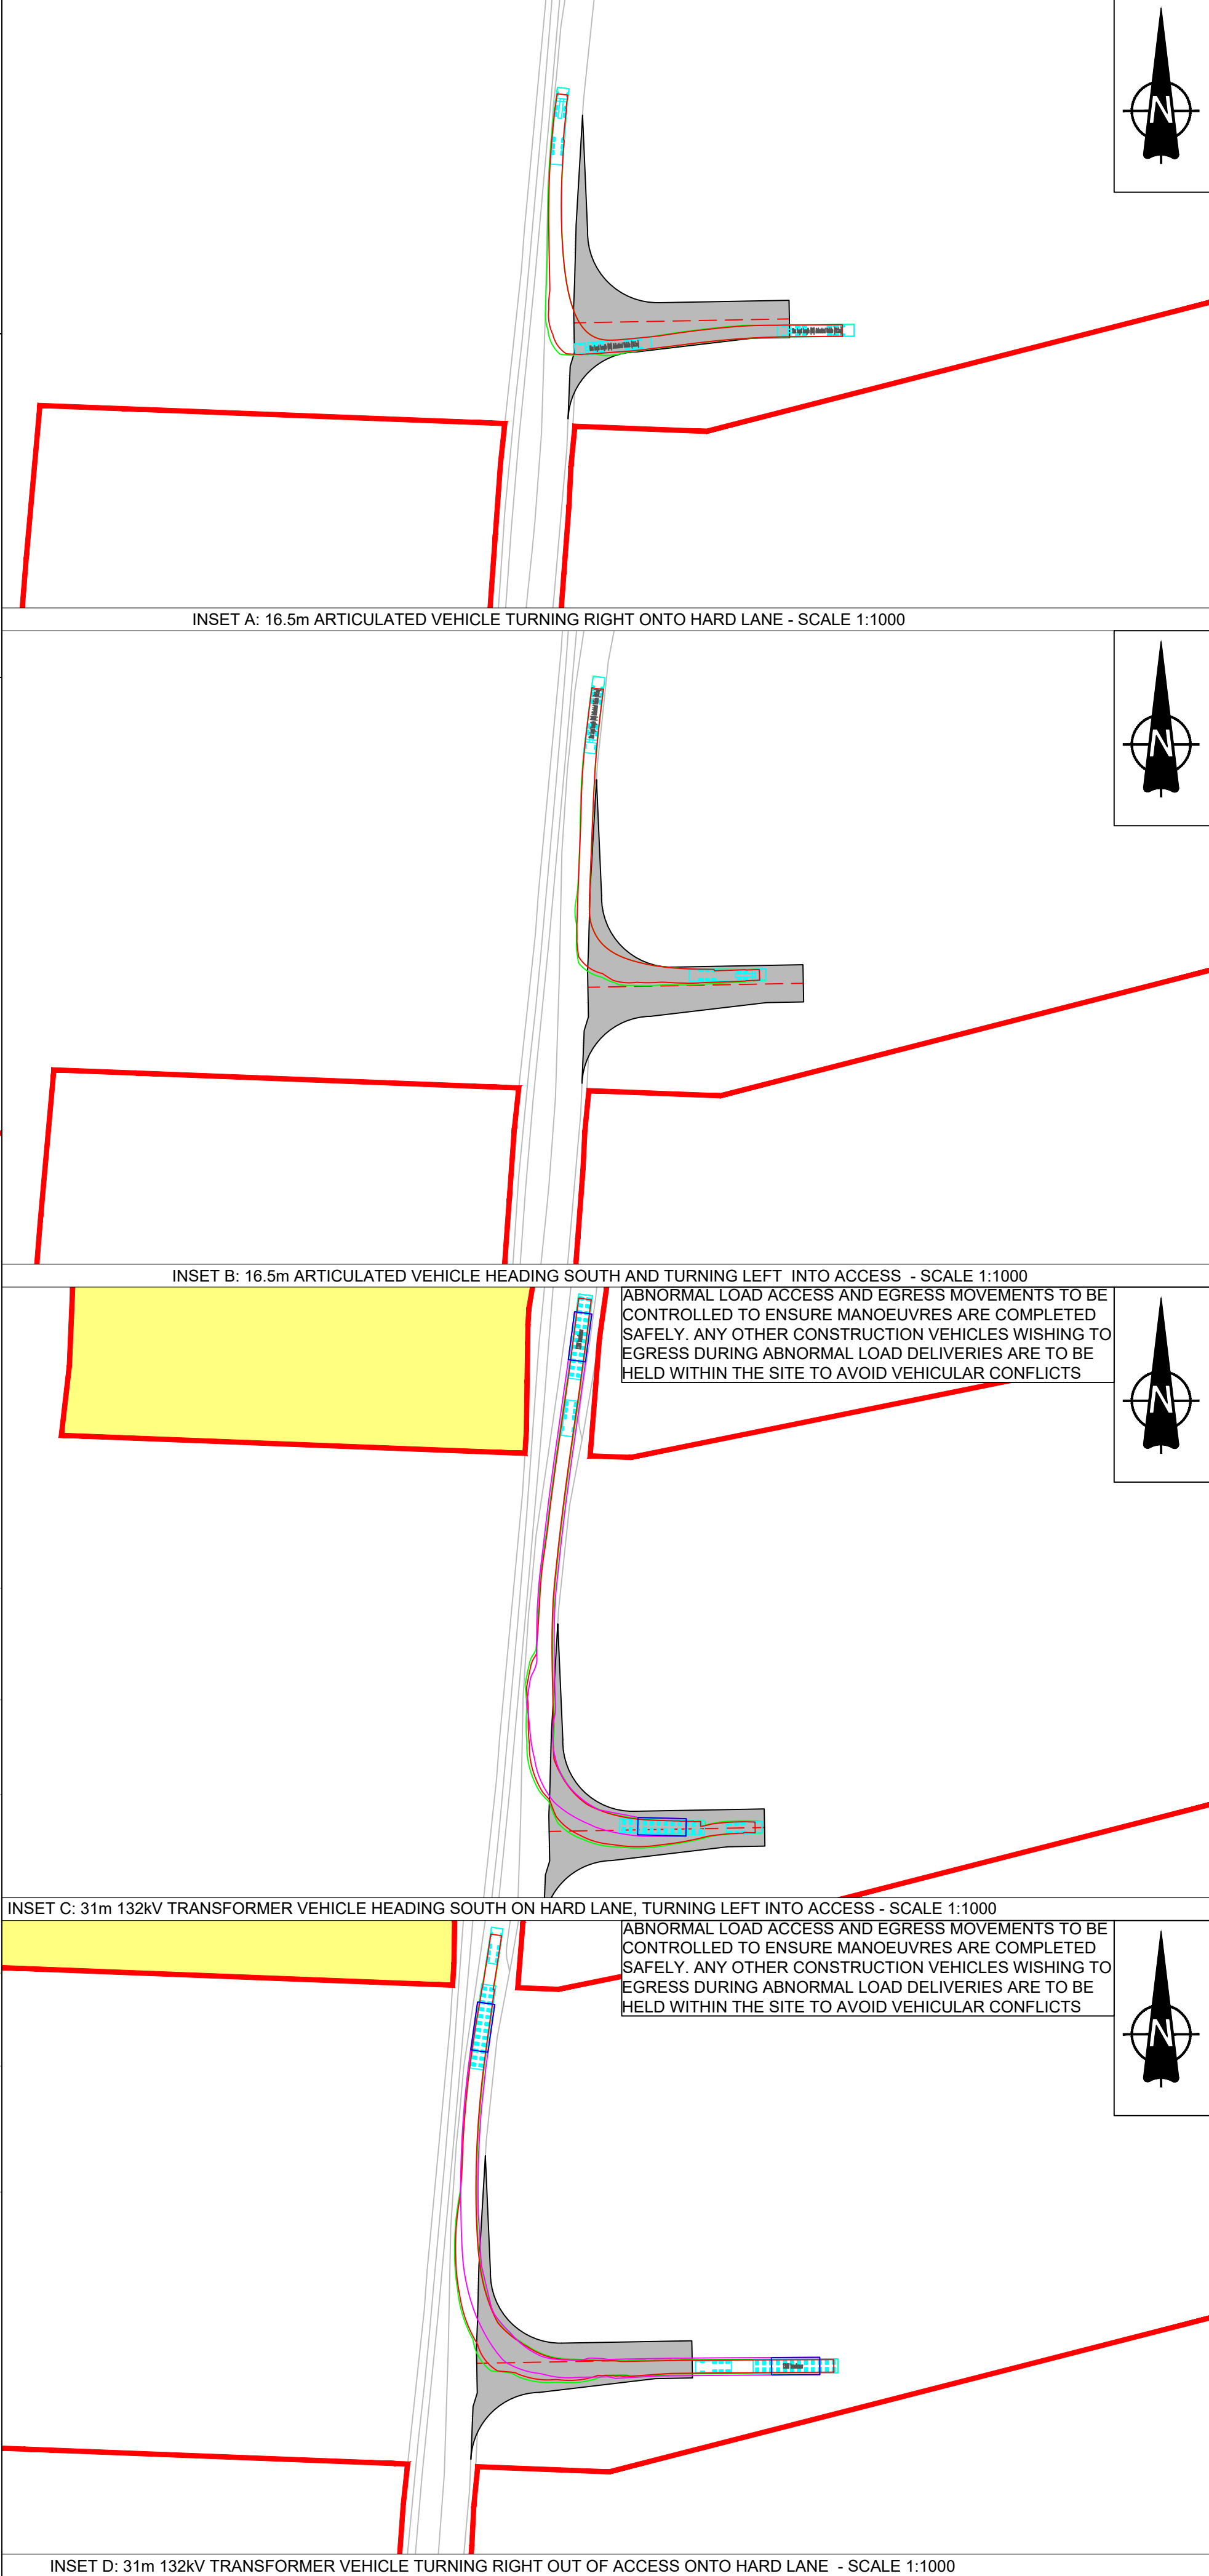

- NOTES**
- This drawing is to be read in conjunction with all other relevant documentation.
 - Do not scale from this drawing, use only printed dimensions.
 - All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
 - This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
 - Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
 - The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
 - Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
 - Junction visibility for the access is based upon DMRB CD109 Table 2.10.

- LEGEND**
- Extent of Access Footprint
 - Order Limits
 - Land Excluded from Order Limits
 - Vehicle Body
 - Vehicle Body Path
 - Vehicle Load
 - Vehicle Load Path
 - Vehicle Wheels Path
 - Edge of Road
 - Access Centreline
 - Junction Visibility
 - Vegetation to be Removed for Vis Splay
 - Indicative Hedgerow Removal Vis Splay
 - Indicative Hedgerow Removal for Bellmouth Access
 - Health and Safety Risk Identifier
 - Existing Public Right of Way

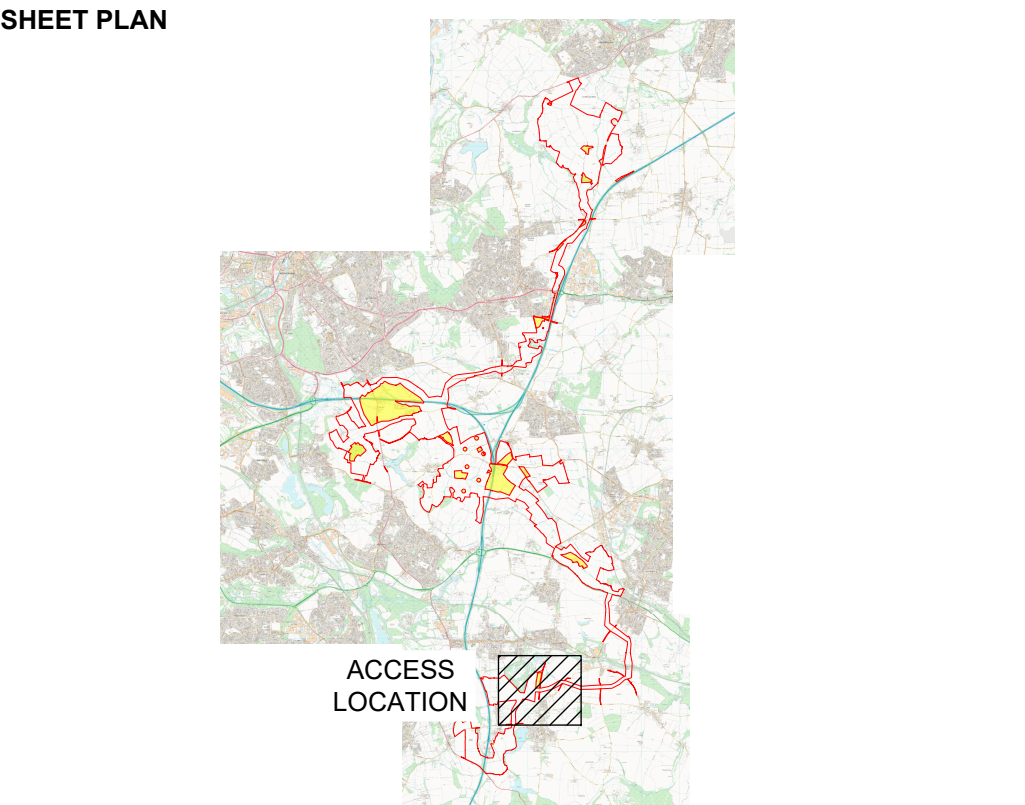

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:
Cable Corridor Area Access CC-25
Appendix 3 - Sheet 48 of 53
Whitestone Solar Farm
Regulation 5(2)(o)

DRAWING DATE: 03/06/2026

SCALE: 1:1000
SIZE: A1


SHEET: Sheet 48 of 53
REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020




EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012	
RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

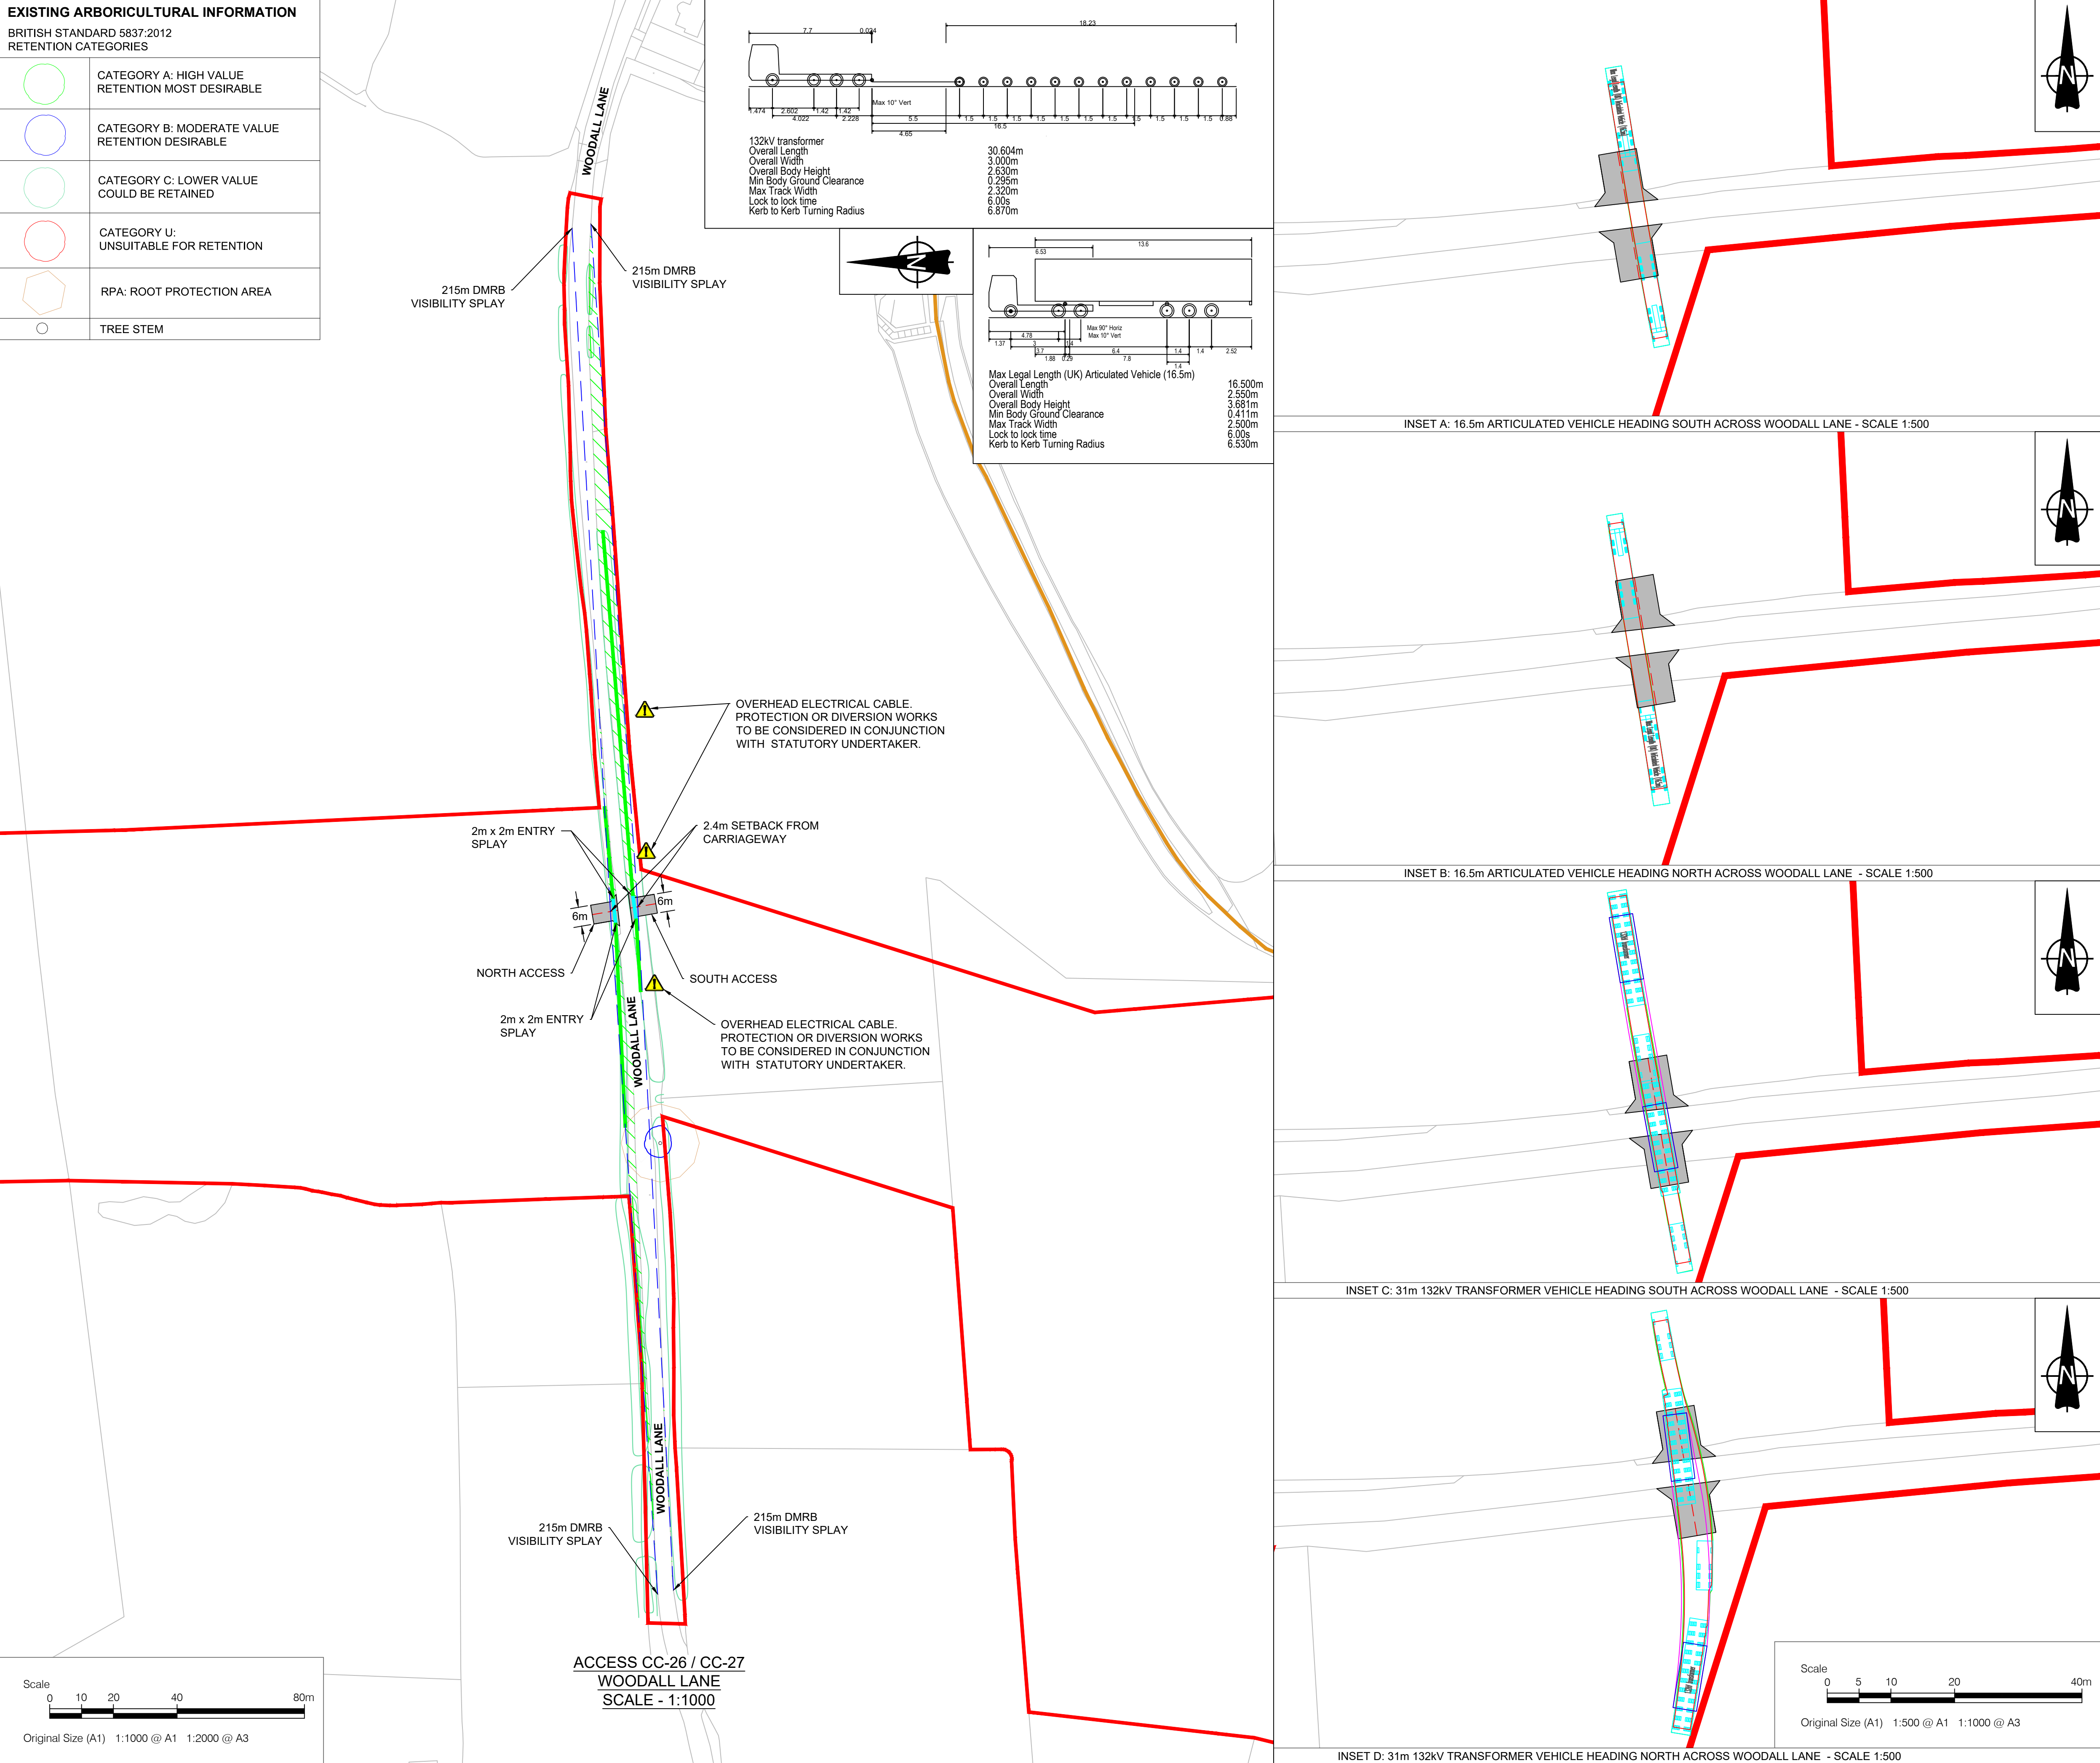

- NOTES**
1. This drawing is to be read in conjunction with all other relevant documentation.
 2. Do not scale from this drawing, use only printed dimensions.
 3. All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
 4. This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
 5. Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
 6. The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
 7. Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
 8. Junction visibility for the access is based upon DMRB CD109 Table 2.10.

- LEGEND**
- Extent of Access Footprint
 - Order Limits
 - Land Excluded from Order Limits
 - Vehicle Body
 - Vehicle Body Path
 - Vehicle Load
 - Vehicle Load Path
 - Vehicle Wheels Path
 - Edge of Road
 - Access Centreline
 - Junction Visibility
 - Vegetation to be Removed for Vis Splay
 - Indicative Hedgerow Removal Vis Splay
 - Indicative Hedgerow Removal for Bellmouth Access
 - Health and Safety Risk Identifier
 - Existing Public Right of Way

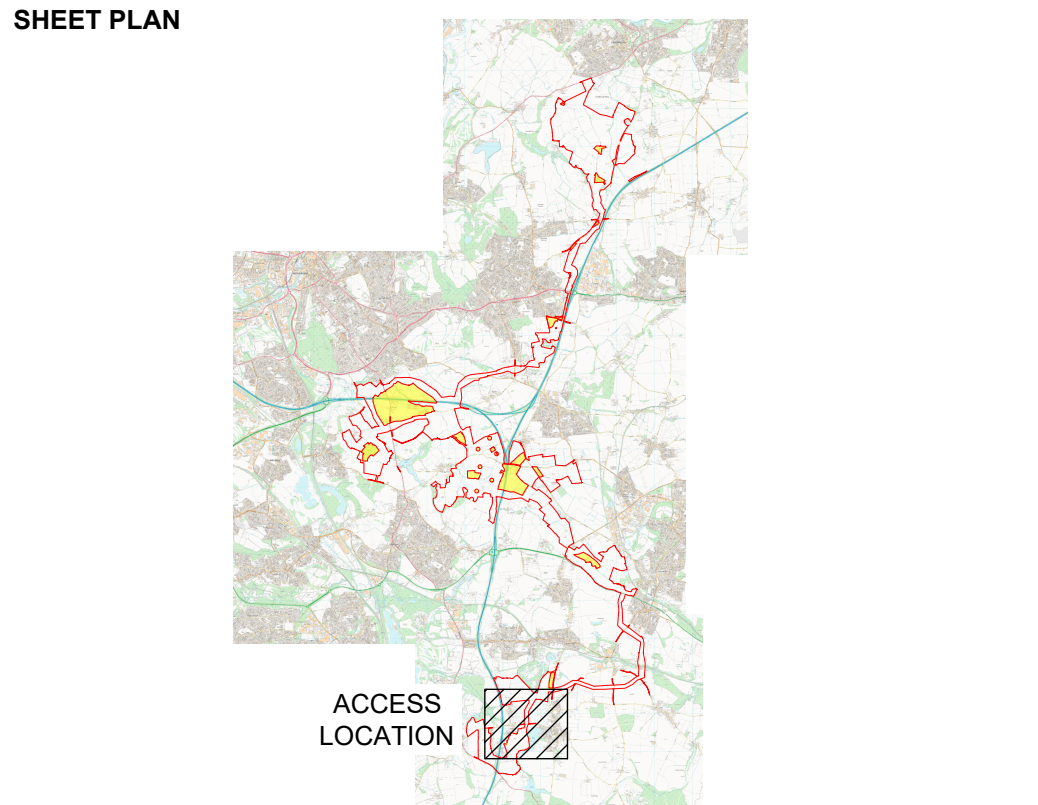

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:
Cable Corridor Area Access CC-26/27
Appendix 3 - Sheet 49 of 53
Whitestone Solar Farm
Regulation 5(2)(o)

DRAWING DATE: 03/06/2026




SCALE: AS SHOWN	SHEET: Sheet 49 of 53
SIZE: A1	REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020



EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012 RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

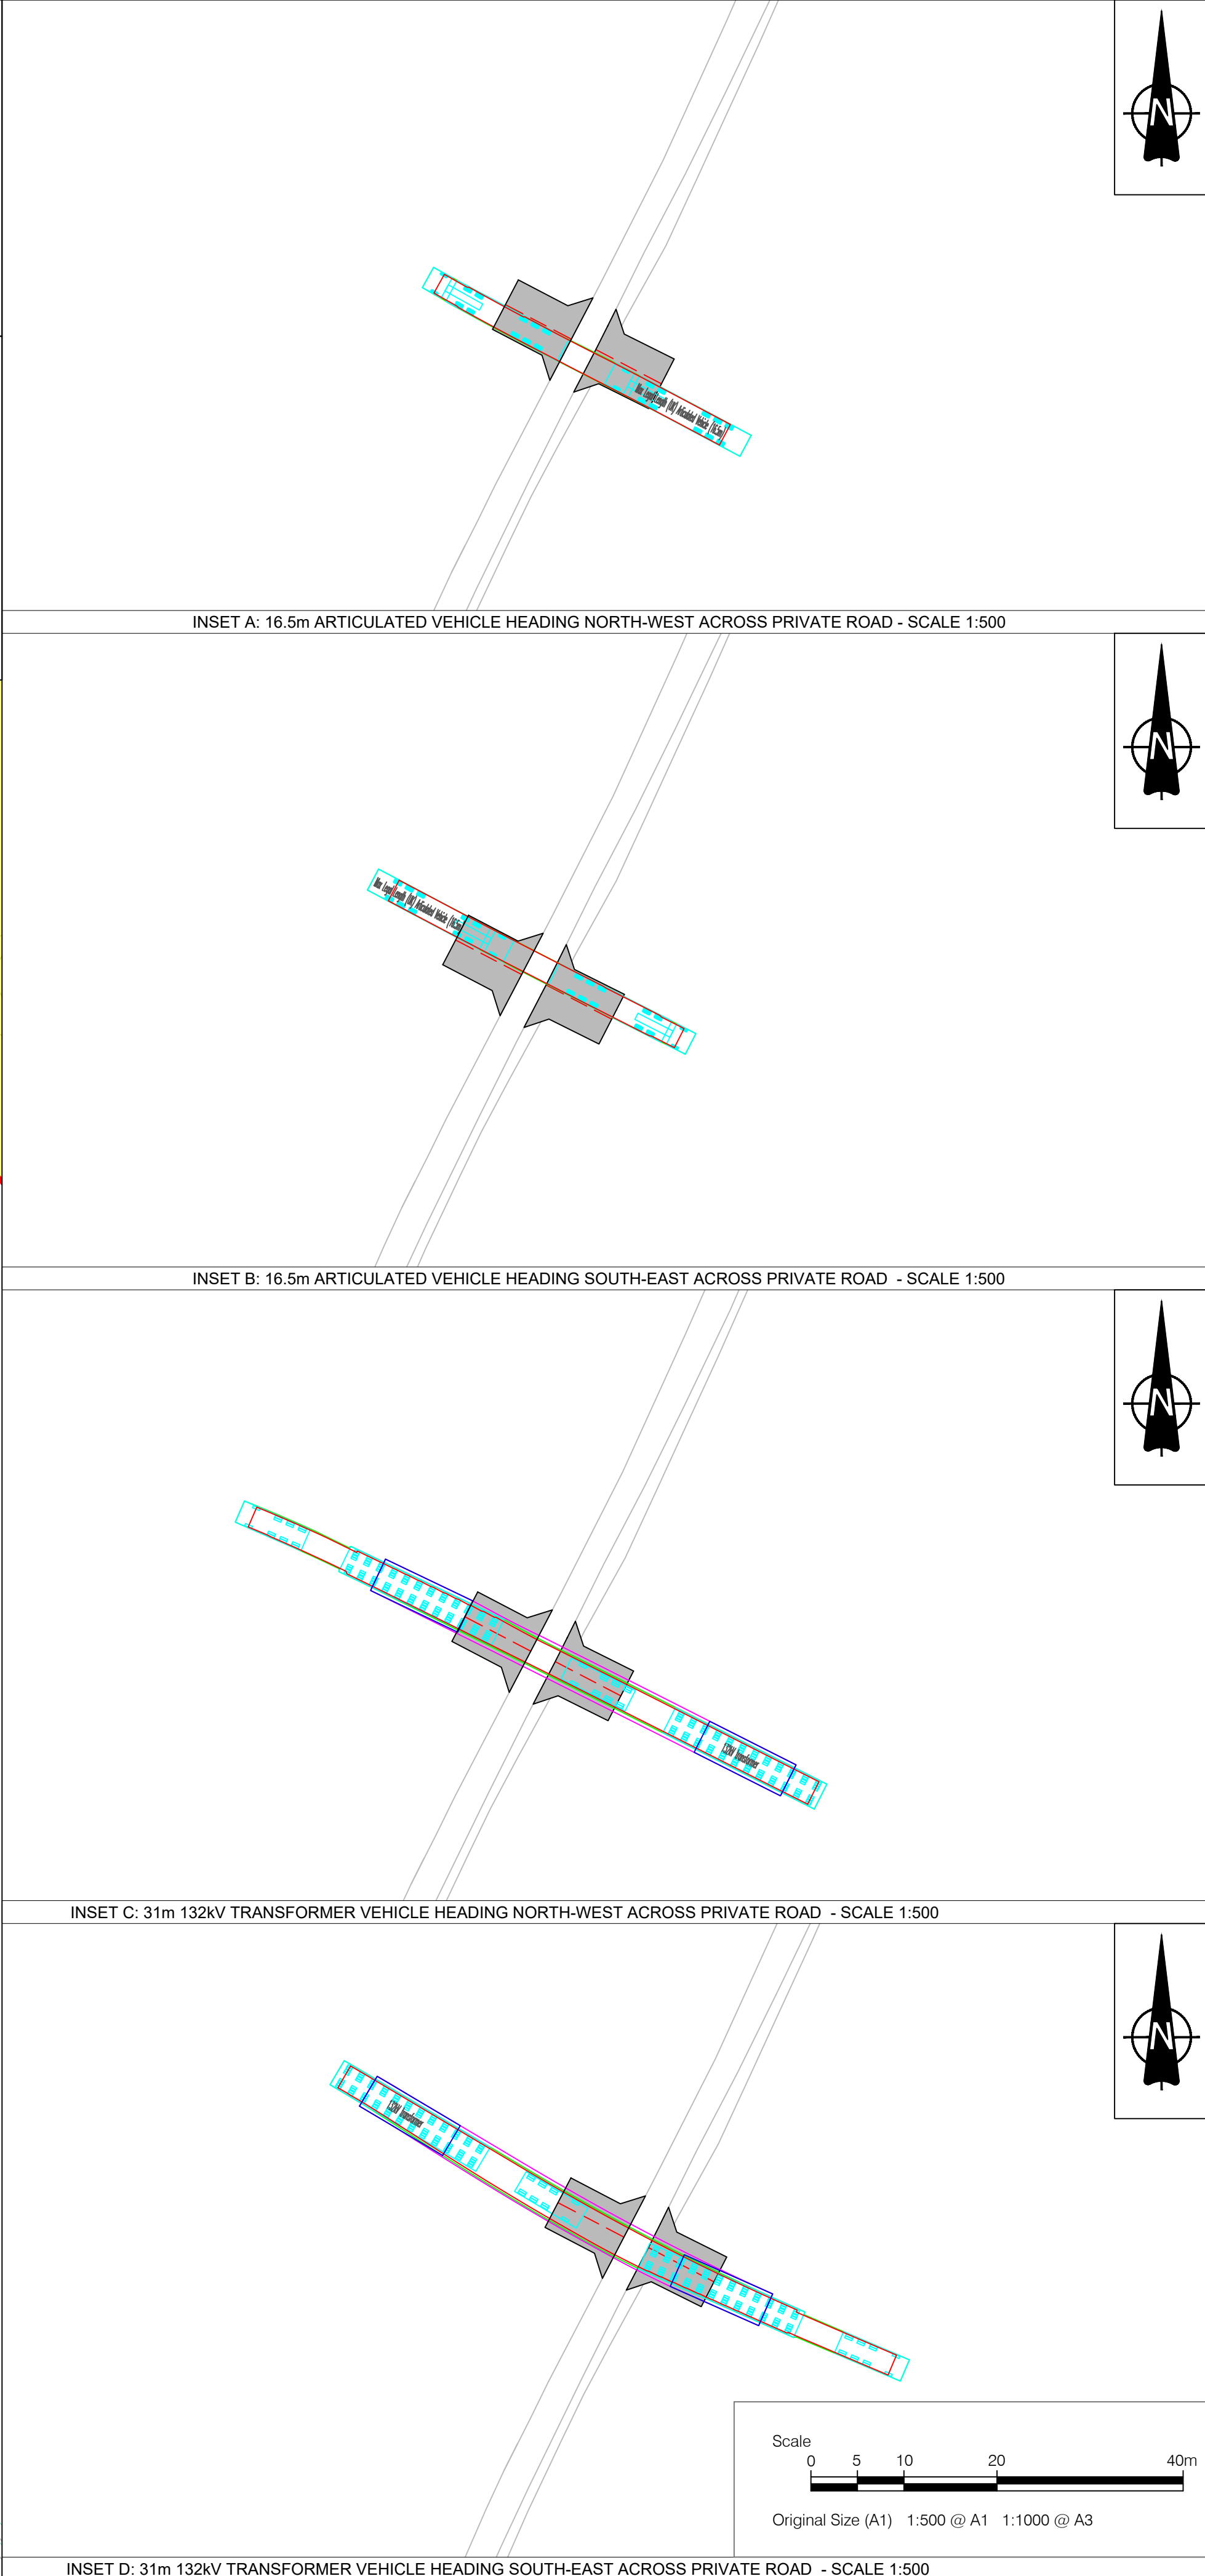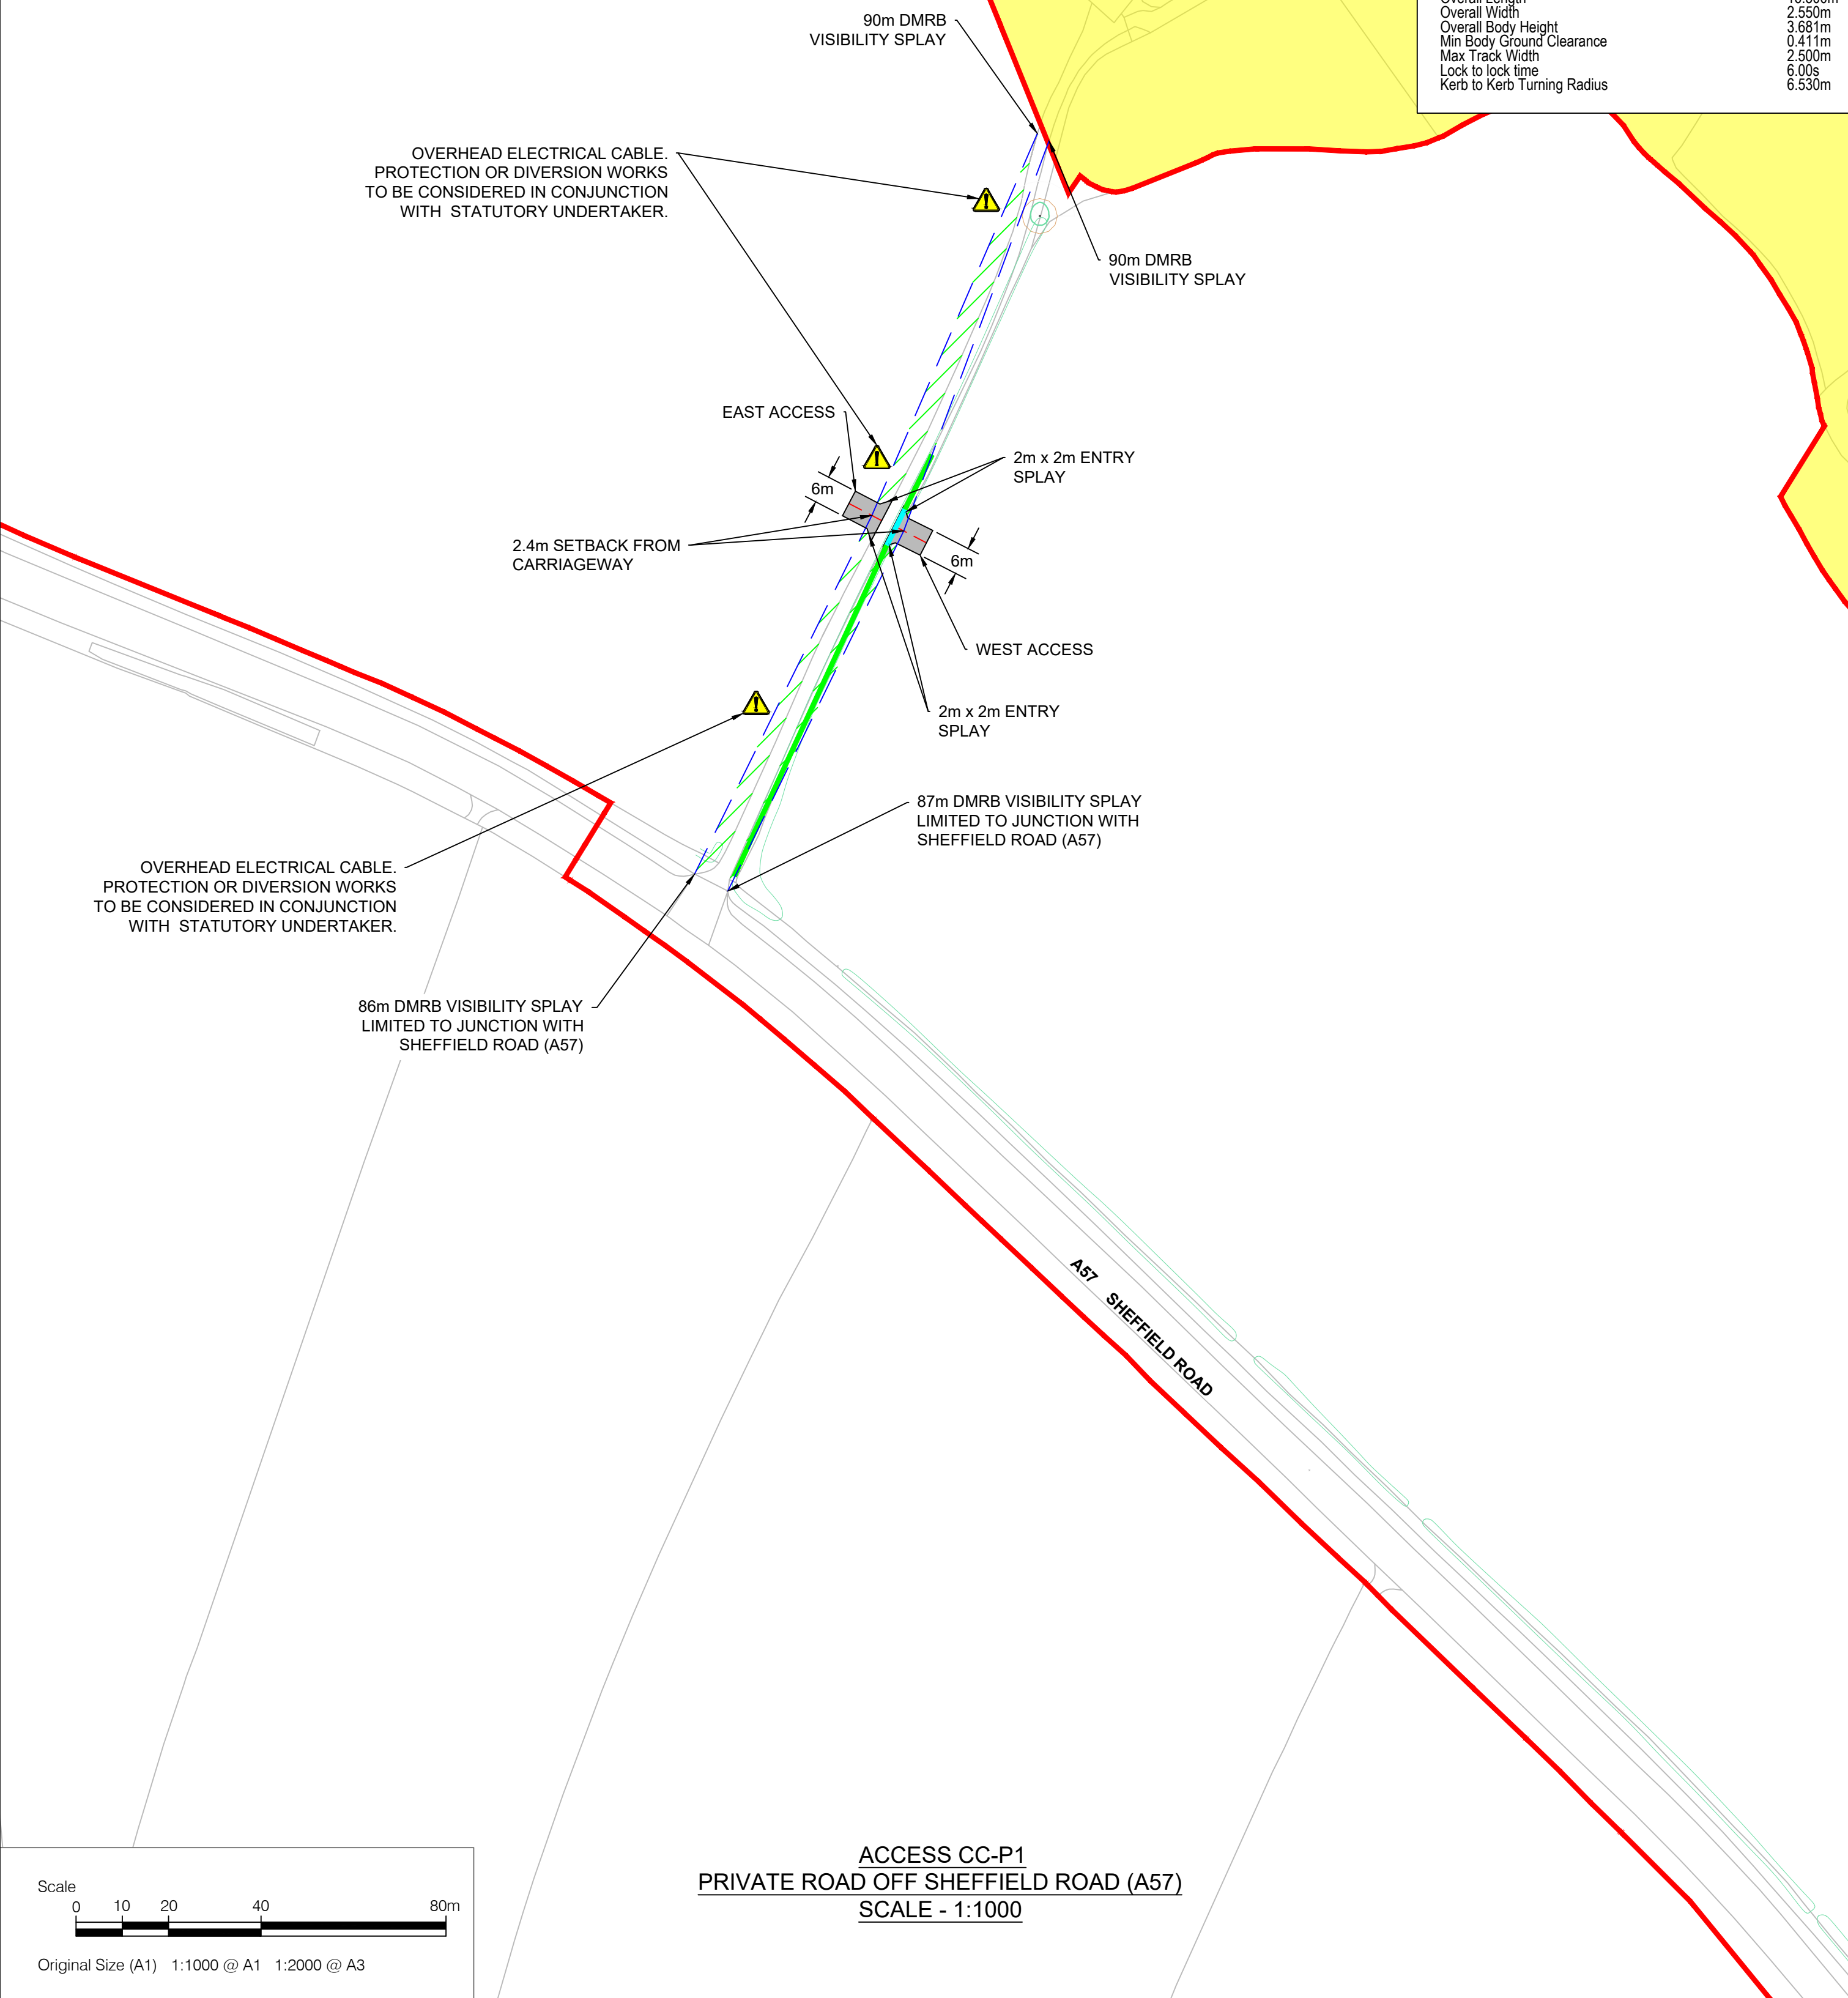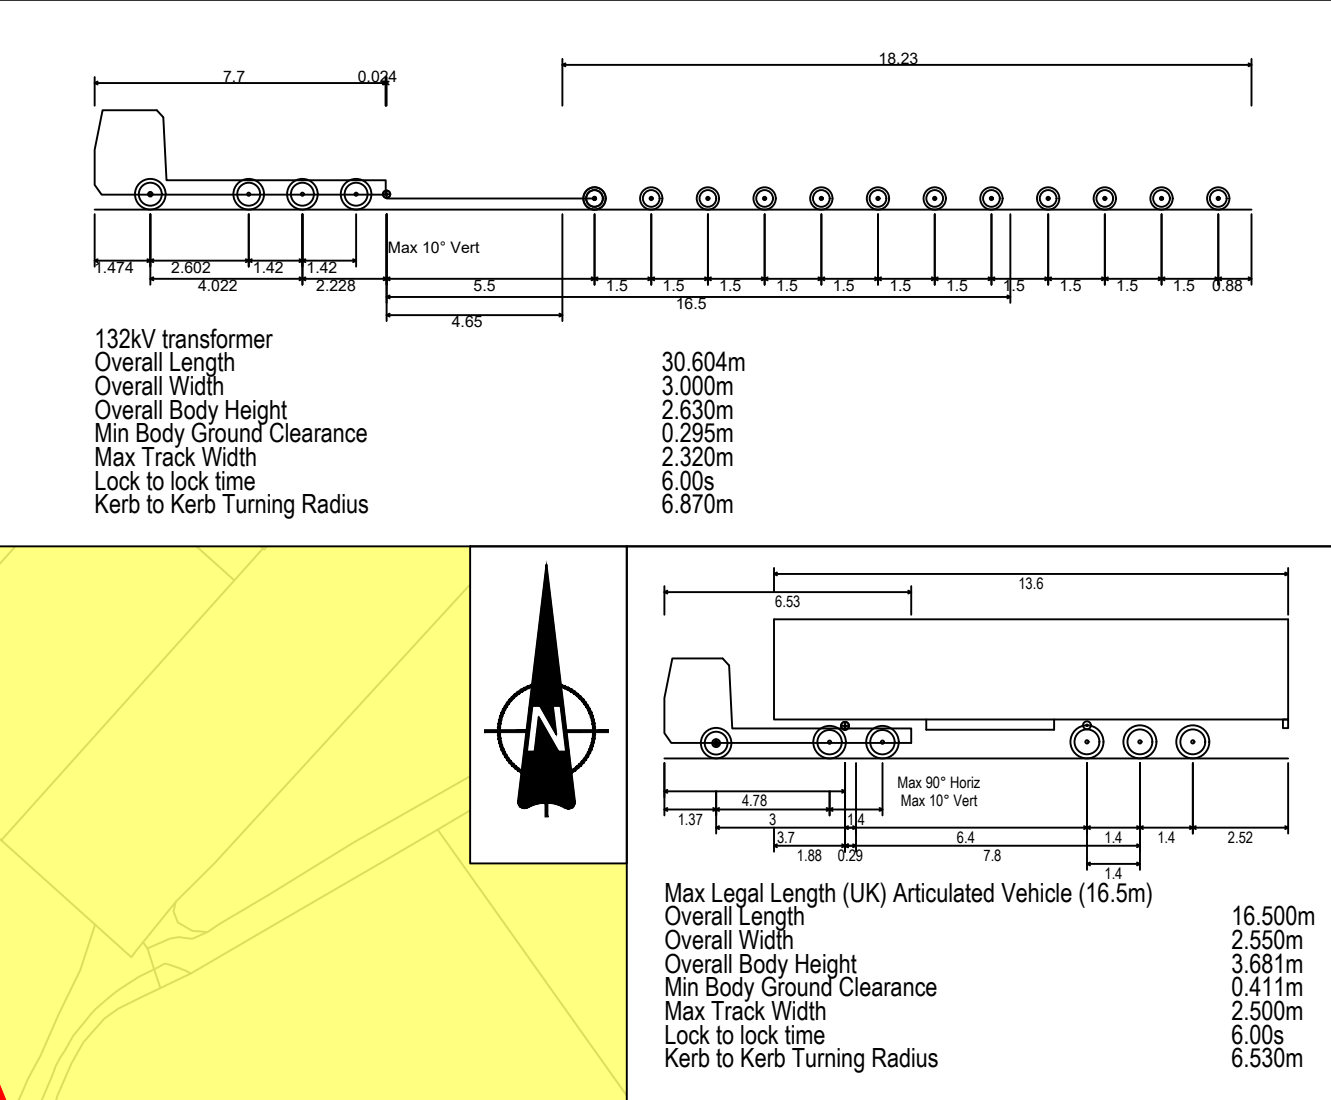

- NOTES**
- This drawing is to be read in conjunction with all other relevant documentation.
 - Do not scale from this drawing, use only printed dimensions.
 - All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
 - This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
 - Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
 - The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
 - Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
 - Junction visibility for the access is based upon DMRB CD109 Table 2.10.
- LEGEND**
- Extent of Access Footprint
 - Order Limits
 - Land Excluded from Order Limits
 - Vehicle Body
 - Vehicle Body Path
 - Vehicle Load
 - Vehicle Load Path
 - Vehicle Wheels Path
 - Edge of Road
 - Access Centreline
 - Junction Visibility
 - Vegetation to be Removed for Vis Splay
 - Indicative Hedgerow Removal Vis Splay
 - Indicative Hedgerow Removal for Bellmouth Access
 - Health and Safety Risk Identifier
 - Existing Public Right of Way

SHEET PLAN

ACCESS LOCATION

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:
Cable Corridor Area Access CC-P1
Appendix 3 - Sheet 50 of 53
Whitestone Solar Farm
Regulation 5(2)(o)

DRAWING DATE: 03/06/2026






SCALE: AS SHOWN	SHEET: Sheet 50 of 53
SIZE: A1	REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020

WHITESTONE
solar farm

EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012	
RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

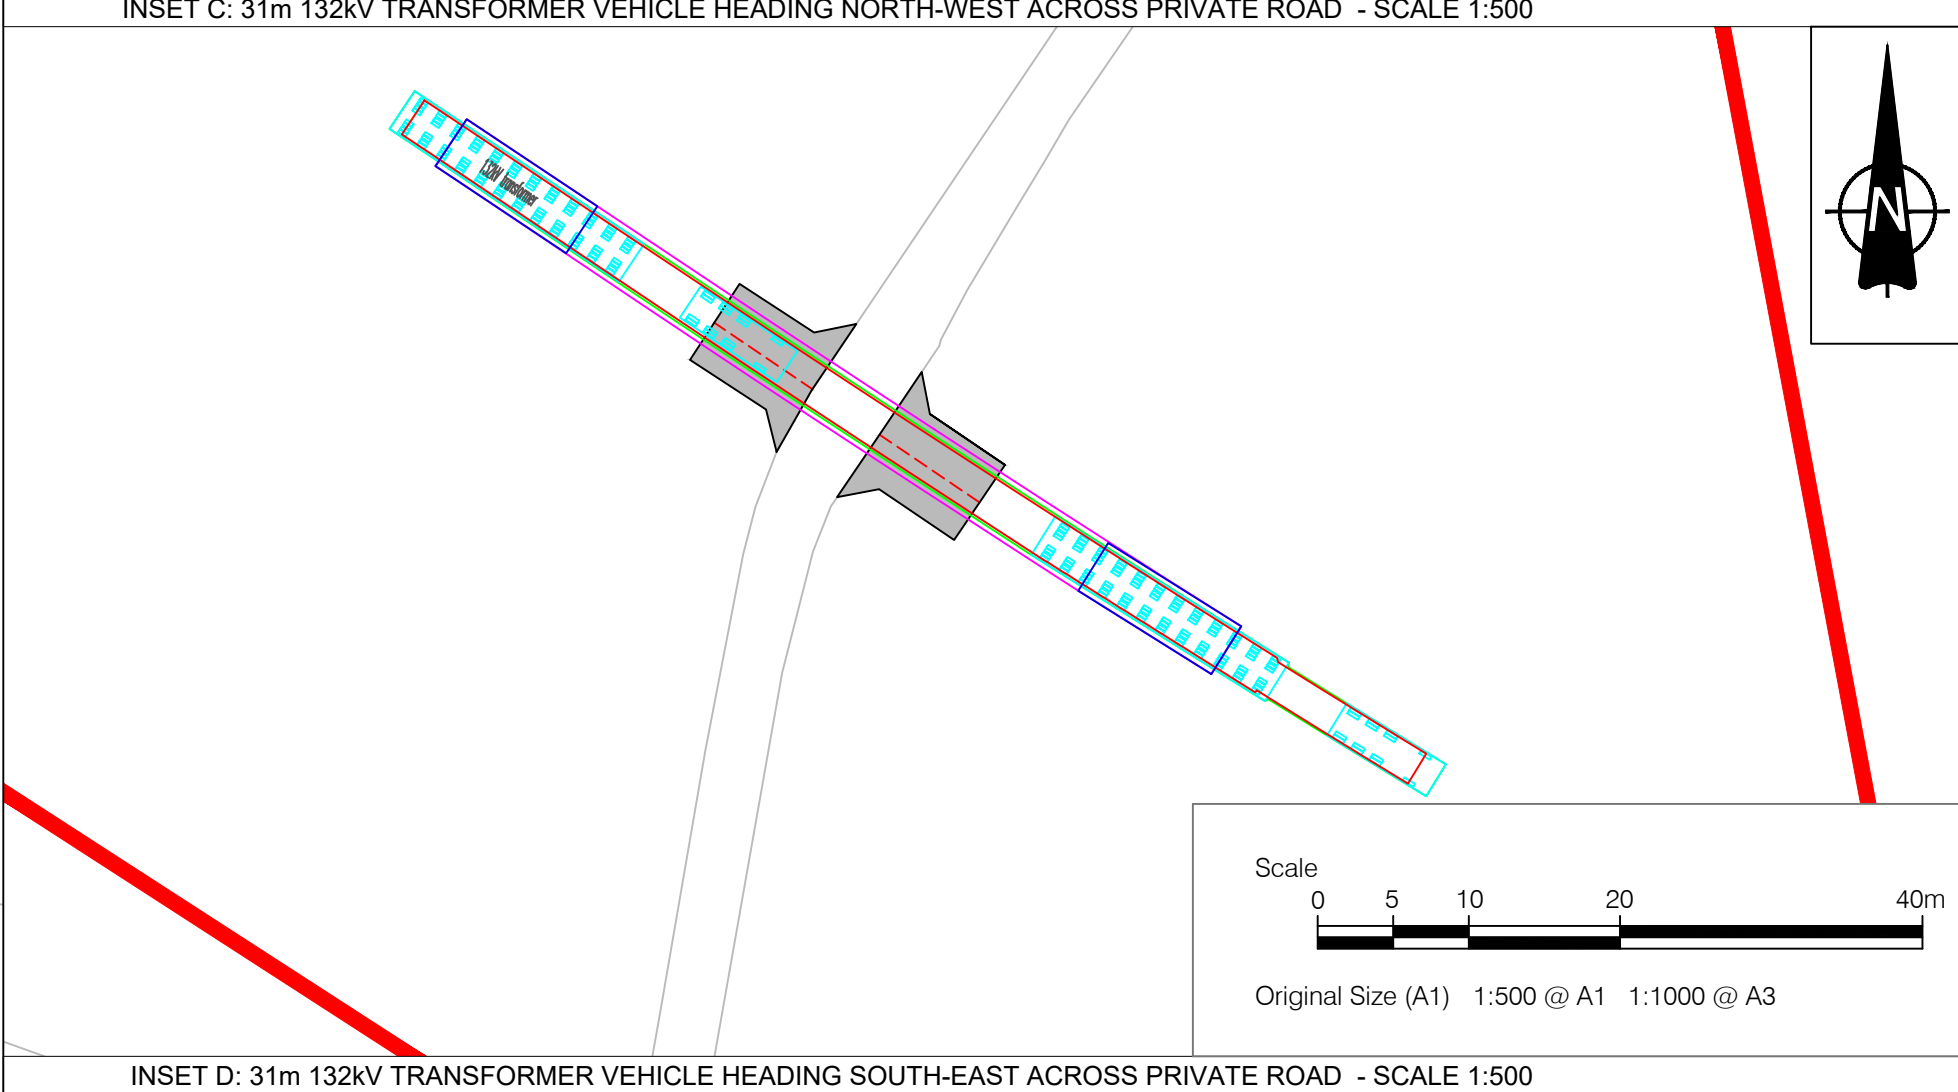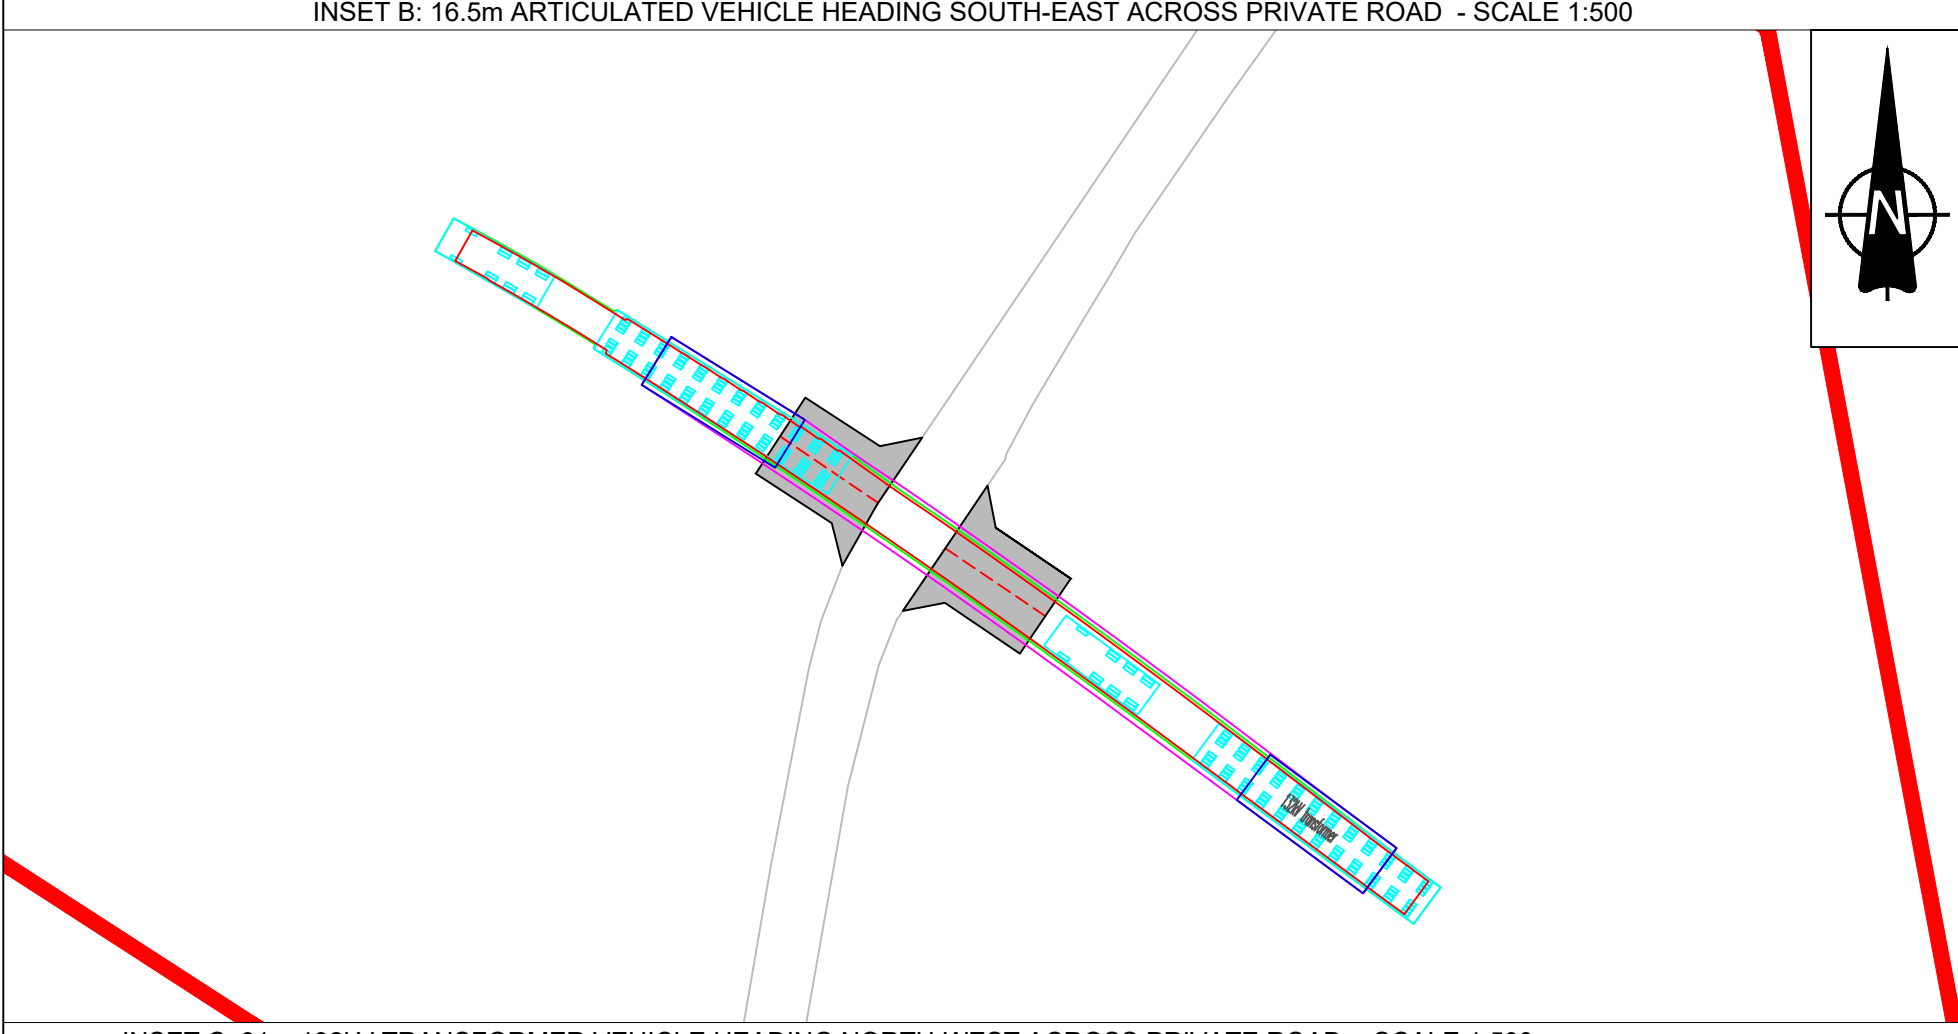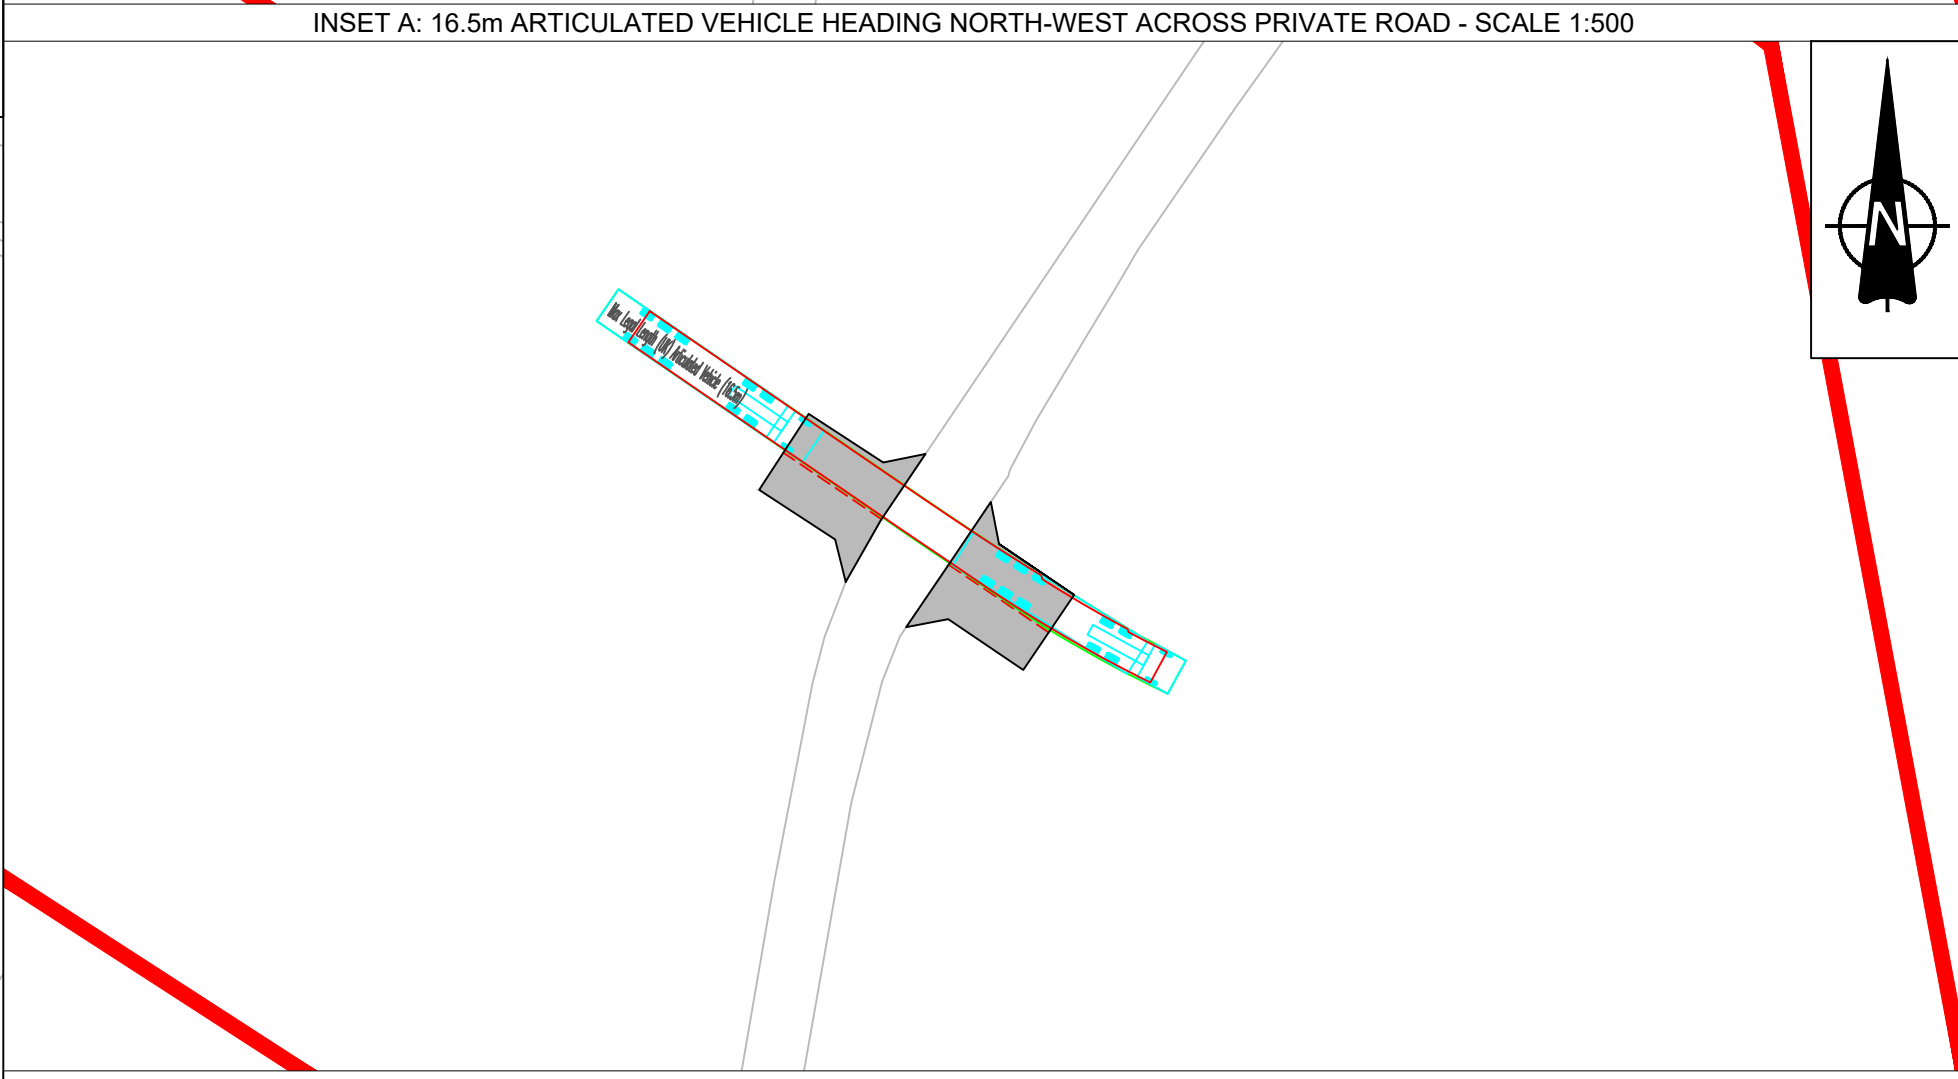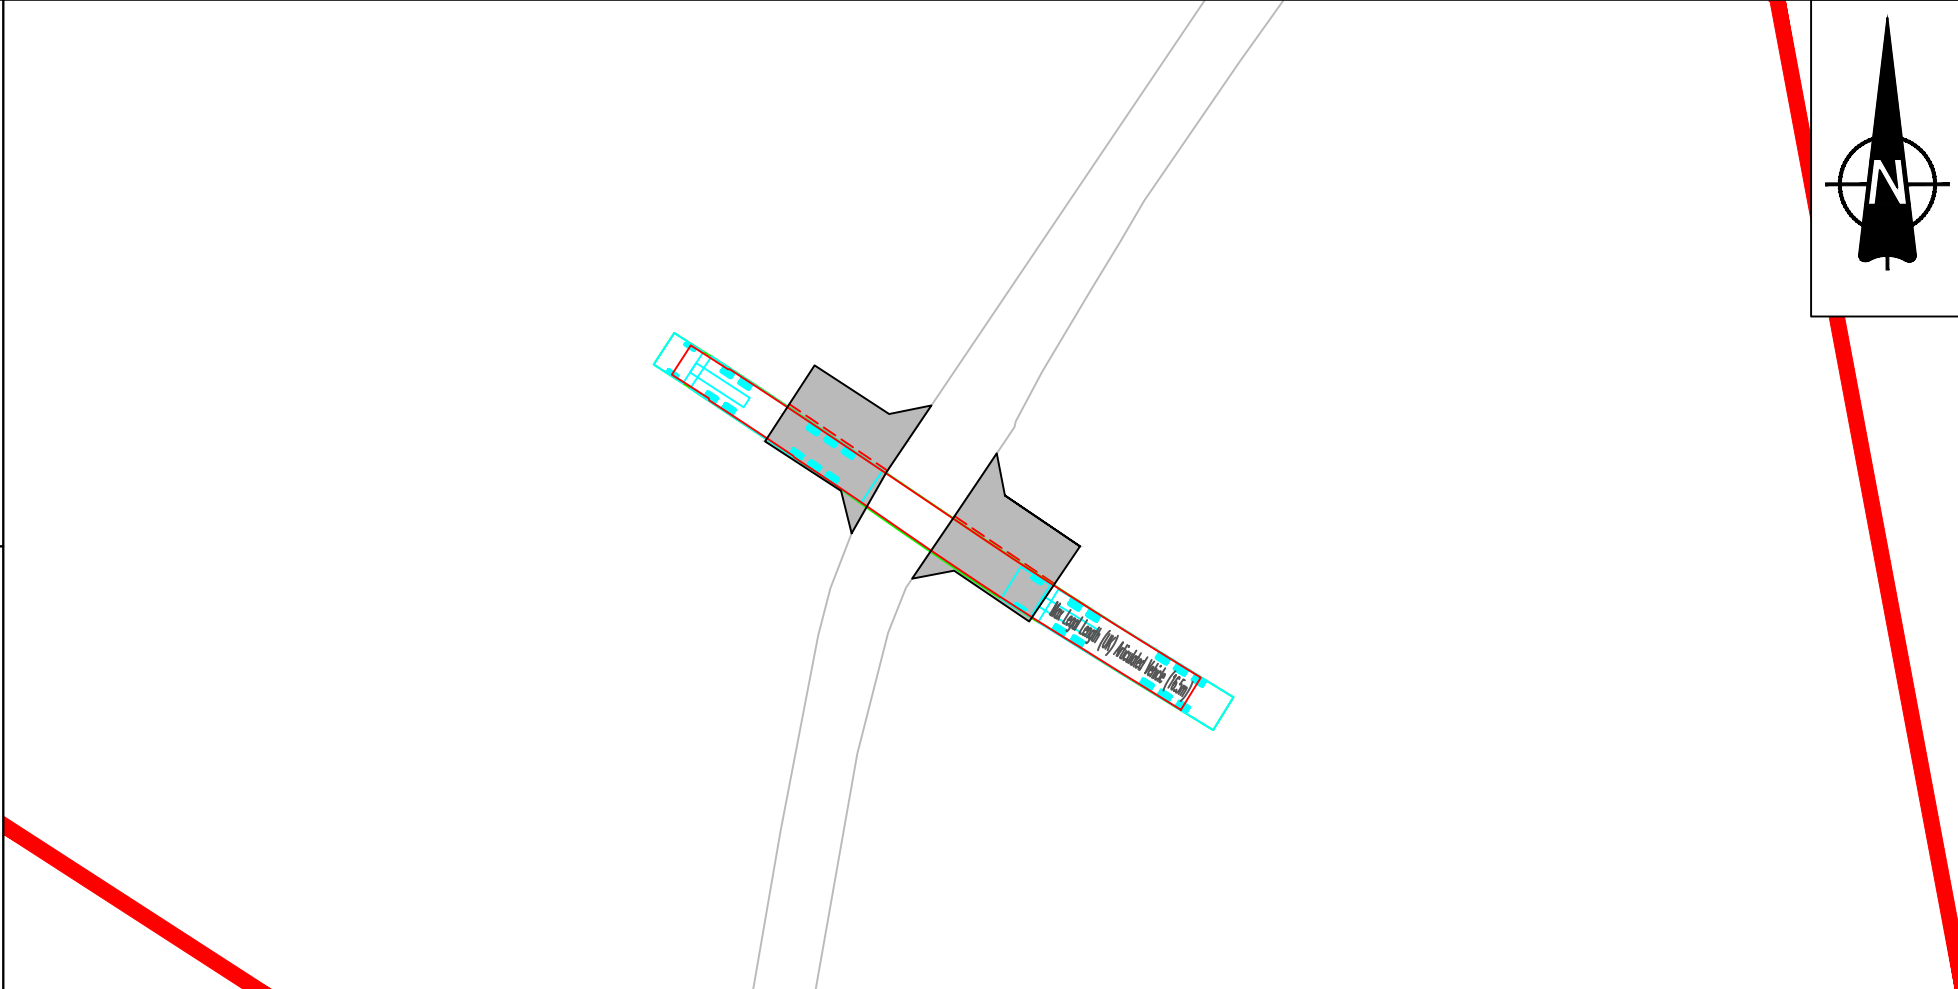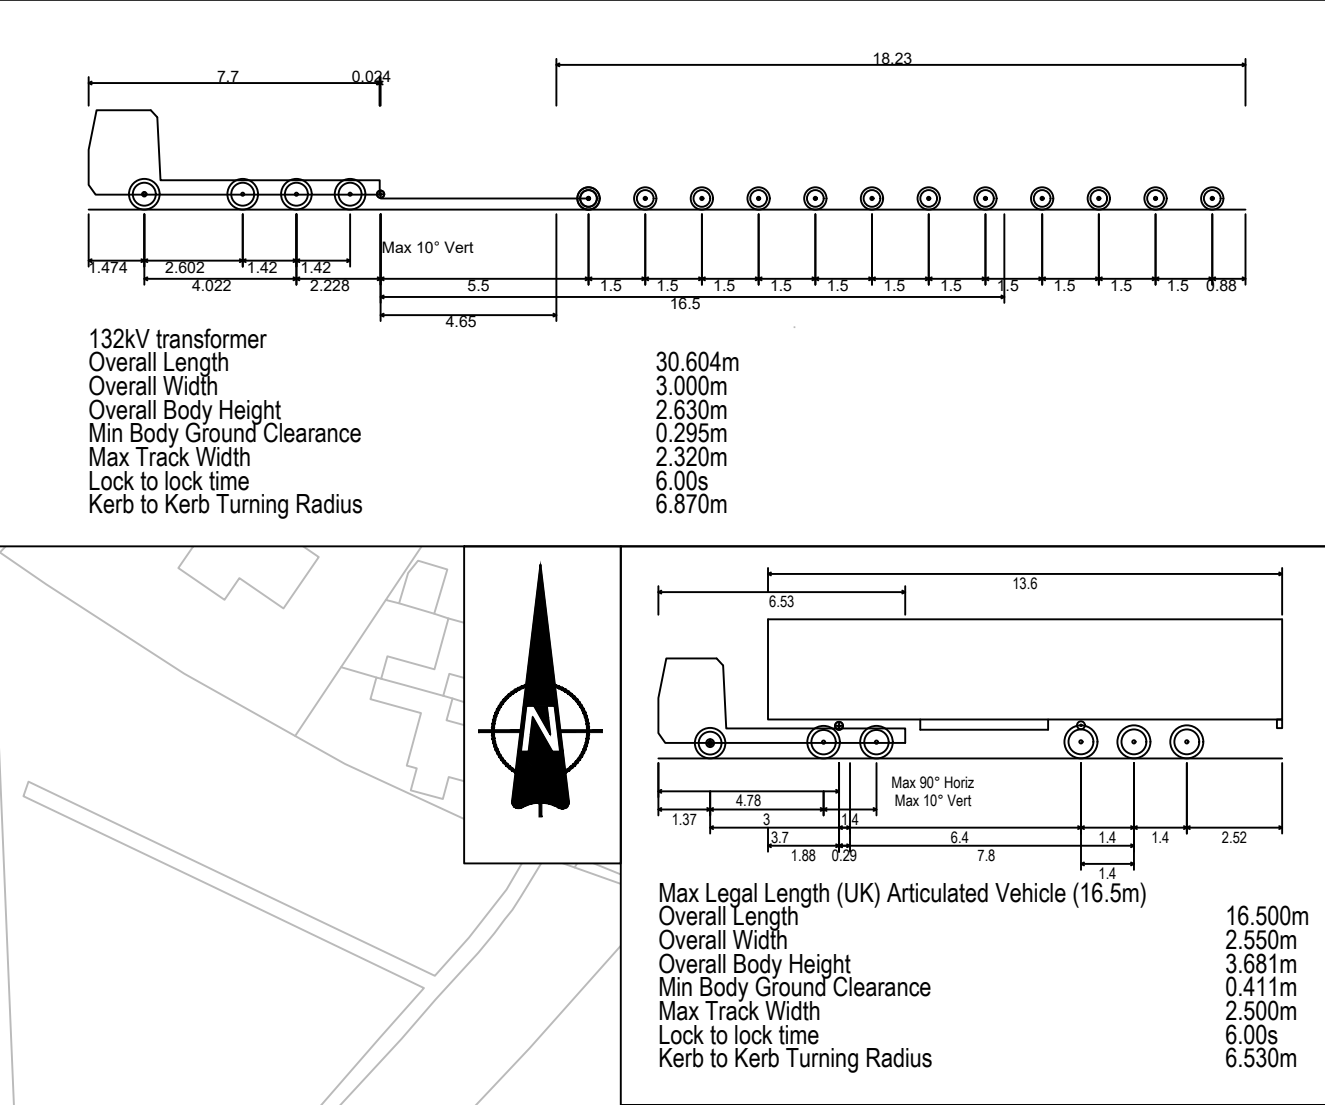

- NOTES**
- This drawing is to be read in conjunction with all other relevant documentation.
 - Do not scale from this drawing, use only printed dimensions.
 - All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
 - This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
 - Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
 - The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
 - Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
 - Junction visibility for the access is based upon DMRB CD109 Table 2.10.
- LEGEND**
- Extent of Access Footprint
 - Order Limits
 - Land Excluded from Order Limits
 - Vehicle Body
 - Vehicle Body Path
 - Vehicle Load
 - Vehicle Load Path
 - Vehicle Wheels Path
 - Edge of Road
 - Access Centreline
 - Junction Visibility
 - Vegetation to be Removed for Vis Splay
 - Indicative Hedgerow Removal Vis Splay
 - Indicative Hedgerow Removal for Bellmouth Access
 - Health and Safety Risk Identifier
 - Existing Public Right of Way

SHEET PLAN

ACCESS LOCATION

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:
Cable Corridor Area Access CC-P2
Appendix 3 - Sheet 51 of 53
Whitestone Solar Farm
Regulation 5(2)(o)


DRAWING DATE: 03/06/2026

SCALE: AS SHOWN	SHEET: Sheet 51 of 53
SIZE: A1	REVISION: 01


DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020

EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012 RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

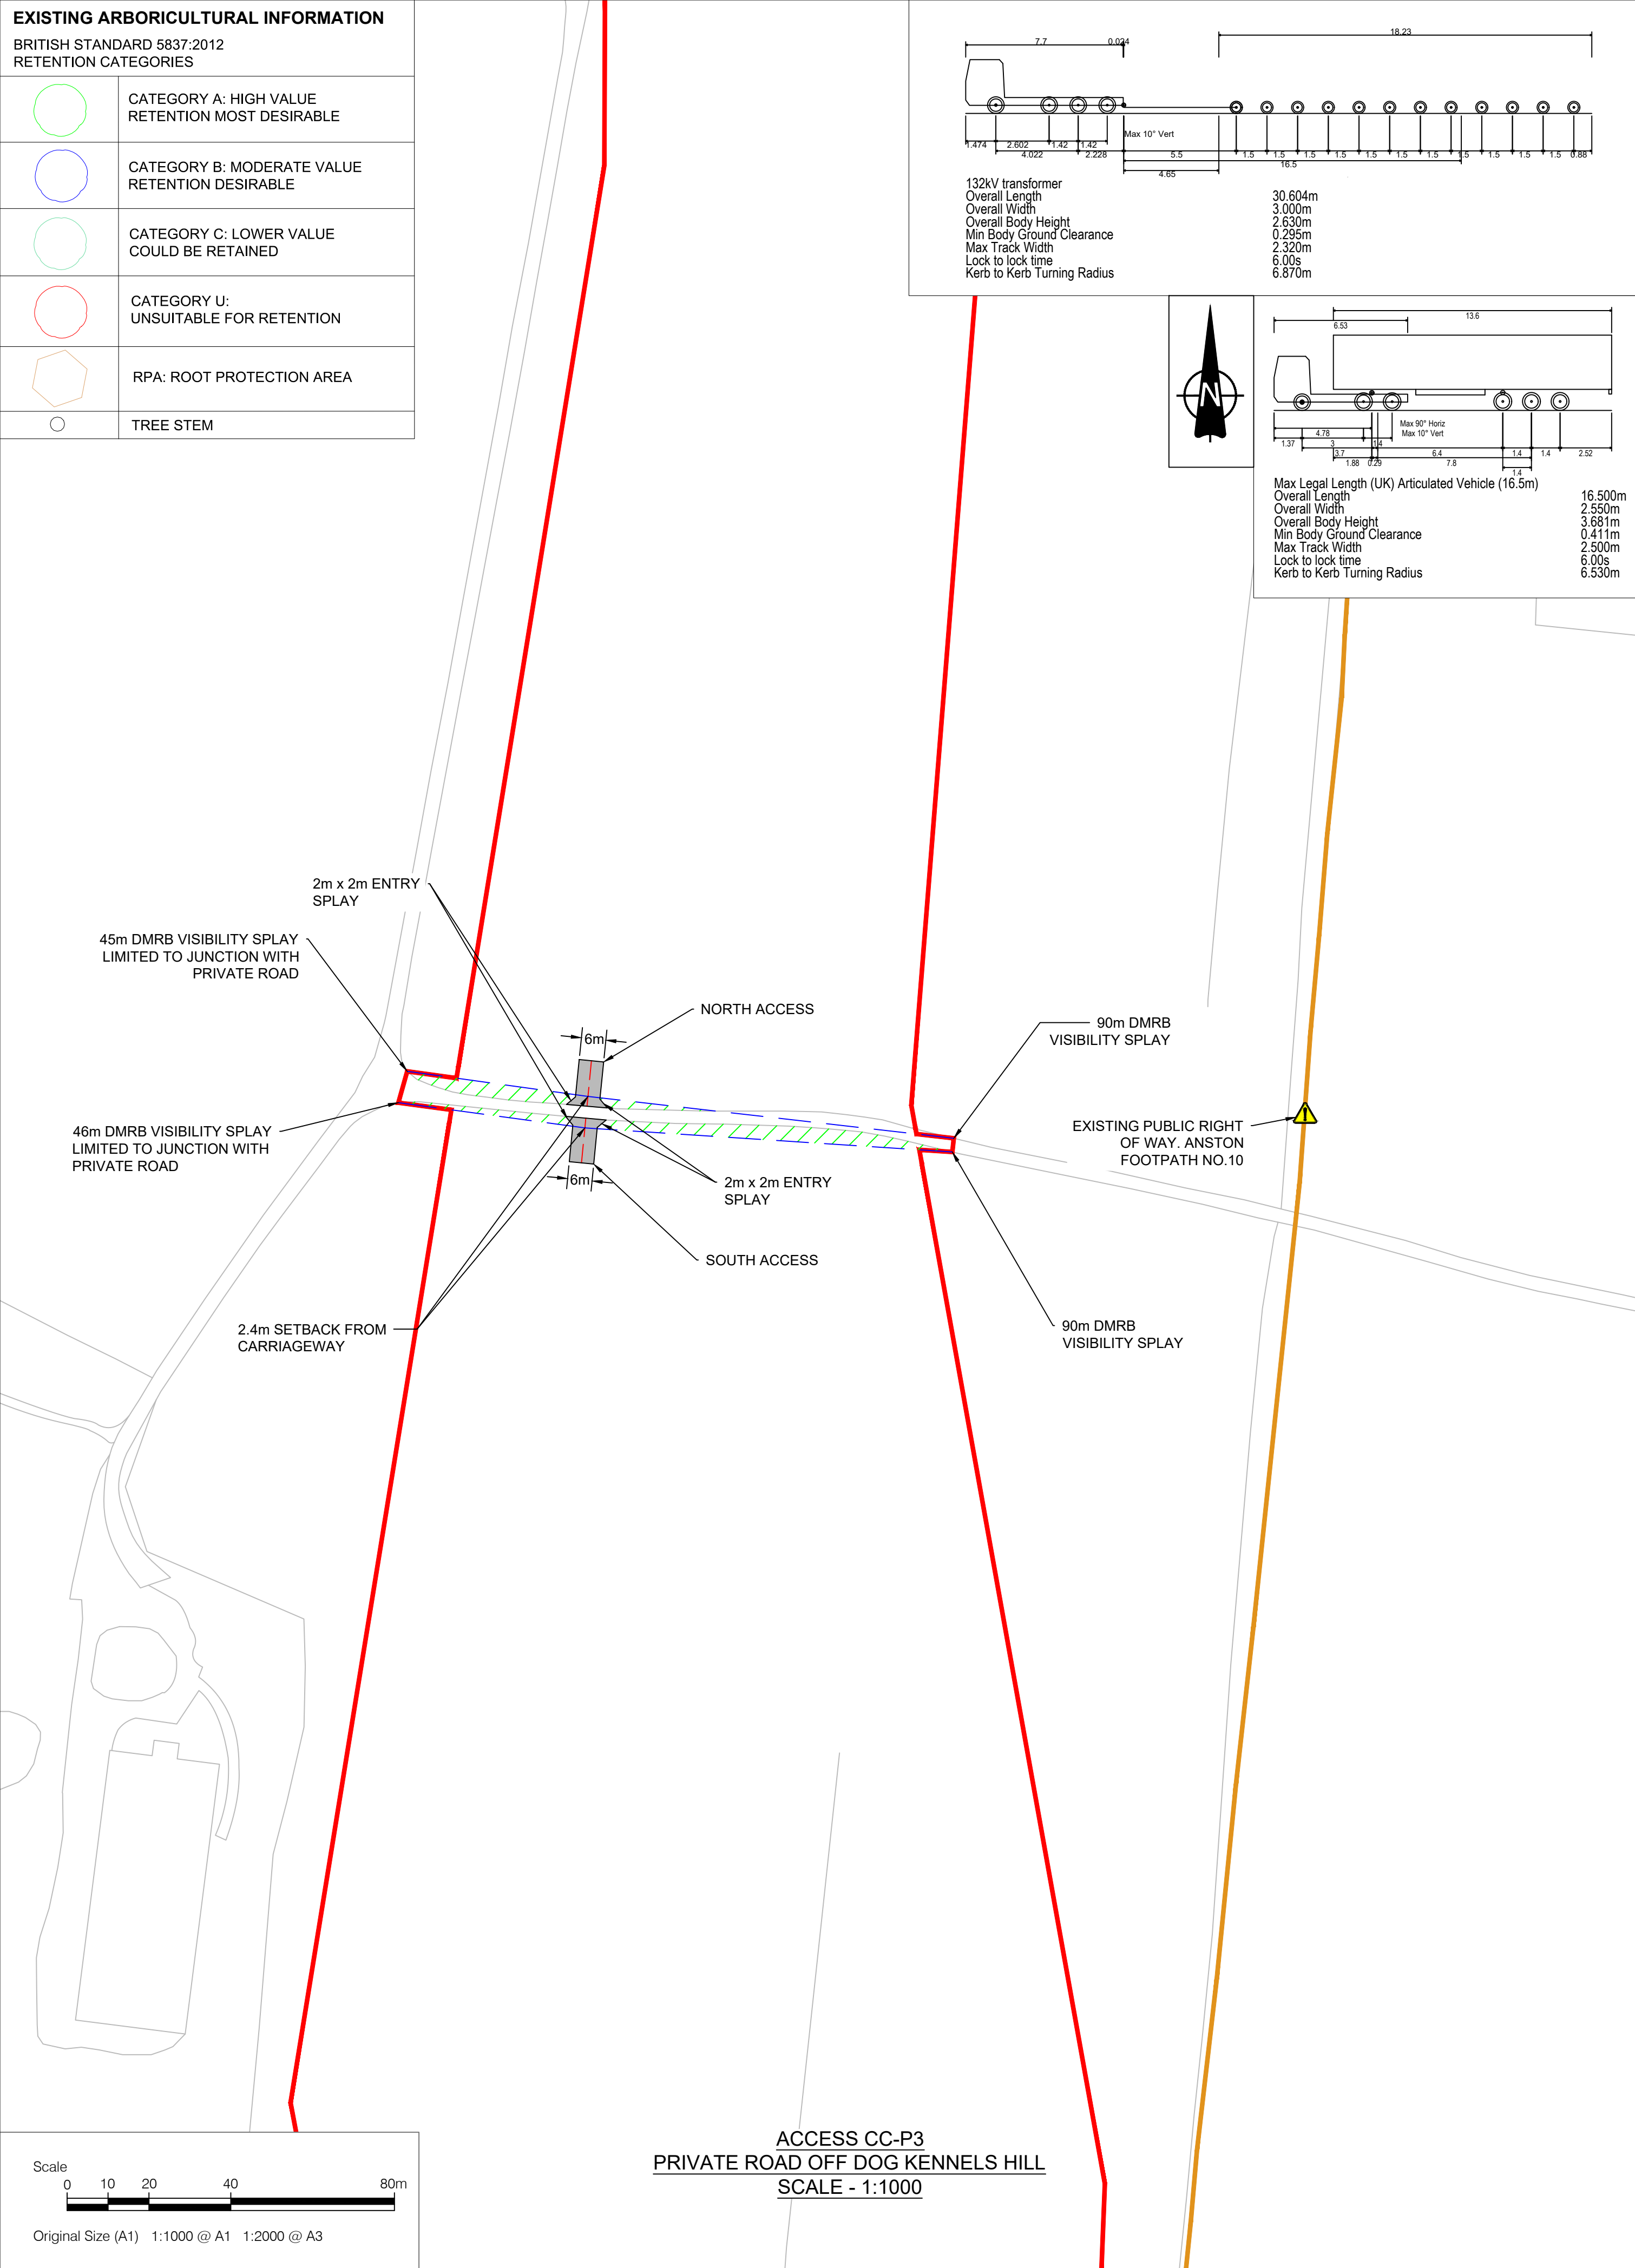

ACCESS CC-P3
PRIVATE ROAD OFF DOG KENNELS HILL
SCALE - 1:1000

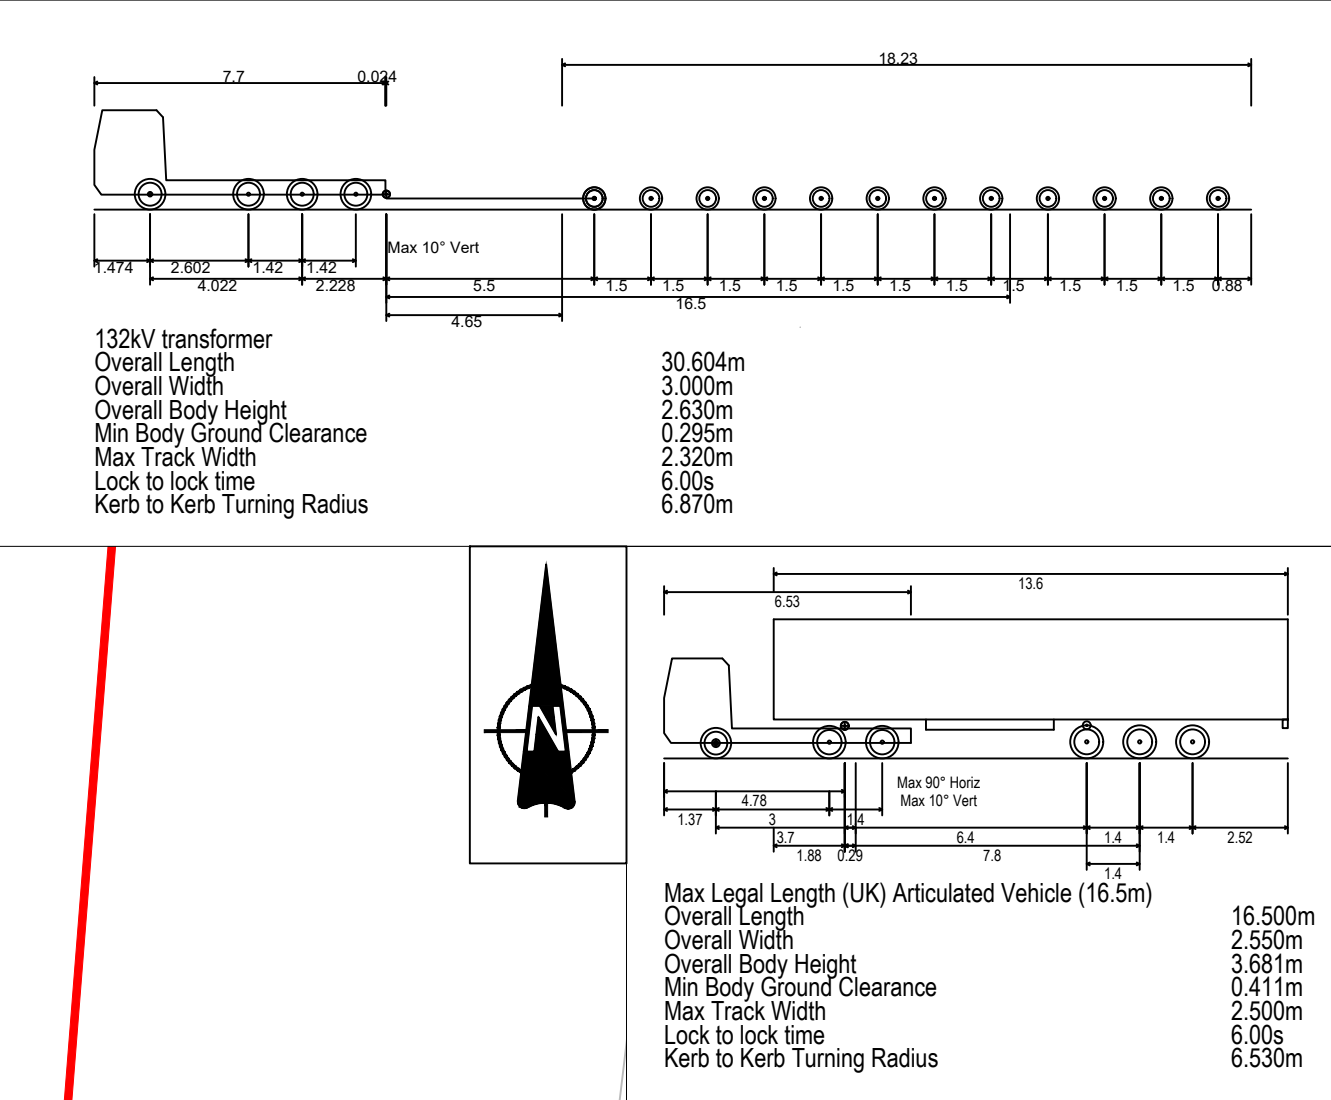


132kV transformer
Overall Length
Overall Width
Overall Body Height
Min Body Ground Clearance
Max Track Width
Lock to lock time
Kerb to Kerb Turning Radius

30.604m
3.000m
2.630m
0.295m
2.320m
6.00s
6.870m

Max Legal Length (UK) Articulated Vehicle (16.5m)
Overall Length
Overall Width
Overall Body Height
Min Body Ground Clearance
Max Track Width
Lock to lock time
Kerb to Kerb Turning Radius

16.500m
2.550m
3.681m
0.411m
2.300m
6.00s
6.530m

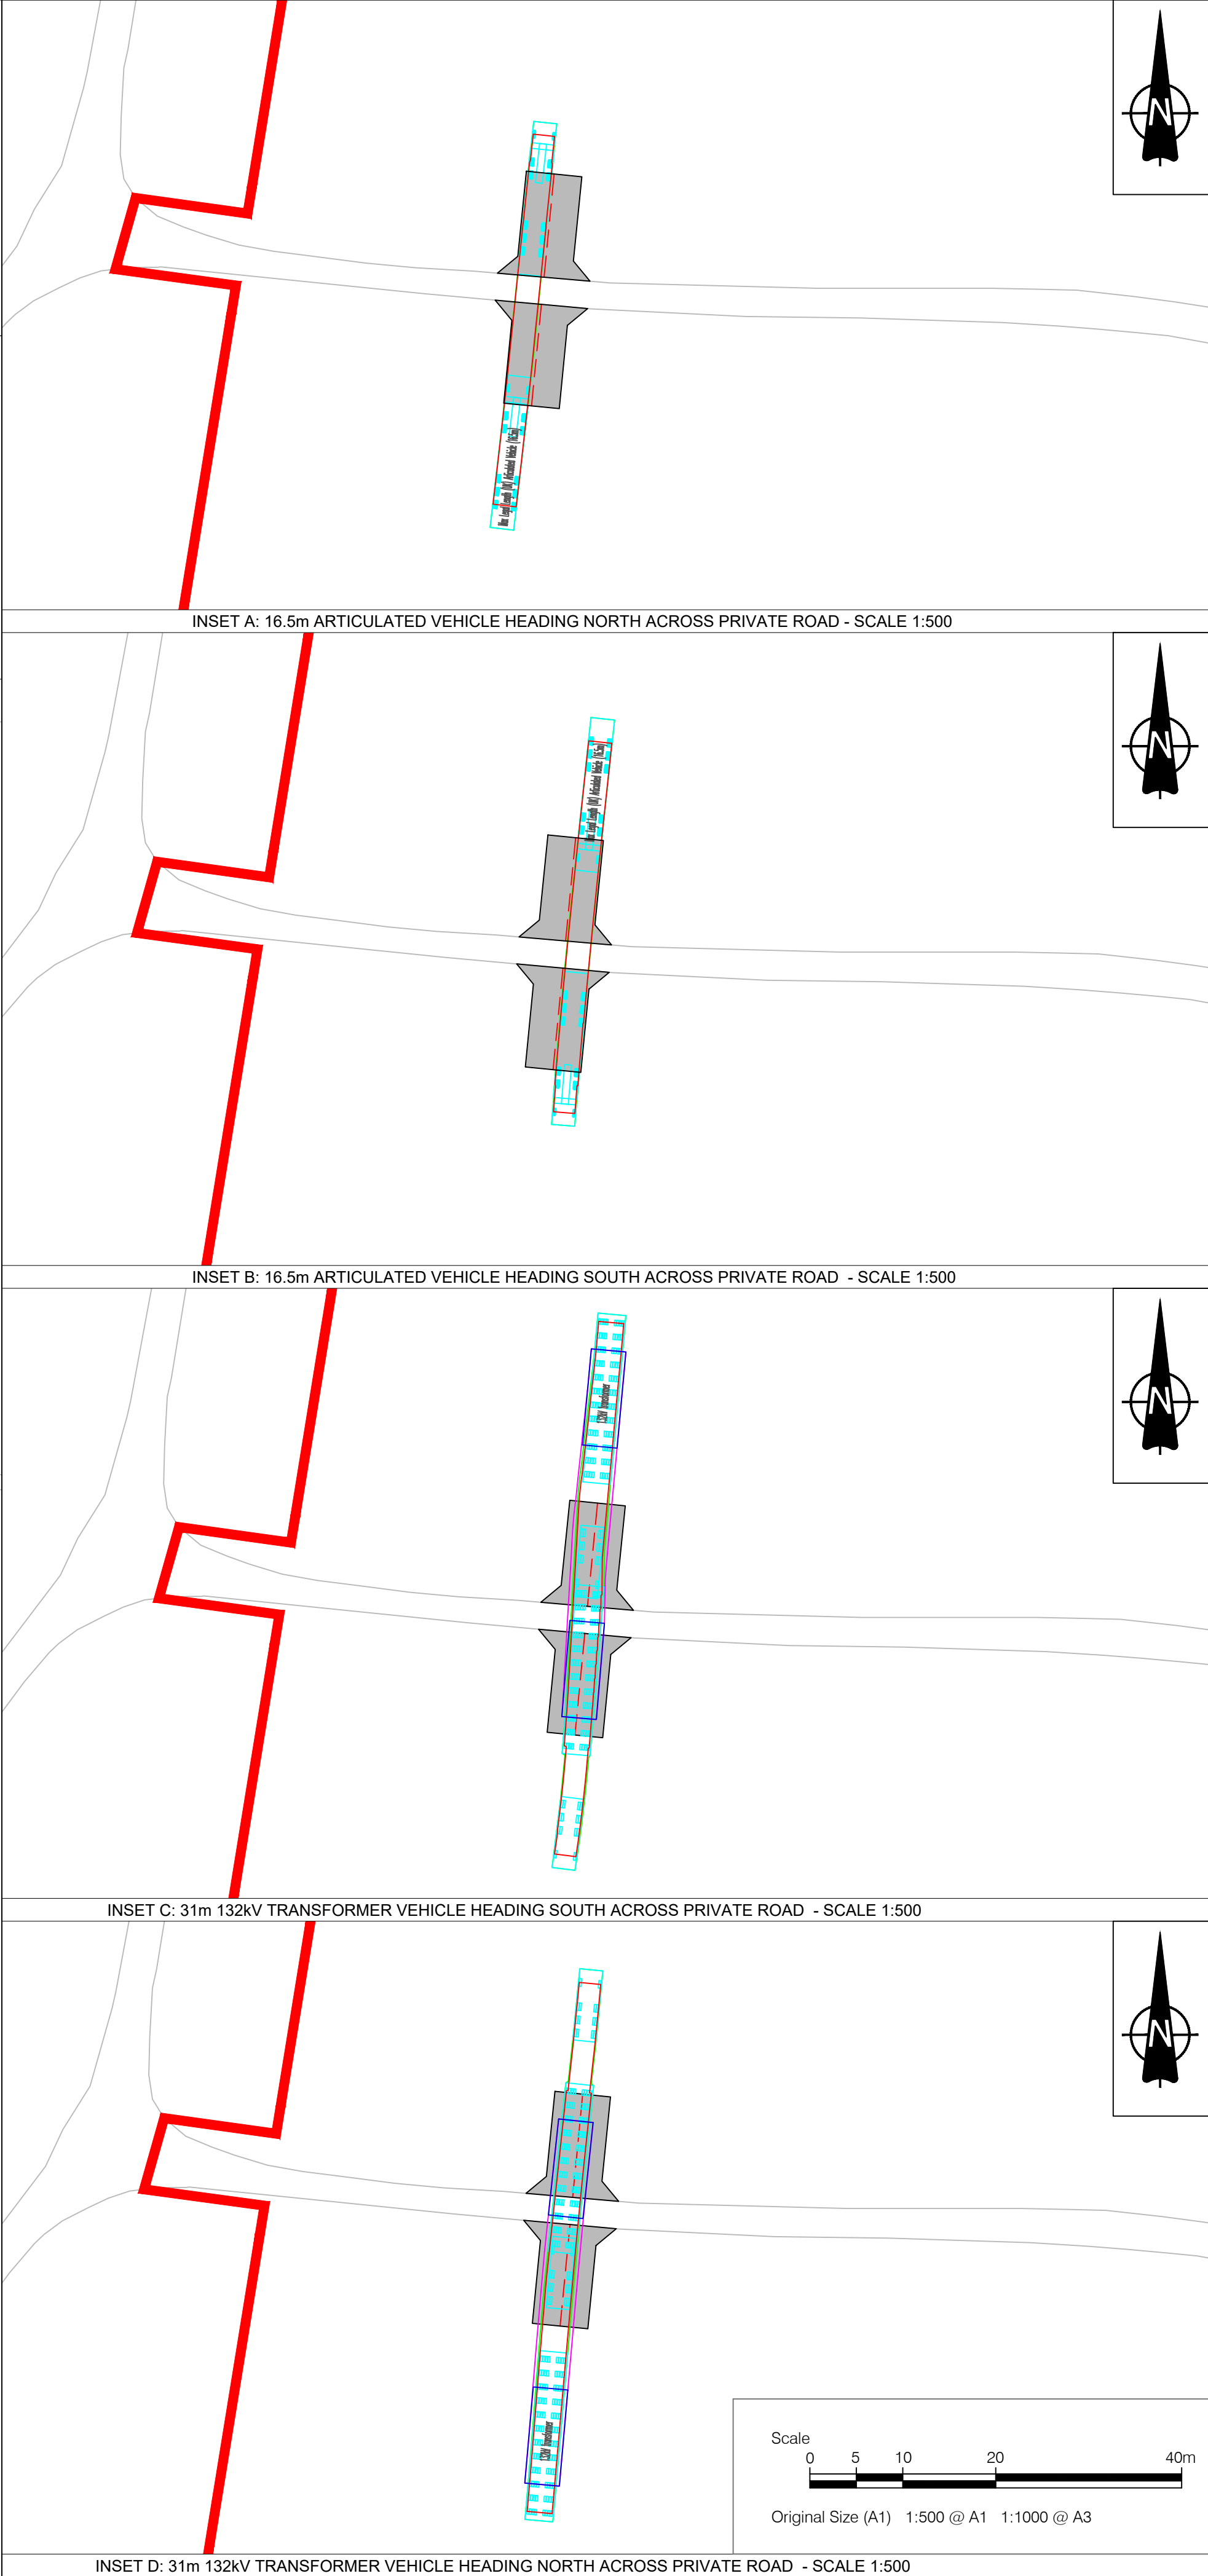

INSET A: 16.5m ARTICULATED VEHICLE HEADING NORTH ACROSS PRIVATE ROAD - SCALE 1:500

INSET B: 16.5m ARTICULATED VEHICLE HEADING SOUTH ACROSS PRIVATE ROAD - SCALE 1:500

INSET C: 31m 132kV TRANSFORMER VEHICLE HEADING SOUTH ACROSS PRIVATE ROAD - SCALE 1:500

INSET D: 31m 132kV TRANSFORMER VEHICLE HEADING NORTH ACROSS PRIVATE ROAD - SCALE 1:500


NOTES

- This drawing is to be read in conjunction with all other relevant documentation.
- Do not scale from this drawing, use only printed dimensions.
- All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
- This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
- Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
- The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
- Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
- Junction visibility for the access is based upon DMRB CD109 Table 2.10.

LEGEND

- Extent of Access Footprint
- Order Limits
- Land Excluded from Order Limits
- Vehicle Body
- Vehicle Body Path
- Vehicle Load
- Vehicle Load Path
- Vehicle Wheels Path
- Edge of Road
- Access Centreline
- Junction Visibility
- Vegetation to be Removed for Vis Splay
- Indicative Hedgerow Removal Vis Splay
- Indicative Hedgerow Removal for Bellmouth Access
- Health and Safety Risk Identifier
- Existing Public Right of Way

SHEET PLAN

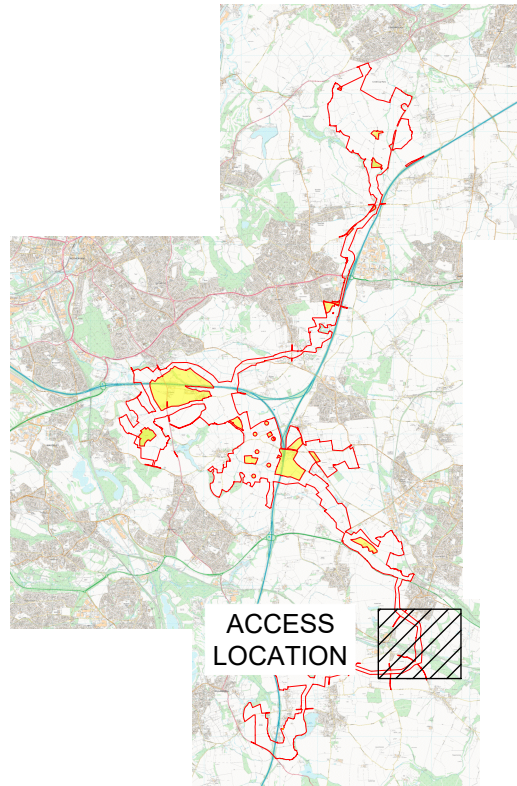

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:
Cable Corridor Area Access CC-P3
Appendix 3 - Sheet 52 of 53
Whitestone Solar Farm
Regulation 5(2)(o)

DRAWING DATE: 03/06/2026











SCALE: AS SHOWN
SIZE: A1
SHEET: Sheet 52 of 53
REVISION: 01

DOCUMENT REFERENCE: EN0110020/APP/5.12

APPLICATION NUMBER: EN0110020




EXISTING ARBORICULTURAL INFORMATION	
BRITISH STANDARD 5837:2012	
RETENTION CATEGORIES	
	CATEGORY A: HIGH VALUE RETENTION MOST DESIRABLE
	CATEGORY B: MODERATE VALUE RETENTION DESIRABLE
	CATEGORY C: LOWER VALUE COULD BE RETAINED
	CATEGORY U: UNSUITABLE FOR RETENTION
	RPA: ROOT PROTECTION AREA
	TREE STEM

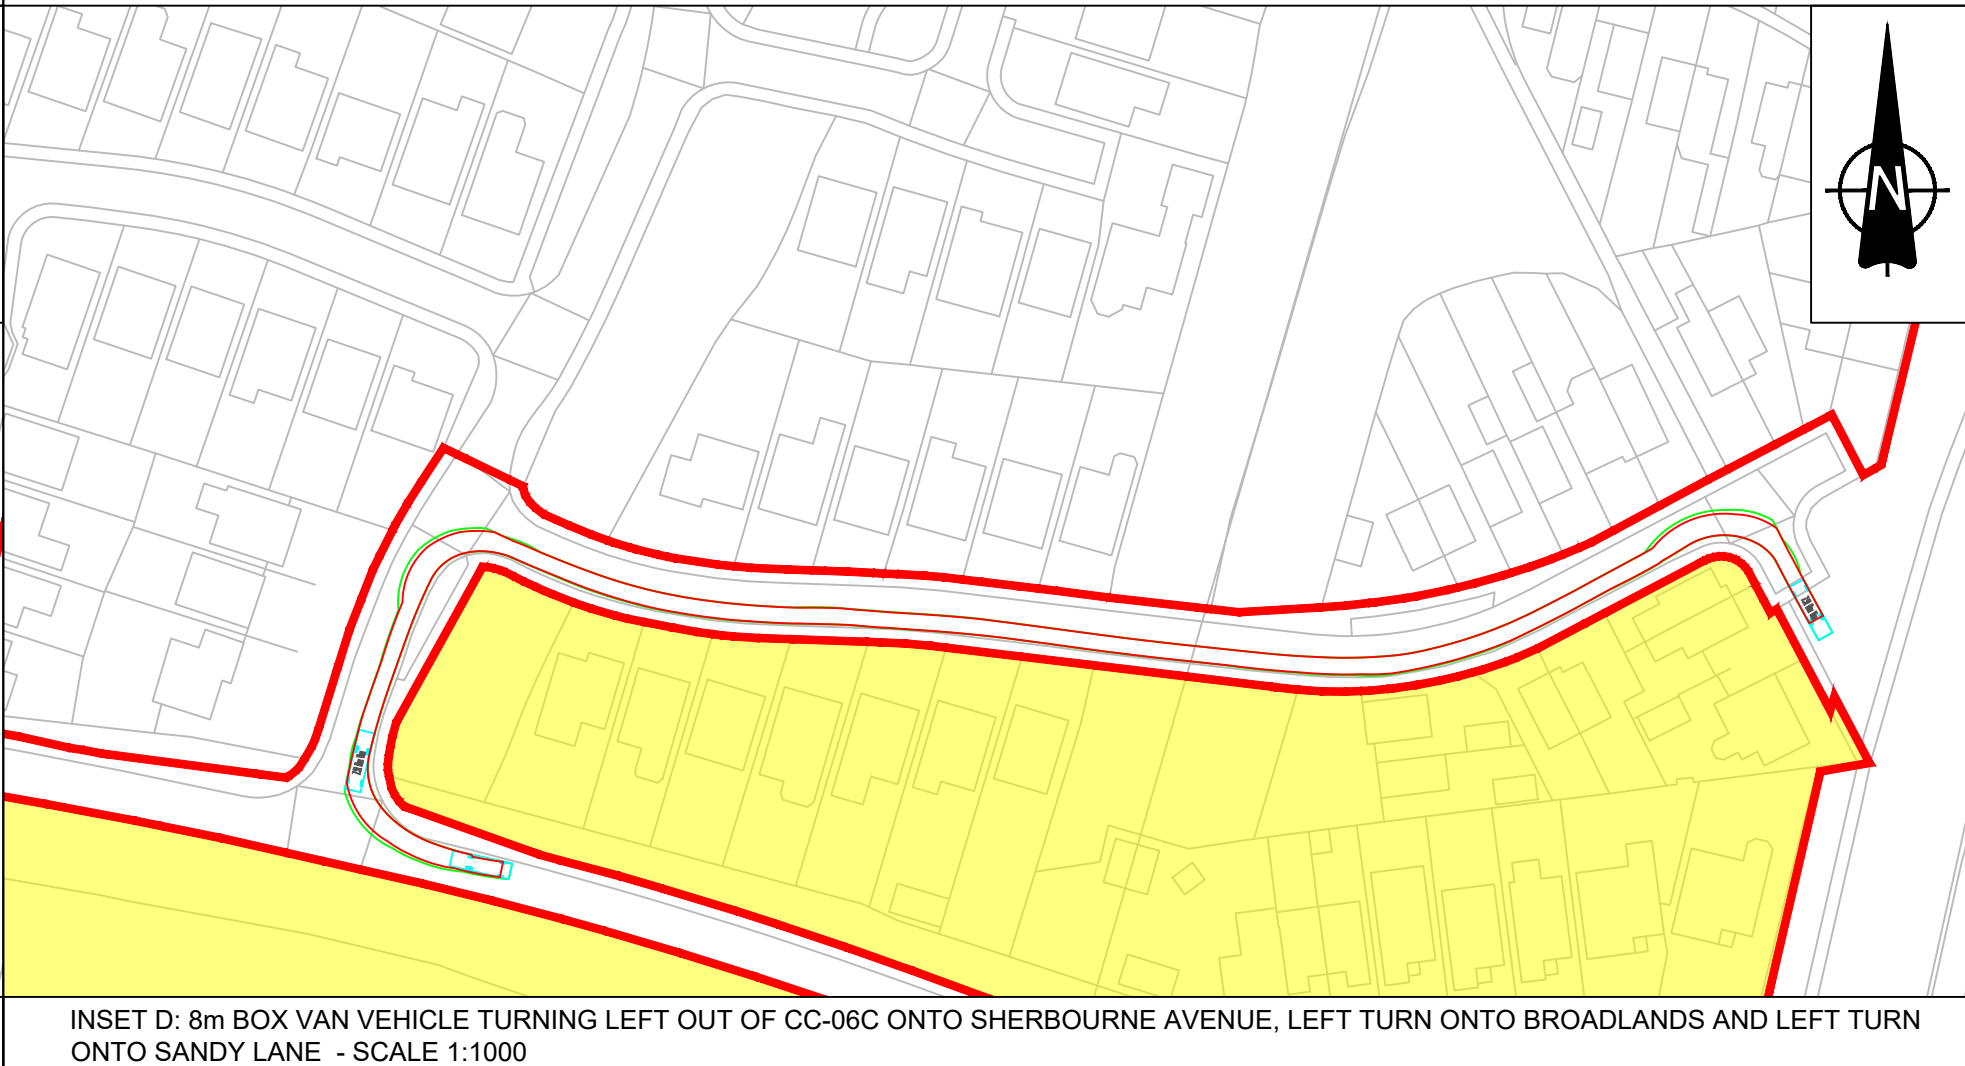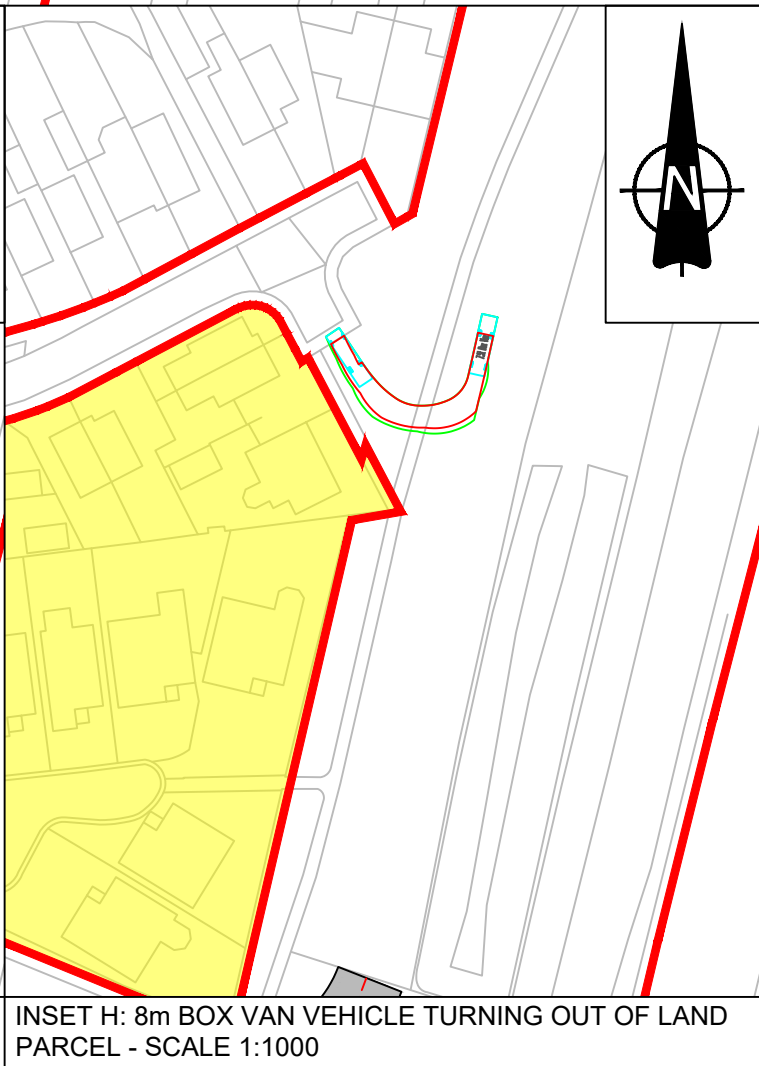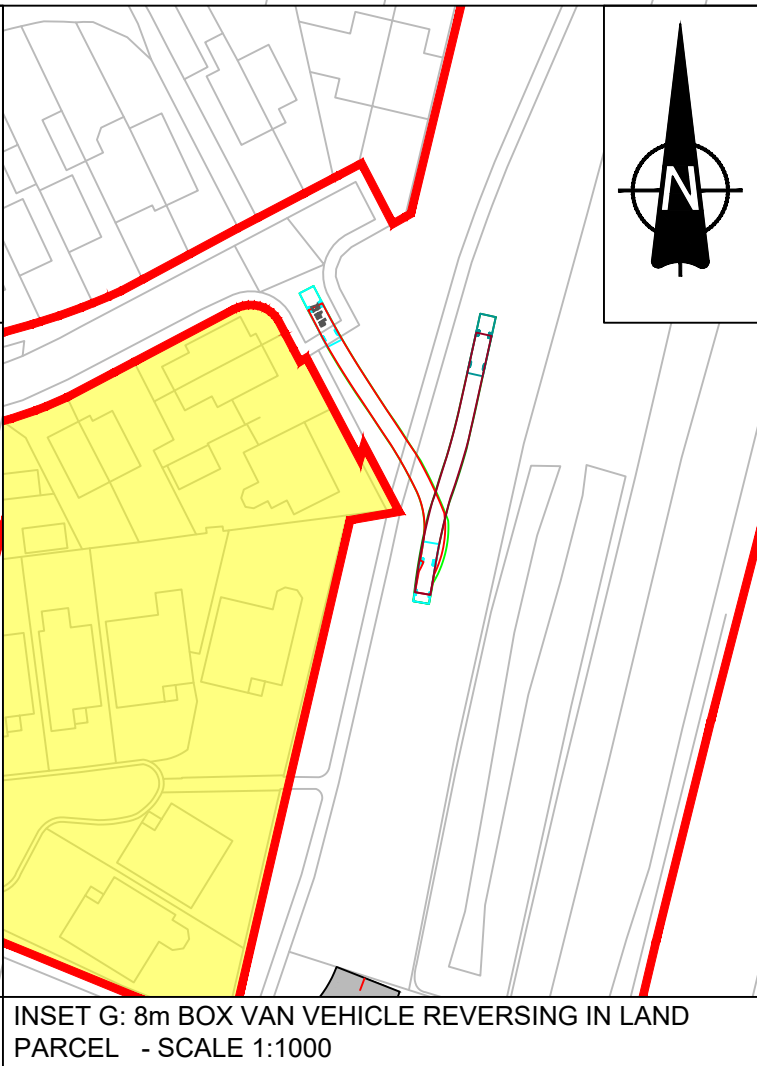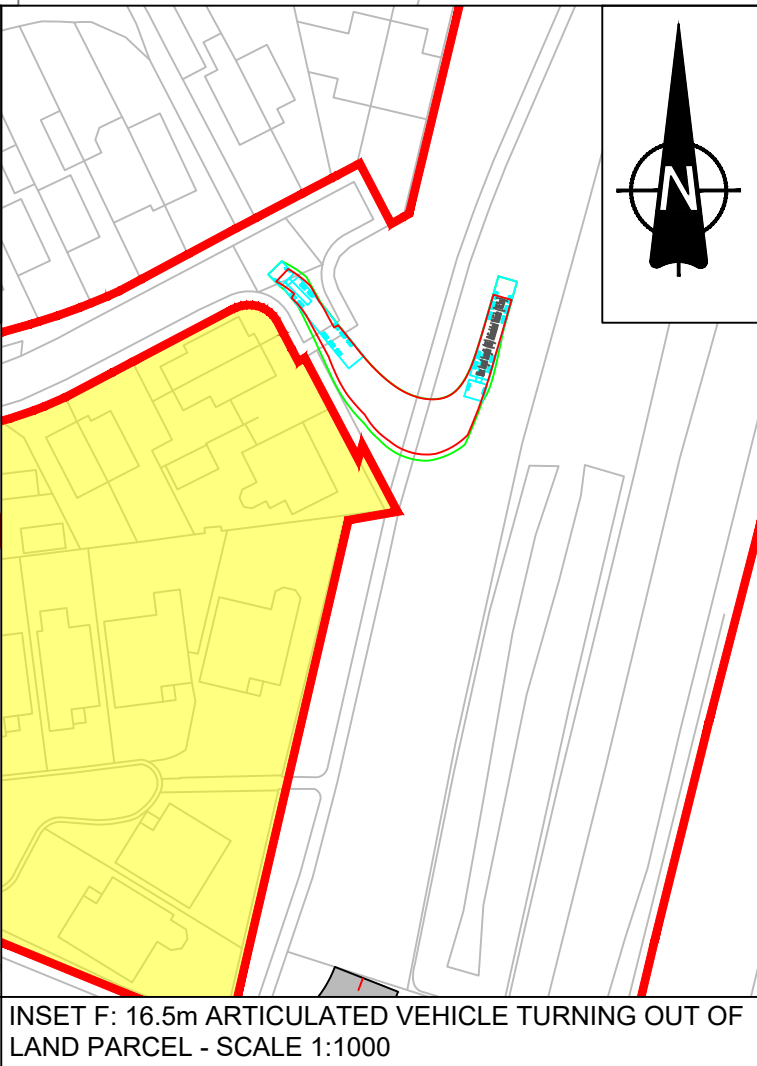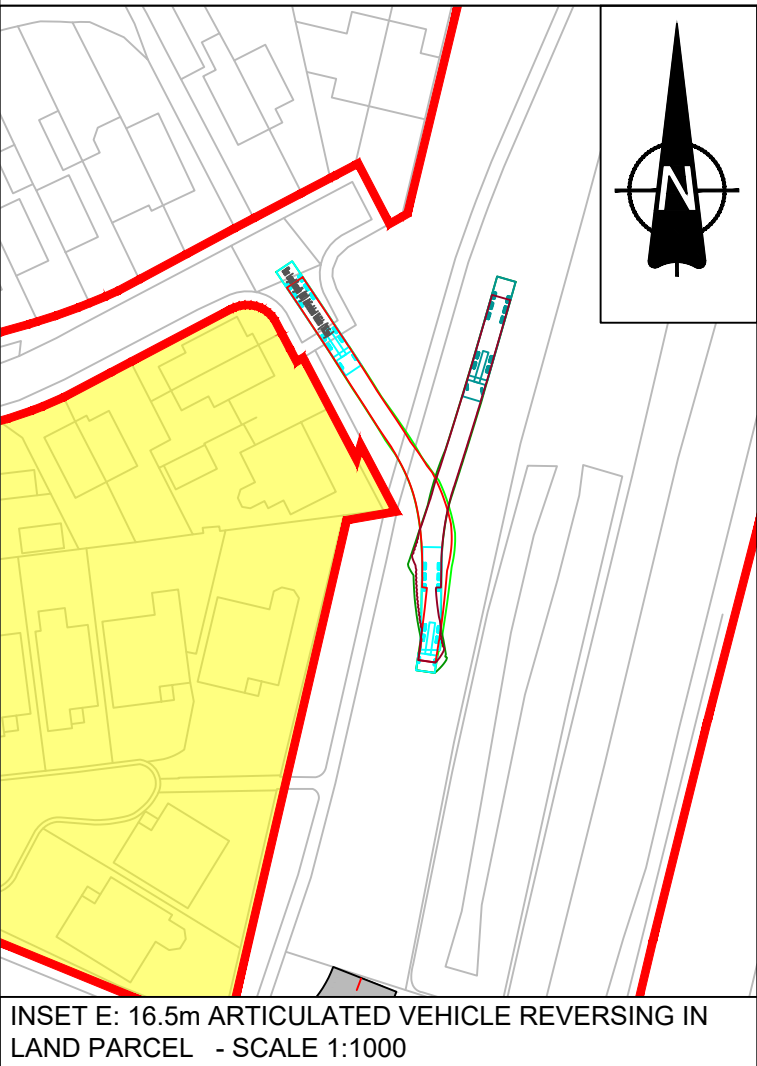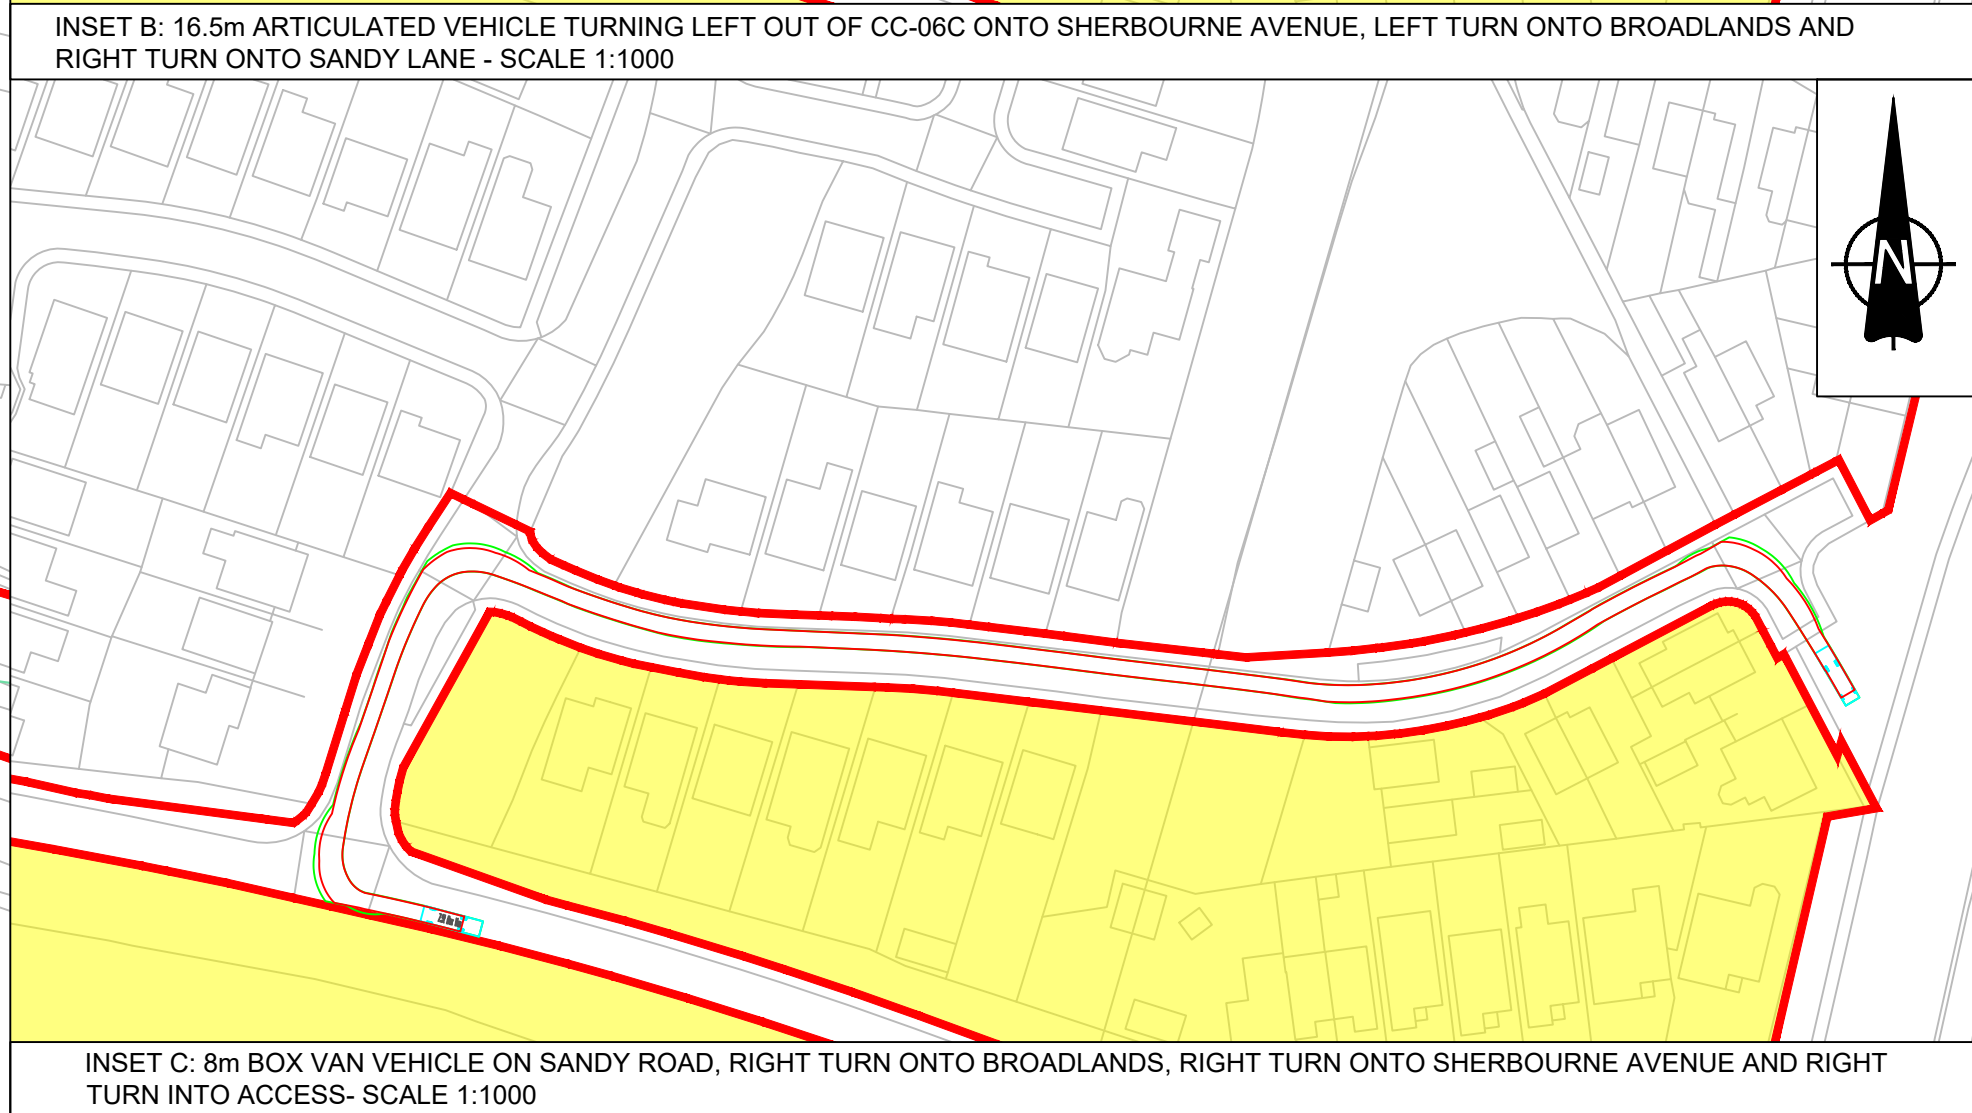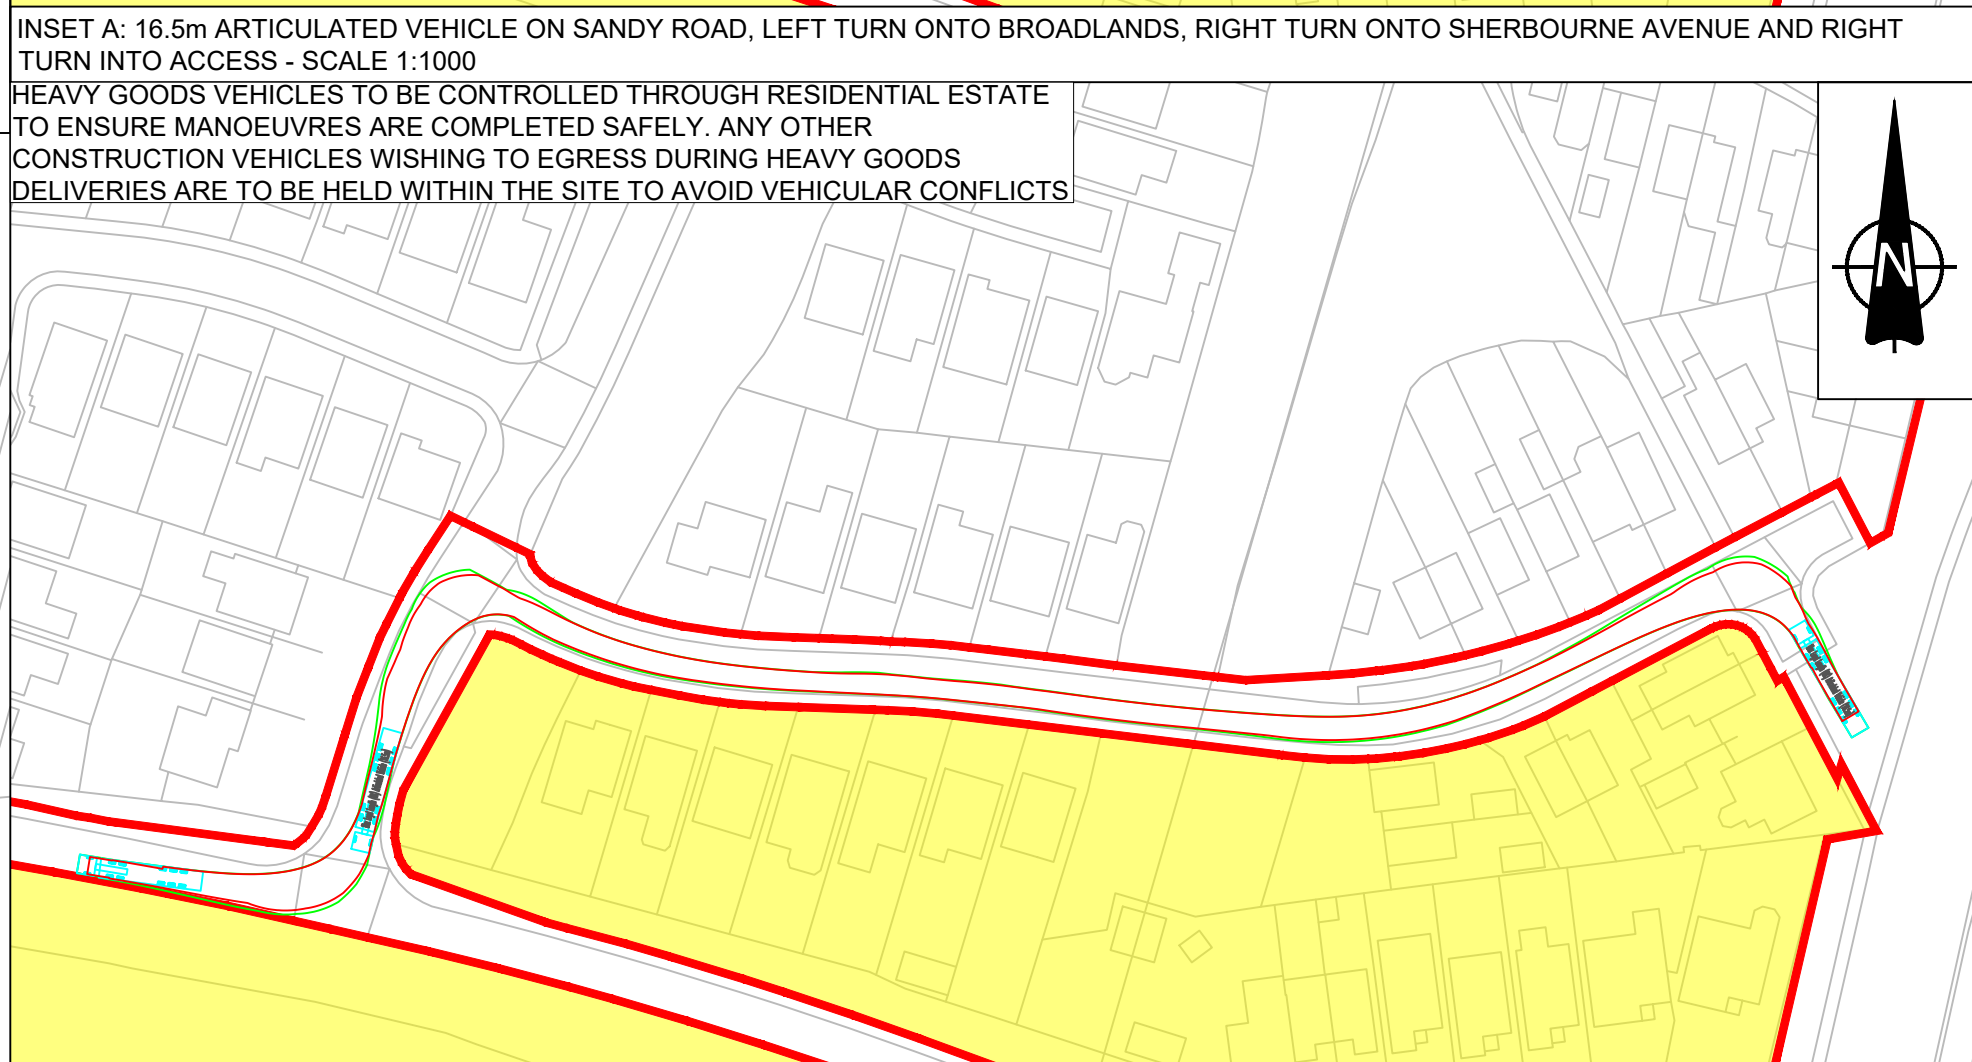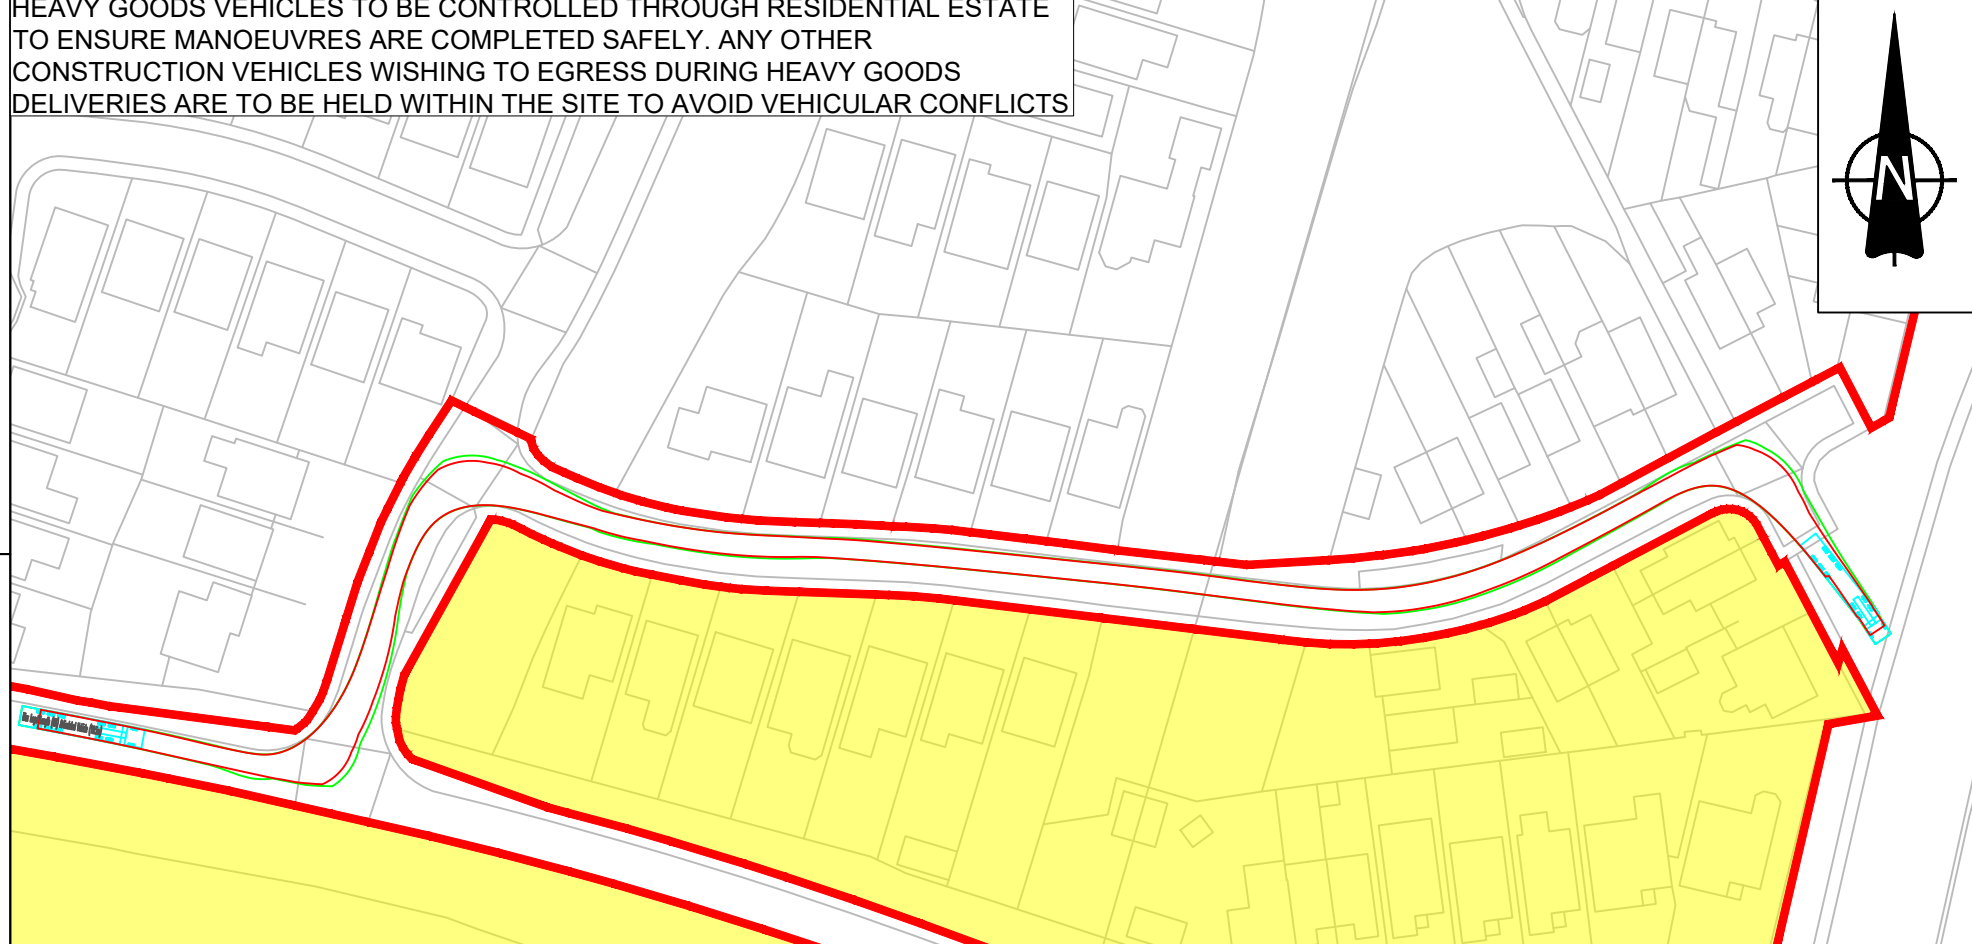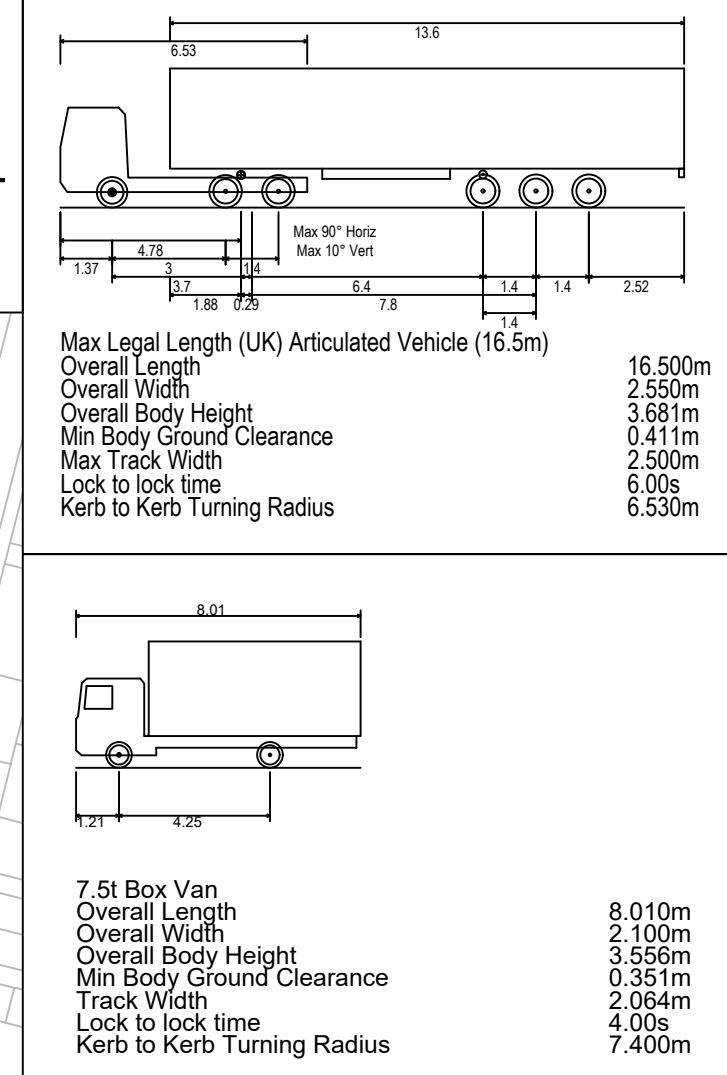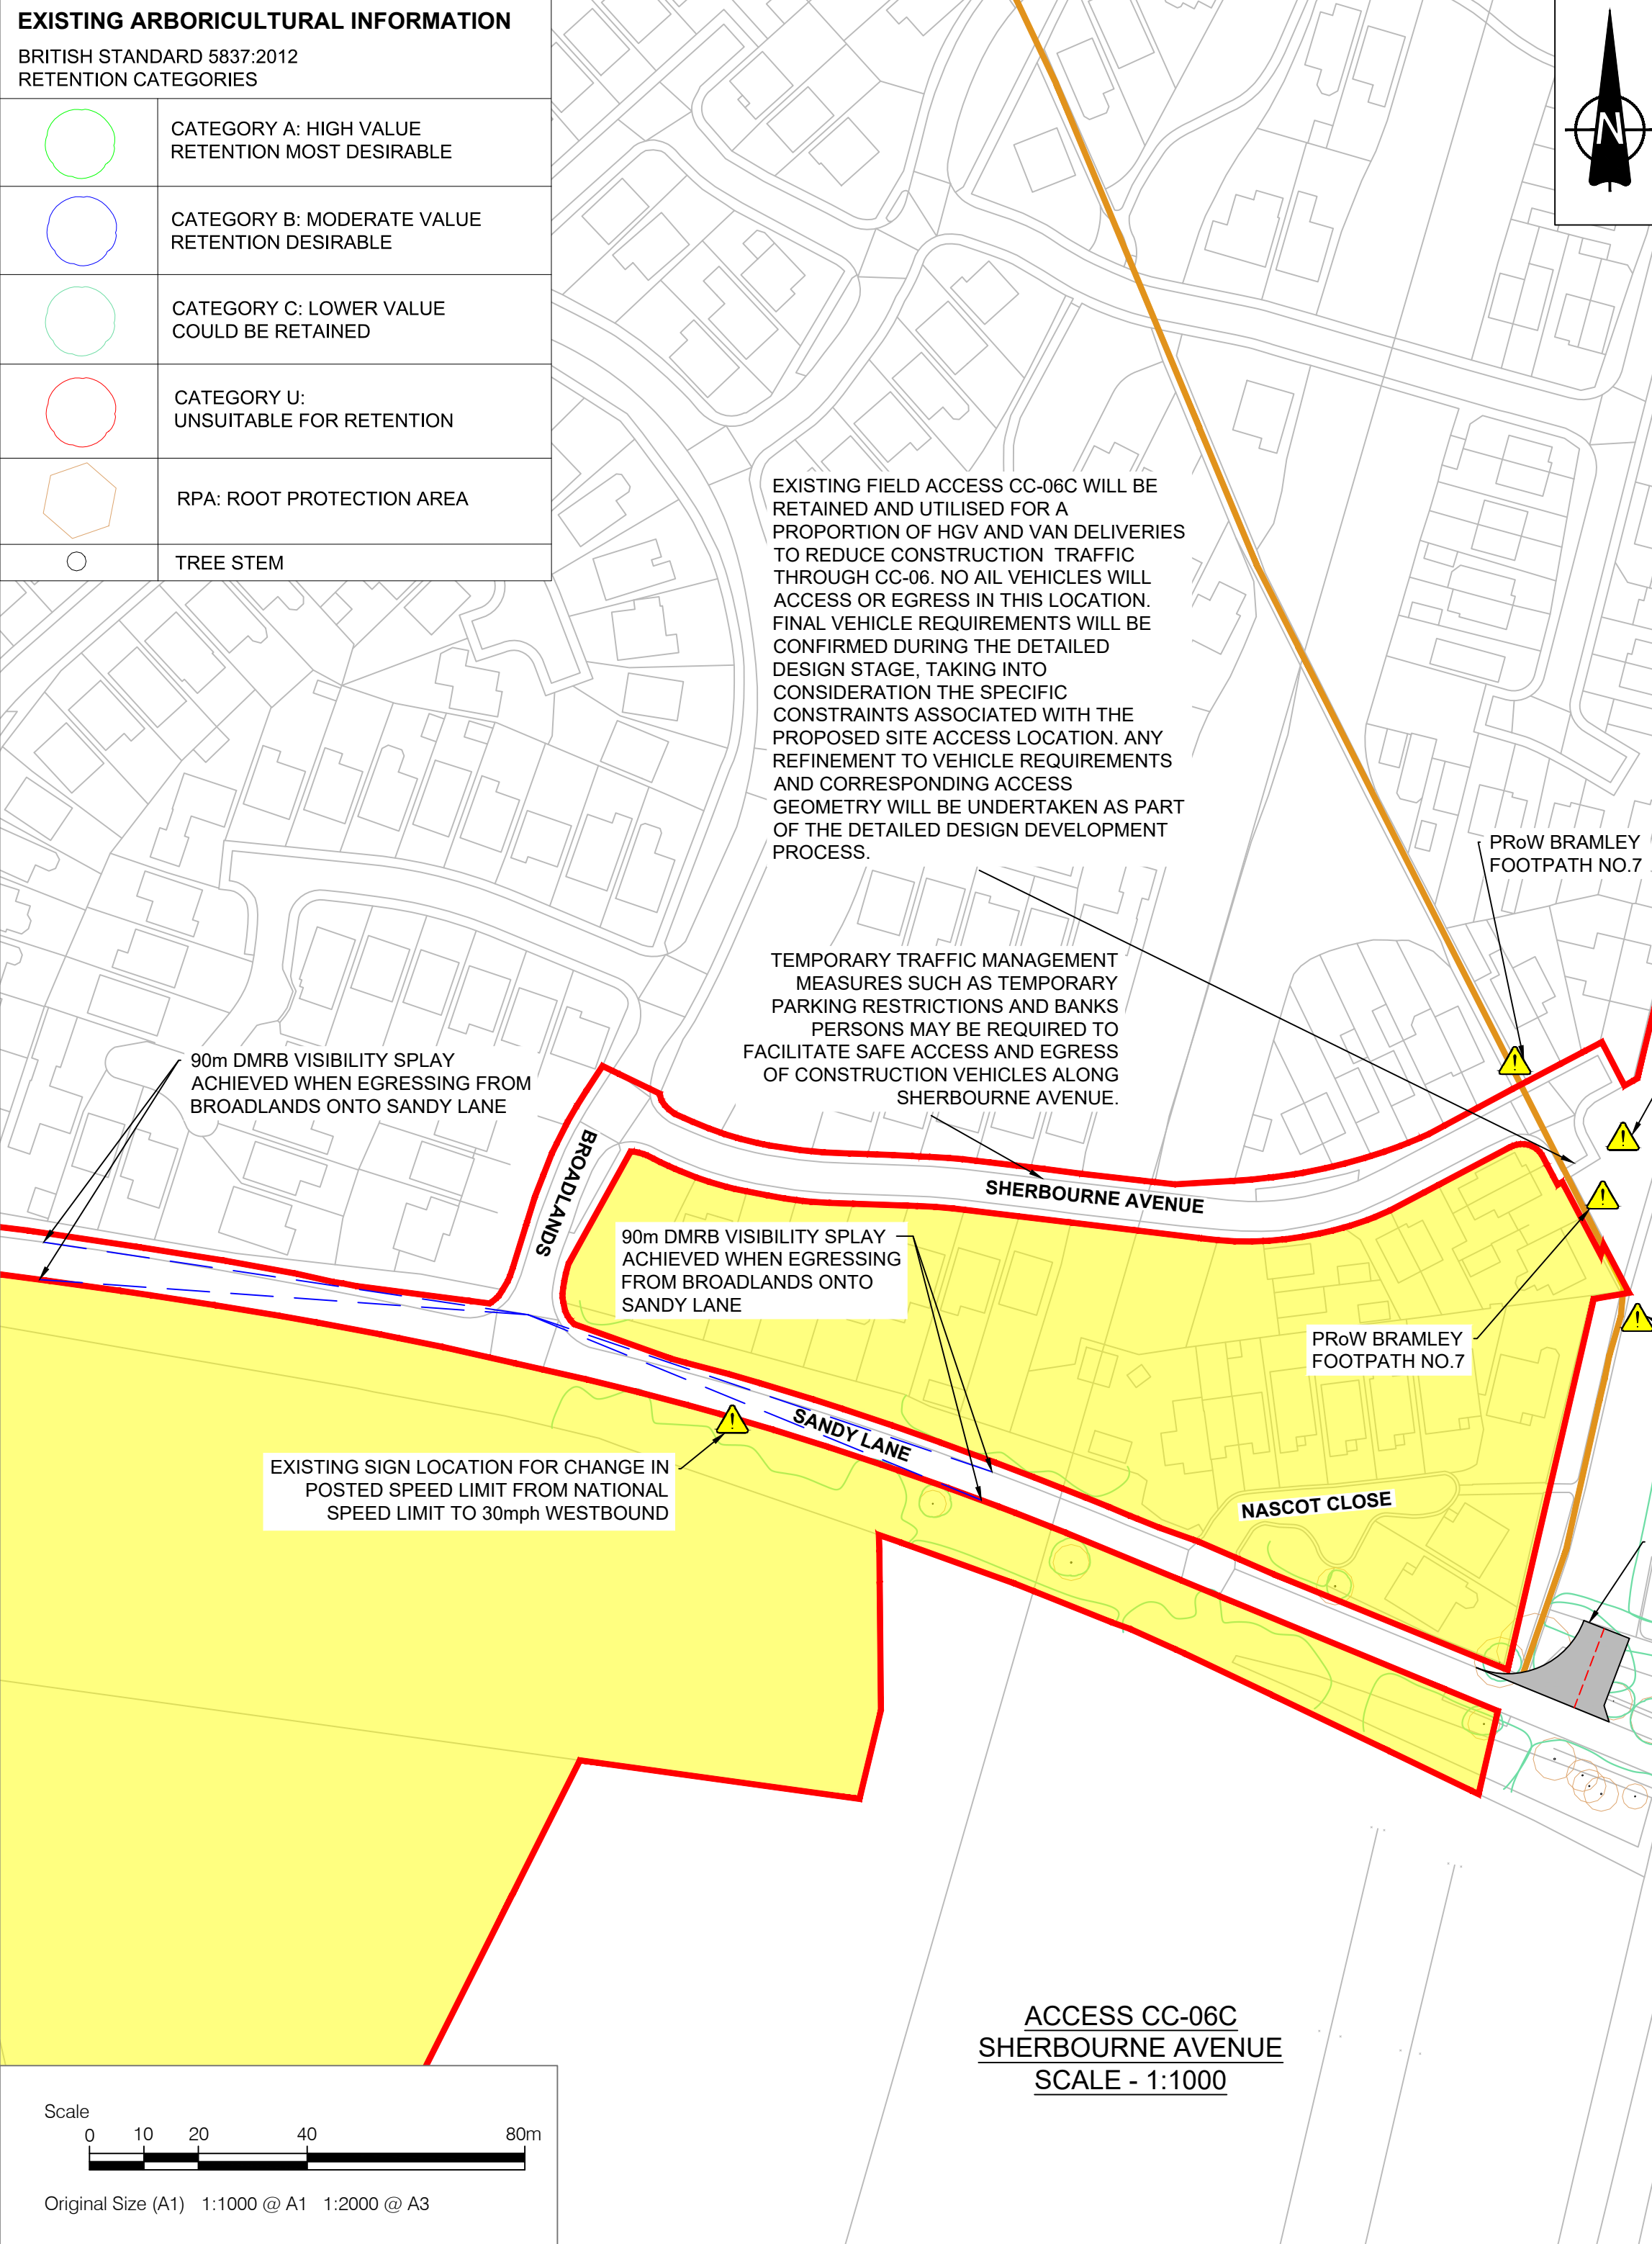

- NOTES**
- This drawing is to be read in conjunction with all other relevant documentation.
 - Do not scale from this drawing, use only printed dimensions.
 - All dimensions in meters, all chainages, levels and coordinates are in meters unless defined otherwise.
 - This drawing is to be read in conjunction with the project Health & Safety File for any identified potential risks.
 - Vegetation to be removed denotes any vegetation features (such as hedgerows) that need to be removed to provide the required junction visibility. Any verge grassland is not to be removed but managed by the relevant maintainer to a low height so as to not impact upon junction visibility.
 - The assessment for hedgerow to be removed has been carried out using aerial imagery and is an approximate value.
 - Vehicle tracking shown is indicative only, and represents approximate vehicle size & arrangement for the design vehicle shown.
 - Junction visibility for the access is based upon DMRB CD109 Table 2.10.

- LEGEND**
- Extent of Access Footprint
 - Order Limits
 - Land Excluded from Order Limits
 - Vehicle Body
 - Vehicle Body Path
 - Vehicle Load
 - Vehicle Load Path
 - Vehicle Wheels Path
 - Edge of Road
 - Access Centreline
 - Junction Visibility
 - Vegetation to be Removed for Vis Splay
 - Indicative Hedgerow Removal Vis Splay
 - Indicative Hedgerow Removal for Bellmouth Access
 - Health and Safety Risk Identifier
 - Existing Public Right of Way

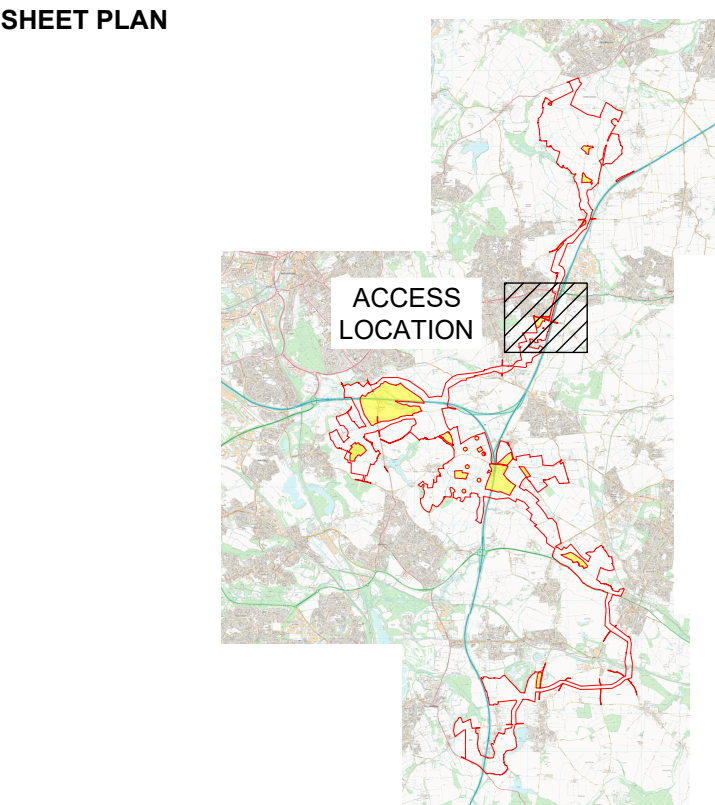

01	03/06/2026	DCO Submission	GH	MEK	JH
ISSUE	DATE	REMARKS	DRAWN	CHECK	APPROVED

TITLE:
Cable Corridor Area Access CC-06C
Appendix 3 - Sheet 53 of 53
Whitestone Solar Farm
Regulation 5(2)(o)

DRAWING DATE: 03/06/2026	
SCALE: 1:1000	SHEET: Sheet 53 of 53
SIZE: A1	REVISION: 01
DOCUMENT REFERENCE: EN0110020/APP/5.12	
APPLICATION NUMBER: EN0110020	





WHITESTONE
solar farm

Contact

Whitestone Net Zero Ltd

info@whitestonesolarfarm.co.uk

0800 688 9936
