

AENC-NG-CNS-REP-0233

Norwich to Tilbury

Volume 8: Examination Documents

Document: 8.3.17 Signed Statement of Common Ground -
Ralos Projects Ltd - Tracked Changes Version

Final Issue C

July 2026

Planning Inspectorate Reference: EN020027

nationalgrid

Revision History

Version	Date	Submitted at
A	26 February 2026	Deadline 1
B	12 May 2026	Deadline 4
<u>C</u>	<u>21 July 2026</u>	<u>Deadline 7</u>

Ralos Projects Ltd

~~Draft~~ Statement of Common Ground

1. Purpose of the Statement of Common Ground

This Statement of Common Ground (SoCG) has been prepared to ~~outline the areas of~~confirm to the Examining Authority where agreement ~~and any remaining points of discussion has been reached and where agreement has not been reached~~ between National Grid and Ralos Projects Ltd regarding specific issues arising during construction and / or operation from the interface between the proposed Norwich to Tilbury Project (the Project) and Land off Marsh Lane, Bracon, Ash, Norfolk.

~~The aim is to clarify the shared understanding of any issues and facilitate an efficient resolution process.~~

This final version of the SoCG has been submitted at Examination Deadline 7.

2. Parties to the SoCG

This SoCG ~~is agreed between~~has been prepared by National Grid (the Applicant) and Ralos Projects Ltd (on behalf of the landowner, Richard Long Group Ltd).

3. Summary of Matters ~~Under Discussion~~

~~As requested by the Examining Authority, the below table provides an ‘at a glance’ summary of matters which are under discussion, together with a deadline by which such matters are expected to be resolved.~~

SoCG-ID	Summary of matter under discussion	Deadline for resolution
7.1	Whether the overhead line works will permanently reduce the solar farm’s developable area.	By deadline 7
7.2	Removal of PV panels for haul road, unsure with pulling area	By deadline 7
7.3	Earthing study needs to be carried out to understand the financial impact	Likely to continue beyond deadline 7
7.4	Potential construction related effects, such as, SUDS, dust or damage to equipment. Haul Road needs to remain.	Likely to continue beyond deadline 7

7.5

~~Additional costs to the stakeholder due to the
NG works going on~~~~Likely to be discussed
beyond deadline 7~~

This final SoCG deals with 13 matters in total, of which 4 are agreed and 9 are under discussion.

Discussions between the Applicant and Ralos Projects Ltd necessarily will continue during detailed design, and for some matters into construction, including on the following matters:

- Project construction programme
- Ralos Projects Ltd scheme design alterations to accommodate the Project (including costs incurred)
- Project method for stringing (once selected)
- Final design of the Project, e.g. of the temporary haul road, final pylon design, position and conductor type
- Earthing assessment results and, if relevant, mitigation measures
- Compensation to Ralos Projects Ltd and Richard Long Group Ltd
- Potential for shading impacts
- Extent to which temporary removal of solar panels and associated structures will be required
- Impact on the existing S106 agreement

4. Background

4.1 Description of the Project/Development

National Grid Electricity Transmission plc ('National Grid') owns and maintains the national high voltage electricity transmission network throughout England and Wales. The transmission network connects the power from where it is generated to the regional Distribution Network Operators who then supply businesses and homes.

National Grid holds the Transmission Licence for England and Wales, and its statutory duty is to develop and maintain an efficient, coordinated and economical system of electricity transmission and to facilitate competition in the generation and supply of electricity, as set out in the Electricity Act 1989.

National Grid has developed plans for Norwich to Tilbury (referred to as the 'Project'). The Project would support the UK's net zero target through the connection of new low carbon energy generation in East Anglia and by reinforcing the transmission network.

The Project comprises reinforcement of the transmission network between the existing Norwich Main Substation in Norfolk and Tilbury Substation in Essex, via Bramford Substation, the new East Anglia Connection Node (EACN) Substation and the new Tilbury North Substation.

The reinforcement is needed because the existing transmission network, even with current upgrading, will not have sufficient capacity for the new renewable energy (a substantial proportion of which would be generated by offshore wind) that is expected to connect to the

network over the next 10 years and beyond. Completion of the Project, together with other new reinforcements across the country, will meet this future energy transmission demand both in East Anglia and across the UK.

The Project is a Nationally Significant Infrastructure Project (NSIP), and National Grid is seeking development consent under statutory procedures set by government. NSIPs are projects of certain types, over a certain size, which are considered by the government to be of national importance, hence permission to build them needs to be given at a national level, by the relevant Secretary of State (in this case the Secretary of State for Energy Security and Net Zero). Instead of applying to the local authority for planning permission, the developer must apply to the Planning Inspectorate for a Development Consent Order (DCO) that would grant development consent.

National Grid has submitted an application for development consent to the Planning Inspectorate. The Examining Authority (consisting of five examining inspectors), after a period of public examination, will make their recommendation to the Secretary of State for Energy Security and Net Zero, who in turn will decide on whether development consent should be granted for the Project.

The Project is identified as critical to delivering a network which supports the clean power pathways for 2030 delivery.

The Planning Act 2008 places duties on National Grid as the DCO applicant to consult with prescribed or affected persons as well as to take account of responses to consultation and publicity. In accordance with these statutory requirements, National Grid has undertaken two non-statutory and one statutory consultation to inform its proposals, with further targeted consultations.

5. Stakeholder Interests

Ralos Projects Ltd has been in correspondence with ~~National Grid~~ the Applicant over ~~the their~~ potential interaction with the ~~Norwich to Tilbury proposals. This Project.~~ The Ralos Projects Ltd interest has been identified as the proposed ~~Solar Farm, and fully consented solar farm,~~ close to ~~Land off~~ Marsh Lane, Bracon, Ash, Norfolk. The Ralos Projects Ltd proposals are understood as: *Solar farm of approximately ~~28MW~~ 32.7MW along with associated ancillary equipment including substations, fences and batteries.* The site is owned by Richard Long Group Ltd and Ralos Projects Ltd is carrying out the development. The site benefits from a direct grid connection to a local ~~33Kv National Grid transmission~~ 33kV UKPN overhead distribution line and ~~it the asset~~ is proposed to be in situation under a temporary permission for 40 years ~~and.~~ It was granted planning permission in July 2025 ~~(Ref: by South Norfolk District Council (planning application reference~~ 2023/1055). The grid connection date is to be confirmed.

~~National Grid is seeking to ensure that the interests of both parties and how they may be affected by the interaction are understood. From this position the aim is for the parties to agree actions to avoid or reduce the implications and for any remedial measures to be agreed. On this basis we seek the input from Ralos Projects Ltd to demonstrate how their interests may be affected, how Ralos Projects Ltd or National Grid and its contractors can collectively reduce those effects and input to agree the implementation of such measures.~~

6. Engagement history

- Non-statutory consultation ~~April-June~~: April - June 2022 (graduated swathe)
- Non-statutory consultation: June – August 2023 (draft alignment)
- Statutory consultation: April – July 2024
- Landowner consultation: June – July 2025
- Teams Meeting ~~Date: 1st October 2024, 10th September 2025, 14th November 2025~~, Dates:
 - ~~4th March 2026, 27th 1 October 2024~~
 - 10 September 2025
 - 14 November 2025
 - 4 March 2026
 - ~~27~~ April 2026 – Meeting to discuss SoCG
 - 22 June 2026 – Meeting to discuss SoCG
 - 29 June 2026 – Meeting to discuss SoCG
 - 2 July 2026 – Meeting to discuss SoCG
 - 6 July 2026 – Meeting to discuss SoCG
 - 13 July 2026 – Meeting to discuss SoCG
- The parties ~~continue~~continued to engage during the examination through regular email correspondence in relation to the matters described in this Statement of Common Ground.

1-3 Strand
London WC2N 5EH

T: +44 (0)20 7004 3000
www.nationalgrid.com



7. ~~6.~~ Matters Agreed

ID	Issue	Agreement reached	Date agreed	Relevant documentation
6.1 <u>7.1</u> Times sale	<u>Consent</u>	Planning application <u>permission</u> has been approved <u>granted</u> for the solar development.	4th of <u>4</u> July 2025	
<u>7.2</u>	<u>Pulling zone south of pylon RG18</u>	<u>The Applicant confirms that the pulling zone at pylon RG18 can be reduced to avoid the solar farm site and the expected reduction has been shared with Ralos Projects Ltd in a drawing (Figure 1: NTZZ-AAJ-OH70-RGZZZ-SKT-ZZ-000001).</u>	<u>22 June 2026</u>	
<u>7.3</u>	<u>SuDs</u>	<u>The location of the proposed sustainable drainage system (SuDS) features is being relocated south, outside of the solar farm site, thereby avoiding a permanent impact within the solar farm site. This is being completed through the ongoing detailed design process.</u>	<u>22 June 2026</u>	
<u>7.4</u>	<u>Regular meetings working towards agreeing Heads of Terms for a Legal Agreement</u>	<u>The Applicant will continue to engage with Ralos Projects Ltd as detailed design progresses with the aim of minimising impacts on the solar farm site. Ralos Projects Ltd and the Applicant have agreed to have a monthly teams meeting, starting following SoCG completion. Ultimately, the parties acknowledge they should aim to agree heads of terms, and then a legal agreement between the parties.</u>	<u>22 June 2026</u>	

8. ~~7.~~ Matters Currently Under Discussion

ID	Issue	National Grid Position	Stakeholder <u>Ralos Projects Ltd</u> Position	Status	Relevant documentation
<u>8.1</u>	<u>Construction programme</u>	<u>The Applicant will provide timely updates to Ralos Projects Ltd as the construction programme develops.</u>	<u>Ralos Projects Ltd require a tentative construction programme to enable them to consider how they can work with the Applicant.</u>		
<u>8.2</u>	<u>Costs associated with Ralos Projects Ltd scheme design alterations</u>	<u>The Applicant welcomes Ralos Projects Ltd's suggestion to review their design in relation to the haul road and understands that Ralos Project Ltd will incur costs in relation to this review. The Applicant also welcomes more discussion with Ralos Projects Ltd on the costs associated with reviewing such options.</u>	<u>Ralos Projects Ltd are trying to work collaboratively with National Grid. Ralos Projects Ltd are prepared to hold discussions with their appointed EPC to consider potential opportunities to evolve their established design. National Grid should be aware that there would be costs associated with reviewing such options and that no assurances can be given regarding the outcome.</u>		
7.4 <u>8.3</u>	Permanent loss of development footprint <u>Method for</u>	<u>The Applicant acknowledges that temporary removal of panels and associated structures and infrastructure may be required to facilitate stringing construction activities. These impacts will be temporary</u>	<u>Ralos Projects Ltd preferred stringing methodology is innovative first choice (method still to be agreed by all parties), and then second choice scaffold. The ground clear option requiring removal of panels and associated structures and infrastructure is the least preferred option.</u>	Ongoing discussion	2023/1055F planning application with South Norfolk Council on behalf of Ralos Projects Ltd.

1-3 Strand
London WC2N 5EH

T: +44 (0)20 7004 3000
www.nationalgrid.com



ID	Issue	National Grid Position	Stakeholder <u>Ralos Projects Ltd</u> Position	Status	Relevant documentation
	<u>stringing</u>	<u>only, and the Applicant will agree with Ralos Projects Ltd how affected areas are reinstated following completion, allowing for the installation (or reinstallation) of solar panels and associated structures and infrastructure thereafter.</u> <u>The method of stringing is currently being assessed. The three main options are ground clear, scaffold or innovative (minimum site access requirement). The Applicant acknowledges Ralos Projects Ltd preference as stated herein and is taking account of that.</u> <u>The ground clear method would require establishment of a temporary working corridor beneath the overhead line (and approximately 10m either side) to allow for safe stringing operations.</u> It is confirmed that there will only be a loss of footprint should the	<u>Ralos Projects Ltd have asked the Applicant to confirm how the compensation code would apply to the impacts on them (eg. are all costs covered, fees, etc.).</u> The permanent loss of development footprint could potentially result in an inability to install the fully consented Solar PV generation facility, causing associated economic loss. <u>Ralos Projects Ltd expects that an undertaking to cover all associated costs & losses, such as professional fees and project management costs, where required will be afforded.</u>		

1-3 Strand
London WC2N 5EH

T: +44 (0)20 7004 3000
www.nationalgrid.com

ID	Issue	National Grid Position	Stakeholder <u>Ralos Projects Ltd</u> Position	Status	Relevant documentation
		proposed pulling zone have to remain for operational purposes. The Applicant, in developing its design (including overhead line alignment and project order limits) and DCO limits of deviation, has identified ‘pulling zones’ for conductor installation and future reconductoring of the overhead line. It is recognised that the ‘pulling zones’ around tower RG18 are of concern to Ralos Projects development. As part of detailed design and construction planning, the Applicant will seek to reduce the size of the zones needed around the aforementioned tower. Where the Applicant needs to retain “pulling zones” that have an impact on the stakeholder’s interest, the Applicant will pay compensation where it is due under either the Compensation Code or relevant statutory provisions. <u>Where impacts are not mitigated and the temporary</u>			

ID	Issue	National Grid Position	Stakeholder <u>Ralos Projects Ltd</u> Position	Status	Relevant documentation
		<u>removal of solar apparatus and associated structures and infrastructure is required to enable construction of the Project, the Applicant welcomes discussions with Ralos Projects Ltd to agree the costs associated with those works in accordance with the compensation code. In accordance with the compensation code this may include an undertaking to cover reasonable associated costs and losses, such as professional fees and project management costs, where required.</u>			
<u>7.2</u> <u>8.4</u>	<u>Temporary- Removal of Panels to create space for construction works</u> <u>Haul road</u>	<u>The Applicant acknowledges that temporary removal of panels and associated structures and infrastructure will be required to facilitate haul road construction activities. The haul road will be formed along the eastern side of the site. These impacts will be temporary only but longer in duration than</u>	<u>Ralos Projects Ltd has requested information relating to a worst case maximum width haul road in order to allow them to consider their design and how it will work with the Applicant's scheme. Ralos Projects Ltd have asked the Applicant to confirm how the compensation code would apply to the impacts on them (eg. are all costs covered, fees, etc.).</u> <u>Removal of panels from the scheme will result in</u>		<u>Ongoing discussion</u>

ID	Issue	National Grid Position	Stakeholder <u>Ralos Projects Ltd</u> Position	Status	Relevant documentation
		<u>stringing activities (almost full duration of Project construction). The Applicant will agree with Ralos Projects Ltd how affected areas will be reinstated following completion, allowing for the installation (or reinstallation) of solar panels and associates structures and infrastructure thereafter.</u> <u>The Applicant is currently evaluating the design of the haul road with the possibility of straightening the road. The Applicant will confirm when this information can be shared.</u> It is not yet confirmed whether the project will require the temporary removal of panels to facilitate its development. The Applicant will continue to engage with Ralos Projects Ltd, as the detailed design develops, to understand and address any implications of the project on the development. The Applicant believes that through	an inability to achieve full generation capability from the Solar PV facility, causing associated economic loss. <u>Ralos Projects Ltd expects that an undertaking to cover all associated costs such as professional fees and project management costs, where required will be afforded.</u>		

1-3 Strand
London WC2N 5EH

T: +44 (0)20 7004 3000
www.nationalgrid.com



ID	Issue	National Grid Position	Stakeholder <u>Ralos Projects Ltd</u> Position	Status	Relevant documentation
		modifications to the detail of its proposals, any potential temporary impacts on either the extent of solar panels or performance of the site, could be limited. <u>Where impacts are not mitigated and the temporary removal of solar apparatus and associated structures and infrastructure is required to enable construction of the Project, the Applicant welcomes discussions with Ralos Projects Ltd to agree the costs associated with those works in accordance with the compensation code. In accordance with the compensation code this may include an undertaking to cover reasonable associated costs, such as professional fees and project management costs, where required.</u>			
<u>7.3</u> <u>8.5</u>	Modificatio ns to Existing	<u>The Applicant acknowledges these concerns and is undertaking further technical</u>	Any <u>Ralos Projects Ltd raised concerns that any requirement for additional earthing</u> in relation to <u>arising from the proximity of the consented</u>		Ongoing discussion

1-3 Strand
London WC2N 5EH

T: +44 (0)20 7004 3000
www.nationalgrid.com

nationalgrid

ID	Issue	National Grid Position	Stakeholder <u>Ralos Projects Ltd</u> Position	Status	Relevant documentation
	<u>Equipment Earthing</u>	<u>assessment to better understand whether any additional earthing requirements could arise and, if so, the extent of any associated impacts. Based on previous studies, significant impacts are not currently expected, however, this will be confirmed through ongoing assessment. Where mitigation is required, the Applicant will work with Ralos Projects Ltd to agree an appropriate solution, including cost considerations where applicable.</u> The Applicant recognises Ralos Projects' concerns in relation to potential earthing implications of the Project on the stakeholder's solar development. Where additional earthing is required as a result of the project. The Applicant will work with stakeholders to ensure sites are protected.	<u>solar farm to the proposed 400kV infrastructure will result in an could impose an unanticipated economic cost burden. This cost burden is not captured in</u> They noted that such costs are not currently accounted for within the CAPEX model for our <u>their</u> solar scheme. <u>Ralos Projects Ltd earthing design is not yet complete.</u>		

1-3 Strand
London WC2N 5EH

T: +44 (0)20 7004 3000
www.nationalgrid.com



ID	Issue	National Grid Position	Stakeholder <u>Ralos Projects Ltd</u> Position	Status	Relevant documentation
		The Applicant is commissioning a report to screen the site for earthing impact from the OHL. Previously, the Applicant completed an earthing screening study of some other sites near the route. The study showed the project will have no earthing impact on solar farms with a project interface. The detailed design of the Project will continue into 2027. It won't be possible to finalise the assessment of earthing requirements until the detailed design is further progressed. Any earthing interaction and coupling studies will be compliant with BS EN 50522, ENA TS 41-24 and the relevant national and NG OHL design standards. If additional earthing is required within your site boundary, the Applicant's proposed approach would be to support to upgrade the existing system. Compensation may be			

ID	Issue	National Grid Position	Stakeholder Position	Ralos Projects Ltd	Status	Relevant documentation
		due under either the Compensation Code or relevant statutory provisions. A technical note on earthing which will be shareable with Ralos Projects Ltd should be available by the end of July. This will identify if the Applicant would benefit from reviewing Ralos Projects Ltd completed earthing system design when it becomes available.				
8.6	<u>Compensation</u>	<u>Where temporary or permanent impacts give rise to losses, these will be addressed through appropriate compensation mechanisms (in accordance with the compensation code), with costs/losses discussed and agreed with Ralos Projects Ltd as necessary.</u> <u>Where additional operational costs/losses are identified and agreed to arise as a direct consequence of the Project, the Applicant is willing to engage</u>	<u>Ralos Projects Ltd has identified that temporary construction activities will give rise to consequential losses and an increased maintenance burden associated with the solar PV facility.</u> <u>Ralos Projects Ltd requires agreed recovery mechanisms to be put in place to ensure full cost recovery in relation to the potential for additional operational costs/losses associated with the solar PV facility and lost revenue through reduced generation export as a result of the Proposed Development.</u>			

ID	Issue	National Grid Position	Stakeholder <u>Ralos Projects Ltd</u> Position	Status	Relevant documentation
		<u>with Ralos Projects Ltd to agree an appropriate approach to addressing such costs/losses (in accordance with the compensation code).</u>			
<u>7.4</u> <u>8.7</u>	Temporary Construction Effects <u>Shading</u>	<u>The Applicant recognises Ralos Projects Ltd's concerns in relation to potential shading implications of the Project on the solar farm development.</u> <u>The final pylon design, conductor type and position information is expected to be available in 2027. Once this information is available the Applicant can share this information with Ralos Projects Ltd. Provisional information can be also shared ahead of this time but this will be subject to change as the design is finalised.</u> Based on the current design, haul roads will need to remain within the solar farm, possibility that SUDS location can be	<u>Ralos Projects Ltd has raised a concern that the Project may cause shading.</u> Any consequential losses and additional maintenance burden resulting from NG works will need to captured and recompensed — for further discussion. <u>Ralos Projects Ltd expects that compensation to cover all associated losses as a result of shading, will be afforded.</u>		Ongoing discussion

ID	Issue	National Grid Position	Stakeholder <u>Ralos Projects Ltd</u> Position	Status	Relevant documentation
		moved, this position will be confirmed through the detailed design. The Applicant will implement appropriate mitigation and reinstatement should any construction related effects arise. <u>Shading could be a compensation matter according to the Compensation Code or any statutory provisions. Such matters would be assessed on a case-by-case basis, in accordance with the Planning Act 2008 and the statutory Compensation Code and are not matters to be determined through the Examination of the DCO.</u>			
7.5 <u>8.8</u>	<u>Other</u> Operational Effects- (excluding reduced panel numbers)	The <u>With the exception of shading, the</u> Applicant does not expect its infrastructure <u>the Project</u> to result in any <u>permanent</u> operational impacts on the solar <u>PV</u> facility. The Applicant will continue to engage with Ralos Projects Ltd to confirm operational interfaces	Consideration should be given to additional operational costs for the Solar PV facility as a result of the NG works <u>Ralos Projects will only accept the full reinstatement of any plant, equipment and assets that were in situation prior to the commencement of any Norwich to Tilbury site works taking place. The solar PV facility must be reinstated to its full, original capability, including any recommissioning, testing &</u>		Ongoing discussion

ID	Issue	National Grid Position	Stakeholder <u>Ralos Projects Ltd</u> Position	Status	Relevant documentation
		as the detailed design progresses and ensure to adverse effects arise Where works affect existing solar PV infrastructure, the Applicant would expect affected assets to be reinstated to an equivalent operational condition following completion of the works. The precise scope of any reinstatement works, including any testing and commissioning requirements, will be determined once the extent of any affected infrastructure has been confirmed. Any compensation arising from the Proposed Development, including claims relating to loss of generation, asset damage, replacement costs or other associated losses, would be considered in accordance with the Compensation Code and any relevant land rights arrangements.	<u>acceptance activities required to support this. The NG project must also ensure that any damages incurred by their works are rectified or suitable replacement assets are supplied, installed, commissioned and set to work such that the original capability is reinstated and that equipment warranties are not compromised. Full compensation for the loss of generation from the first point the panels and associated structures & infrastructure were switched out, to their full reinstatement to solar PV generation capability must also be provided. Any associated project & site management costs/fees incurred by Ralos Projects Ltd in support of the above must also be fully reimbursed.</u>		
<u>8.9</u>	<u>S106</u>	<u>The Applicant notes this</u>	<u>The landscape mitigation secured through the</u>		

ID	Issue	National Grid Position	Stakeholder <u>Ralos Projects Ltd</u> Position	Status	Relevant documentation
	<u>Impact on Ralos Project Ltd site</u>	<u>concern. Should the Proposed Development affect landscaping required pursuant to the Section 106 Agreement, the Applicant would engage with Ralos Projects Ltd and Richard Long Group Ltd to resolve concerns. The Applicant will welcome evidenced claims for associated costs in so far as they accord with the compensation code.</u>	<u>S106 and conditions on planning permission reference 2023/1055 was crucial in the consented solar PV scheme being able to demonstrate an acceptable landscape impact and ultimately enabled the application to be approved. It is noted in particular that the S106 secured early planting which allowed a period of time for it to mature in advance of the completion of the project.</u> <u>Based on the plans within the Norwich to Tilbury DCO and likely timescales for its implementation it is clear that a Deed of Variation (DoV) of the original S106 will be required. This will need to address the following points within the area affected:</u> <u>Amend planting timescales to facilitate replacement planting of mitigation features following the DCO's impact</u> <u>Timescale for re-planting of mitigation to be conducted in the first planting season following the land becoming available following the DCO works</u> <u>Amend planting specifications to include more mature plants to directly compensate for loss of screening which will be between 1 and 3</u>		

ID	Issue	National Grid Position	Stakeholder <u>Ralos Projects Ltd</u> Position	Status	Relevant documentation
			<u>years behind the rest of the mitigation at a minimum and will likely be much longer depending on the DCO start date.</u> <u>Amend management plans to account for later planting and to extend the period for replacement planting in the event of new planting dying within 10 years of planting</u> <u>Amend management plans of areas between panels to account for period of removal/disturbance</u> <u>Introduction of a requirement to re-plant of any existing landscape feature (trees or hedge) that screened the development within the S106 area that is removed as part of the DCO project</u> <u>Require land conditions to be restored to its current baseline to ensure mitigation planting can take hold and mature in the same way it can on the existing site.</u> <u>These details will be subject to the submission of revised documents and the legal instruction to process a DoV from the applicant and the Local Planning Authority to their respective legal teams. The details will not be agreed until the DoV is</u>		

1-3 Strand
London WC2N 5EH

T: +44 (0)20 7004 3000
www.nationalgrid.com



ID	Issue	National Grid Position	Stakeholder <u>Ralos Projects Ltd</u> Position	Status	Relevant documentation
			<u>signed by all relevant parties, sealed by the Local Planning Authority and completed. The Local Planning Authority expects the applicant to cover the legal costs of any DoV requested; in the same way it does for the original S106 agreement. The DoV will be required to demonstrate that the application remains acceptable following the amendments in order for the Local Planning Authority to be able to sign it off.</u> <u>We have noted that there is also an unexpected contamination condition that would pick up a requirement to assess and remediate any contamination discovered on site; this would likely pick up anything introduced from the DCO and then found during re-planting or reinstatement of solar apparatus and associated structures & infrastructure. There are also conditions relating to ecology and tree protection that may require additional details submitted or amendments made to facilitate the DCO development. This would likely be in the form of additional discharge of condition applications with the associated documents to be submitted. Discharge of condition applications currently cost £309 per</u>		

1-3 Strand
London WC2N 5EH

T: +44 (0)20 7004 3000
www.nationalgrid.com



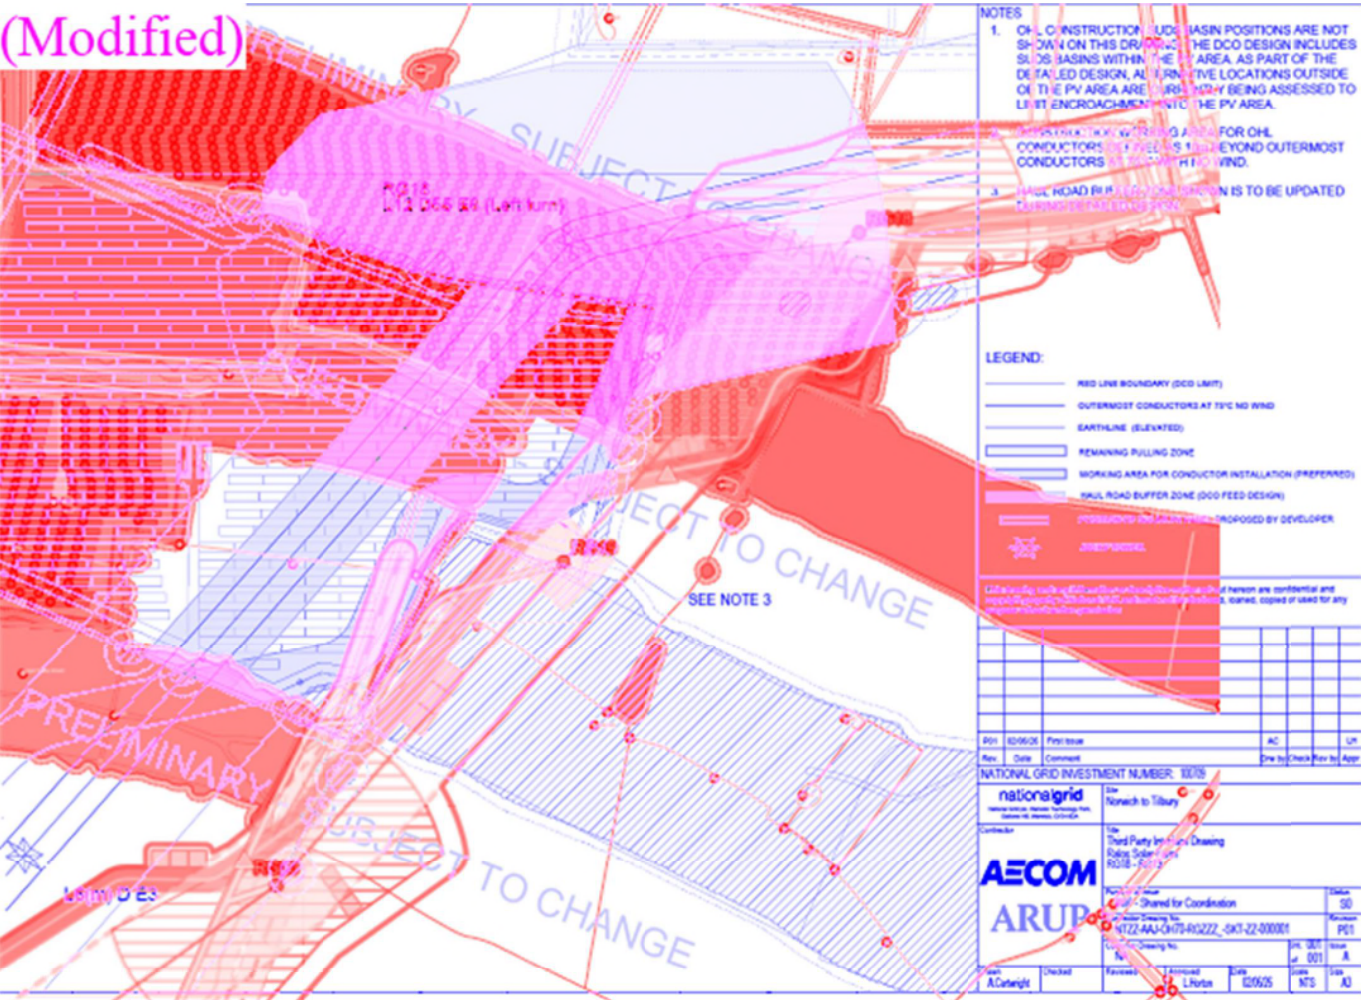
ID	Issue	National Grid Position	Stakeholder Position	Status	Relevant documentation
			<u>Ralos Projects Ltd</u> <u>application, and this rises with inflation each year.</u>		

1-3 Strand
London WC2N 5EH

T: +44 (0)20 7004 3000
www.nationalgrid.com



Figure 1 Interaction between the Project alignment and the Ralos Project Ltd. development




1-3 Strand
London WC2N 5EH


T: +44 (0)20 7004 3000
www.nationalgrid.com



9. ~~8.~~ **Signatures**

This Statement of Common Ground is agreed upon by the undersigned parties:


For National Grid 

Name:  _____

Position: Project Director

Date: 20/07/2026

For Ralos Projects Ltd [and Richard Long Group Ltd](#)

Name:  _____ 

Position: Director

Date: 20. 07. 26

National Grid plc
National Grid House,
Warwick Technology Park,
Gallows Hill, Warwick.
CV34 6DA United Kingdom

Registered in England and Wales
No. 4031152
[nationalgrid.com](https://www.nationalgrid.com)

Summary report: Litera Compare for Word 11.16.0.74 Document comparison done on 7/15/2026 12:55:25 PM	
Style name: Default Style	
Intelligent Table Comparison: Active	
Original filename: 8.3.17 Draft Statement of Common Ground - Ralos Projects Ltd Revision B Clean Version.docx	
Modified filename: 8.3.17 Signed Statement of Common Ground - Ralos Projects Ltd Revision C Clean Version.docx	
Changes:	
Add	152
Delete	66
Move From	0
Move To	0
Table Insert	6
Table Delete	16
Table moves to	0
Table moves from	0
Embedded Graphics (Visio, ChemDraw, Images etc.)	1
Embedded Excel	0
Format changes	0
Total Changes:	241
